



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation

480th Flash Report on Central Sector Infrastructure Projects



Scan the QR code to access
the PAIMANA Portal.

(Rs. 150 crore
& above)

OCTOBER 2025



CONTENTS

I. Overview*	2-4
II. North Eastern Region	5-6
III. As per Harmonized Master List (HML) 2022	7-13
IV. Major Infrastructure Central Ministries & Departments	14-19
V. Appendix : <i>List of Tables</i>	20 onwards
Table 1: Ministry-wise Ongoing Projects	
Table 2: State-wise Ongoing Projects	
Table 3: Completed Projects	
Table 4: Newly Added Projects	
Table 5: Ongoing Projects of North Eastern Region	
Table 6: All Ongoing Projects	

**Note: This report is web-generated from the PAIMANA portal (ipm.mospi.gov.in) as of October 2025, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies (excluding Ministry of Road Transport & Highways, may reflect from next month onwards) on the IPM portal (indiainvestmentgrid.gov.in) latest by 14th November 2025.*





Overview





Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above

OCTOBER 2025

820 | 16

Ongoing Projects |
Line Ministries & Departments

₹ 25,52,632

Original Cost
(crores)

₹ 30,83,532

Revised Cost
(crores)

₹ 16,11,188

(52.25% of Revised Cost)

Expenditure
(crores)

6


Commissioned during month

30

Newly Added during month


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

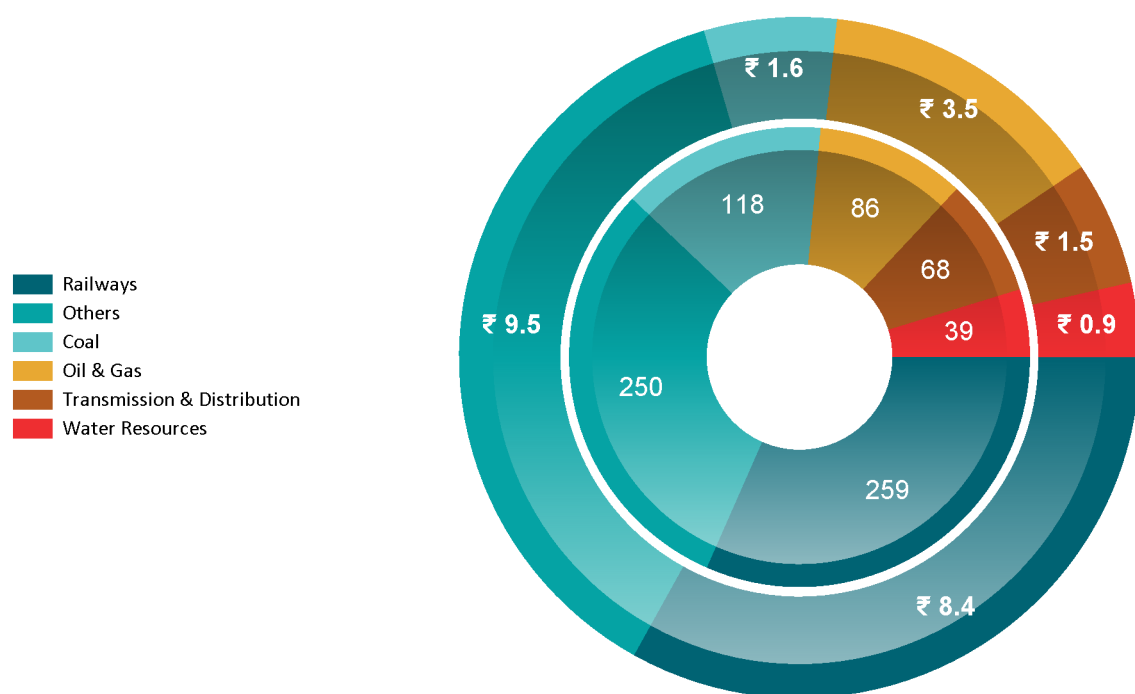


Ministry Comparison : Major Ministries*


[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

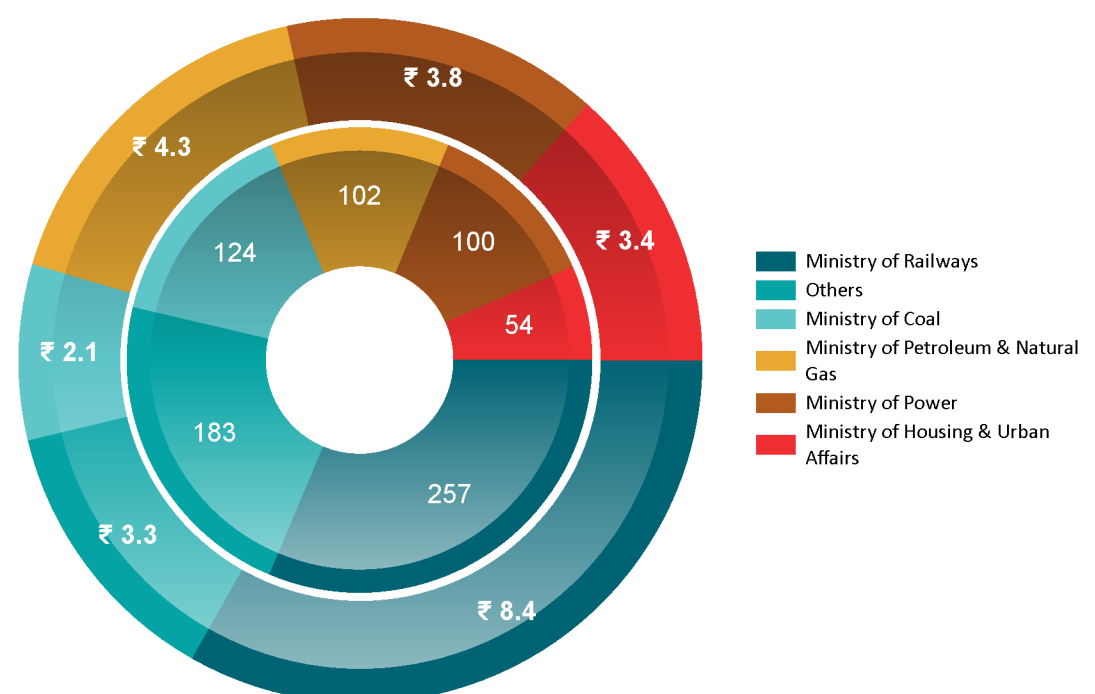

Cost Analytics : Major Sectors*

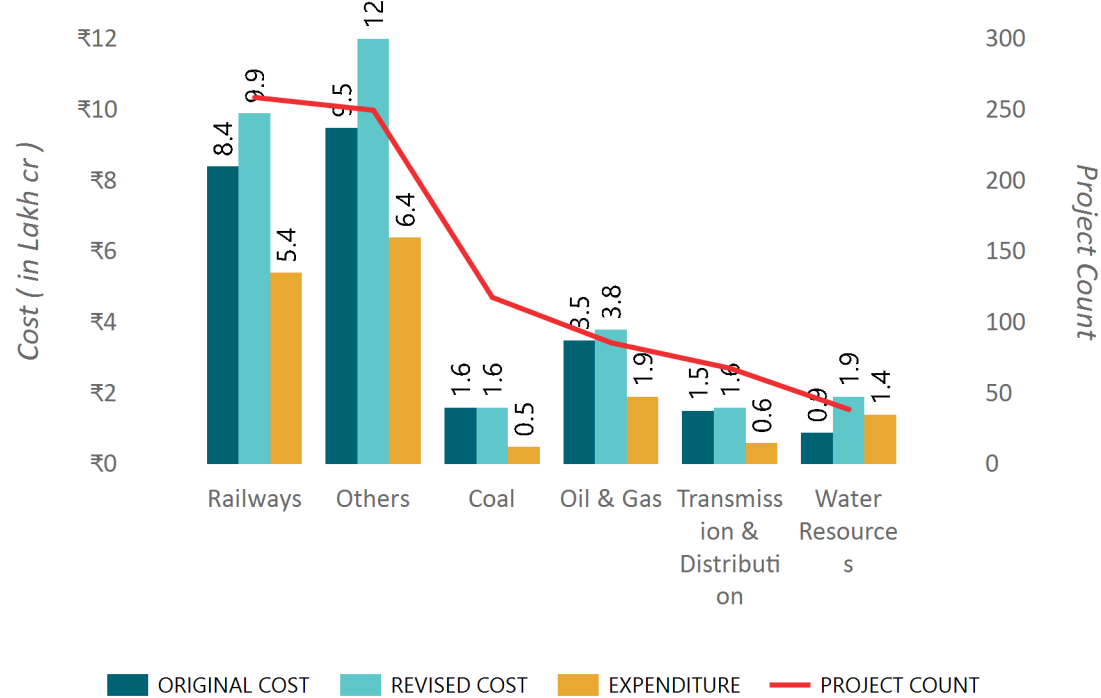


Cost Analytics : Major Ministries*

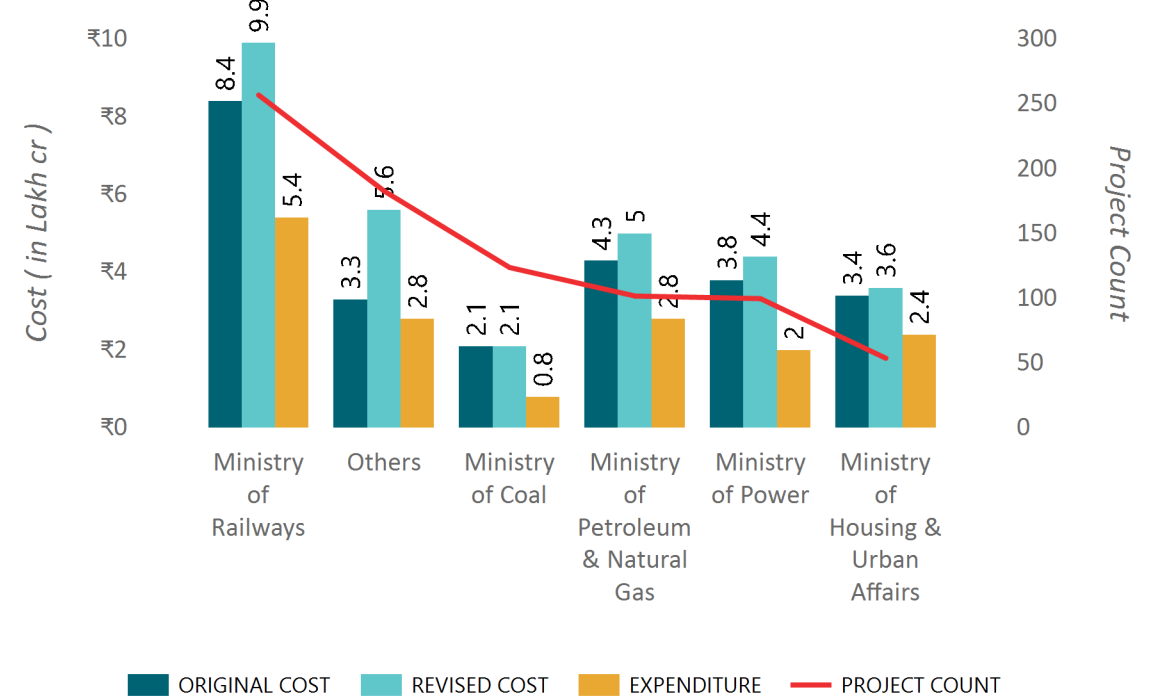


Note: * as per Project Count

Analytics: as per HML

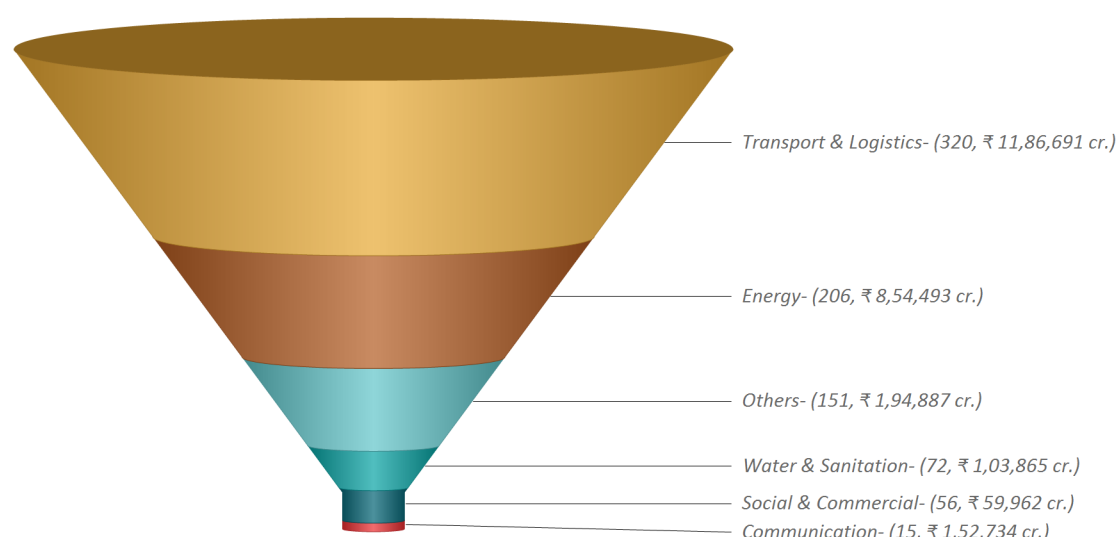


Note: all indicated legends are in format (Project count, Original Cost in crores)

Physical & Financial progress (%) : Project count

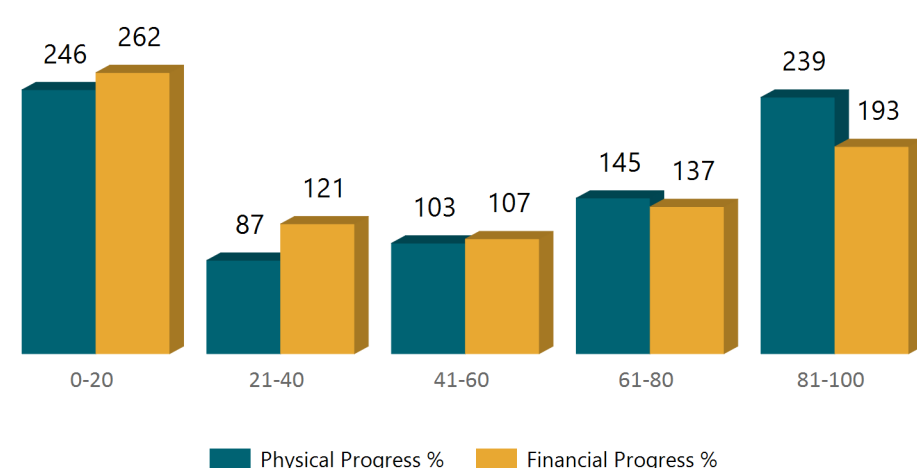




State Comparison : Major States*

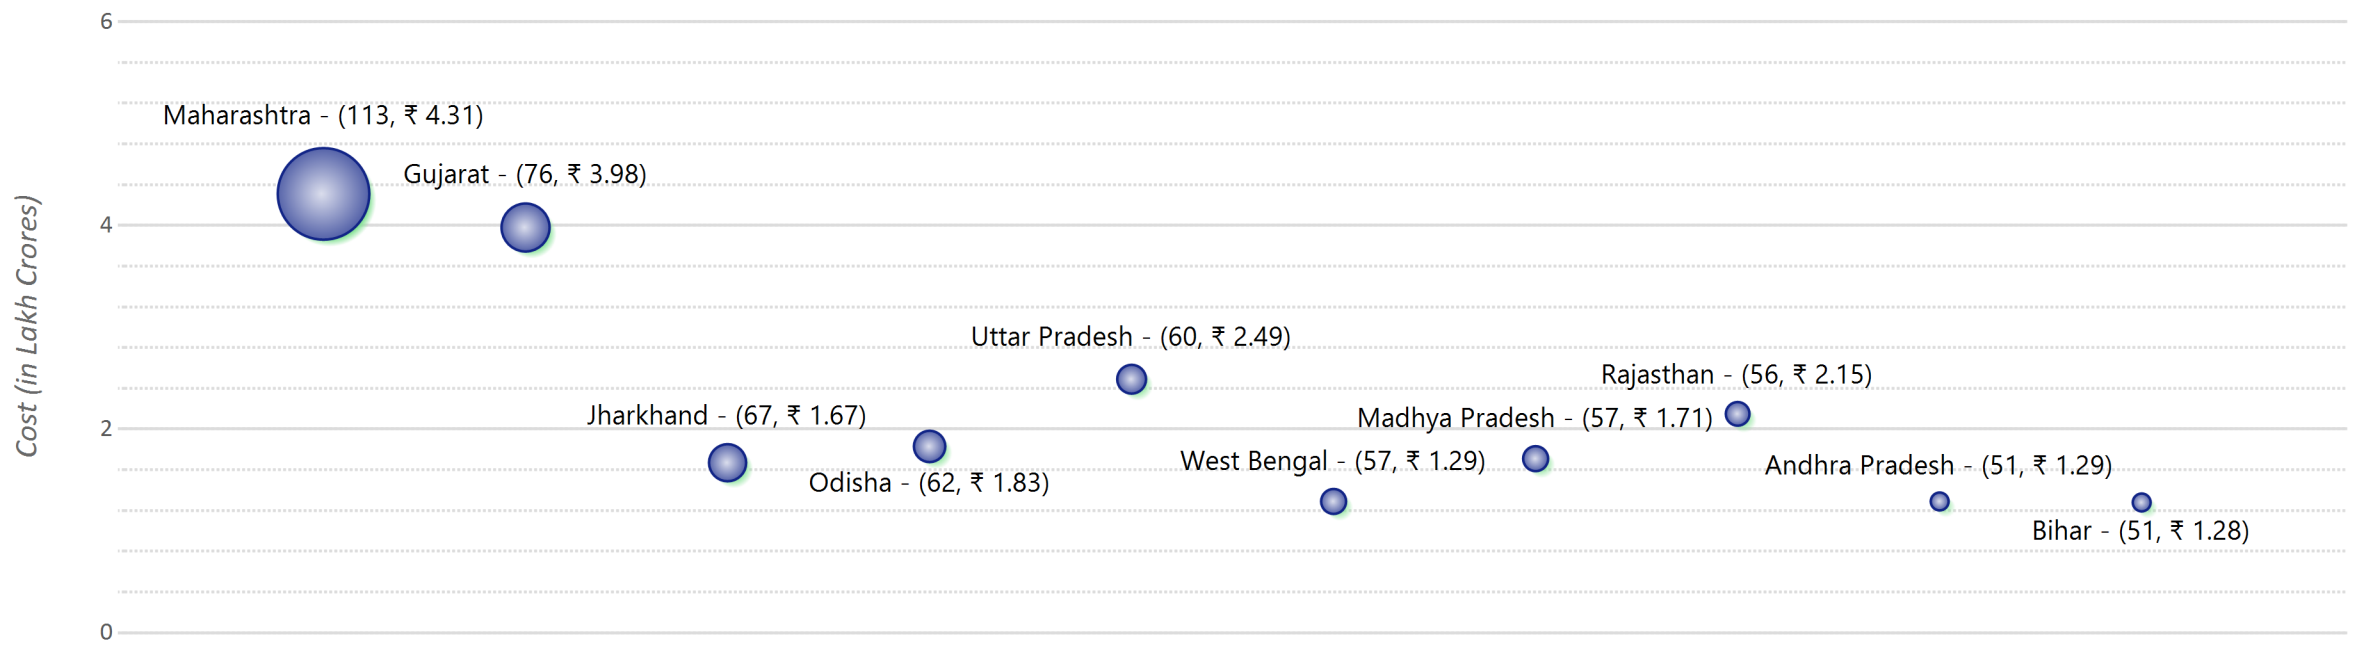


Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count

Ministry-wise Distribution of total 239 projects with reported Physical Progress between 81-100%

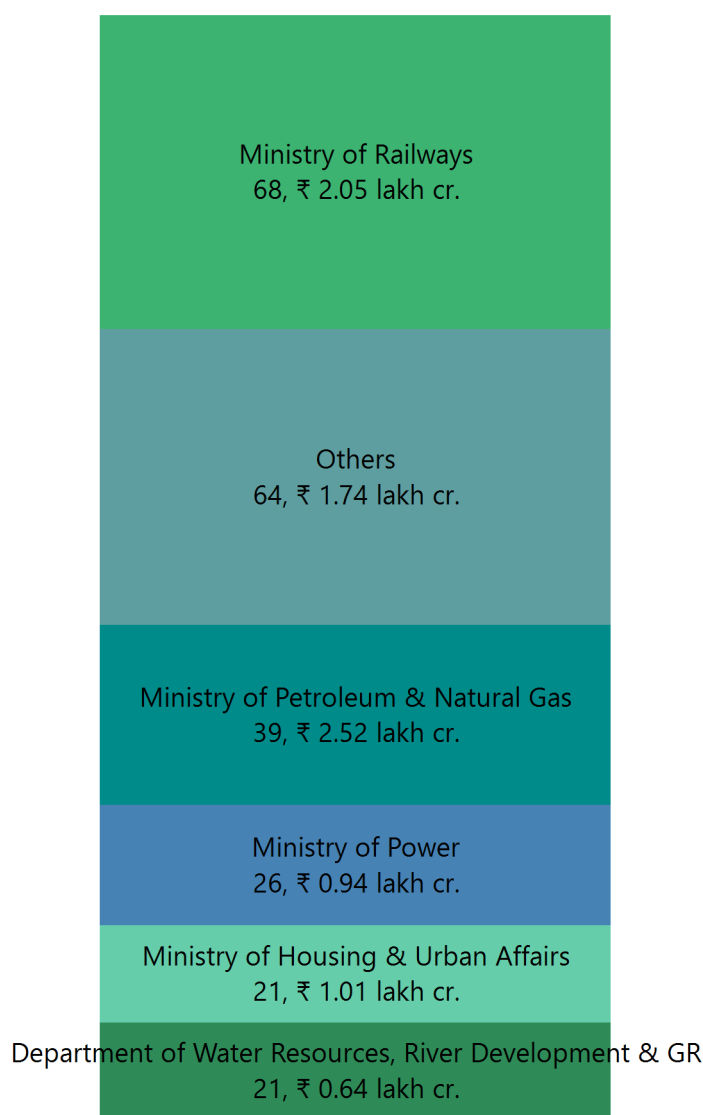

Total Ongoing Projects: Mega & Major

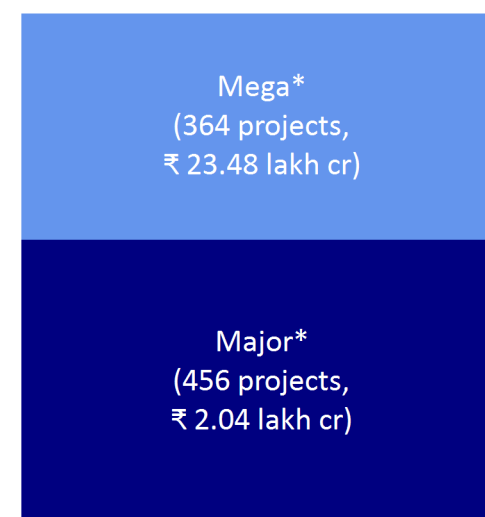


Total North East Region Ongoing Projects: Mega & Major




Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost $\geq$ 1000 crore
* Major project if having original cost $<$ 1000 crore

Project volume (nos.)

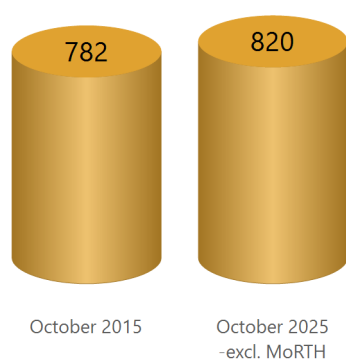


Change in Project Count : +5%

Total Project value (in lakh crore)

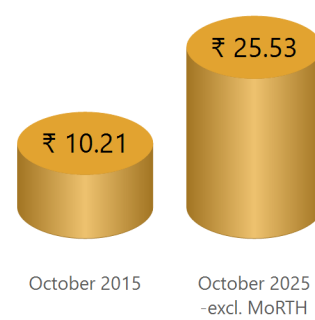

Change in Total Value : +153%

Cumulative Expenditure (in lakh crore)

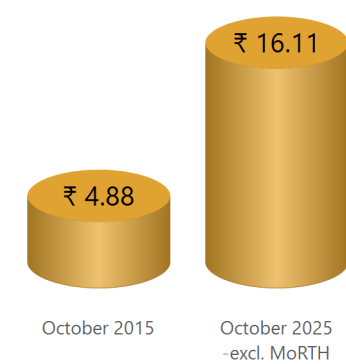

Change in Expenditure : +225%



North Eastern Region





Special Focus : North Eastern Region

OCTOBER 2025

56 | 11

Ongoing Projects |
Line Ministries & Departments

₹ 1,87,809

Original Cost
(crores)

₹ 2,75,787

Revised Cost
(crores)

₹ 1,91,404

(69.4% of Revised Cost)

Expenditure
(crores)

0


Commissioned during month

2


Newly Added during month

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

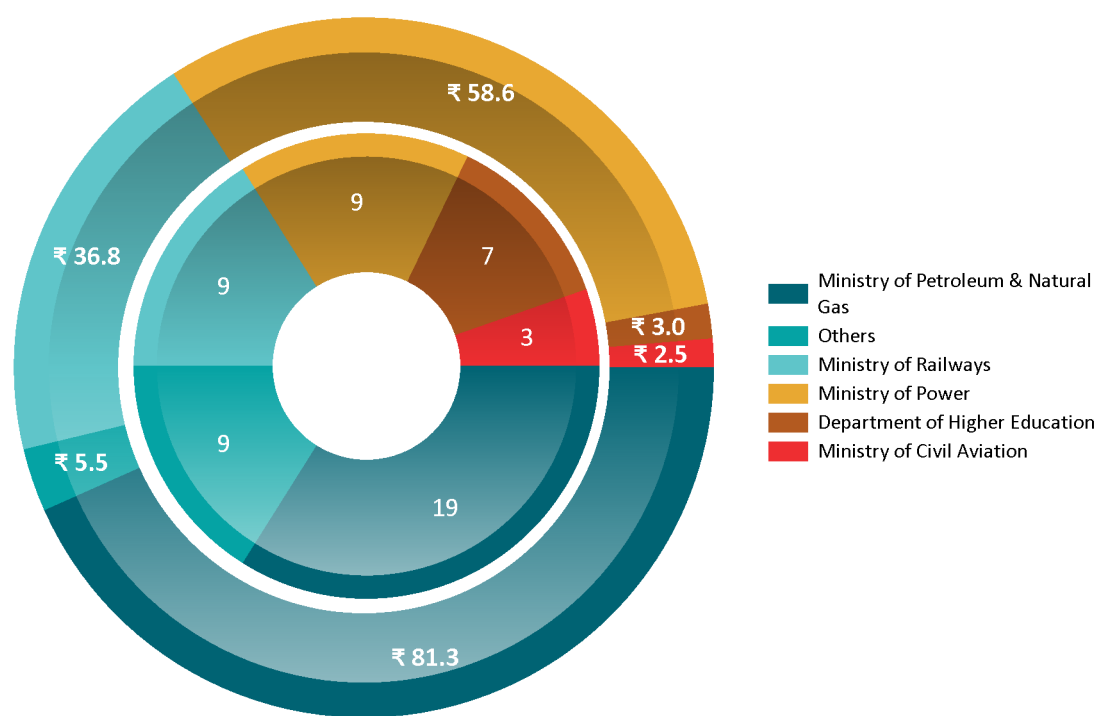


Cost Analytics : Major Ministries*

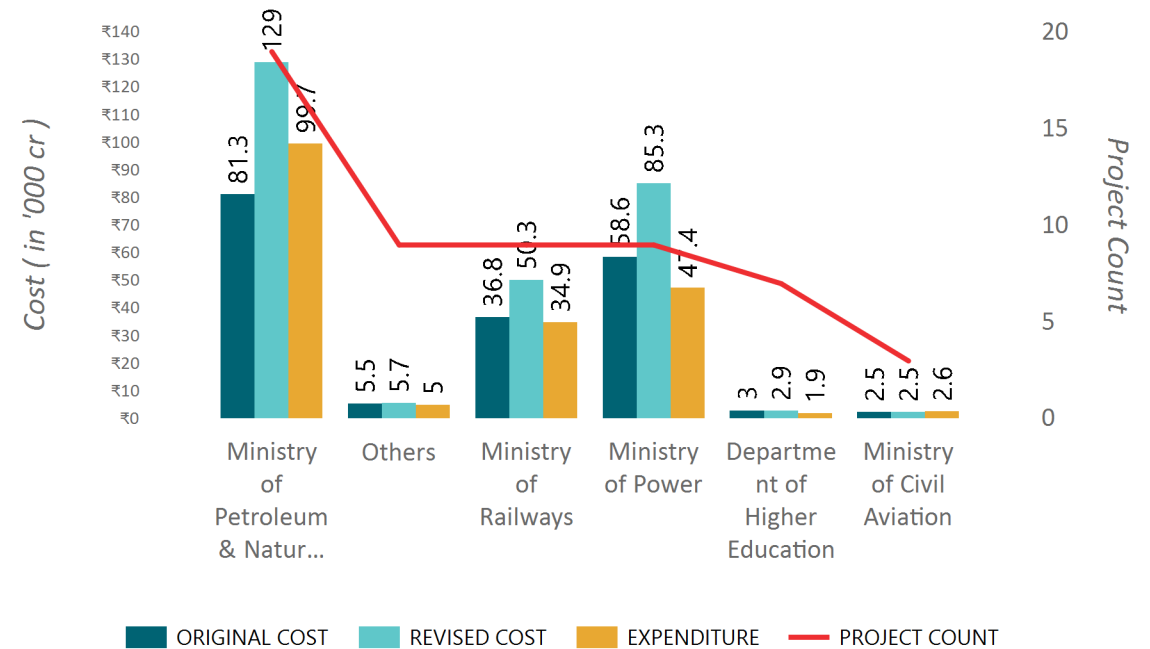


Note: * as per Project Count

Analytics: as per HML

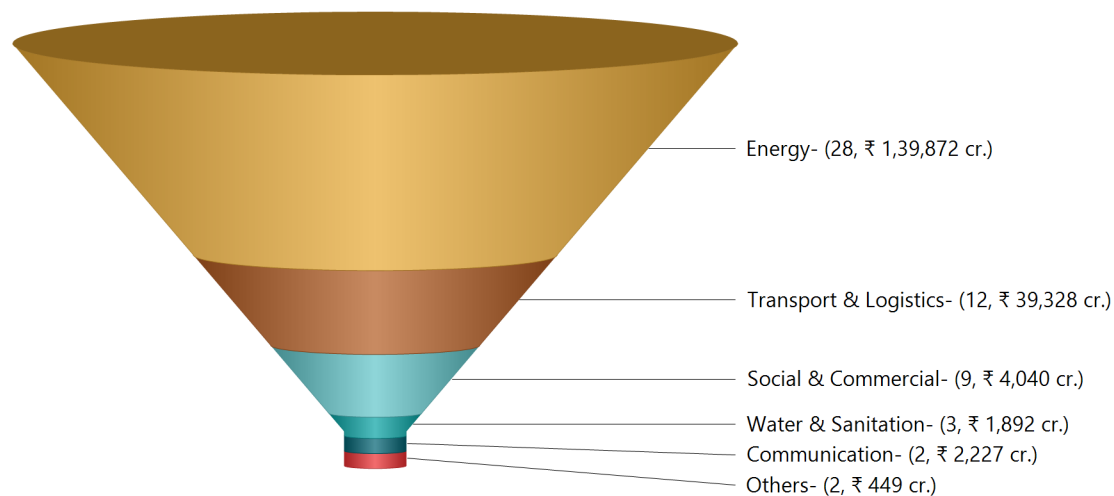


Physical & Financial progress (%) : Project count

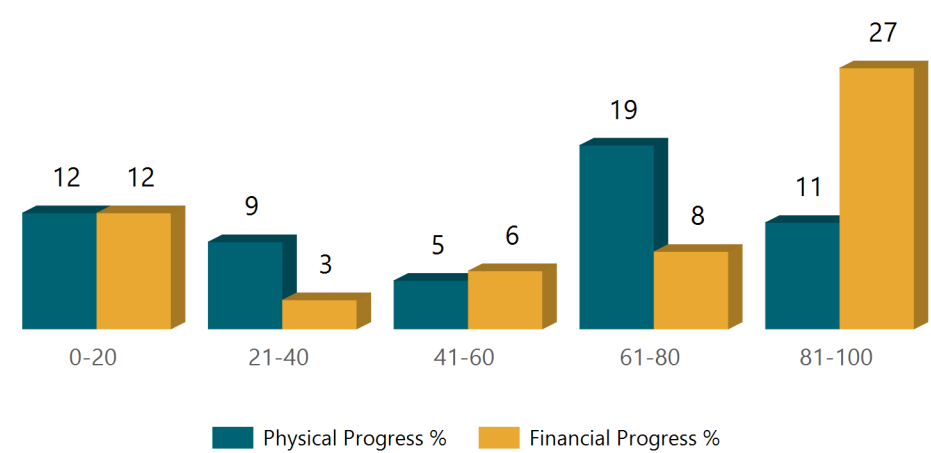

Note: all indicated legends are in format (Project count, Original Cost in crores)

State Comparison : All States

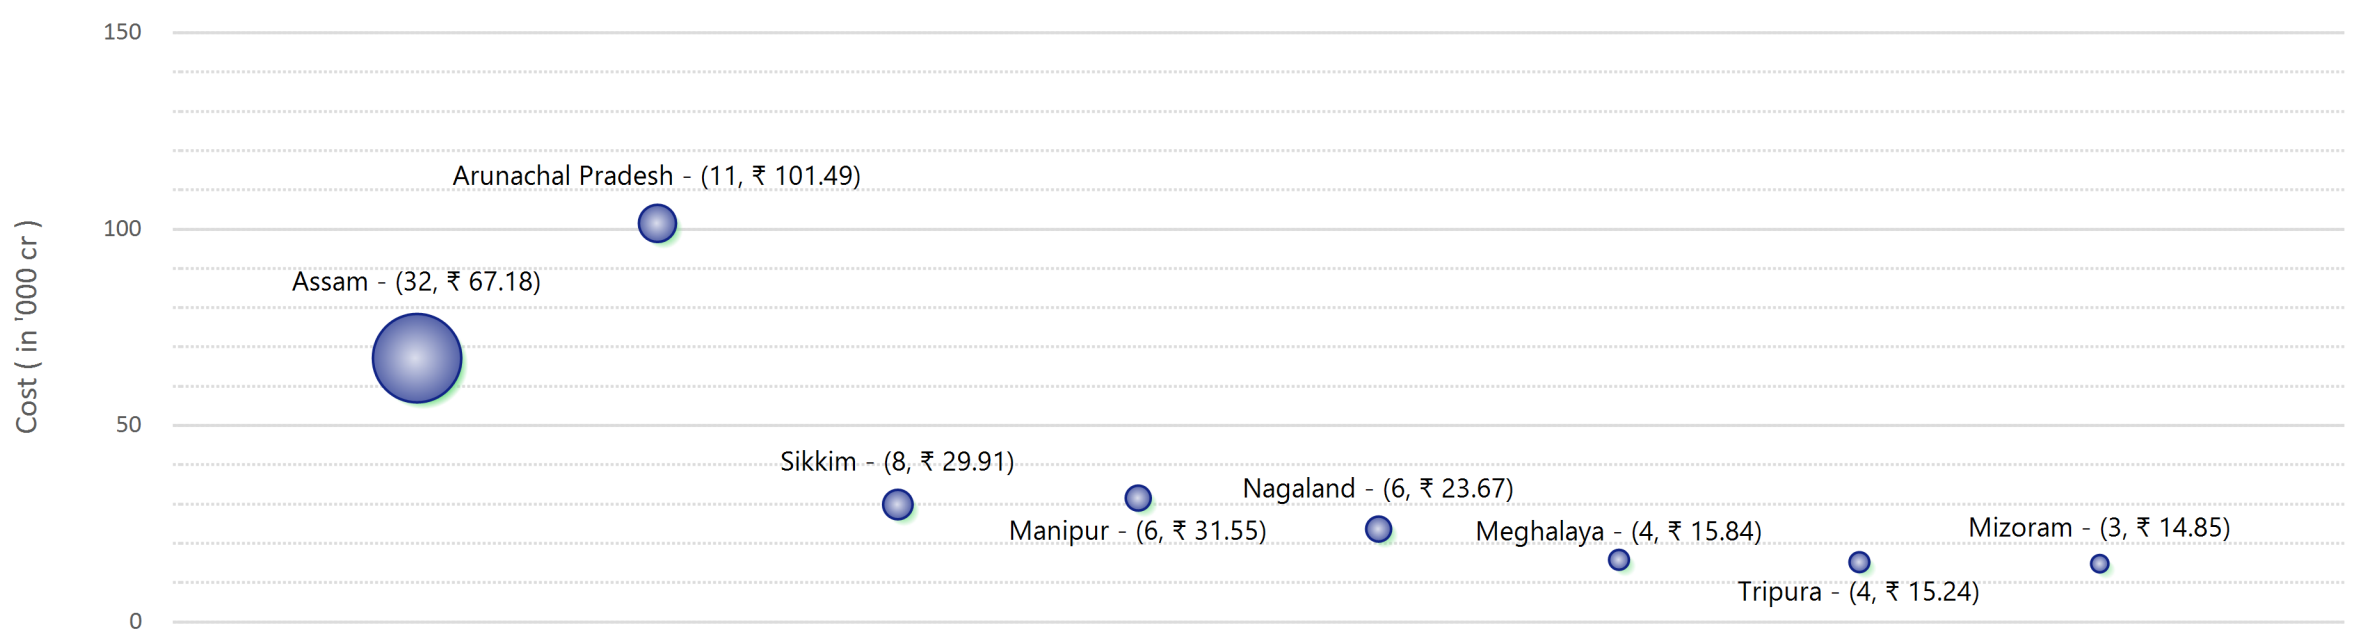

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022



HML Category 1 : Transport & Logistics

OCTOBER 2025

320

Ongoing Projects

₹ 11,86,691

Original Cost
(crores)

₹ 13,57,437

Revised Cost
(crores)

₹ 7,74,860


(57.08% of Revised Cost)
Expenditure
(crores)

4

Commissioned during month

11

Newly Added during month

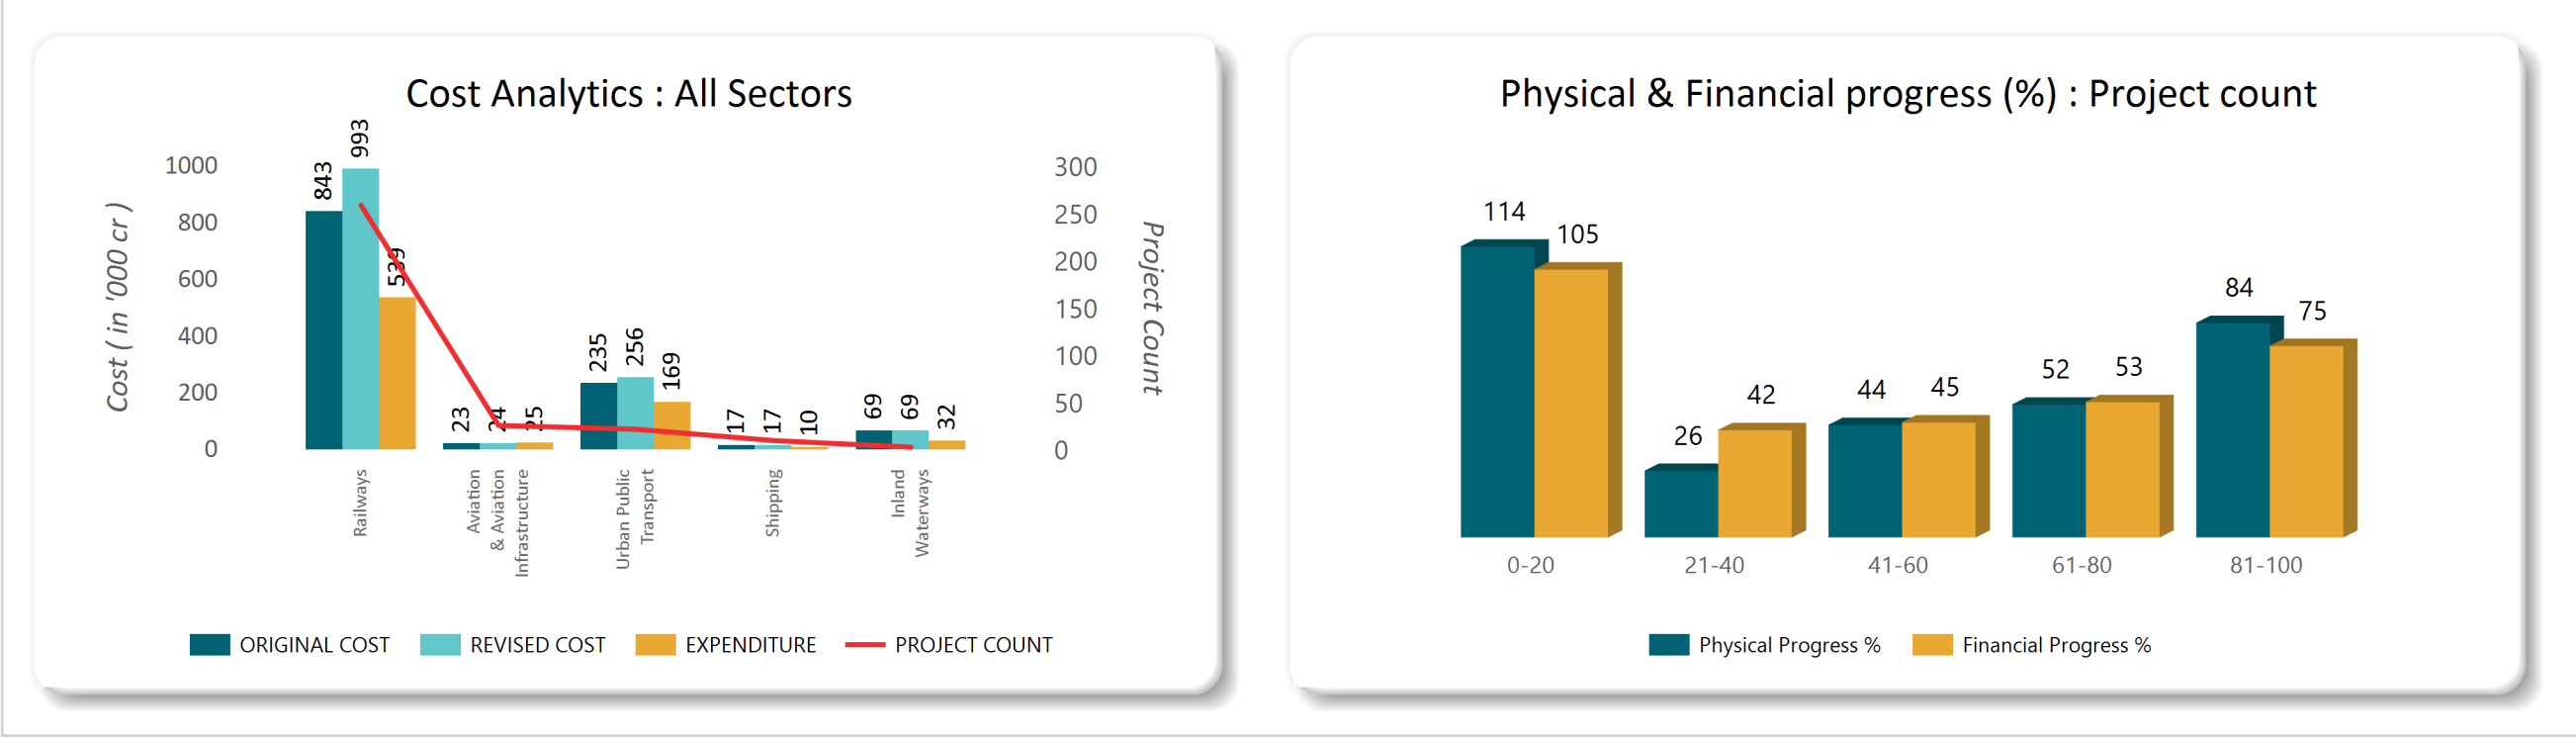

Sector - Overview					
S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Railways	259	842,708	992,534	538,551
2	Aviation & Aviation Infrastructure	26	23,050	23,511	24,797
3	Urban Public Transport	22	235,217	255,798	168,648
4	Shipping	10	16,923	17,090	10,375
5	Inland Waterways	3	68,792	68,504	32,489

Major On-going Projects Monitored under PAIMANA						
S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	617321	GODHANI-KALUMNA CHORD 13.7 KM	150,000		1,940	11
2	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	82,968	55
3	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		28,779	47
4	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
5	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65

HML Category 2 : Energy

OCTOBER 2025

206
Ongoing Projects

₹ 8,54,493
Original Cost
(crores)


₹ 9,88,403
Revised Cost
(crores)

₹ 4,99,484
(50.53% of Revised Cost)
Expenditure
(crores)


2
Commissioned during month

4
Newly Added during month

Cost Analytics : All Sectors

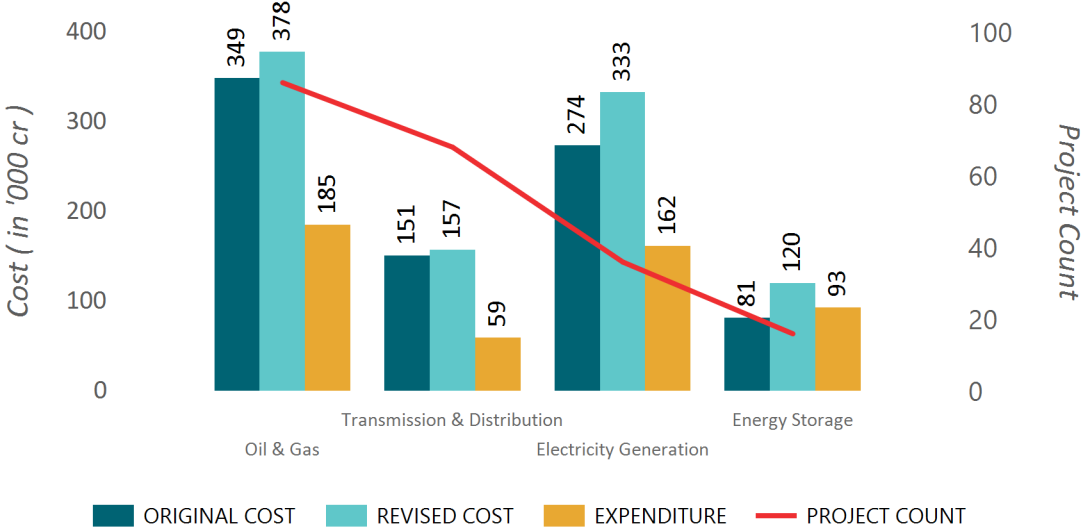

Physical & Financial progress (%) : Project count

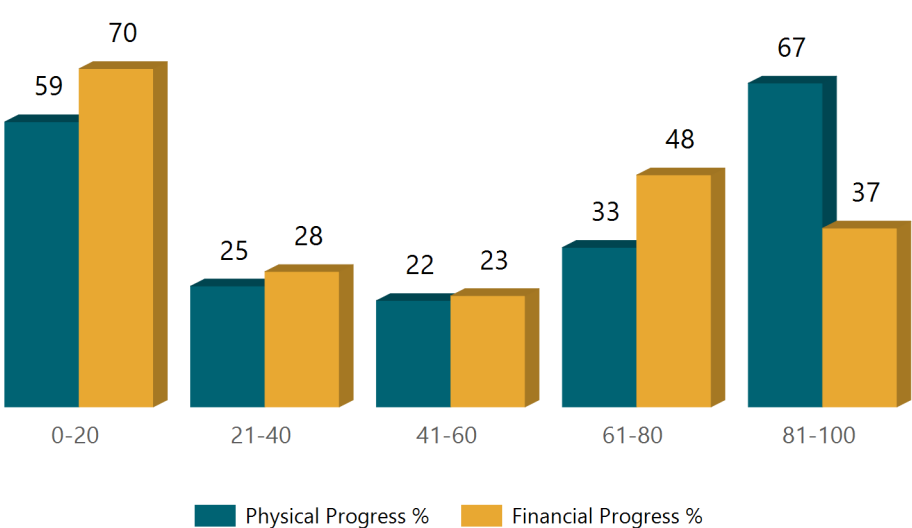

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	86	348,776	377,915	185,369
2	Transmission & Distribution	68	150,796	157,311	59,404
3	Electricity Generation	36	273,620	332,953	161,522
4	Energy Storage	16	81,301	120,224	93,189

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,955	16
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	61,927	89
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA	34,627	36,225	26,555	90
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	32,184	96
5	602182	DIBANG MULTIPURPOSE PROJECT	31,876		3,709	16

HML Category 3 : Water & Sanitation

OCTOBER 2025

72
Ongoing Projects



₹ 1,03,865
Original Cost
(crores)

₹ 2,03,719
Revised Cost
(crores)

₹ 1,78,860
(87.8% of Revised Cost)
Expenditure
(crores)

0
Commissioned during month

0
Newly Added during month

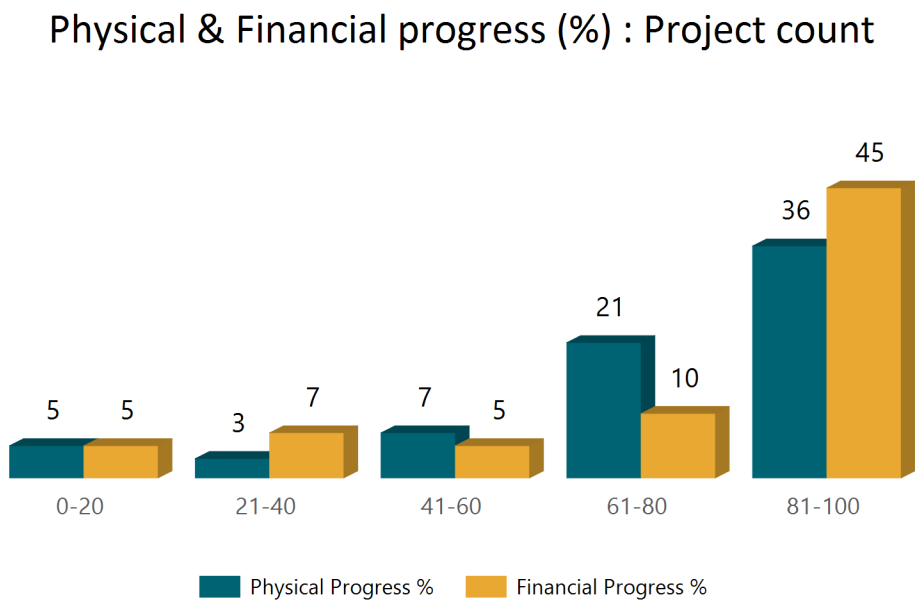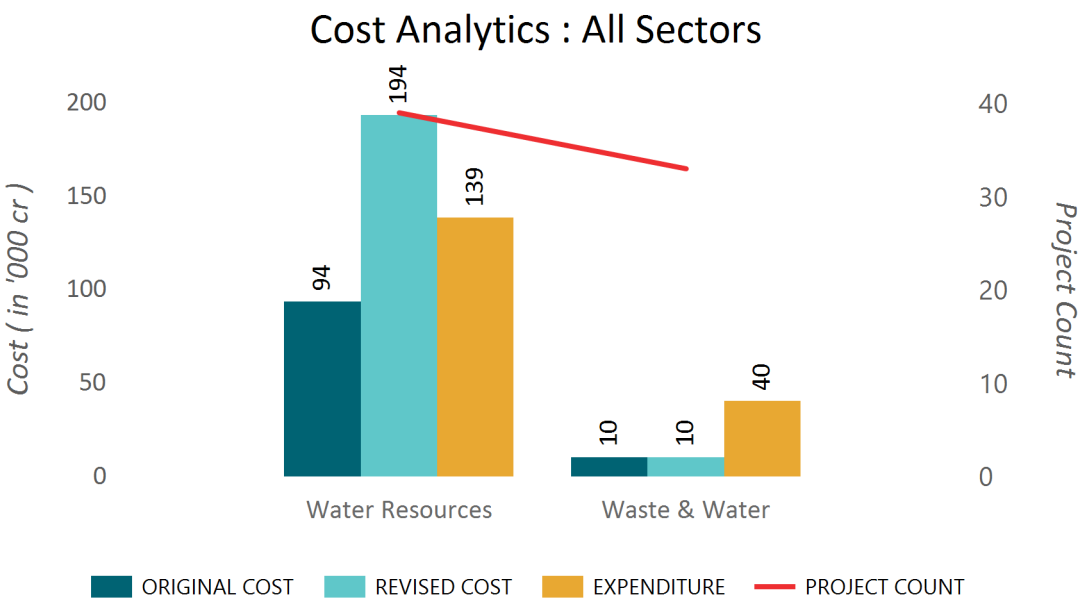

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	39	93,740	193,594	138,530
2	Waste & Water	33	10,125	10,125	40,331

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,861	93
2	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	24,838	84
3	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,665	87
4	400112	JIGAON IRRIGATION PROJECT	7,223		8,723	90
5	701386	GOSIKHURD PROJECT	7,196	12,770	13,765	72

HML Category 4 : Communication

OCTOBER 2025

15
Ongoing Projects

₹ 1,52,734
Original Cost
(crores)


₹ 2,74,827
Revised Cost
(crores)

₹ 77,355
(28.15% of Revised Cost)
Expenditure
(crores)


0
Commissioned during month

0
Newly Added during month

Cost Analytics : All Sectors

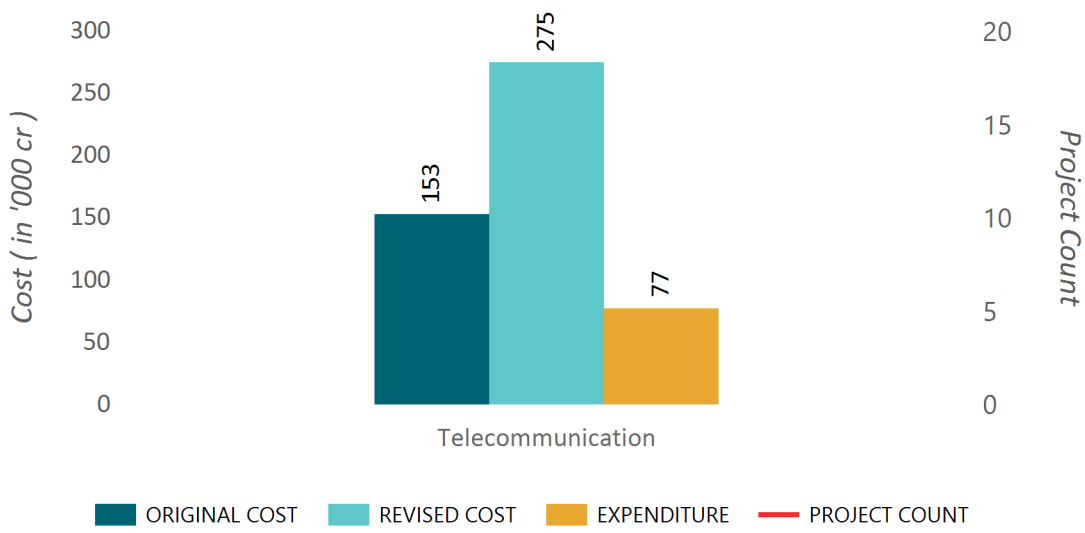

Physical & Financial progress (%) : Project count

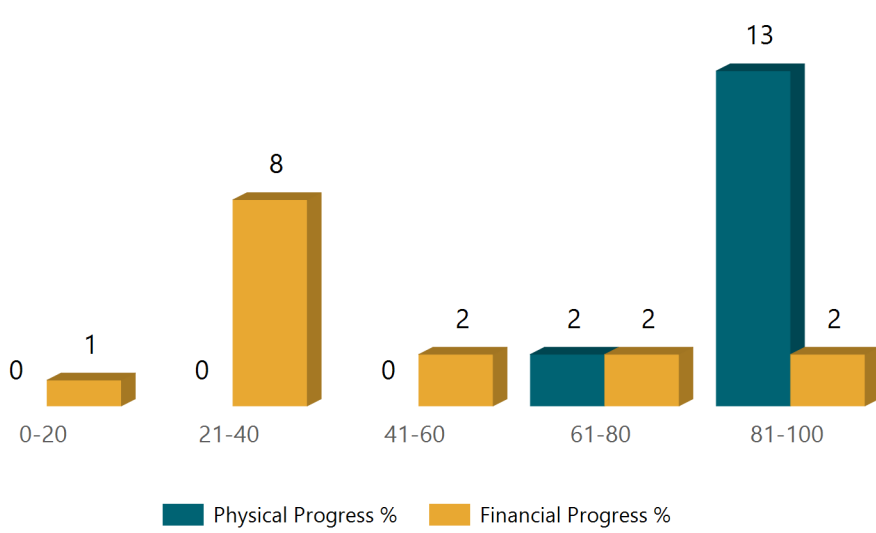

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	15	152,734	274,827	77,355

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	706775	BHARATNET	61,109	188,000	46,432	81
2	701593	4G SERVICES BY BSNL	28,466	19,592	8,419	96
3	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	30,620	9,792	76
4	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		8,448	97
5	701602	PROVISION OF 4G BASED MOBILE SERVICES IN 7,287 UNCOVERED VILLAGES OF 44 ASPIRATIONAL DISTRICT ACROSS 5 STATES OF ANDHRA PRADESH, CHHATTISGARH, JHARKHAND, MAHARASHTRA & ODISHA	3,685		1,135	81

HML Category 5 : Social & Commercial

OCTOBER 2025

56

Ongoing Projects

₹ 59,962

Original Cost
(crores)

₹ 60,847

Revised Cost
(crores)

₹ 15,566



(25.58% of Revised Cost)
Expenditure
(crores)

0

Commissioned during month

15

Newly Added during month

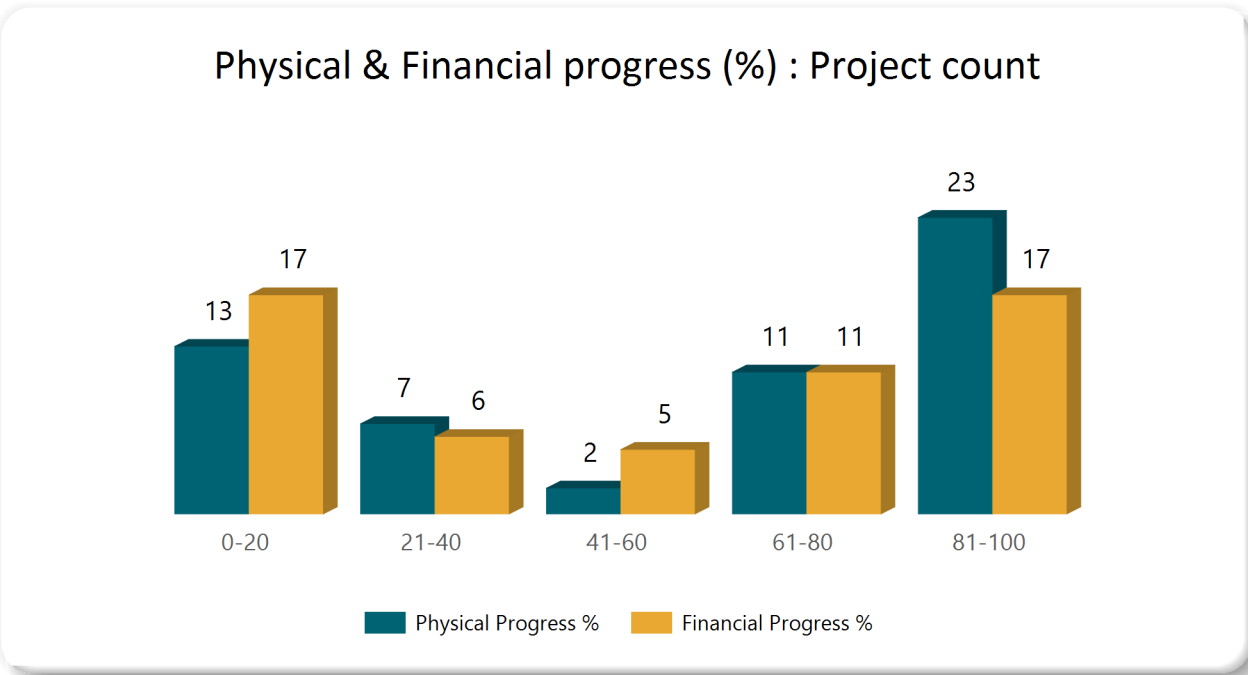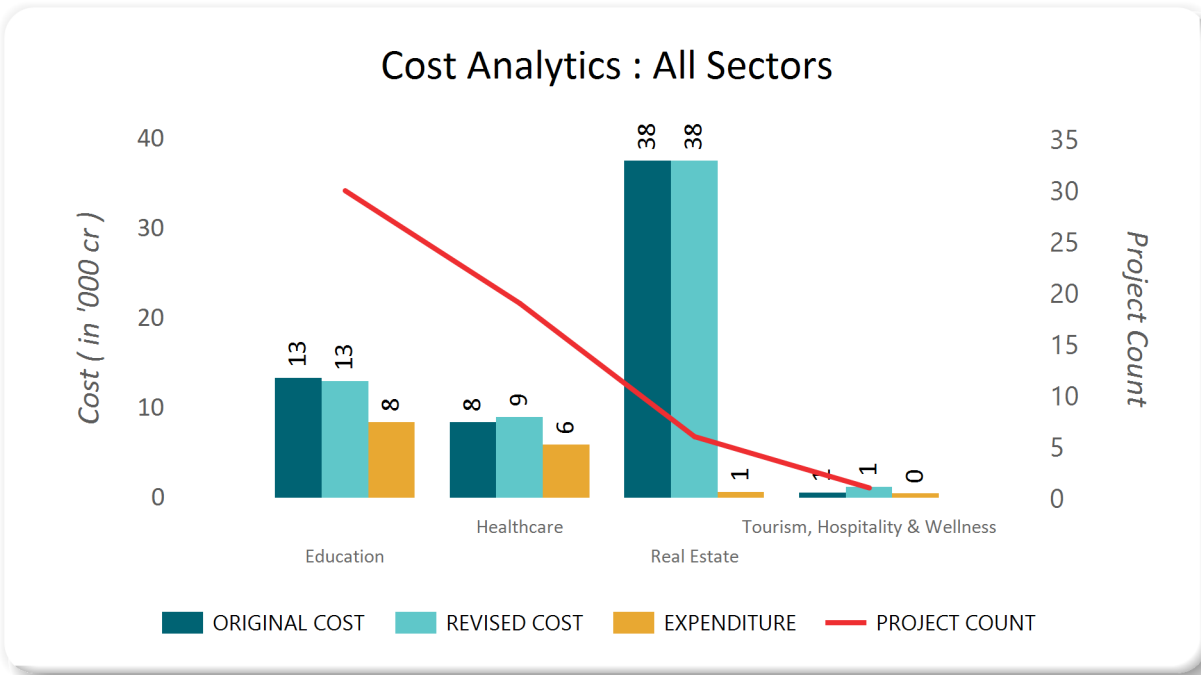

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Education	30	13,374	13,013	8,462
2	Healthcare	19	8,424	9,005	5,958
3	Real Estate	6	37,591	37,591	649
4	Tourism, Hospitality & Wellness	1	573	1,238	497

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850		0	0
2	701658	KRISHNAPATNAM NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	2,139		473	21
3	701167	AIIMS KASHMIR AT AWANTIPORA JAMMU & KASHMIR	1,828	1,828	1,322	68
4	701657	TUMAKURU NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	1,702		117	10
5	701173	AIIMS MAJRA REWARI HARYANA	1,299		349	28

Other Sectors

OCTOBER 2025

151
Ongoing Projects

₹ 1,94,887
Original Cost
(crores)


₹ 1,98,299
Revised Cost
(crores)

₹ 65,063
(32.81% of Revised Cost)
Expenditure
(crores)

0
Commissioned during month

0
Newly Added during month

Physical & Financial progress (%) : Project count

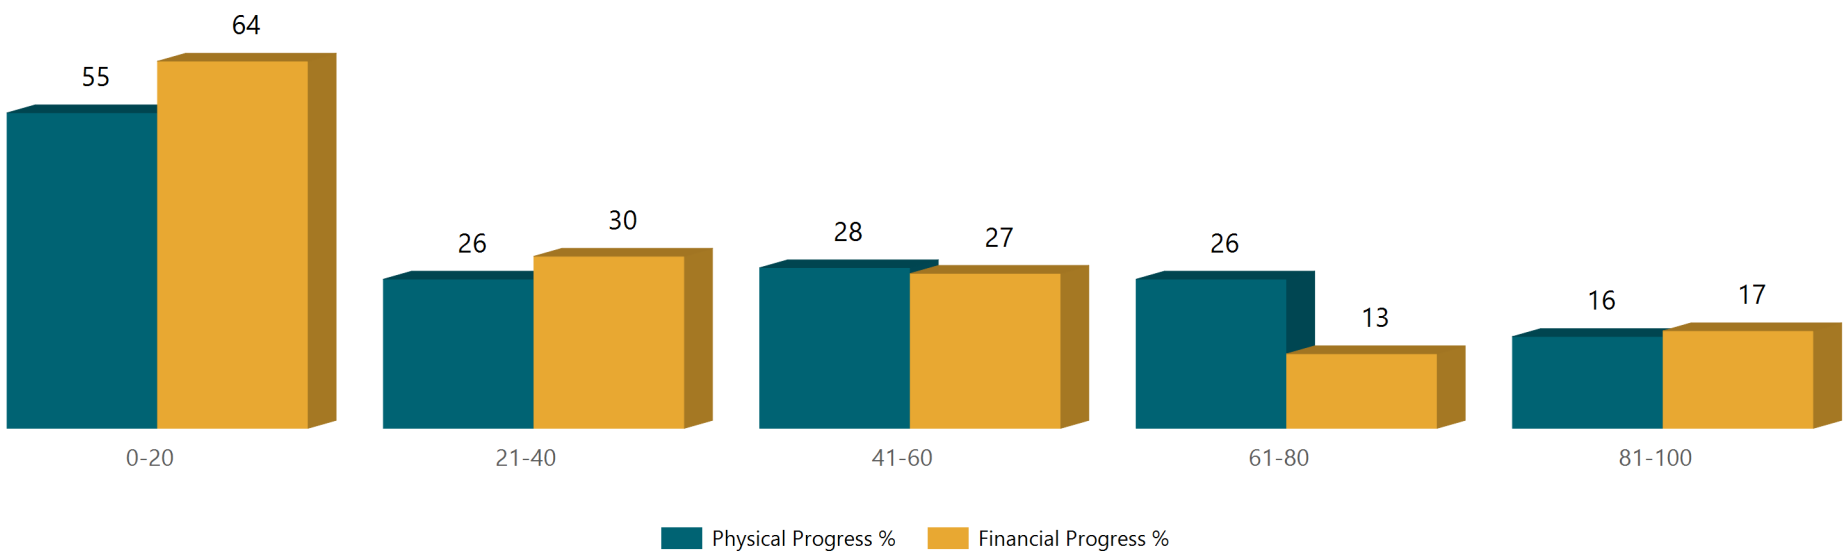

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	118	159,638	157,376	49,200
2	Steel	20	19,267	22,505	8,653
3	Metals & Mining	10	14,436	16,873	6,490
4	Construction	3	1,546	1,546	719

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400424	GEVRA OC [70 MTY]	11,816		6,687	78
2	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,735	17
3	400150	RPR MAGADH EXP OCP	7,254		1,601	38
4	617416	REVISED JHARIA MASTER PLAN FOR DEALING WITH FIRE, SUBSIDENCE & REHABILITATION OF AFFECTED FAMILIES IN JHARIA COALFIELD- REG.	5,940		0	8
5	616253	BLOCK E OCP	5,851		20	3



Major Infrastructure Central Ministries & Departments





Ministry of Railways

OCTOBER 2025

257

Ongoing Projects

₹ 8,39,222

Original Cost
(crores)

₹ 9,88,283

Revised Cost
(crores)

₹ 5,36,735

(54.31% of Revised Cost)
Expenditure
(crores)

130 | ₹ 778,396

Mega Projects
Count | Original Cost (crores)

127 | ₹ 60,827

Major Projects
Count | Original Cost

4


Commissioned during month

10

Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

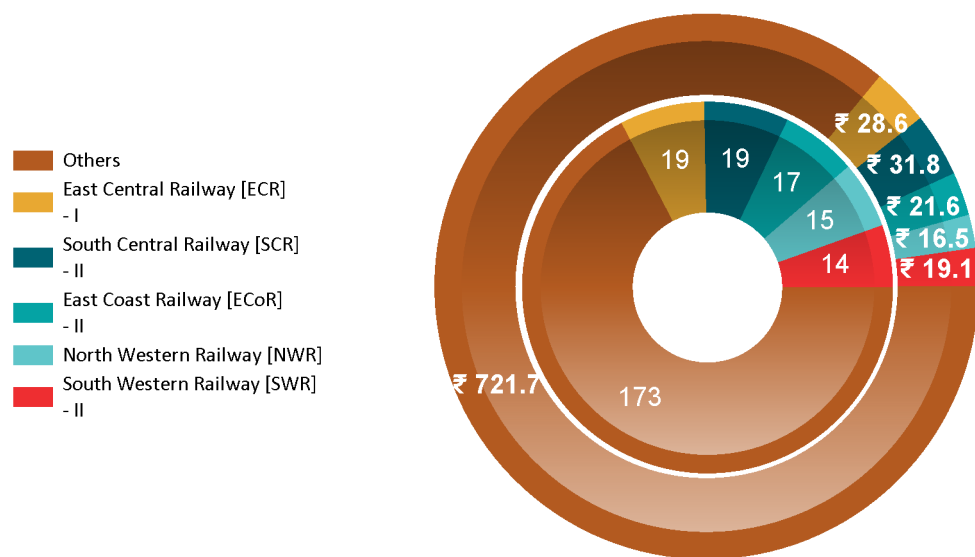


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Physical & Financial progress (%) : Project count

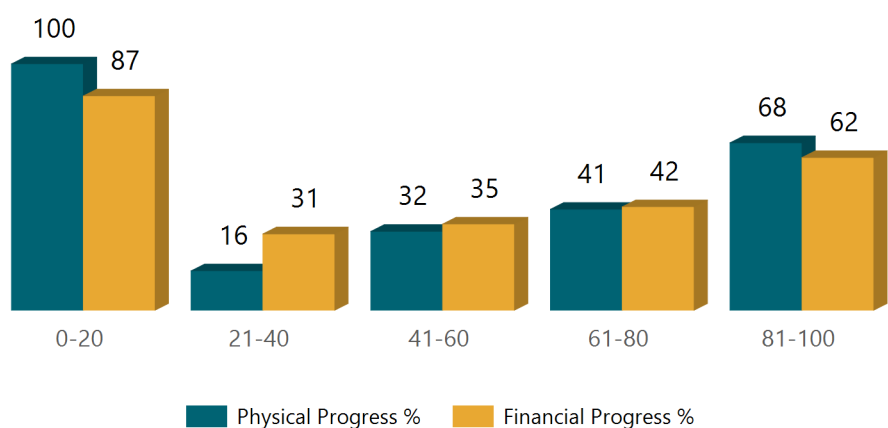

Cost Analytics : Major Sectors*

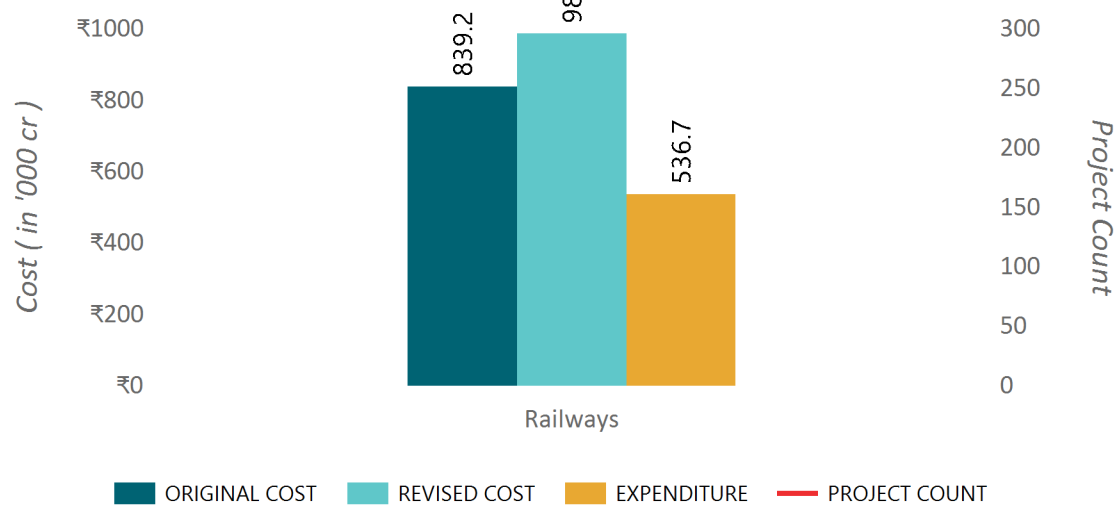

State Comparison : Major States*

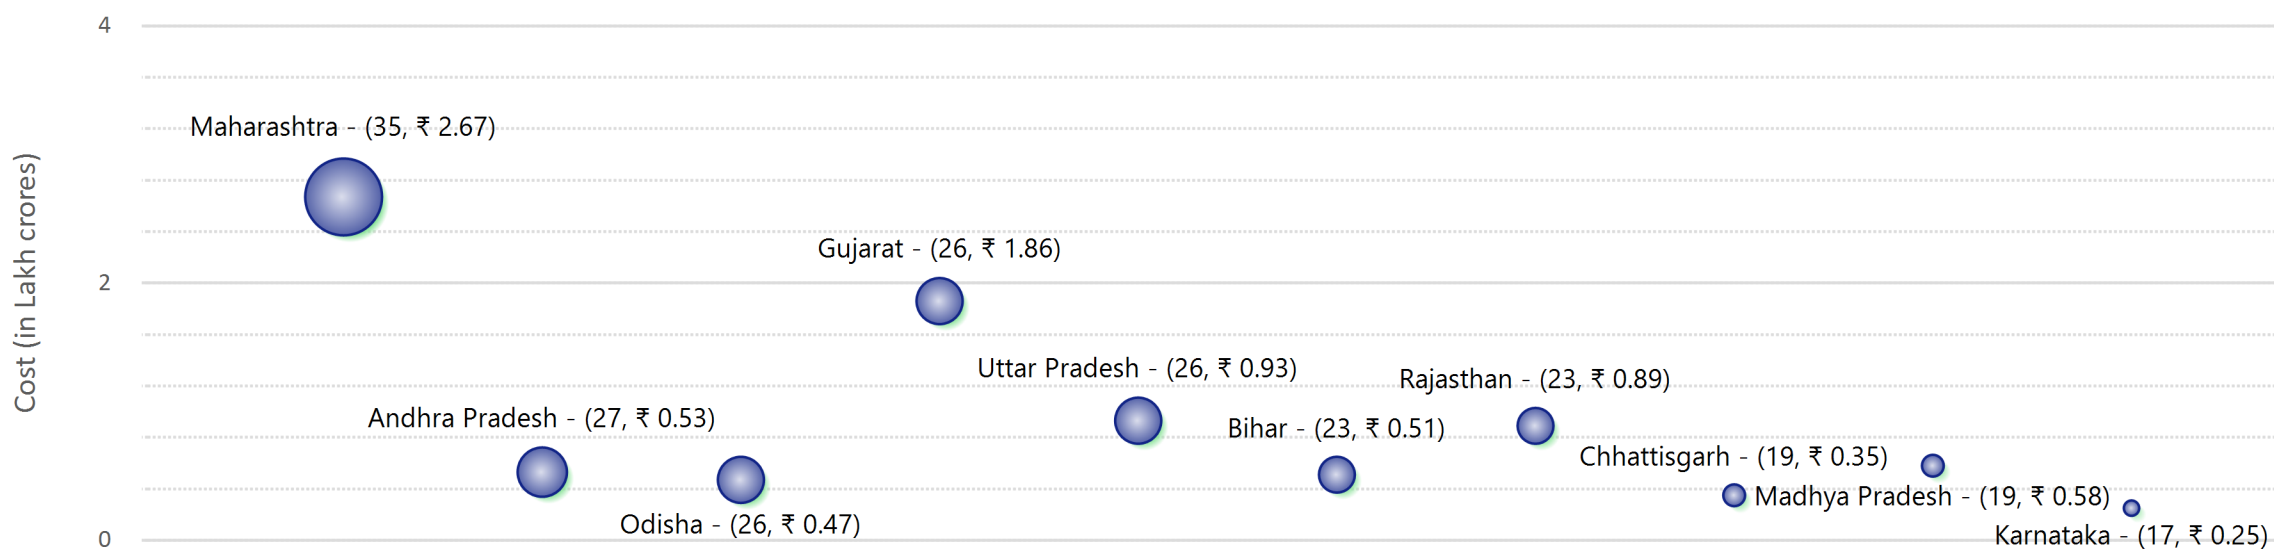

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	617321	GODHANI-KALUMNA CHORD 13.7 KM	150,000	150,000	1,940	11
2	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	82,968	55
3	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
4	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
5	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-III A	33,690	33,690	2,436	16



Ministry of Coal

OCTOBER 2025

124

Ongoing Projects

₹ 2,11,242

Original Cost
(crores)

₹ 2,14,006

Revised Cost
(crores)

₹ 75,489

(35.27% of Revised Cost)
Expenditure
(crores)

39 | ₹ 169,485

Mega Projects
Count | Original Cost (crores)

85 | ₹ 41,757

Major Projects
Count | Original Cost

0


Commissioned during month

1

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

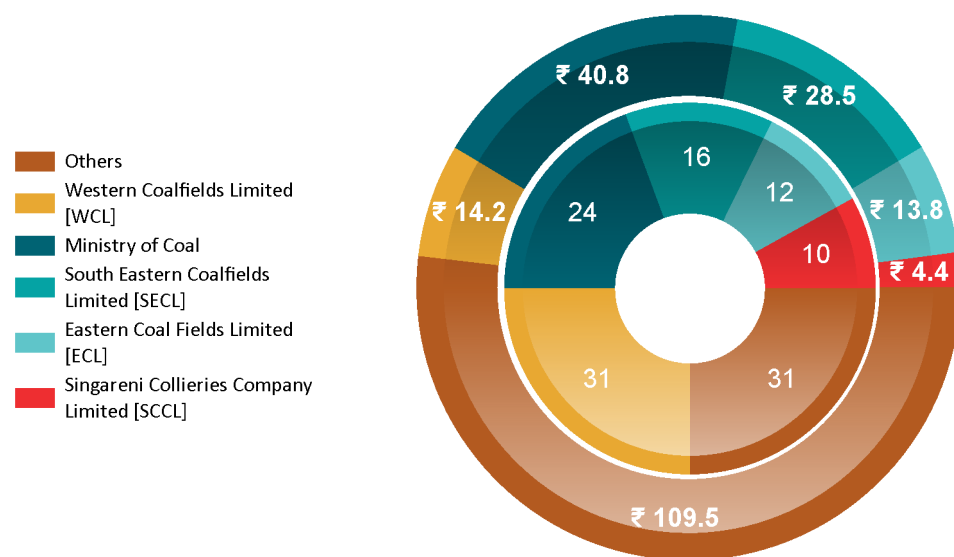


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

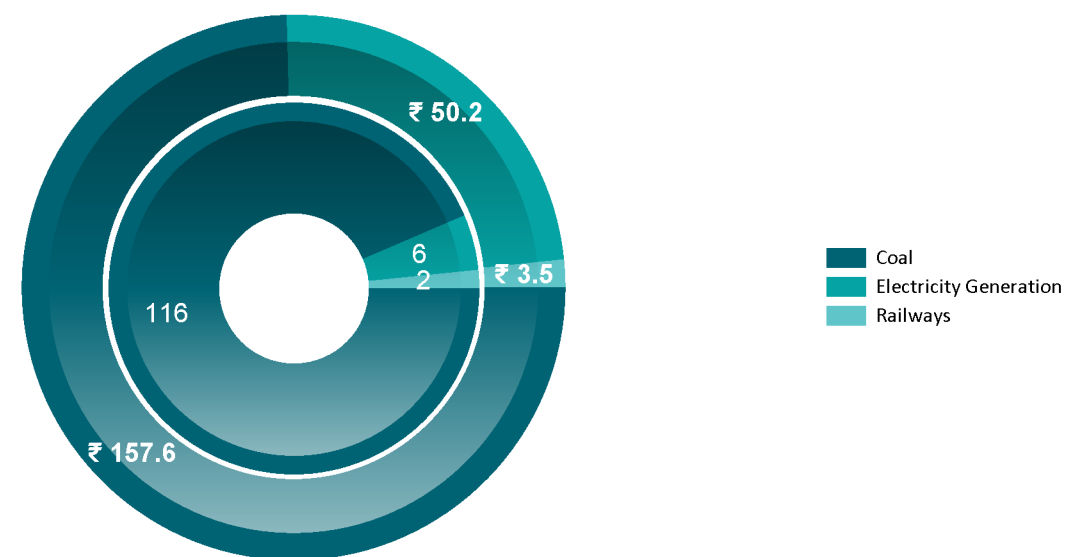


Physical & Financial progress (%) : Project count

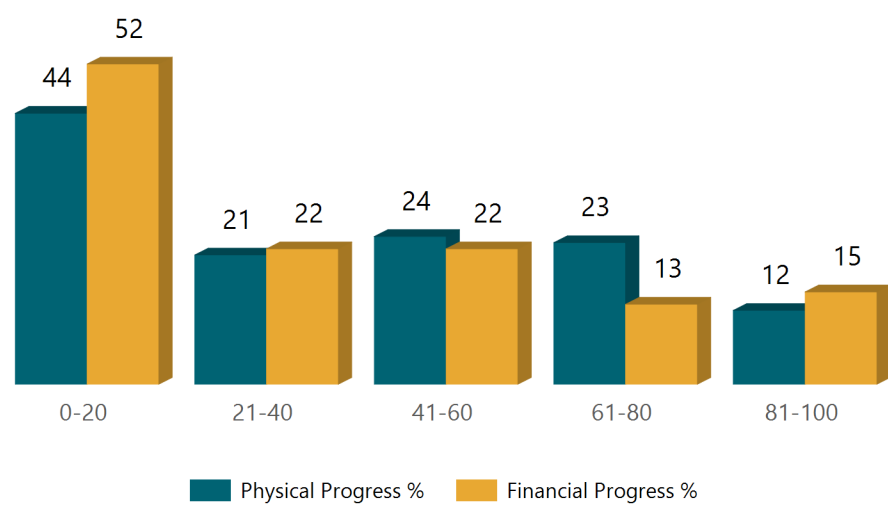

Cost Analytics : Major Sectors*

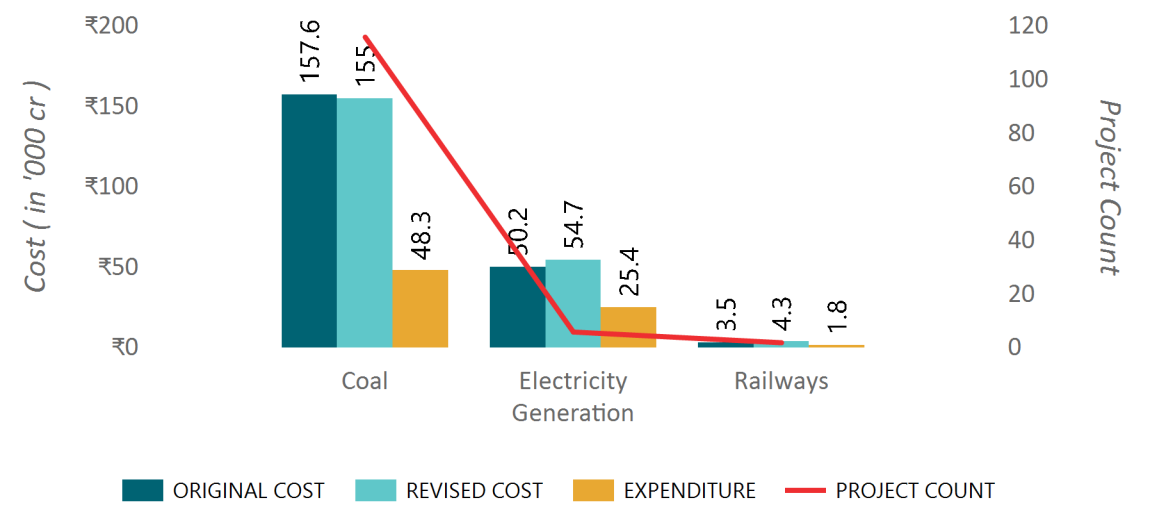

State Comparison : Major States*

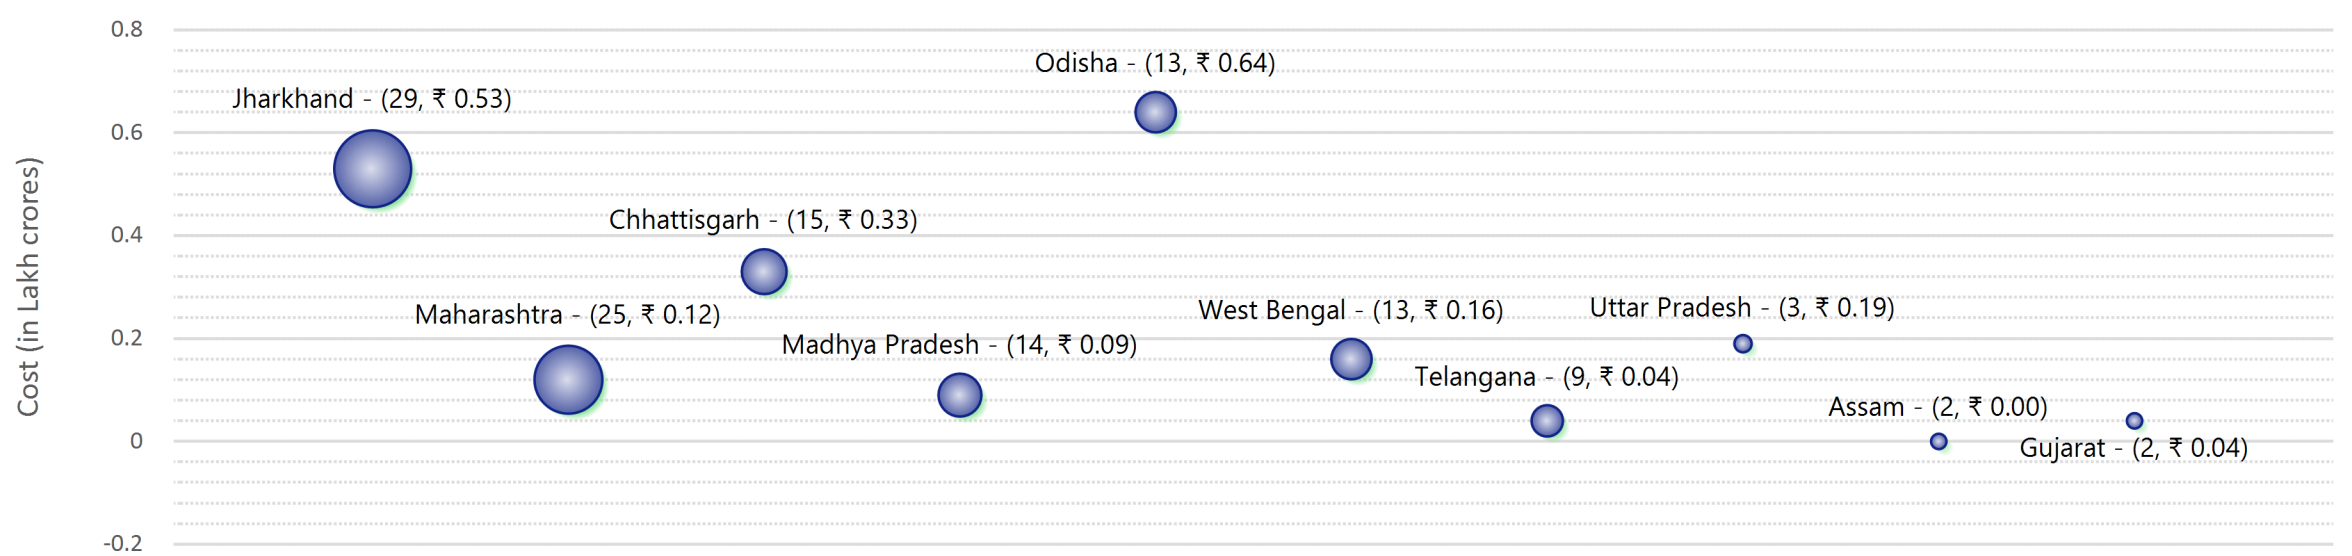

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	2,549	1
2	400259	GHATAMPUR THERMAL POWER PLANT 3 X 660 MW	17,238	21,781	20,522	93
3	400424	GEVRA OC [70 MTY]	11,816	11,816	6,687	78
4	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,735	17
5	400150	RPR MAGADH EXP OCP	7,254	7,254	1,601	38



Ministry of Petroleum & Natural Gas

OCTOBER 2025

102

Ongoing Projects

₹ 4,30,077

Original Cost
(crores)

₹ 4,98,139

Revised Cost
(crores)

₹ 2,78,558

(55.92% of Revised Cost)

Expenditure
(crores)

48 | ₹ 405,555

Mega Projects
Count | Original Cost (crores)

54 | ₹ 24,522

Major Projects
Count | Original Cost

2


Commissioned during month

0

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

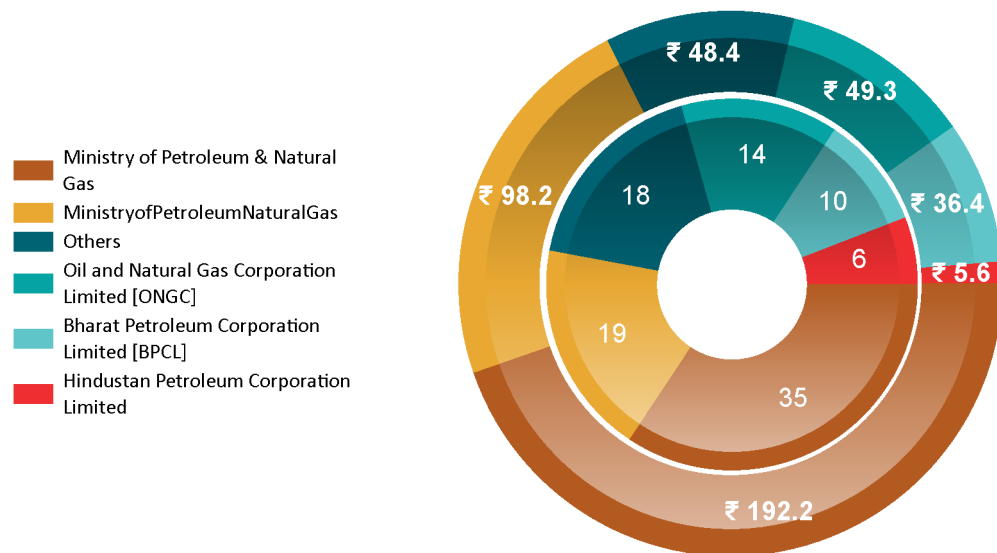


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

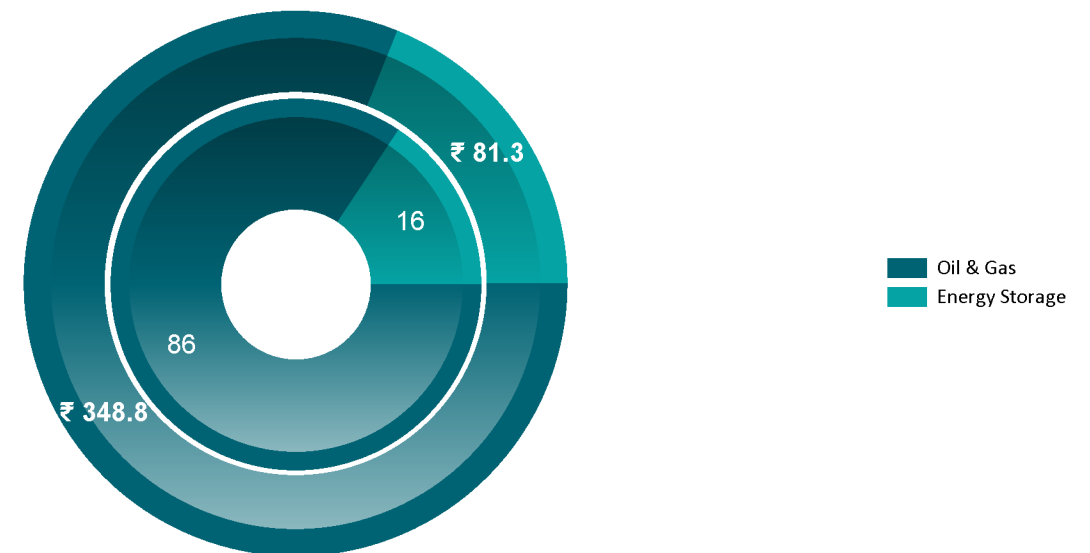


Physical & Financial progress (%) : Project count

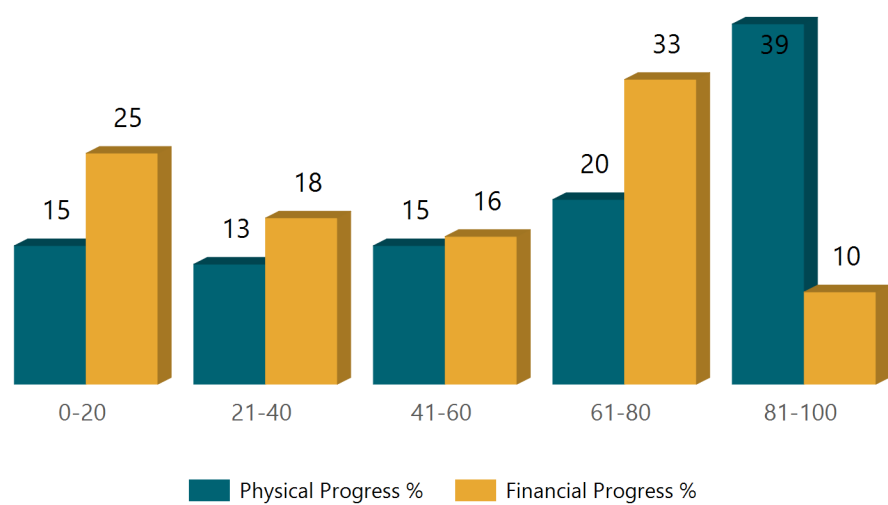

Cost Analytics : Major Sectors*

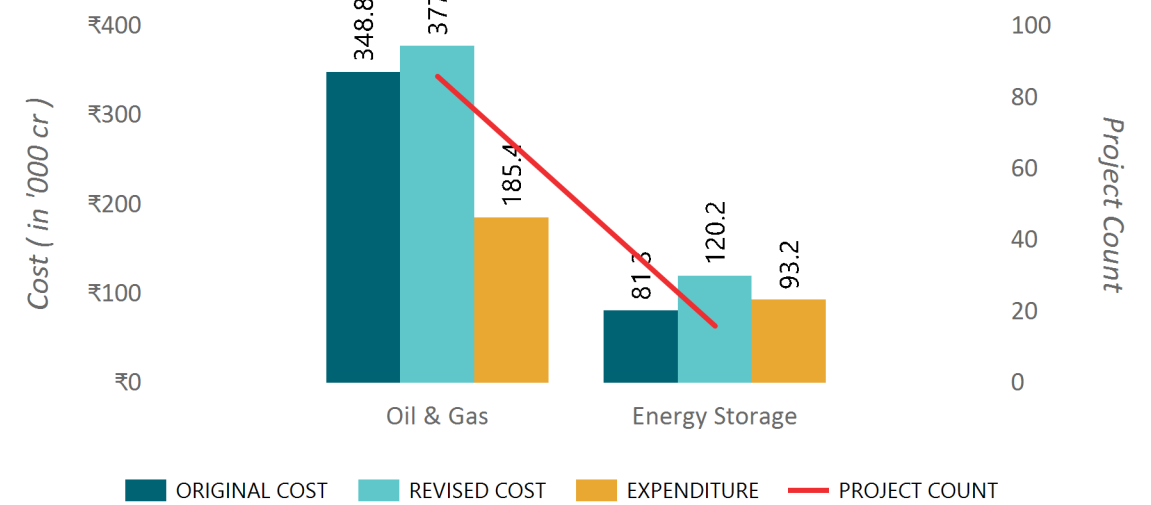

State Comparison : Major States*

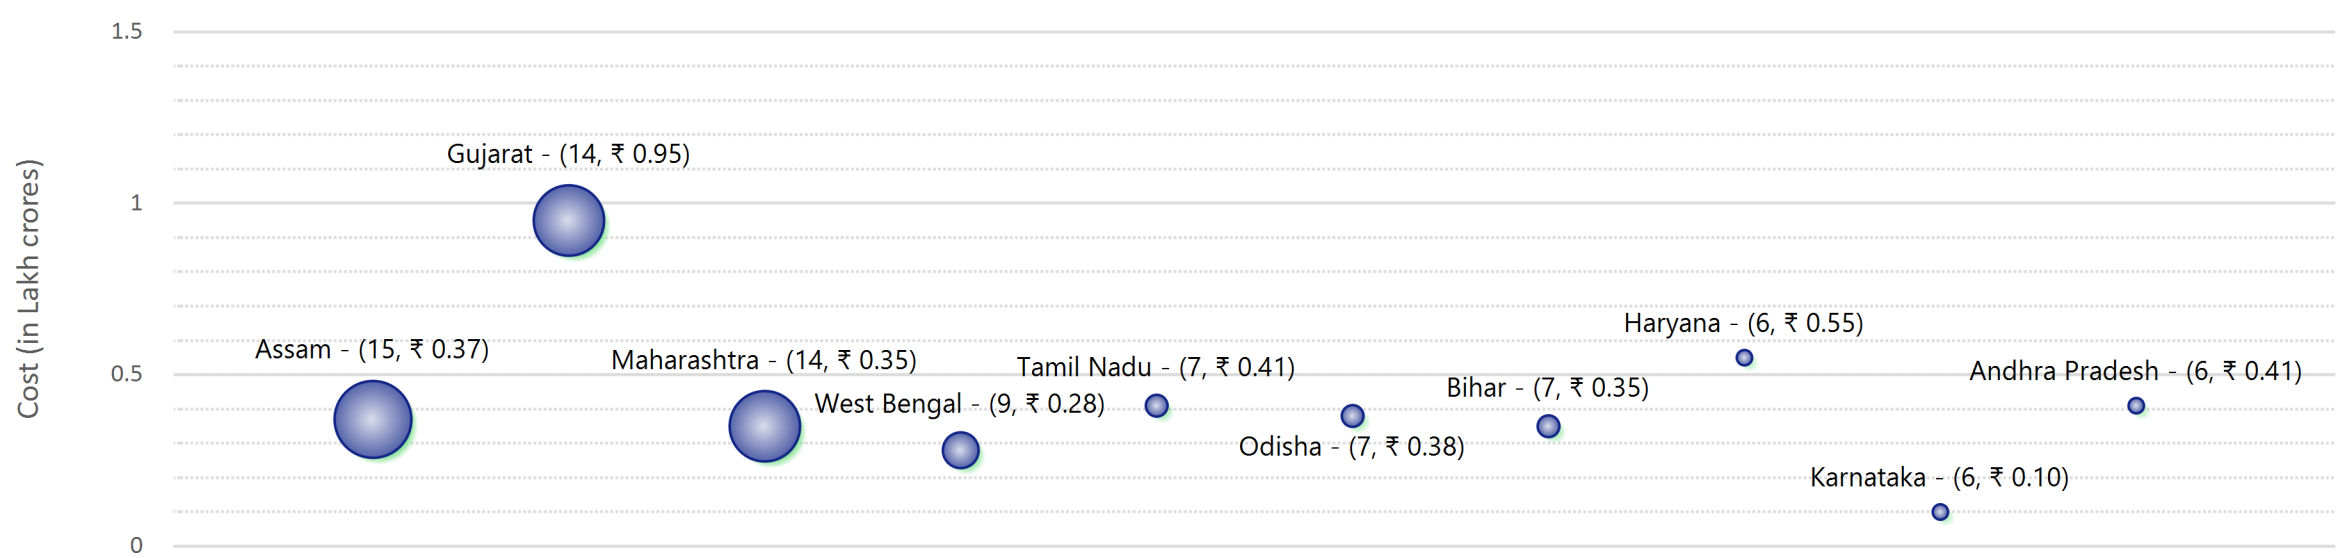

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,955	16
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	61,927	89
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	26,555	90
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	32,184	96
5	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,342	10



Ministry of Power

OCTOBER 2025

100

Ongoing Projects

₹ 3,76,297

Original Cost
(crores)

₹ 4,37,884

Revised Cost
(crores)

₹ 1,96,452

(44.86% of Revised Cost)

Expenditure
(crores)

65 | ₹ 361,496

Mega Projects
Count | Original Cost (crores)

35 | ₹ 14,801

Major Projects
Count | Original Cost

0


Commissioned during month

3

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

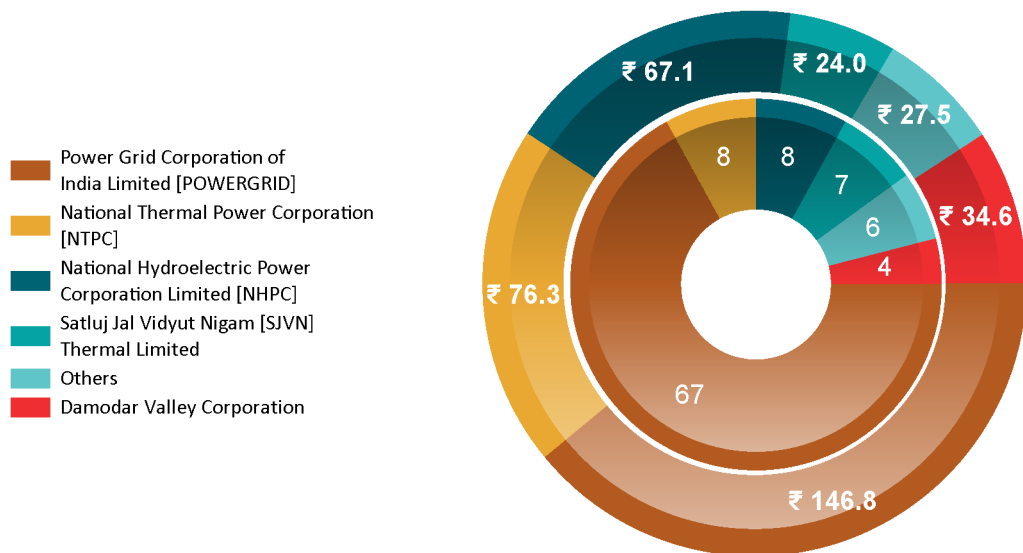


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

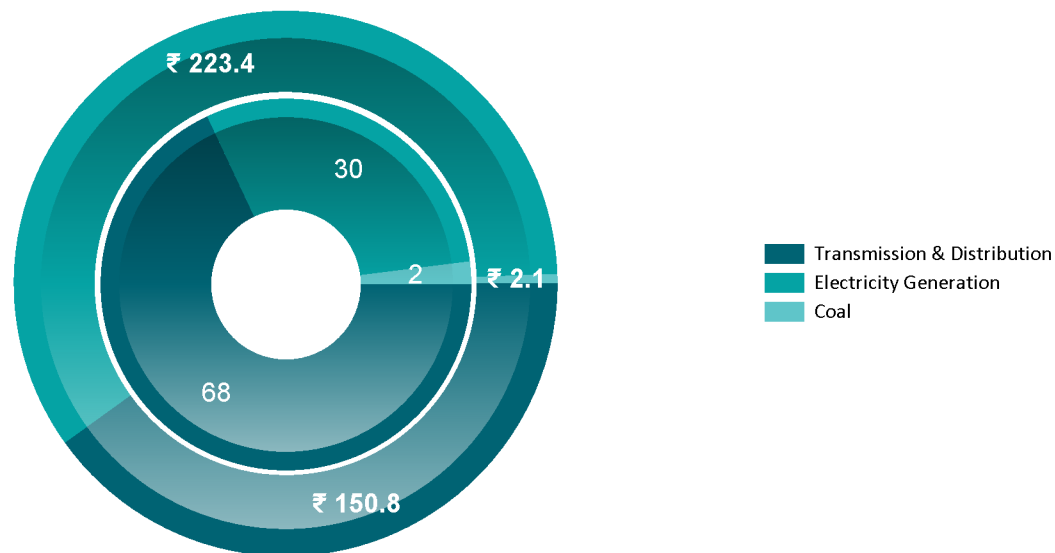


Physical & Financial progress (%) : Project count

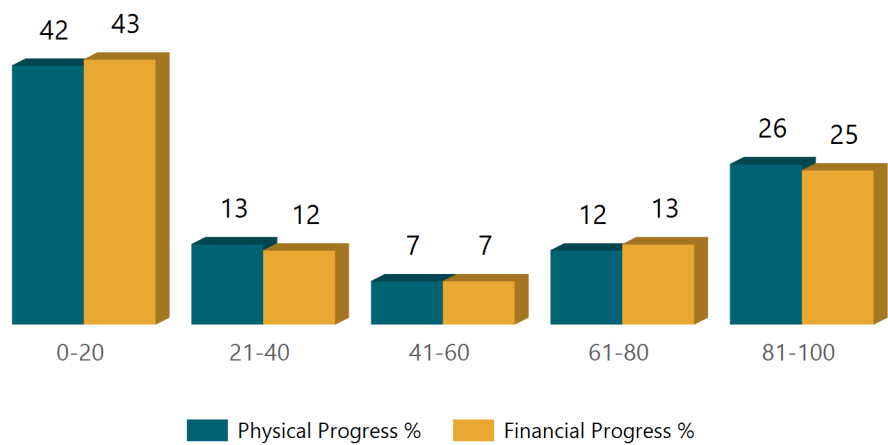

Cost Analytics : Major Sectors*

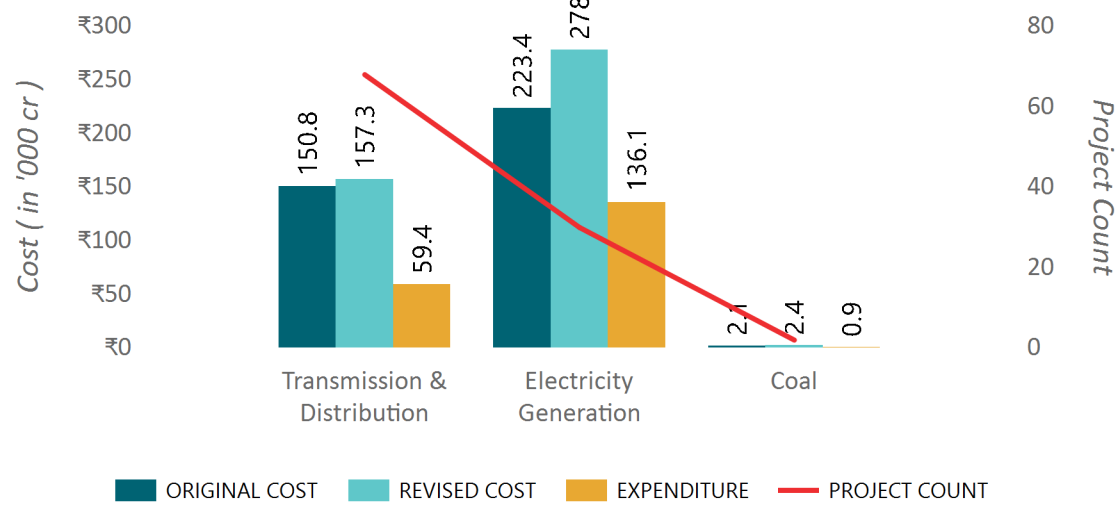

State Comparison : Major States*

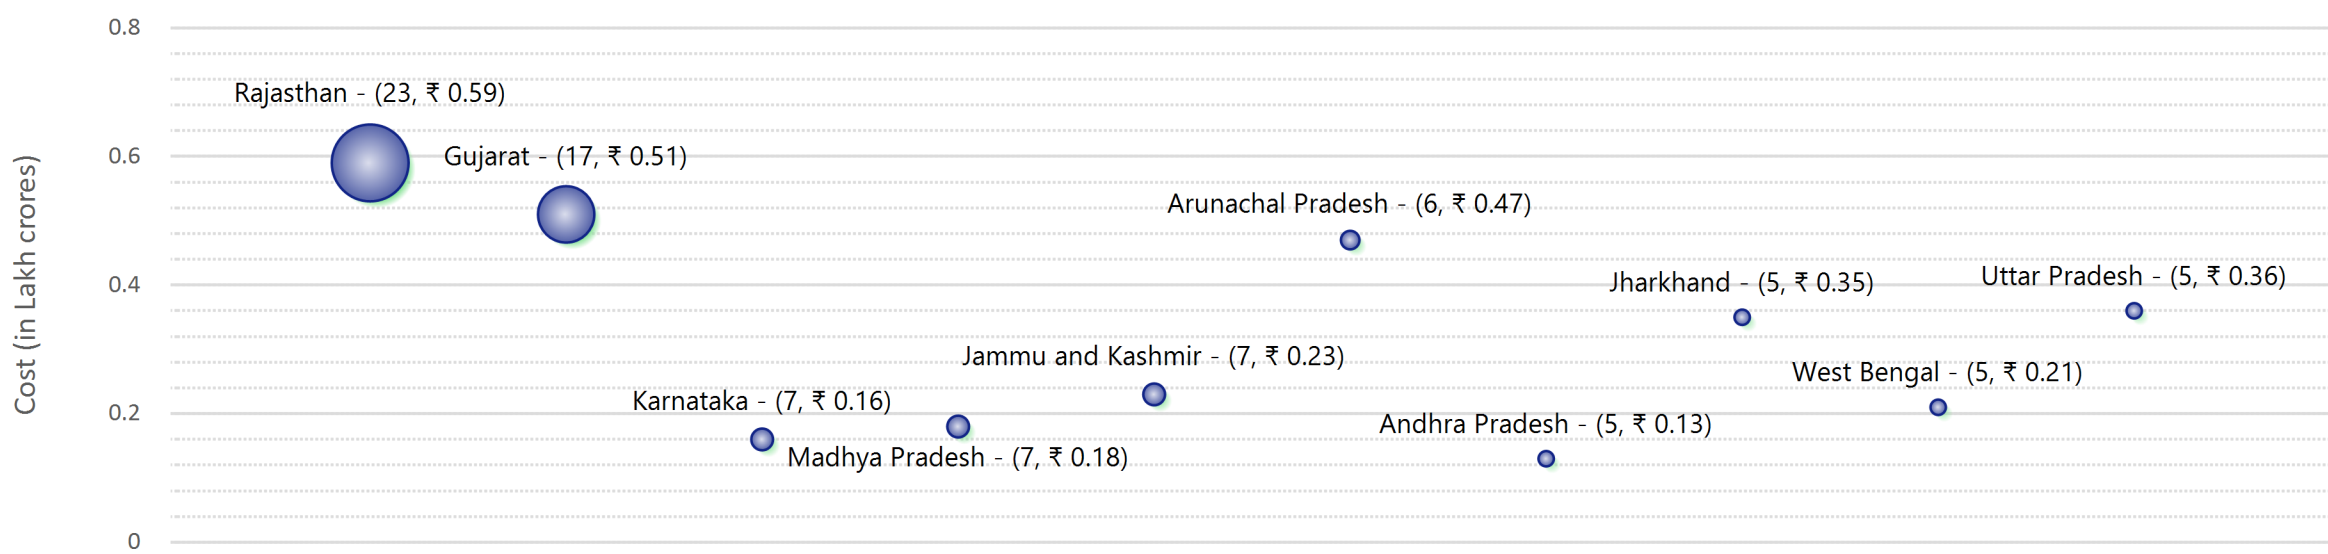

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	3,709	16
2	615347	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV NAME POWERGRID WEST CENTRAL TRANSMISSION LIMITED]	24,819	24,819	1,985	2
3	400062	RAGHUNATHPUR THERMAL POWER STATION PHASE II [2X660 MW] AT RAGHUNATHPUR, PURULIA, WEST BENGAL	17,673	17,673	1,409	2
4	612142	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III [2X800 MW]	17,195	17,195	1,979	11
5	400261	PATRATU THERMAL POWER STATION EXPANSION PROJECT PHASE-I [3X800 MW]	17,112	20,302	17,861	85



Ministry of Housing & Urban Affairs

OCTOBER 2025

54

Ongoing Projects

₹ 3,39,589

Original Cost
(crores)

₹ 3,60,170

Revised Cost
(crores)

₹ 2,36,807

(65.75% of Revised Cost)
Expenditure
(crores)

21 | ₹ 329,540

Mega Projects
Count | Original Cost (crores)

33 | ₹ 10,049

Major Projects
Count | Original Cost

0


Commissioned during month

0

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

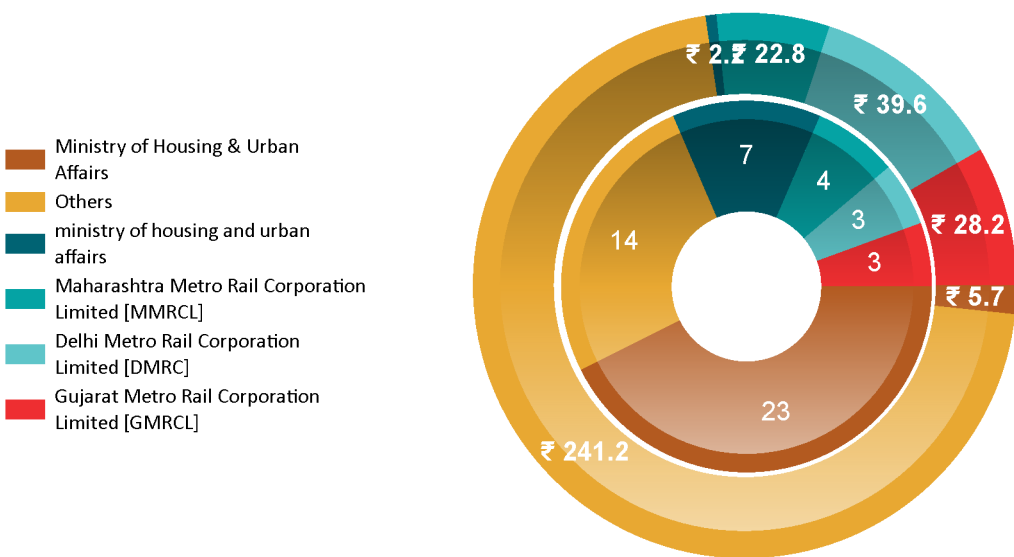


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

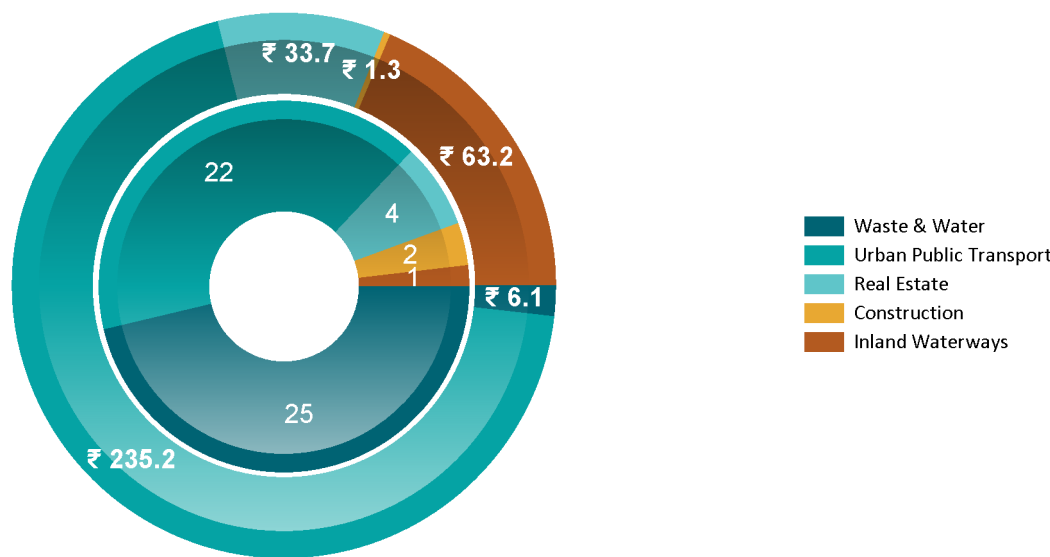


Physical & Financial progress (%) : Project count

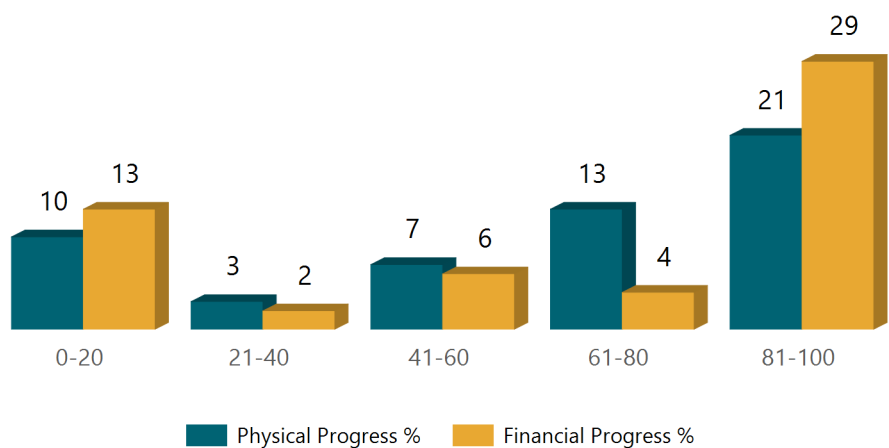

Cost Analytics : Major Sectors*

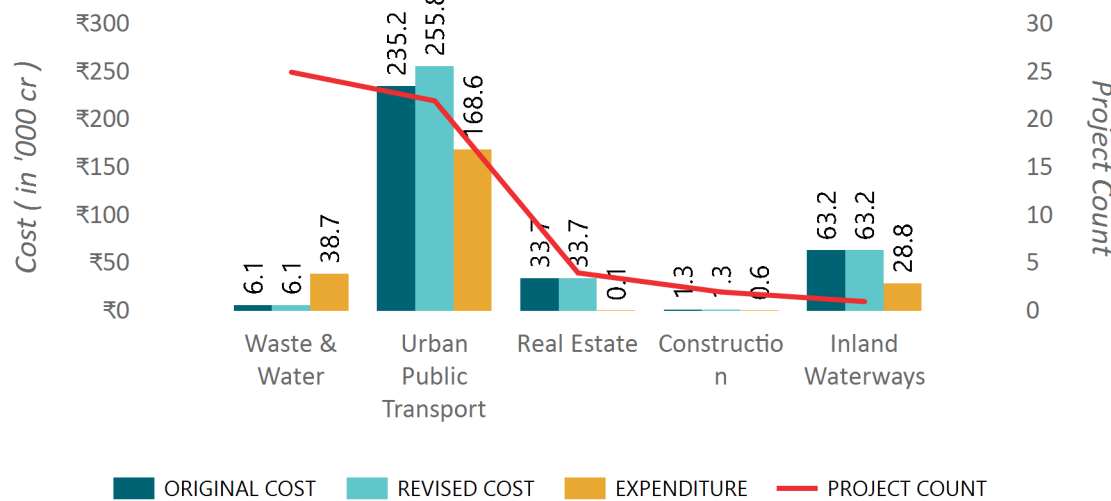

State Comparison : Major States*

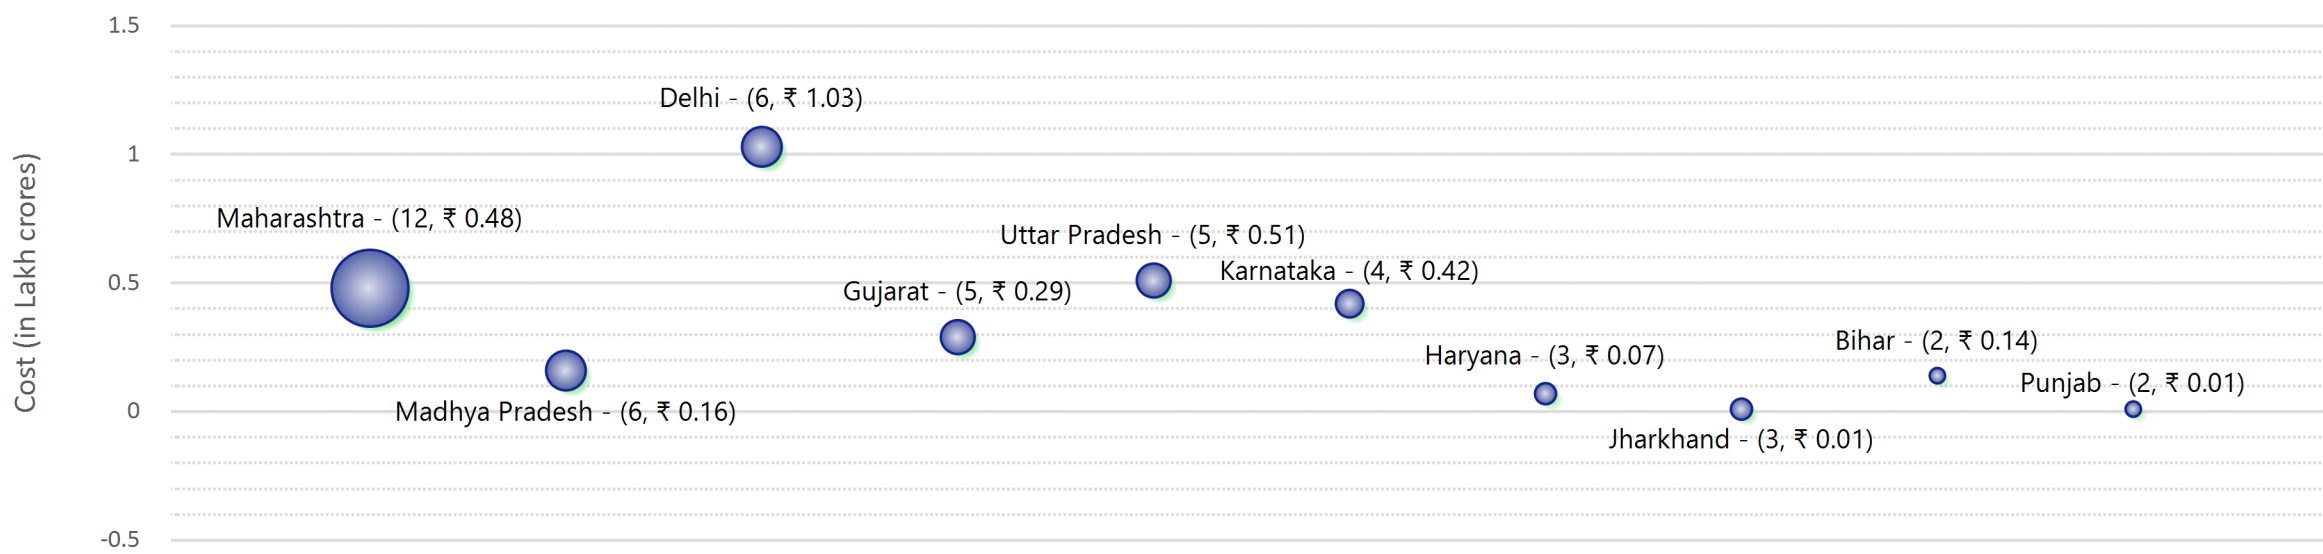

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246	63,246	28,779	47
2	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850	32,850	0	0
3	702633	DELHI-GHAZIABAD-MEERUT REGIONAL RAPID TRANSIT SYSTEM [RRTS] CORRIDOR	30,274	30,274	26,612	95
4	702635	CONSTRUCTION OF BANGALORE METRO RAIL PROJECT PHASE 2.	26,405	30,695	29,618	94
5	702632	DMRTS PHASE - IV [3 PRIORITY CORRIDORS]	24,949	24,949	17,838	71



List of Tables




Table 1: Ministry-wise Ongoing Projects





Ministry-wise Ongoing Projects

OCTOBER 2025

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Real Estate	2	3841.25 3841.25	590.15
		Total	2	3,841.25	590.15
2	Department of Higher Education	Education	29	12467.21 12401.2	7908.95
		Total	29	12,467.21	7,908.95
3	Department of Sports	Education	1	906.47 611.74	553.38
		Total	1	906.47	553.38
4	Department of Telecommunications	Telecommunication	15	152734.45 274827	77354.9
		Total	15	152,734.45	77,354.90
5	Department of Water Resources, River Development & GR	Waste & Water	8	4039.12 4039.12	1643.05
		Water Resources	39	93740.23 193594	138530
		Total	47	97,779.35	140,173.05
6	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	26	23049.84 23511	24797.1
		Total	26	23,049.84	24,797.10
7	Ministry of Coal	Coal	116	157554.96 155011	48288.1
		Electricity Generation	6	50201.48 54744.6	25385.2
		Railways	2	3485.86 4250.56	1815.47
		Total	124	211,242.30	75,488.77
8	Ministry of Health & Family Welfare	Healthcare	3	4155 4492.95	2477.91
		Total	3	4,155.00	2,477.91
9	Ministry of Housing & Urban Affairs	Construction	2	1290.53 1290.52	633.46
		Inland Waterways	1	63246 63246	28779
		Real Estate	4	33749.85 33749.8	58.58
		Urban Public Transport	22	235216.87 255798	168648
		Waste & Water	25	6085.6 6085.6	38687.6
		Total	54	339,588.85	236,806.64
10	Ministry of Labour and Employment	Healthcare	15	3576.21 3818.61	3422.37
		Total	15	3,576.21	3,422.37
11	Ministry of Mines	Construction	1	255.37 255.37	85.9
		Metals & Mining	9	12736.35 15116.5	6356.85
		Total	10	12,991.72	6,442.75
12	Ministry of Petroleum & Natural Gas	Energy Storage	16	81301.48 120224	93188.6
		Oil & Gas	86	348775.78 377915	185369
		Total	102	430,077.26	278,557.60
13	Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58
		Inland Waterways	2	5546.18 5258.15	3710.31
		Shipping	10	16923.41 17089.9	10375
		Tourism, Hospitality & Wellness	1	573 1238.05	496.63
		Total	14	23,735.59	14,639.94
14	Ministry of Power	Coal	2	2083 2365	911.94
		Electricity Generation	30	223418.07 278208	136137
		Transmission & Distribution	68	150796.17 157311	59403.7
		Total	100	376,297.24	196,452.64
15	Ministry of Railways	Railways	257	839222.35 988283	536735
		Total	257	839,222.35	536,735.00
16	Ministry of Steel	Metals & Mining	1	1700 1756.2	133.22
		Steel	20	19266.64 22504.9	8653.34
		Total	21	20,966.64	8,786.56
Total			820	2,552,631.73	1,611,187.71



Table 2: State-wise Ongoing Projects



Ongoing Projects State-Wise

OCTOBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1		Ministry of Steel	Steel	1	2518.39 2518.39	152.23
	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	6	19714.58 22972.8	11505.50
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	177 197	183.32
		Ministry of Railways	Railways	2	150819 150819	2520.51
	PAN India	Department of Telecommunications	Telecommunication	6	141891.67 264213	74254.01
	Total			16	315120.64	88615.57
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 209.88	0.00
	Total			1	209.88	0.00
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	2139.44 2139.44	472.80
		Department of Higher Education	Education	1	305 305	19.96
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1835.88
		Department of Water Resources, River Development & GR	Water Resources	3	10901.5 57269.5	26326.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1224.86 1224.86	676.79
		Ministry of Housing & Urban Affairs	Waste & Water	1	172.22 172.22	799.74
		Ministry of Labour and Employment	Healthcare	1	384.27 384.27	105.00
		Ministry of Petroleum & Natural Gas	Energy Storage	2	2898.34 3050	2344.92
			Oil & Gas	4	37804 37864	32464.75
		Ministry of Power	Transmission & Distribution	5	13395.24 13395.2	4917.60
		Ministry of Railways	Railways	27	52663.77 59888.8	33853.71
		Total			51	129035.81
	4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 592.61
Department of Telecommunications			Telecommunication	1	1255.49 1255.49	284.04
Ministry of Petroleum & Natural Gas			Energy Storage	1	43129 79459	61926.61
			Oil & Gas	1	9265 9265	6603.95
Ministry of Power			Electricity Generation	4	41850.64 61640.8	29133.62
			Transmission & Distribution	2	4963.8 9338.7	7705.17
Ministry of Railways			Railways	1	435 1250	542.07
Total			11	101491.54	106745.73	
5	Assam	Department of Higher Education	Education	1	153.71 153.71	124.33
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 256.16	44.70
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1712 1712	2397.37
		Ministry of Coal	Coal	2	449.23 449.23	187.07
		Ministry of Housing & Urban Affairs	Waste & Water	1	186.8 186.8	1664.41
		Ministry of Labour and Employment	Healthcare	1	143.23 154.75	101.83
		Ministry of Petroleum & Natural Gas	Energy Storage	3	10768.4 11947.4	10126.88
			Oil & Gas	12	26269.15 36624	27088.69
		Ministry of Power	Electricity Generation	1	6285.33 26075.5	25244.57
			Transmission & Distribution	1	5111.33 6700	5317.79
		Ministry of Railways	Railways	7	14593.57 16308.6	10247.14
	Total			32	67184.4	82828.82
6	Bihar	Department of Higher Education	Education	1	499.21 499.21	441.47
		Department of Telecommunications	Telecommunication	4	4220.71 3992.24	1070.43
		Department of Water Resources, River Development & GR	Waste & Water	5	2351.43 2351.43	1303.45
			Water Resources	2	2193.34 3088.88	598.72
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3541.56 3541.56	1338.95

Ongoing Projects State-Wise

OCTOBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Ministry of Housing & Urban Affairs	Urban Public Transport	1	13365.77 13365.8	4039.77
			Waste & Water	1	158.78 158.78	602.50
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9921.29
			Oil & Gas	6	24473.5 26338.2	13509.65
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3526.99
		Ministry of Power	Electricity Generation	1	10439.09 13756.6	12571.15
			Transmission & Distribution	2	751.63 751.63	1.03
		Ministry of Railways	Railways	23	50603.79 55072	22922.70
		Total		51	128195.99	71848.10
7	Chhattisgarh	Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1835.88
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 1109.33	855.96
		Ministry of Coal	Coal	14	31042.56 31042.6	13042.96
			Railways	1	1686.22 1686.22	353.12
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	10056.25 10467	6682.30
		Ministry of Power	Electricity Generation	2	25321 25321	3730.56
			Transmission & Distribution	1	385.84 385.84	382.40
		Ministry of Railways	Railways	19	34549.26 36180.5	18969.33
		Ministry of Steel	Metals & Mining	1	1700 1756.2	133.22
			Steel	6	7530.14 10050.1	5536.55
		Total		51	120260.7	51522.28
8	Dadra & Nagar Haveli and Daman & Diu	Ministry of Housing & Urban Affairs	Waste & Water	1	210 210	0.00
		Ministry of Power	Transmission & Distribution	1	4546.26 4546.26	4210.30
		Ministry of Railways	Railways	1	108000 108000	82967.89
		Total		3	112756.26	87178.19
9	Delhi	Department of Higher Education	Education	2	706.49 709.42	312.96
		Department of Telecommunications	Telecommunication	1	248.2 248.2	236.91
		Ministry of Housing & Urban Affairs	Construction	1	646.53 646.52	545.86
			Real Estate	1	32850 32850	0.00
			Urban Public Transport	4	69853.45 69853.4	44578.92
		Ministry of Power	Transmission & Distribution	4	4356.47 4908.47	4066.48
		Ministry of Railways	Railways	15	28623.17 28623.2	5954.91
		Total		28	137284.31	55696.04
10	Goa	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	255.69 255.69	154.30
		Ministry of Railways	Railways	2	5804.49 6182.62	6215.96
		Total		3	6060.18	6370.26
11	Gujarat	Department of Higher Education	Education	1	490.63 490.63	313.84
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Department of Water Resources, River Development & GR	Water Resources	2	25739.93 40082.8	36815.85
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1305 1551	718.20
		Ministry of Coal	Electricity Generation	2	3719.69 3719.69	981.48
		Ministry of Housing & Urban Affairs	Real Estate	1	539 539	39.63
			Urban Public Transport	3	28177.49 30329	24498.08
			Waste & Water	1	200 200	100.00
		Ministry of Labour and Employment	Healthcare	3	973.35 973.35	270.39
		Ministry of Petroleum & Natural Gas	Energy Storage	3	62245 98575	77278.48
			Oil & Gas	11	32704.12 32296.3	23575.09

Ongoing Projects State-Wise						OCTOBER 2025
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
11	Gujarat	Ministry of Ports, Shipping and Waterways	Shipping	3	4514.64 4681.1	1104.03
			Tourism, Hospitality & Wellness	1	573 1238.05	496.63
		Ministry of Power	Electricity Generation	1	339.35 339.35	317.59
			Transmission & Distribution	16	50389.44 50388.9	13736.39
		Ministry of Railways	Railways	26	185518.86 262039	219809.16
		Total			76	397766.39
12	Haryana	Ministry of Health & Family Welfare	Healthcare	1	1299 1299	349.41
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	6230.99 6230.99	72.38
			Waste & Water	2	491.2 491.2	3435.51
		Ministry of Petroleum & Natural Gas	Energy Storage	1	9028 9028	7292.34
			Oil & Gas	5	45925.07 49596.1	36223.79
		Ministry of Power	Transmission & Distribution	4	13362 13914	3062.26
		Ministry of Railways	Railways	4	53464 126368	125637.70
		Total			18	129800.26
13	Himachal Pradesh	Department of Higher Education	Education	3	811.15 921.89	595.63
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Power	Electricity Generation	4	7728.04 12301.5	4286.22
		Ministry of Railways	Railways	3	17005 17005.1	9510.37
		Total			11	25881.08
14	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 500.91	484.52
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 861.37	212.12
		Ministry of Health & Family Welfare	Healthcare	1	1828 1828	1321.70
		Ministry of Labour and Employment	Healthcare	1	131.05 164.93	1747.76
		Ministry of Petroleum & Natural Gas	Energy Storage	1	676.89 715.89	550.45
			Oil & Gas	2	1059.9 1059.9	234.30
		Ministry of Power	Electricity Generation	4	22207.77 27945.1	12904.53
			Transmission & Distribution	3	825.43 825.43	599.25
		Total			15	28352.23
15	Jharkhand	Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1835.88
		Department of Water Resources, River Development & GR	Water Resources	2	5430.04 12010.3	5941.33
		Ministry of Coal	Coal	28	51354.95 51119.3	10572.55
			Railways	1	1799.64 2564.34	1462.35
		Ministry of Housing & Urban Affairs	Waste & Water	3	654.14 654.14	3255.30
		Ministry of Mines	Metals & Mining	2	3370.02 3370.02	23.43
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9921.29
			Oil & Gas	3	2010.07 2010.07	628.64
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3526.99
		Ministry of Power	Coal	2	2083 2365	911.94
			Electricity Generation	2	31470 34660	19242.94
			Transmission & Distribution	1	1842.25 1842.25	1648.05
		Ministry of Railways	Railways	12	41769.95 42630.6	15247.24
		Ministry of Steel	Steel	6	2854.58 3572.87	1383.16
		Total			67	167382.99
16	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1701.81 1701.81	117.35
		Department of Higher Education	Education	1	420.41 420.41	364.44

Ongoing Projects State-Wise

OCTOBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	Karnataka	Department of Water Resources, River Development & GR	Water Resources	1	770.16 1606.07	1515.32
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1143.4 1143.4	553.88
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	41193.24 45483.2	38533.60
			Waste & Water	2	337.69 337.69	1644.73
		Ministry of Labour and Employment	Healthcare	2	428.92 428.92	27.80
		Ministry of Petroleum & Natural Gas	Energy Storage	1	678 1732	800.88
			Oil & Gas	5	9662 12693.6	8966.37
		Ministry of Ports, Shipping and Waterways	Shipping	1	153.23 153.23	50.10
		Ministry of Power	Transmission & Distribution	7	16061.01 16061	3412.08
		Ministry of Railways	Railways	17	25363.29 31781.9	17620.93
		Ministry of Steel	Steel	1	1043.63 1043.63	288.87
		Total		44	98956.79	73896.35
17	Kerala	Department of Higher Education	Education	1	1006.45 1217.4	641.73
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	484.57 484.57	91.67
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1957.05 1957.05	425.58
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	7996.87 10990.9	5019.06
		Ministry of Ports, Shipping and Waterways	Shipping	1	1799 1799	1558.39
		Ministry of Railways	Railways	3	2846 5183.64	2862.02
		Total		10	16089.94	10598.45
18	Ladakh	Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480 640	471.59
		Ministry of Power	Transmission & Distribution	1	288.71 288.71	280.02
		Total		3	1105.6	979.43
19	Madhya Pradesh	Department of Higher Education	Education	1	496.28 496.28	38.62
		Department of Telecommunications	Telecommunication	3	3883.82 3691.11	842.61
		Department of Water Resources, River Development & GR	Water Resources	3	2628.27 2941.14	2892.91
		Ministry of Coal	Coal	14	8634.02 8634.02	3457.47
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	14442.2 14442.2	7899.62
			Waste & Water	4	1243.05 1243.05	9847.62
		Ministry of Mines	Metals & Mining	1	1856.36 1856.36	940.27
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10088 10088	8059.53
			Oil & Gas	2	51211.25 51622	8616.20
		Ministry of Power	Transmission & Distribution	7	17765 17765	3666.37
		Ministry of Railways	Railways	19	58468.02 72465.1	43676.54
		Total		57	170716.27	89937.76
20	Maharashtra	Department of Higher Education	Education	2	250.33 446.26	183.91
		Department of Telecommunications	Telecommunication	4	7608.59 7608.59	2001.90
		Department of Water Resources, River Development & GR	Water Resources	11	22660.36 32345.7	33732.04
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	332.26
		Ministry of Coal	Coal	25	12455.88 12455.9	3205.76
		Ministry of Housing & Urban Affairs	Urban Public Transport	7	46771.57 60911.6	33511.04
			Waste & Water	5	1088.72 1088.72	8573.67
		Ministry of Labour and Employment	Healthcare	3	884.31 886.08	548.78
		Ministry of Petroleum & Natural Gas	Energy Storage	1	281.35 389.67	238.39
			Oil & Gas	13	34264.24 37660.4	21424.44

Ongoing Projects State-Wise						OCTOBER 2025
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
20	Maharashtra	Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58.00
			Shipping	2	6900 6900	6064.89
		Ministry of Power	Transmission & Distribution	3	29589.67 29589.7	6229.42
		Ministry of Railways	Railways	35	266858.79 358832	267526.11
		Total		113	430807.29	383630.61
21	Manipur	Department of Sports	Education	1	906.47 611.74	553.38
		Department of Water Resources, River Development & GR	Water Resources	1	1449.44 1822.24	1837.91
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499 499	155.72
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6603.95
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5317.79
		Ministry of Railways	Railways	1	14323 21885.9	15598.11
		Total		6	31554.24	30066.86
22	Meghalaya	Department of Higher Education	Education	1	494.52 494.52	419.57
		Department of Telecommunications	Telecommunication	1	971.96 971.96	208.25
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6603.95
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5317.79
		Total		4	15842.81	12549.56
23	Mizoram	Department of Higher Education	Education	1	474.23 474.23	167.55
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6603.95
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5317.79
		Total		3	14850.56	12089.29
24	Nagaland	Department of Higher Education	Education	1	275.63 275.63	261.24
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	9492.62 9492.62	6614.75
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5317.79
		Ministry of Railways	Railways	2	8786.7 8786.7	5585.56
		Total		6	23666.28	17779.34
25	Odisha	Department of Higher Education	Education	1	1229.32 773.76	838.21
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1835.88
		Department of Water Resources, River Development & GR	Water Resources	2	1556.46 5291.33	5342.49
		Ministry of Coal	Coal	12	36526.28 34218	13233.80
			Electricity Generation	1	27212.96 27213	2549.31
		Ministry of Labour and Employment	Healthcare	1	164.6 164.6	16.40
		Ministry of Mines	Metals & Mining	5	7343.97 9724.14	5258.15
		Ministry of Petroleum & Natural Gas	Energy Storage	2	12886.34 14217	12204.27
			Oil & Gas	5	25285.44 23768.5	16095.66
		Ministry of Ports, Shipping and Waterways	Shipping	1	3004.63 3004.63	1149.79
		Ministry of Power	Electricity Generation	1	11843.75 12543	4839.68
			Transmission & Distribution	1	342.69 342.69	0.71
		Ministry of Railways	Railways	25	46848.33 51580.4	33305.37
			Railways	1	267.61 267.61	0.00
		Ministry of Steel	Steel	1	1105.23 1105.23	790.11
		Total		62	182764.78	97459.83
26	Puducherry	Department of Higher Education	Education	1	618.34 544.34	529.90
		Ministry of Railways	Railways	1	713 981	598.38
		Total		2	1331.34	1128.28
27	Punjab	Department of Higher Education	Education	2	559.3 559.3	290.39

Ongoing Projects State-Wise

OCTOBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
27	Punjab	Department of Water Resources, River Development & GR	Water Resources	2	3727.07 5177.86	5182.41
		Ministry of Housing & Urban Affairs	Waste & Water	2	545.53 545.53	2807.11
		Ministry of Petroleum & Natural Gas	Oil & Gas	5	12693.36 12693.4	8097.02
		Ministry of Power	Transmission & Distribution	1	5969 5969	485.87
		Ministry of Railways	Railways	3	15702.64 15703	9117.19
	Total			15	39196.9	25979.99
28	Rajasthan	Department of Telecommunications	Telecommunication	2	758.54 530.07	369.83
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1367 1367	696.69
		Ministry of Coal	Electricity Generation	1	1813 1813	1167.40
		Ministry of Petroleum & Natural Gas	Energy Storage	3	52618.05 88948.1	69364.07
			Oil & Gas	2	10599 10599	6656.41
		Ministry of Power	Electricity Generation	1	5491.89 5491.89	5084.68
			Transmission & Distribution	22	53646.51 54198.2	19895.80
	Ministry of Railways	Railways	23	88639.51 164210	140285.65	
Total			56	214933.5	243520.53	
29	Sikkim	Department of Higher Education	Education	2	999.82 924.82	359.78
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 323.26	38.69
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6603.95
		Ministry of Power	Electricity Generation	2	6686.33 7576.15	5273.06
			Transmission & Distribution	1	4754.42 9129.32	7705.14
	Ministry of Railways	Railways	1	7877 12133	9039.91	
Total			8	29905.83	29020.53	
30	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1207 1207	183.02
		Ministry of Coal	Electricity Generation	1	218.03 218.03	164.70
		Ministry of Housing & Urban Affairs	Inland Waterways	1	63246 63246	28778.98
		Ministry of Labour and Employment	Healthcare	1	152.95 152.95	107.83
		Ministry of Mines	Metals & Mining	1	166 166	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	2334 3448.71	1767.45
			Oil & Gas	4	38385 46153	6149.73
		Ministry of Power	Transmission & Distribution	1	548 548	37.86
	Ministry of Railways	Railways	7	8370.7 11490.2	5856.10	
Total			20	114627.68	43180.67	
31	Telangana	Department of Higher Education	Education	1	262 262	186.49
		Department of Telecommunications	Telecommunication	3	3923.59 3923.59	866.62
		Department of Water Resources, River Development & GR	Water Resources	4	11670.14 24129.6	11936.34
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	332.26
		Ministry of Coal	Coal	9	3890.03 3890.03	2513.80
		Ministry of Health & Family Welfare	Healthcare	1	1028 1365.95	806.80
		Ministry of Housing & Urban Affairs	Construction	1	644 644	87.60
		Ministry of Labour and Employment	Healthcare	1	211.13 211.13	198.95
		Ministry of Power	Transmission & Distribution	2	5694.56 5694.56	4808.49
	Ministry of Railways	Railways	11	19213.75 22977.8	10959.90	
Total			34	47037.68	32697.25	
32	Tripura	Ministry of Petroleum & Natural Gas	Energy Storage	1	656 656	509.92
			Oil & Gas	2	9474.33 9396.51	6674.05

Ongoing Projects State-Wise

OCTOBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
32	Tripura	Ministry of Power	Transmission & Distribution	1	5111.33 6700	5317.79
		Total		4	15241.66	12501.76
33	Uttar Pradesh	Department of Higher Education	Education	1	246 246	198.02
		Department of Telecommunications	Telecommunication	4	4220.71 3992.24	1070.43
		Department of Water Resources, River Development & GR	Waste & Water	2	1532.96 1532.96	243.43
			Water Resources	3	2953.27 6309.81	4689.88
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	5	7268.31 7323.51	17022.23
		Ministry of Coal	Coal	2	1328.09 1328.09	1052.76
			Electricity Generation	1	17237.8 21780.9	20522.30
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	49730.1 49730.1	41774.16
			Waste & Water	2	797.47 797.47	5957.01
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11068.45 11068.5	8286.57
			Oil & Gas	3	17824.68 18213.1	1645.07
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3526.99
		Ministry of Power	Electricity Generation	2	28284.42 30471.2	14867.23
			Transmission & Distribution	3	8114.81 8114.81	2073.46
		Ministry of Railways	Railways	26	92690.92 167547	147592.53
		Total		60	248667.17	270522.07
34	Uttarakhand	Department of Higher Education	Education	1	650.85 650.85	195.52
		Department of Water Resources, River Development & GR	Water Resources	1	2584.1 2584.1	968.52
		Ministry of Housing & Urban Affairs	Real Estate	1	150.97 150.97	18.95
		Ministry of Labour and Employment	Healthcare	1	102.4 297.63	297.63
		Ministry of Power	Electricity Generation	3	11663.95 26070	20164.22
		Ministry of Railways	Railways	1	38953 38953	24645.15
		Total		8	54105.27	46289.99
35	West Bengal	Department of Higher Education	Education	1	500 442	390.60
		Department of Telecommunications	Telecommunication	2	3462.17 3462.17	700.60
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 154.73	96.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1877.3 1877.3	418.18
		Ministry of Coal	Coal	13	15863.74 15863.7	2866.12
		Ministry of Mines	Construction	1	255.37 255.37	85.90
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9921.29
			Oil & Gas	8	18159.65 19007.2	11678.42
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3526.99
			Shipping	2	551.91 551.91	447.78
		Ministry of Power	Electricity Generation	3	20091.84 20091.8	3721.21
			Transmission & Distribution	2	751.63 751.63	1.03
		Ministry of Railways	Railways	15	47626.45 58198.4	34098.13
		Ministry of Steel	Steel	5	4214.67 4214.67	502.42
		Total		57	129106.64	68454.84




Table 3: Completed Projects



Completed Projects During Month

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
	Ministry of Petroleum & Natural Gas					
	Oil & Gas					
1	HP Trijet Unit in Visakh Refinery (Hindustan Petroleum Corporation Limited) 709761	Andhra Pradesh	07/2024 (07/2024)	11/2025 (07/2027) (11/2025)	193 (193)	0.43
2	Bathinda Sangrur Pipeline (Ministry of Petroleum and Natural Gas) 612998	Punjab	11/2021 (11/2021)	10/2015 (05/2024) (10/2025)	367 (397)	355.93
	Total (2)				560	356.36
	Ministry of Railways					
	Railways					
3	Vijapur Ambliyasani Gauge Conversion (Western Railway (WR) - II) 611938	Gujarat	05/2022 (05/2022)	10/2025 (05/2026) (10/2025)	415.38 (415.38)	701.04
4	Himmatnagar Khedbrahma Gauge Conversion (Western Railway (WR) - II) 611939	Gujarat	06/2022 (04/2017)	08/2025 (06/2001) (08/2025)	482.42 (482.42)	894.4
5	Domingarh-Gorakhpur-Gorakhpur Cantt.-Kusumhi - 3rd Railway Line Project (North Eastern Railway (NER)) 705566	Uttar Pradesh	11/2016 (06/2018)	09/2025 (02/2025) (09/2025)	351 (521.47)	499.64
6	Bahraich - Nanpara - Nepalganj Road Gauge Conversion (North Eastern Railway (NER)) 705863	Uttar Pradesh	07/2020 (04/2021)	09/2025 (07/2025) (09/2025)	950 (550)	507.02
	Total (4)				2198.8	2602.1

Note: Cumulative Expenditure is as per last reporting by Central Line Ministries/ Departments on the IPM portal, this may not be the actual completion cost.



Table 4: Newly Added Projects



Newly Added Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
	Department of Sports				
	Education				
1	National Sports University [NSU], Imphal [Manipur] (<i>Department of Sports & Youth Affairs</i>) (400081)	Manipur	(01/2022)	08/2024 (11/2025)	906.47 (611.74)
	Total (1)				906.47
	Ministry of Coal				
	Electricity Generation				
2	600 MW Khavda Solar Power Project (<i>NLC India Limited [NLCIL]</i>) (617730)	Gujarat	08/2023 (06/2024)	06/2026 (-)	3335.85 (-)
	Total (1)				3335.85
	Ministry of Labour and Employment				
	Healthcare				
3	Construction of 350 beds + 50 Super Specialty beds ESIC Hospital Sheelanagar, Visakhapatnam, Andhra Pradesh (<i>Employee's State Insurance Company [ESIC]</i>) (612167)	Andhra Pradesh	02/2021 (04/2023)	10/2025 (01/2026)	384.27 (-)
4	Construction of 200 bedded ESIC Hospital with 62 Nos Staff quarters , Beltola (<i>Employee's State Insurance Company [ESIC]</i>) (612201)	Assam	12/2017 (10/2021)	04/2025 (10/2025)	143.23 (154.75)
5	Demolition, Construction and upgradation of ESI Hospital, Kalol, Gujarat from 50 beds to 150 beds. (<i>Employee's State Insurance Company [ESIC]</i>) (612211)	Gujarat	08/2022 (10/2023)	10/2025 (06/2026)	205.87 (-)
6	C/o Construction of 200 bedded [Up-gradable to 300 bedded] ESI Hospital at Surat Gujarat. (<i>Employee's State Insurance Company [ESIC]</i>) (612185)	Gujarat	06/2019 (03/2021)	06/2025 (05/2025)	209.36 (-)
7	350 Bedded [Upgradable to 500 beds] ESI Hospital at Sanand (<i>Employee's State Insurance Company [ESIC]</i>) (612186)	Gujarat	06/2022 (04/2023)	03/2026 (02/2026)	558.12 (-)
8	Construction of 100 bedded ESIC Hospital & 32 nos. of Staff qtrs at OMPURA J&K. (<i>Employee's State Insurance Company [ESIC]</i>) (612239)	Jammu and Kashmir	09/2019 (12/2021)	09/2024 (05/2025)	131.05 (164.93)
9	Construction of 200 bed ESI Hospital at Bommasandra, Karnataka (<i>Employee's State Insurance Company [ESIC]</i>) (612745)	Karnataka	02/2015 (10/2024)	01/2027 (-)	278 (-)
10	Construction of 100 bed ESI Hospital and Staff Quarters [32 Nos.] at Harohalli, Karnataka (<i>Employee's State Insurance Company [ESIC]</i>) (612748)	Karnataka	07/2019 (03/2025)	02/2027 (-)	150.92 (-)
11	Construction of 200 Bedded [Upgradable to 500 Bedded including 50 beds of SST] ESIC Hospital at Bibewadi, Pune (<i>Employee's State Insurance Company [ESIC]</i>) (612188)	Maharashtra	05/2018 (03/2023)	09/2025 (02/2026)	429.25 (-)
12	Construction of 200 Bedded ESIC Hospital at Butibori, Nagpur, Maharashtra. (<i>Employee's State Insurance Company [ESIC]</i>) (612213)	Maharashtra	10/2013 (08/2022)	08/2025 (08/2025)	194.93 (196.7)
13	Upgradation & Extension of ESIC Hospital and Construction of PG Hostel / Staff Housing for ESIC Hospital at Andheri, Mumbai (<i>Employee's State Insurance Company [ESIC]</i>) (616691)	Maharashtra	(06/2009)	08/2025 (12/2025)	260.13 (-)
14	Construction of 100 Bedded ESI Hospital at Duburi, Odisha. (<i>Employee's State Insurance Company [ESIC]</i>) (612513)	Odisha	12/2010 (02/2025)	06/2027 (-)	164.6 (-)
15	Construction of 100 Bedded ESIC Hospital building and 32 Nos Residential Quarters at Vallam Vadangal, SIPCOT, Sriperumbudur (<i>Employee's State Insurance Company [ESIC]</i>) (612178)	Tamil Nadu	02/2015 (03/2023)	06/2025 (-)	152.95 (-)
16	Construction of New OPD Block 200 Bed ward Basement + GF + 6 Floors at the location of old OPD block, at existing ESIC Hospital/ Medical college campus, Sanathnagar, Hyderabad (<i>Employee's State Insurance Company [ESIC]</i>) (612688)	Telangana	11/2017 (10/2021)	06/2024 (06/2025)	211.13 (-)
17	CONSTRUCTION OF 300 BEDDED HOSPITAL AT HARIDWAR (<i>Employee's State Insurance Company [ESIC]</i>) (612259)	Uttarakhand	02/2021 (12/2021)	10/2024 (06/2025)	102.4 (297.63)
	Total (15)				3576.21
	Ministry of Ports, Shipping and Waterways				
	Shipping				
18	Mechanization of Berth No.14 for handling Containers and other cargo on DBFOT basis - Phase II (<i>New Mangalore Port Authority</i>) (617804)	Karnataka	(06/2024)	03/2027 (-)	153.23 (-)
	Total (1)				153.23
	Ministry of Power				
	Transmission & Distribution				
19	Provision of ICT Augmentation & Bus Reactor at Bhuj-II PS (<i>Power Grid Corporation of India Limited [POWERGRID]</i>) (617801)	Gujarat	03/2025 (03/2025)	12/2026 (03/2027)	581.74 (-)
20	Transmission System Strengthening at Davanagere for Integration of RE Generation [SPV Name - POWERGRID Davanagere Power Transmission Limited] (<i>Power Grid Corporation of India Limited [POWERGRID]</i>) (617803)	Karnataka	09/2025 (09/2025)	09/2027 (-)	379 (-)

Newly Added Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
21	Augmentation of Transformation Capacity and Implementation of Line Bays at Mandsaur S/S for RE Interconnection [SPV Name- POWERGRID Mandsaur I RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617802)	Madhya Pradesh	10/2025 (10/2025)	03/2028 (-)	319 (-)
	Total (3)				1279.74
	Ministry of Railways				
	Railways				
22	3rd Line between Gudur Renigunta 83.17 Km (South Central Railway [SCR] - II) (617216)	Andhra Pradesh	10/2024 (10/2024)	03/2027 (-)	877.34 (-)
23	Tiupati Katpadi 104.39 kms (South Central Railway [SCR] - II) (617210)	Andhra Pradesh	04/2025 (04/2025)	03/2029 (-)	1215.56 (-)
24	Malugur- Palasamudram New Line Project [17.975 Km] (South Western Railway [SWR] - II) (611615)	Andhra Pradesh	09/2022 (07/2026)	11/2027 (12/2027)	342 (-)
25	Construction of Bulb line at Nabinagar Ankorah of East Central Railway (East Central Railway [ECR] - I) (617231)	Bihar	06/2024 (06/2024)	06/2028 (-)	611.74 (-)
26	KHARSIA- NAYA RAIPUR-PARMALKASA 5th and 6th Line [278KM] (CAO/C/SECR) (617200)	Chhattisgarh	04/2025 (04/2025)	03/2031 (-)	7853.84 (-)
27	Construction of New BG line between Hassan to Belur [27 Km] (South Western Railway [SWR] - II) (400023)	Karnataka	03/2019 (12/2025)	04/2028 (04/2027)	749 (-)
28	Belgaum-Dharwad via Kittur [73.10Km] (South Western Railway [SWR] - II) (706835)	Karnataka	09/2020 (03/2025)	12/2027 (03/2029)	1591 (-)
29	Gondia-Balharshah [Chanda Fort] Doubling [240 Km] (South East Central Railway) (617201)	Maharashtra	04/2025 (04/2025)	03/2031 (-)	4373.04 (-)
30	Rail Connectivity to Errupalem Amravati Namburu 57 Km (South Central Railway [SCR] - II) (617214)	Multi-States (Andhra Pradesh, Telangana)	11/2024 (11/2024)	03/2027 (-)	2047.4 (-)
31	Buramara-Chakulia new line [59.96 km] (South Eastern Railway [SER] - I) (616588)	Multi-States (Jharkhand, Odisha, West Bengal)	08/2024 (12/2024)	12/2029 (-)	1459.13 (-)
32	Jeypore-Malkanagiri New Railway Line Project (East Coast Railway [ECOR] - II) (705742)	Odisha	02/2018 (12/2023)	07/2033 (07/2033)	2344 (-)
33	Bangriposi-Gorumahisani new line [85.60 km] (CAO/C/SER) (616586)	Odisha	08/2024 (09/2025)	12/2029 (-)	2269.49 (-)
34	Badampahar-Kendujhargarh new line [82.06 km] (CAO/C/SER) (616587)	Odisha	08/2024 (09/2025)	12/2029 (-)	1875.72 (-)
35	Doubling between Bhadrachalam Road and Dornakal (South Central Railway [SCR] - II) (616856)	Telangana	08/2023 (04/2025)	04/2029 (-)	770.12 (-)
	Total (14)				28379.38




Table 5: Ongoing Projects

North Eastern Region



Ongoing Projects of North-East Region							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (11/2025)	1712 (1712)	2397.37	91
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	155.72	41
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	38.69	14
	Total (3)				2534.26	2591.78	
	Ministry of Coal						
	Coal						
4	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	81.47	0
5	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.6	3
	Total (2)				449.23	187.07	
	Department of Higher Education						
	Education						
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (-)	592.61 (592.61)	550.27	80
7	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (10/2025)	153.71 (153.71)	124.33	97
8	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (07/2025)	494.52 (494.52)	419.57	89
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (12/2029)	474.23 (474.23)	167.55	4
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	261.24	97
11	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	121.56	14
12	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (03/2026)	314.06 (314.06)	238.22	85
	Total (7)				2990.52	1882.74	
	Department of Sports						
	Education						
13	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081)	Manipur	NA (01/2022)	08/2024 (11/2025)	906.47 (611.74)	553.38	94
	Total (1)				906.47	553.38	
	Ministry of Power						
	Electricity Generation						
14	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3708.61	16
15	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	64.36	3
16	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	116.08	2
17	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	25244.57	97
18	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	3817.49	70
19	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (12/2025)	938.29 (1828.11)	1455.57	93
	Total (6)				48536.97	34406.68	
	Transmission & Distribution						
20	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	0.03	0

Ongoing Projects of North-East Region

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
21	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	7705.14	82
22	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (03/2026)	5111.33 (6700)	5317.79	96
	Total (3)				10075.13	13022.96	
	Ministry of Petroleum & Natural Gas						
	Energy Storage						
23	Rajasthan Refinery Project (MinistryofPetroleumNaturalGas) (701263)	Arunachal Pradesh	10/2017 (10/2017)	10/2022 (03/2026)	43129 (79459)	61926.61	89
24	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Assam	01/2019 (01/2019)	07/2024 (03/2026)	10228 (11407)	9921.29	88
25	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	63.31	50
26	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	142.28	57
27	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	06/2022 (06/2022)	09/2025 (06/2026)	656 (656)	509.92	89
	Total (5)				54553.4	72563.41	
	Oil & Gas						
28	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	05/2021 (05/2021)	10/2023 (05/2026)	412.3 (577)	445.73	87
29	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	07/2020 (07/2020)	07/2024 (12/2025)	12366 (22494)	17659.09	78
30	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	01/2018 (01/2018)	02/2020 (12/2025)	682.9 (726.93)	491.64	94
31	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Assam	06/2021 (06/2021)	12/2024 (12/2025)	860 (860)	615.47	99
32	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	12/2020 (12/2020)	03/2024 (12/2025)	430.76 (430.76)	330.99	87
33	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (MinistryofPetroleumNaturalGas) (709776)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277 (323.09)	188.04	68
34	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (MinistryofPetroleumNaturalGas) (709779)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768 (740)	123.97	44
35	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2026)	344.99 (344.99)	215.98	48
36	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	09/2023 (09/2023)	05/2026 (05/2026)	198.7 (198.7)	50.26	40
37	DCU Revamp Project (NRL) (709864)	Assam	08/2021 (08/2021)	07/2024 (06/2026)	370 (370)	266.35	64
38	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	04/2023 (04/2023)	12/2024 (12/2025)	293.5 (293.5)	97.22	96
39	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura)	04/2020 (04/2020)	03/2024 (03/2026)	9265 (9265)	6603.95	86
40	Augmentation/ Revamping of Dimapur Depot, Dimapur (MinistryofPetroleumNaturalGas) (709786)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 (227.62)	10.8	25
41	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022 (03/2022)	05/2024 (12/2025)	209.33 (131.51)	70.1	66
	Total (14)				26706.1	27169.59	
	Ministry of Labour and Employment						
	Healthcare						
42	Construction of 200 bedded ESIC Hospital with 62 Nos Staff quarters , Beltola (Employee's State Insurance Company [ESIC]) (612201)	Assam	12/2017 (10/2021)	04/2025 (10/2025)	143.23 (154.75)	101.83	93
	Total (1)				143.23	101.83	

Ongoing Projects of North-East Region

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Railways						
	Railways						
43	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
44	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
45	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
46	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3727.78	93
47	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15598.11	69
48	Murkongselek-Pasighat (Northeast Frontier Railway (NFR) - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (03/2023)	03/2025 (05/2026)	435 (1250)	542.07	61
49	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5571.82	81
50	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
51	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Sikkim	10/2009 (05/2010)	05/2015 (12/2027)	7877 (12133)	9039.91	84
	Total (9)				36793.57	34885.16	
	Department of Telecommunications						
	Telecommunication						
52	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (03/2026)	971.96 (971.96)	208.25	99
53	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (03/2026)	1255.49 (1255.49)	284.04	91
	Total (2)				2227.45	492.29	
	Ministry of Housing & Urban Affairs						
	Waste & Water						
54	Dibrugarh Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702682)	Assam	02/2016 (01/2020)	03/2023 (12/2025)	186.8 (186.8)	1664.41	100
	Total (1)				186.8	1664.41	
	Department of Water Resources, River Development & GR						
	Water Resources						
55	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55
56	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
	Total (2)				1705.6	1882.61	




Table 6: All Ongoing Projects





All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Civil Aviation							
Aviation & Aviation Infrastructure							
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport (Airport Authority of India [AAI]) (612786)	Andhra Pradesh	03/2023 (01/2024)	01/2026 (03/2026)	265.91 (265.91)	67.22	39
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. (Airport Authority of India [AAI]) (701107)	Andhra Pradesh	06/2020 (09/2020)	09/2022 (12/2025)	611.8 (611.8)	507.14	84
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. (Airport Authority of India [AAI]) (701121)	Andhra Pradesh	12/2022 (08/2023)	08/2025 (12/2025)	347.15 (347.15)	102.43	57
4	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (11/2025)	1712 (1712)	2397.37	91
5	Development of New Civil Enclave at Bihta (Airport Authority of India [AAI]) (612183)	Bihar	08/2024 (03/2025)	09/2027 (-)	1413 (1413)	0	1
6	Development of New Civil Enclave and associated works at Darbhanga Airport (Airport Authority of India [AAI]) (612194)	Bihar	07/2024 (07/2024)	01/2026 (-)	911.66 (911.66)	213.22	38
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna (Airport Authority of India [AAI]) (701101)	Bihar	12/2018 (10/2018)	07/2023 (11/2025)	1216.9 (1216.9)	1125.73	95
8	Goa Airport Terminal Building Extension Project (Airport Authority of India [AAI]) (701105)	Goa	11/2017 (12/2019)	12/2021 (09/2025)	255.69 (255.69)	154.3	94
9	Development of Dholera International Greenfield Airport , Gujarat (Airport Authority of India [AAI]) (701126)	Gujarat	06/2022 (07/2022)	06/2026 (06/2026)	1305 (1551)	718.2	67
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. (Airport Authority of India [AAI]) (611047)	Jammu and Kashmir	07/2022 (07/2023)	06/2026 (06/2026)	861.37 (861.37)	212.12	39
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport (Airport Authority of India [AAI]) (612787)	Karnataka	06/2023 (01/2024)	01/2026 (03/2026)	320.47 (320.47)	81.22	45
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. (Airport Authority of India [AAI]) (612788)	Karnataka	06/2023 (02/2024)	01/2026 (01/2026)	322.45 (322.45)	140.4	59
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 (Airport Authority of India [AAI]) (612789)	Kerala	06/2023 (02/2024)	09/2025 (03/2026)	484.57 (484.57)	91.67	23
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh (Airport Authority of India [AAI]) (400010)	Ladakh	07/2018 (09/2018)	09/2021 (10/2025)	480 (640)	471.59	77
15	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	155.72	41
16	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, Jewar [earlier MOPA, without ASMGCS], HIAL & BIAL (Airport Authority of India [AAI]) (611570)	Multi-States (Karnataka, Maharashtra, Telangana, Uttar Pradesh)	NA (10/2022)	09/2025 (08/2026)	500.48 (500.48)	332.26	75
17	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. (Airport Authority of India [AAI]) (701127)	Rajasthan	05/2022 (04/2023)	11/2024 (11/2025)	480 (480)	317.88	96
18	Construction of New Integrated Passenger Terminal Building at Udaipur Airport (Airport Authority of India [AAI]) (701128)	Rajasthan	06/2023 (11/2022)	03/2026 (10/2026)	887 (887)	378.81	50
19	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	38.69	14
20	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAI]) (611602)	Tamil Nadu	05/2018 (06/2023)	07/2025 (06/2026)	1207 (1207)	183.02	25
21	Construction of New Terminal Building, Second Link Taxi Track, Apron Expansion, and associated works at Prayagraj Airport- On Design & Build Basis. (Airport Authority of India [AAI]) (612063)	Uttar Pradesh	NA (08/2023)	11/2024 (08/2025)	219.18 (274.38)	215.2	100
22	Lucknow Airport-Terminal 3- Phase 1 & Other Associated Works (Adani Airport Holdings Limited) (701091)	Uttar Pradesh	06/2018 (09/2018)	03/2026 (-)	3100 (3100)	16024.42	100
23	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAI]) (701113)	Uttar Pradesh	07/2024 (07/2024)	07/2027 (07/2027)	2869.65 (2869.65)	361.71	18
24	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAI]) (701122)	Uttar Pradesh	06/2024 (07/2024)	07/2026 (-)	579 (579)	88.64	20
25	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAI]) (611495)	West Bengal	08/2024 (10/2023)	01/2027 (01/2027)	1549 (1549)	310.58	13

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
26	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCB Airport Kolkata. <i>(Airport Authority of India [AAI])</i> (612791)	West Bengal	04/2023 (12/2023)	02/2025 (08/2026)	328.3 (328.3)	107.6	49
	Total (26)				23049.84	24797.14	
	Ministry of Coal						
	Coal						
27	TIKAK EXTENSION OCP <i>(MIS MoCoal Integration Logins)</i> (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	81.47	0
28	TIRAP OCP <i>(MIS MoCoal Integration Logins)</i> (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.6	3
29	PORDA CHINTAPANI OCP [10 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400144)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	2310.12 (2310.12)	87.97	10
30	CHHAL OC SEAM III [6 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400145)	Chhattisgarh	12/2013 (12/2013)	03/2022 (11/2025)	610.63 (610.63)	579.82	85
31	BAROUD OC EXPANSION [3.0-10.0M] <i>(South Eastern Coalfields Limited [SECL])</i> (400149)	Chhattisgarh	08/2020 (08/2020)	03/2029 (-)	2309.8 (2309.8)	937.38	50
32	DIPKA EXPANSION OCP [40 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400354)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	5241.4 (5241.4)	2841.08	37
33	GEVRA OC [70 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400424)	Chhattisgarh	03/2016 (03/2016)	03/2023 (03/2026)	11816.4 (11816.4)	6687.44	78
34	JAMPALI OC RCE [2.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613795)	Chhattisgarh	05/2020 (05/2020)	03/2025 (06/2025)	278.64 (278.64)	210.07	82
35	AMERA OC RCE [1.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613798)	Chhattisgarh	02/2015 (02/2015)	03/2026 (-)	335.97 (335.97)	88.24	42
36	AMGAON OC RCE [1.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613799)	Chhattisgarh	07/2015 (07/2015)	03/2026 (-)	316.11 (316.11)	188.62	78
37	JAGANNATHPUR OC RCE PROJECT <i>(South Eastern Coalfields Limited [SECL])</i> (613800)	Chhattisgarh	07/2016 (07/2016)	03/2025 (03/2026)	459.49 (459.49)	274.35	96
38	MAHAMAYA OCP [1.50 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613801)	Chhattisgarh	05/2018 (05/2018)	03/2026 (-)	410.26 (410.26)	182.83	54
39	KATKONA RO UG MINE <i>(South Eastern Coalfields Limited [SECL])</i> (615191)	Chhattisgarh	01/2023 (01/2023)	03/2029 (-)	329.21 (329.21)	61.34	2
40	PELMA OC MDO <i>(South Eastern Coalfields Limited [SECL])</i> (616234)	Chhattisgarh	10/2022 (10/2022)	03/2033 (-)	1725.04 (1725.04)	15.66	40
41	KUSMUNDA OC EXPANSION PROJECT <i>(SECL - CIL)</i> (617287)	Chhattisgarh	11/2024 (11/2024)	03/2030 (-)	4516.88 (4516.88)	775.13	21
42	MANIKPUR OC EXPANSION PROJECT <i>(South Eastern Coalfields Limited [SECL])</i> (617288)	Chhattisgarh	01/2025 (01/2025)	03/2029 (-)	382.61 (382.61)	113.03	21
43	HURA C OCP <i>(ECL - CIL)</i> (400018)	Jharkhand	08/2022 (08/2022)	03/2029 (-)	859.41 (859.41)	451.62	62
44	KONAR EXPANSION OCP <i>(Ministry of Coal)</i> (400073)	Jharkhand	01/2022 (01/2022)	03/2032 (-)	799.34 (799.34)	429.65	45
45	KARO EXPANSION OCP <i>(Ministry of Coal)</i> (400074)	Jharkhand	01/2022 (01/2022)	03/2029 (-)	908.47 (908.47)	269.26	22
46	SANGHMITRA OC <i>(Ministry of Coal)</i> (400136)	Jharkhand	03/2024 (03/2024)	03/2032 (-)	2660 (2660)	0	0
47	CHANDRAGUPT OCP <i>(Ministry of Coal)</i> (400138)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	973.5 (973.5)	440.56	24
48	KOTRE BASANTPUR PACHMO OCP <i>(Ministry of Coal)</i> (400139)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	861.06 (625.4)	455.95	42
49	Pachwara South Coal Block <i>(NLC India Limited [NLCIL])</i> (400142)	Jharkhand	03/2016 (11/2019)	09/2028 (-)	2242.9 (2242.9)	1220.76	74
50	RPR MAGADH EXP OCP <i>(Ministry of Coal)</i> (400150)	Jharkhand	08/2020 (08/2020)	03/2028 (-)	7254.37 (7254.37)	1600.77	38
51	NORTH URIMARI EXPANSION OCP <i>(Ministry of Coal)</i> (400151)	Jharkhand	07/2021 (07/2021)	03/2029 (-)	778.8 (778.8)	696.05	67
52	EPR ROHINI - KARKETTA OCP <i>(Ministry of Coal)</i> (400153)	Jharkhand	01/2021 (01/2021)	03/2028 (-)	1020.42 (1020.42)	84.74	21
53	EPR PUNDI OCP <i>(Ministry of Coal)</i> (400154)	Jharkhand	11/2020 (11/2020)	03/2027 (-)	713.35 (713.35)	236.58	10
54	EPR ASHOK OC <i>(Ministry of Coal)</i> (400155)	Jharkhand	05/2021 (05/2021)	03/2031 (-)	2898.28 (2898.28)	179.7	24

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
55	EPR AMRAPALI OCP (Ministry of Coal) (400156)	Jharkhand	02/2020 (02/2020)	03/2028 (-)	5136.15 (5136.15)	1168.11	42
56	RAJRAPPA RCE OCP (Ministry of Coal) (400160)	Jharkhand	12/2009 (12/2009)	03/2016 (03/2027)	510.85 (510.85)	488.69	76
57	CHITRA EAST OC (Eastern Coal Fields Limited [ECL]) (400172)	Jharkhand	08/2018 (08/2018)	03/2026 (03/2028)	513.99 (513.99)	229.86	51
58	JHARKHAND-LAIYO OCP (Ministry of Coal) (400352)	Jharkhand	08/2020 (08/2020)	03/2031 (-)	764.57 (764.57)	145.81	29
59	MOONIDIH XV SEAM UG (Ministry of Coal) (400425)	Jharkhand	08/2011 (08/2011)	03/2019 (05/2026)	1230.27 (1230.27)	631.73	81
60	2.5 MTPA PATHERDIH NLW WASHERY (Ministry of Coal) (611017)	Jharkhand	10/2015 (04/2016)	04/2018 (03/2026)	334.27 (334.27)	142.64	48
61	AMALAGAMATED NTST KUJAMA OCP 8.5MTY (Ministry of Coal) (611864)	Jharkhand	01/2023 (01/2023)	03/2030 (-)	4011.85 (4011.85)	404.49	28
62	MURAI DIH UG PROJECT (Ministry of Coal) (613808)	Jharkhand	02/2011 (02/2011)	04/2014 (12/2026)	339.87 (339.87)	191	70
63	TAPIN SOUTH EXPN (Ministry of Coal) (615349)	Jharkhand	11/2020 (11/2020)	03/2028 (-)	230.41 (230.41)	22.02	20
64	SIRKA OC (Ministry of Coal) (615822)	Jharkhand	05/2020 (05/2020)	03/2028 (-)	222.82 (222.82)	140.58	53
65	TETARIAKHAR OC (Ministry of Coal) (615843)	Jharkhand	11/2019 (11/2019)	03/2025 (03/2027)	243.52 (243.52)	44.64	29
66	CHUPERBHITA SIMLONG OCP MDO 6 (Eastern Coal Fields Limited [ECL]) (616225)	Jharkhand	12/2023 (12/2023)	03/2037 (-)	979.08 (979.08)	0	0
67	JARANGDIH EXPN. OCP 1.5 MTY (CCL - CIL) (616236)	Jharkhand	02/2020 (02/2020)	03/2029 (-)	414.37 (414.37)	85.6	32
68	BLOCK E OCP (Ministry of Coal) (616253)	Jharkhand	03/2024 (03/2024)	03/2029 (-)	5850.83 (5850.83)	20.32	3
69	Revised Jharia Master Plan for Dealing with Fire, Subsidence & Rehabilitation of affected families in Jharia Coalfield- Reg. (Bharat Coking Coal Limited [BCCL]) (617416)	Jharkhand	06/2025 (07/2025)	12/2028 (-)	5940.47 (5940.47)	0	8
70	AMADAND OCP[4.0MTY] (Ministry of Coal) (400148)	Madhya Pradesh	03/2016 (03/2016)	03/2021 (03/2027)	869.44 (869.44)	275.35	75
71	RAMPUR BATURA OCP [4.0MTY] (South Eastern Coalfields Limited [SECL]) (400152)	Madhya Pradesh	07/2019 (07/2019)	03/2026 (-)	1248.93 (1248.93)	498.04	44
72	BLOCK B EXPANSION [3.5 TO 8.0 (Northern Coalfields Limited [NCL]) (400162)	Madhya Pradesh	07/2019 (07/2019)	03/2023 (03/2027)	998.71 (998.71)	470.87	47
73	NIGAH I EXPANSION [15 TO 25 MTP (Northern Coalfields Limited [NCL]) (400321)	Madhya Pradesh	11/2020 (11/2020)	03/2025 (03/2028)	1729.68 (1729.68)	833.62	48
74	KANCHAN OC EXP (South Eastern Coalfields Limited [SECL]) (613802)	Madhya Pradesh	12/2014 (12/2014)	03/2026 (-)	371.04 (371.04)	144.61	58
75	JHIRIA WEST OCP [1.5 MTY] (South Eastern Coalfields Limited [SECL]) (613803)	Madhya Pradesh	01/2024 (01/2024)	03/2029 (-)	366.94 (366.94)	34.07	41
76	RPR TAWA-III UG 0.84 MTY (Western Coalfields Limited [WCL]) (613804)	Madhya Pradesh	12/2021 (12/2021)	03/2027 (-)	314.09 (314.09)	6.84	17
77	AMALGAMATED DHANKASA & JAMUNIA (Western Coalfields Limited [WCL]) (615185)	Madhya Pradesh	09/2022 (09/2022)	03/2027 (-)	399.2 (399.2)	93.52	66
78	RPR OF VISHNUPURI UG TO OC (Western Coalfields Limited [WCL]) (615187)	Madhya Pradesh	11/2022 (11/2022)	03/2029 (-)	220.62 (220.62)	0	11
79	URDHAN EXPANSION OC COST PLUS (Western Coalfields Limited [WCL]) (615194)	Madhya Pradesh	07/2022 (01/2023)	03/2031 (-)	206.88 (206.88)	27.19	0
80	SHARDA UG MINE (Western Coalfields Limited [WCL]) (615195)	Madhya Pradesh	07/2022 (09/2023)	03/2028 (-)	166.25 (166.25)	5.08	9
81	GANDHIGRAM UG MINE (Western Coalfields Limited [WCL]) (615206)	Madhya Pradesh	08/2019 (08/2019)	03/2026 (-)	414.15 (414.15)	15.52	56
82	BHATADI EXPANSION OC (Western Coalfields Limited [WCL]) (400033)	Maharashtra	02/2020 (05/2022)	03/2028 (-)	580.61 (580.61)	73.77	28
83	AMALGAMATED YEKONA I & YEKONA (Western Coalfields Limited [WCL]) (400177)	Maharashtra	08/2015 (08/2015)	03/2025 (03/2026)	727.28 (727.28)	539.93	80
84	DINESH[MAKARDHOKRA-III] OC (Western Coalfields Limited [WCL]) (400178)	Maharashtra	02/2020 (02/2020)	03/2027 (-)	822.88 (822.88)	621.94	34
85	DHUPTALA OC [SASTI UG TO OC] (Western Coalfields Limited [WCL]) (400353)	Maharashtra	02/2019 (10/2021)	03/2028 (-)	711.01 (711.01)	169.11	19



All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
86	SAONER UG MINE -1 EXPANSION 1. (<i>Western Coalfields Limited [WCL]</i>) (615184)	Maharashtra	01/2022 (01/2022)	03/2028 (-)	228.64 (228.64)	143.37	68
87	SASTI EXPANSION OPENCAST (<i>Western Coalfields Limited [WCL]</i>) (615186)	Maharashtra	08/2020 (08/2020)	03/2026 (-)	319.04 (319.04)	91.48	20
88	NEW MAJRI UG TO OC 3 MTY COST (<i>Western Coalfields Limited [WCL]</i>) (615188)	Maharashtra	05/2019 (09/2022)	03/2027 (-)	402.27 (402.27)	60.03	24
89	MAKARDHOKRA EXPN OC 4.9 MTY (<i>Western Coalfields Limited [WCL]</i>) (615189)	Maharashtra	06/2022 (06/2022)	03/2026 (-)	361.87 (361.87)	76.32	11
90	SINGHORI DEEP OC MIN 2.0 MTY (<i>Western Coalfields Limited [WCL]</i>) (615190)	Maharashtra	05/2022 (05/2022)	03/2029 (-)	335.75 (335.75)	26.98	6
91	GOKUL EXTENSION OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615192)	Maharashtra	04/2021 (04/2021)	03/2026 (-)	309.58 (309.58)	43.88	8
92	KOLGAON EXPANSION DEEP OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615199)	Maharashtra	01/2023 (09/2023)	03/2027 (-)	198.71 (198.71)	0.76	2
93	BALLARPUR NORTH WEST OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615330)	Maharashtra	12/2022 (12/2022)	03/2029 (-)	360.81 (360.81)	0.02	4
94	GADEGAON OC 3 MTY (<i>Western Coalfields Limited [WCL]</i>) (615331)	Maharashtra	10/2023 (10/2023)	03/2030 (-)	497.41 (497.41)	0.08	0
95	GHONSA EXPANSION DEEP OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615914)	Maharashtra	03/2021 (03/2021)	03/2029 (-)	184.71 (184.71)	14.48	5
96	AMLG GAURI PAUNI EXPANSION OC (<i>Western Coalfields Limited [WCL]</i>) (615916)	Maharashtra	04/2024 (04/2024)	03/2030 (-)	1225.21 (1225.21)	79.73	2
97	GAURIDEEP/GAURI CENTRAL OCP 7. (<i>Western Coalfields Limited [WCL]</i>) (615917)	Maharashtra	08/2023 (06/2024)	03/2030 (-)	973.07 (973.07)	0.24	0
98	RPR OF BHANEGAON OC (<i>Western Coalfields Limited [WCL]</i>) (615918)	Maharashtra	02/2017 (09/2022)	03/2028 (-)	405.2 (405.2)	12.39	7
99	N. EXTN. MUNGOLI NIRGUDA D OCP (<i>Western Coalfields Limited [WCL]</i>) (615919)	Maharashtra	06/2024 (06/2024)	03/2029 (-)	1024.91 (1024.91)	170.94	0
100	NILJAI EXPANSION DEEP OCP (<i>Western Coalfields Limited [WCL]</i>) (615982)	Maharashtra	08/2016 (11/2018)	03/2024 (03/2026)	319.75 (319.75)	367.6	79
101	UKNI DEEP OC MINE -COST PLUS (<i>Western Coalfields Limited [WCL]</i>) (616044)	Maharashtra	11/2018 (01/2019)	03/2021 (03/2026)	237.06 (237.06)	165.57	87
102	AMALGAMATED INDER-KAMPTEE DEEP OC (<i>Western Coalfields Limited [WCL]</i>) (616050)	Maharashtra	09/2018 (09/2018)	03/2024 (03/2026)	235.9 (235.9)	237.12	98
103	ADASA UG TO OC MINE (<i>Western Coalfields Limited [WCL]</i>) (616223)	Maharashtra	11/2018 (11/2018)	03/2024 (03/2026)	316 (316)	308.84	86
104	AMAL GONDEGAON GHATROHANA EXPN (<i>Western Coalfields Limited [WCL]</i>) (616229)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	668.54 (668.54)	1.18	0
105	WAGHODA UG MINE [1.02 MTY] (<i>Western Coalfields Limited [WCL]</i>) (617233)	Maharashtra	01/2024 (01/2025)	03/2030 (-)	379.3 (379.3)	0	0
106	KOLARPIMPRI EXPANSION OC [2.5 (<i>Western Coalfields Limited [WCL]</i>) (617278)	Maharashtra	06/2024 (02/2025)	03/2030 (-)	630.37 (630.37)	0	0
107	Master Plan for Jharia and Raniganj Coalfields (<i>Bharat Coking Coal Limited [BCLL]</i>) (400313)	Multi-States (Jharkhand, West Bengal)	08/2009 (08/2009)	08/2019 (12/2028)	2661.73 (2661.73)	791.42	43
108	BINA KAKRI AMALGAMATION EXPANS (<i>Northern Coalfields Limited [NCL]</i>) (400369)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020 (08/2020)	03/2024 (03/2027)	836.42 (836.42)	809.2	89
109	KHADIA EXPANSION [10 TO 16 MTP (<i>Northern Coalfields Limited [NCL]</i>) (615183)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021 (06/2021)	03/2025 (03/2027)	491.67 (491.67)	243.56	47
110	SUBHADRA OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400165)	Odisha	05/2021 (05/2021)	04/2032 (-)	1693.81 (1693.81)	1323.62	42
111	SIARMAL OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400166)	Odisha	02/2021 (02/2021)	03/2029 (-)	5194.95 (5194.95)	3456.93	55
112	BALARAM EXPANSION OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400183)	Odisha	06/2020 (08/2020)	03/2029 (-)	3504.21 (3504.21)	922.92	53
113	GOPALJI KANIHA OCP [10 TO 30 M (<i>MCL - CIL</i>) (400185)	Odisha	04/2022 (04/2022)	03/2030 (-)	8416.19 (6107.87)	1734.86	17
114	INTEGRATED LAKHANPUR-BELPAHAR- (<i>Mahanadi Coalfields Limited [MCL]</i>) (400187)	Odisha	05/2018 (05/2018)	03/2027 (-)	2434.75 (2434.75)	1834.91	69
115	BHARATPUR RE-ORGANIZATION OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400392)	Odisha	11/2018 (11/2018)	03/2029 (-)	2838.86 (2838.86)	1673.49	47
116	BASUNDHARA WEST EXTENSION OPEN (<i>MCL - CIL</i>) (615193)	Odisha	05/2014 (05/2014)	03/2019 (03/2029)	479.15 (479.15)	274.52	64

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
117	Naini Coal Mine (Singareni Collieries Company Limited [SCCL]) (615857)	Odisha	03/2020 (03/2020)	03/2026 (-)	494.3 (494.3)	491.33	80
118	INTEGRATED KULDA GARJANBAHAL O (Mahanadi Coalfields Limited [MCL]) (616226)	Odisha	04/2023 (04/2023)	03/2033 (-)	3563.5 (3563.5)	568.97	3
119	BHUBANESWARI EXPN OCP 50 MTY (MCL - CIL) (616231)	Odisha	03/2024 (03/2024)	03/2033 (-)	5366.27 (5366.27)	466.28	14
120	HINGULA II OC EXPN PH III 15 M (MCL - CIL) (616232)	Odisha	11/2022 (11/2022)	03/2029 (-)	1561.85 (1561.85)	273.03	24
121	BALABHADRA OCP (MCL - CIL) (616233)	Odisha	04/2023 (04/2023)	03/2030 (-)	978.44 (978.44)	212.94	11
122	Jawahar Khani Open Cast Mine (Singareni Collieries Company Limited [SCCL]) (615818)	Telangana	12/2021 (12/2021)	03/2025 (03/2027)	297.88 (297.88)	46.83	20
123	Kalyanikhani Opencast Project (Singareni Collieries Company Limited [SCCL]) (615858)	Telangana	03/2016 (05/2017)	03/2026 (-)	384.32 (384.32)	283.94	75
124	Kakathiya Khani Opencast - III Project Phase - I (Singareni Collieries Company Limited [SCCL]) (615859)	Telangana	03/2017 (05/2017)	03/2026 (-)	413.84 (413.84)	397.55	79
125	Godavarikhani Coal Mine - 5 (Singareni Collieries Company Limited [SCCL]) (615860)	Telangana	07/2019 (05/2019)	03/2025 (03/2026)	607.04 (607.04)	191.37	71
126	Indaram Opencast Project (Singareni Collieries Company Limited [SCCL]) (615861)	Telangana	08/2017 (12/2022)	03/2025 (03/2026)	424.81 (424.81)	404.96	80
127	Goleti Opencast Mine (Singareni Collieries Company Limited [SCCL]) (615862)	Telangana	07/2021 (08/2021)	03/2026 (-)	345.6 (345.6)	76.19	21
128	Venkatesh Khani Coal Mine (Singareni Collieries Company Limited [SCCL]) (615863)	Telangana	10/2020 (06/2020)	03/2026 (-)	484.5 (484.5)	477.14	97
129	Ramagundam OC-II Extension Project (Singareni Collieries Company Limited [SCCL]) (615864)	Telangana	11/2015 (06/2015)	03/2026 (-)	489.62 (489.62)	405.54	77
130	Kakatiyakhani OC - 2 Project (Singareni Collieries Company Limited [SCCL]) (615865)	Telangana	08/2017 (09/2017)	03/2025 (03/2026)	442.42 (442.42)	230.28	63
131	MOHANPUR EXPANSION OC -PHASE I (Eastern Coal Fields Limited [ECL]) (400173)	West Bengal	11/2020 (11/2020)	03/2026 (03/2030)	888.99 (888.99)	115.8	30
132	BONJEMEHARI EXPANSION OCP (Eastern Coal Fields Limited [ECL]) (400180)	West Bengal	08/2021 (08/2021)	03/2026 (03/2030)	570.11 (570.11)	82.25	16
133	NAKRAKONDA KUMARDIH- B OCP (Eastern Coal Fields Limited [ECL]) (400181)	West Bengal	08/2018 (08/2018)	03/2029 (-)	502.68 (502.67)	71.11	26
134	SIDULI [OC & UG] (ECL - CIL) (400182)	West Bengal	05/2018 (05/2018)	03/2027 (03/2030)	535.18 (535.17)	5.28	14
135	TILABONI UG (Eastern Coal Fields Limited [ECL]) (400186)	West Bengal	01/2023 (01/2023)	03/2029 (-)	749.08 (749.07)	52.55	10
136	JHANJRA EXPANSION UG (Eastern Coal Fields Limited [ECL]) (400312)	West Bengal	04/2020 (04/2020)	03/2029 (-)	1210.12 (1210.12)	537.77	44
137	SONEPUR BAZARI EXPANSION OCP [(Eastern Coal Fields Limited [ECL]) (400315)	West Bengal	07/2021 (07/2021)	03/2029 (-)	5365.88 (5365.88)	583.82	17
138	2.0 MTPA BHOJUDIH NLW WASHERY (Ministry of Coal) (611016)	West Bengal	12/2015 (03/2019)	09/2020 (12/2025)	384.57 (384.57)	354.75	97
139	ITAPARA OCP (Eastern Coal Fields Limited [ECL]) (612816)	West Bengal	12/2023 (12/2023)	03/2030 (-)	929.1 (929.1)	68.9	7
140	SHYAMSUNDARPUR UG INCLUDING SA (Eastern Coal Fields Limited [ECL]) (613793)	West Bengal	04/2020 (04/2020)	03/2026 (03/2028)	483.65 (483.65)	60.46	12
141	PARASEA-BELBAID UG PROJECT (Eastern Coal Fields Limited [ECL]) (613794)	West Bengal	01/2023 (01/2023)	03/2028 (-)	389.1 (389.1)	132.48	21
142	PARASCOLE JAMBAD OCP (Eastern Coal Fields Limited [ECL]) (616230)	West Bengal	11/2024 (11/2024)	03/2037 (-)	1193.55 (1193.55)	9.53	0
Total (116)					157554.96	48288.11	
Electricity Generation							
143	50 MW Wind Power Project (NLC India Limited [NLCIL]) (617299)	Gujarat	07/2022 (01/2024)	06/2025 (01/2026)	383.84 (383.84)	314.83	45
144	600 MW Khavda Solar Power Project (NLC India Limited [NLCIL]) (617730)	Gujarat	08/2023 (06/2024)	06/2026 (-)	3335.85 (3335.85)	666.65	17
145	NLC Talabira Thermal Power Project (NLC India Limited [NLCIL]) (400231)	Odisha	01/2017 (01/2024)	03/2030 (-)	27212.96 (27213)	2549.31	1
146	300 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (612819)	Rajasthan	07/2022 (03/2023)	09/2024 (12/2025)	1813 (1813)	1167.4	85

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
147	50 MW Solar PP Minedout Area (NLC India Limited [NLCIL]) (615327)	Tamil Nadu	08/2023 (02/2024)	03/2025 (12/2025)	218.03 (218.03)	164.7	69
148	Ghatampur Thermal Power Plant 3 X 660 MW (NLC India Limited [NLCIL]) (400259)	Uttar Pradesh	07/2016 (02/2016)	11/2020 (12/2025)	17237.8 (21780.9)	20522.3	93
Total (6)					50201.48	25385.19	
Railways							
149	Dharamjaigarh-Korba (Railway) (400203)	Chhattisgarh	05/2018 (03/2017)	12/2026 (08/2026)	1686.22 (1686.22)	353.12	42
150	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] (Ministry of Coal) (400416)	Jharkhand	02/2018 (05/2022)	06/2025 (06/2026)	1799.64 (2564.34)	1462.35	61
Total (2)					3485.86	1815.47	
Ministry of Power							
Coal							
151	Tubed Coal Mine (Damodar Valley Corporation) (400192)	Jharkhand	07/2016 (10/2016)	05/2026 (05/2026)	1581 (1581)	598.06	35
152	Badam Coal Mining project of NTPC (National Thermal Power Corporation [NTPC]) (603293)	Jharkhand	02/2019 (09/2019)	12/2056 (04/2027)	502 (784)	313.88	59
Total (2)					2083	911.94	
Electricity Generation							
153	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3708.61	16
154	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	64.36	3
155	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	116.08	2
156	Buxar Thermal Power Project [1320 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602579)	Bihar	03/2019 (06/2019)	01/2024 (12/2025)	10439.09 (13756.6)	12571.15	92
157	Lara Super Thermal Power Project Stage-II [2 x 800 MW] (National Thermal Power Corporation [NTPC]) (611930)	Chhattisgarh	08/2023 (08/2023)	06/2028 (-)	15530 (15530)	2874	18
158	Sipat Super Thermal Power Project, Stage-III [1x800 MW] (National Thermal Power Corporation [NTPC]) (617188)	Chhattisgarh	09/2024 (09/2024)	09/2029 (-)	9791 (9791)	856.56	8
159	Bagodara Solar Power Project (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709747)	Gujarat	03/2021 (05/2021)	12/2025 (12/2025)	339.35 (339.35)	317.59	51
160	Dhaulasidh Hydro Electric Project [66 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602582)	Himachal Pradesh	10/2020 (05/2021)	11/2025 (03/2027)	687.97 (1561.21)	986.12	70
161	Luhri Stage-I Hydro Electric Project [210 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602593)	Himachal Pradesh	11/2020 (11/2020)	01/2026 (10/2029)	1810.56 (3584.53)	1793.11	51
162	382 MW Sunni Dam HEP (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602633)	Himachal Pradesh	NA (04/2018)	03/2027 (-)	2615 (2615)	495.57	0.5
163	Sunni Dam Hydro Electric Project [382 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (611586)	Himachal Pradesh	01/2023 (01/2023)	04/2028 (12/2029)	2614.51 (4540.71)	1011.42	30
164	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW (National Hydroelectric Power Corporation Limited [NHPC]) (602525)	Jammu and Kashmir	10/2014 (02/2018)	04/2020 (12/2026)	8112.12 (12728)	7581.19	74
165	Kiru HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (602532)	Jammu and Kashmir	03/2019 (02/2020)	09/2023 (12/2026)	4287.59 (5409)	3116.72	72
166	Rattle HE Project - 850 MW, Rattle Hydroelectric Power Corporation Limited. (National Hydroelectric Power Corporation Limited [NHPC]) (602535)	Jammu and Kashmir	02/2021 (01/2022)	02/2026 (11/2028)	5281.94 (5281.94)	1112.08	25
167	Kwar HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (605155)	Jammu and Kashmir	05/2022 (11/2022)	11/2026 (03/2028)	4526.12 (4526.12)	1094.54	24
168	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] (National Thermal Power Corporation [NTPC]) (400261)	Jharkhand	07/2017 (11/2017)	03/2023 (11/2026)	17112 (20302)	17861.4	85
169	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand (Damodar Valley Corporation) (611509)	Jharkhand	04/2023 (11/2024)	03/2029 (-)	14358 (14358)	1381.54	3
170	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	25244.57	97
171	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion (National Thermal Power Corporation [NTPC]) (602961)	Odisha	08/2022 (09/2022)	05/2027 (03/2028)	11843.75 (12543)	4839.68	40
172	BIKANER SOLAR POWER PROJECT (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709748)	Rajasthan	10/2021 (05/2022)	04/2024 (12/2025)	5491.89 (5491.89)	5084.68	88
173	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	3817.49	70

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
174	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] -A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (12/2025)	938.29 (1828.11)	1455.57	93
175	Khurja super Thermal Power Plant [2X660 MW] (THDC India Limited) (602194)	Uttar Pradesh	03/2019 (08/2019)	02/2024 (09/2025)	11089.42 (13276.2)	12888.23	100
176	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] (National Thermal Power Corporation [NTPC]) (612142)	Uttar Pradesh	03/2024 (03/2024)	02/2030 (-)	17195 (17195)	1979	11
177	Tapovan-Vishnugad HEP [4x130 MW] (National Thermal Power Corporation [NTPC]) (602185)	Uttarakhand	NA (11/2006)	03/2013 (04/2029)	2978 (10907.3)	6769.58	77
178	Tehri Pumped Storage Plant Project [4x250 MW] (THDC India Limited) (602193)	Uttarakhand	07/2006 (06/2011)	06/2022 (12/2025)	4825.6 (8339)	8149.63	98
179	Vishnugad Pipalkoti Hydro Electric Project [444 MW] (THDC India Limited) (602195)	Uttarakhand	08/2008 (01/2014)	12/2022 (03/2027)	3860.35 (6823.72)	5245.01	73
180	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal (Damodar Valley Corporation) (400062)	West Bengal	01/2023 (02/2025)	06/2029 (-)	17673 (17673)	1408.8	2
181	Rammam-III HEPP [3x40 MW] (National Thermal Power Corporation [NTPC]) (602184)	West Bengal	10/2014 (09/2014)	09/2019 (03/2029)	1381.84 (1381.84)	1382.42	47
182	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 (Damodar Valley Corporation) (602538)	West Bengal	06/2019 (02/2021)	01/2024 (12/2025)	1037 (1037)	929.99	67
	Total (30)				223418.07	136136.69	
Transmission & Distribution							
183	Transmission Scheme for Solar Energy Zone in Ananthpuram 2500MW and Kurnool 1000MW (Power Grid Corporation of India Limited [POWERGRID]) (611967)	Andhra Pradesh	09/2023 (09/2023)	09/2025 (03/2026)	1248.69 (1248.69)	998.95	87
184	Augmentation of 1x1500 MVA 3rd 765/400 kV transformation capacity at Kurnool New Substation (Power Grid Corporation of India Limited [POWERGRID]) (612856)	Andhra Pradesh	05/2023 (12/2023)	09/2025 (01/2026)	163.61 (163.61)	85.07	62
185	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617183)	Andhra Pradesh	03/2025 (03/2025)	12/2027 (-)	2886 (2886)	131.31	1
186	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	0.03	0
187	Western Region Expansion Scheme-XXV (Power Grid Corporation of India Limited [POWERGRID]) (611737)	Chhattisgarh	02/2023 (02/2023)	11/2023 (10/2025)	385.84 (385.84)	382.4	100
188	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan 8.1 GW under Phase II- Part- G1 (Power Grid Corporation of India Limited [POWERGRID]) (608301)	Delhi	02/2022 (02/2022)	09/2023 (12/2025)	359.47 (359.47)	341.49	97
189	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part B (Power Grid Corporation of India Limited [POWERGRID]) (611656)	Gujarat	03/2023 (03/2023)	03/2025 (11/2025)	1167.55 (1167)	1147.74	97
190	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part C (Power Grid Corporation of India Limited [POWERGRID]) (611657)	Gujarat	03/2023 (03/2023)	03/2025 (12/2025)	2820.99 (2820.99)	2736.36	93
191	Establishment of Khavda Pooling Station-2 KPS2 in Khavda RE Park KPS2 TRANSMISSION SYSTEM LIMITED (Power Grid Corporation of India Limited [POWERGRID]) (611660)	Gujarat	03/2023 (03/2023)	12/2024 (11/2025)	966.79 (966.79)	936.24	97
192	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (612139)	Gujarat	12/2023 (12/2023)	12/2025 (12/2026)	3751.82 (3751.82)	1688.32	28
193	Transmission System for Evacuation of Power from potential Renewable Energy zone in Khavda Area of Gujarat under Phase IV [7 GW] Part E3 (Power Grid Corporation of India Limited [POWERGRID]) (612151)	Gujarat	07/2023 (07/2023)	07/2025 (03/2026)	334 (334)	118.1	36
194	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (612855)	Gujarat	05/2024 (05/2024)	05/2026 (06/2026)	679 (679)	135.8	27
195	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615342)	Gujarat	10/2024 (10/2024)	07/2026 (-)	329 (329)	13.17	3
196	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] (Power Grid Corporation of India Limited [POWERGRID]) (615343)	Gujarat	11/2024 (11/2024)	11/2026 (-)	501 (501)	8.11	2
197	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345)	Gujarat	10/2024 (10/2024)	10/2026 (03/2027)	4766 (4766)	714.9	9
198	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069)	Gujarat	02/2025 (02/2025)	02/2027 (-)	466 (466)	24.3	2

All Ongoing Projects						OCTOBER 2025	
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
199	Augmentation of Banaskantha [Raghanesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182)	Gujarat	03/2025 (03/2025)	03/2027 (-)	172 (172)	17.27	15
200	Augmentation of Transformation Capacity at Bhuj-II PS [GIS] (Power Grid Corporation of India Limited [POWERGRID]) (617391)	Gujarat	02/2025 (02/2025)	11/2026 (03/2027)	488.29 (488.29)	0.12	0
201	Jamnagar Transmission Limited (Adani Transmission Limited) (617405)	Gujarat	NA (10/2024)	10/2026 (-)	4000 (4000)	0	0
202	Provision of ICT Augmentation & Bus Reactor at Bhuj-II PS (Power Grid Corporation of India Limited [POWERGRID]) (617801)	Gujarat	03/2025 (03/2025)	12/2026 (03/2027)	581.74 (581.74)	0.2	0
203	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272)	Haryana	06/2024 (06/2024)	12/2026 (-)	370 (370)	18.55	6
204	Transmission system for evacuation of Power from Pakaldul HEP in Chenab Valley HEPs - LTA System (Power Grid Corporation of India Limited [POWERGRID]) (608302)	Jammu and Kashmir	02/2022 (02/2022)	04/2025 (11/2025)	318.12 (318.12)	317.12	100
205	Transmission Scheme for evacuation of Power from Ratle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179)	Jammu and Kashmir	07/2024 (07/2024)	07/2026 (03/2027)	218.6 (218.6)	2.11	0
206	Implementation of Transmission Systems in the State of Jharkhand consisting of 400/220/132/33 kV transmission lines and substations under Jharkhand Consultancy Project (Power Grid Corporation of India Limited [POWERGRID]) (617326)	Jharkhand	02/2012 (02/2012)	03/2026 (-)	1842.25 (1842.25)	1648.05	95
207	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140)	Karnataka	12/2023 (12/2023)	12/2025 (06/2026)	2889.39 (2889.39)	1533.89	54
208	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672)	Karnataka	01/2025 (01/2025)	06/2027 (-)	1354 (1354)	40.62	1
209	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068)	Karnataka	02/2025 (02/2025)	06/2027 (-)	288 (288)	6.91	1
210	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184)	Karnataka	03/2025 (03/2025)	09/2027 (-)	3453 (3453)	52.48	1
211	Transmission System Strengthening at Davanagere for Integration of RE Generation [SPV Name - POWERGRID Davanagere Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617803)	Karnataka	09/2025 (09/2025)	09/2027 (-)	379 (379)	6.6	0
212	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344)	Madhya Pradesh	10/2024 (10/2024)	10/2026 (03/2027)	3674 (3674)	624.58	17
213	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346)	Madhya Pradesh	08/2024 (08/2024)	08/2026 (12/2026)	2708 (2708)	1029.04	41
214	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279)	Madhya Pradesh	06/2025 (06/2025)	12/2027 (-)	558 (558)	33.48	1
215	Augmentation of Transformation Capacity and Implementation of Line Bays at Mandsaur S/S for RE Interconnection [SPV Name- POWERGRID Mandsaur I RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617802)	Madhya Pradesh	10/2025 (10/2025)	03/2028 (-)	319 (319)	0.1	0
216	Transmission System for Evacuation of power from Potential RE Zone in Khavda Area of Gujarat under phase IV 7GW-Part E4 (Power Grid Corporation of India Limited [POWERGRID]) (611966)	Maharashtra	11/2023 (11/2023)	07/2025 (03/2026)	224.41 (224.41)	33.66	18
217	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185)	Multi-States (Andhra Pradesh, Karnataka)	03/2025 (03/2025)	03/2027 (-)	5550 (5550)	332.68	1
218	Transmission System for Kurnool Wind Energy Zone/ Solar Energy Zone Part-A and Part-B (Power Grid Corporation of India Limited [POWERGRID]) (900808)	Multi-States (Andhra Pradesh, Telangana)	11/2022 (03/2023)	11/2024 (01/2026)	3546.94 (3546.94)	3369.59	97
219	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	7705.14	82
220	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (03/2026)	5111.33 (6700)	5317.79	96
221	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271)	Multi-States (Bihar, Odisha, West Bengal)	09/2024 (09/2024)	03/2026 (06/2026)	342.69 (342.69)	0.71	0

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
222	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270)	Multi-States (Bihar, West Bengal)	11/2024 (11/2024)	05/2026 (03/2027)	408.94 (408.94)	0.32	0
223	Transmission Network Expansion in Gujarat to increase its ATC from ISTS Part B (Power Grid Corporation of India Limited [POWERGRID]) (400005)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	01/2022 (07/2022)	06/2023 (12/2025)	4546.26 (4546.26)	4210.3	93
224	Transmission System Strengthening Scheme for evacuation of power from SEZ in Rajasthan 8.1 GW under Phase II Part G (Power Grid Corporation of India Limited [POWERGRID]) (608922)	Multi-States (Delhi, Haryana, Rajasthan)	05/2022 (05/2022)	11/2023 (11/2025)	1666 (2218)	2129.28	96
225	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735)	Multi-States (Delhi, Rajasthan)	12/2022 (12/2022)	03/2025 (07/2026)	331 (331)	135.71	31
226	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132)	Multi-States (Delhi, Rajasthan)	02/2024 (02/2024)	08/2025 (06/2026)	2000 (2000)	1460	68
227	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347)	Multi-States (Gujarat, Maharashtra)	11/2024 (11/2024)	05/2029 (-)	24819 (24819)	1985.46	2
228	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5969 (5969)	485.87	9
229	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Siwani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340)	Multi-States (Haryana, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5357 (5357)	428.56	13
230	Transmission System for Strengthening of Srinagar-Leh Tr. System (Power Grid Corporation of India Limited [POWERGRID]) (606781)	Multi-States (Jammu and Kashmir, Ladakh)	03/2022 (03/2022)	12/2024 (11/2025)	288.71 (288.71)	280.02	99
231	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138)	Multi-States (Karnataka, Telangana)	02/2024 (02/2024)	02/2026 (06/2026)	2147.62 (2147.62)	1438.9	67
232	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (-)	2227 (2227)	779.45	23
233	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (03/2027)	3251 (3251)	942.79	26
234	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [Rajasthan V Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025 (03/2025)	03/2027 (-)	5028 (5028)	256.93	2
235	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023 (12/2023)	12/2025 (06/2026)	2056 (2056)	1603.68	62
236	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024 (12/2024)	12/2026 (03/2027)	5846 (5846)	467.68	9
237	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan[8.1 GW] under phase-II- Part E (Power Grid Corporation of India Limited [POWERGRID]) (611659)	Rajasthan	03/2023 (03/2023)	09/2024 (11/2025)	1433.28 (1433)	1418.67	98
238	Transmission System for Evacuation of Power from REZ in Rajasthan 20GW under Phase III- Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (611947)	Rajasthan	11/2023 (11/2023)	06/2025 (03/2026)	428.3 (428.3)	291.24	73
239	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part H (Power Grid Corporation of India Limited [POWERGRID]) (611948)	Rajasthan	10/2023 (10/2023)	04/2025 (01/2026)	2211.29 (2211.29)	1945.93	88
240	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949)	Rajasthan	10/2023 (10/2023)	04/2025 (03/2026)	1796.02 (1796.02)	1436.81	89
241	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part B1 (Power Grid Corporation of India Limited [POWERGRID]) (611950)	Rajasthan	09/2023 (09/2023)	04/2025 (12/2025)	2190.54 (2190.54)	1949.58	91
242	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part E1 (Power Grid Corporation of India Limited [POWERGRID]) (611951)	Rajasthan	12/2021 (08/2023)	02/2025 (12/2025)	688.74 (688.74)	654.3	97
243	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134)	Rajasthan	12/2023 (12/2023)	12/2025 (06/2026)	2998.34 (2998.34)	2008.88	57
244	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332)	Rajasthan	08/2024 (08/2024)	08/2026 (12/2026)	3279 (3279)	918.12	26

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
245	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (615335)	Rajasthan	08/2024 (08/2024)	08/2026 (12/2026)	1382 (1382)	138.2	9
246	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (615337)	Rajasthan	08/2024 (08/2024)	02/2026 (03/2026)	369 (369)	103.32	22
247	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (615338)	Rajasthan	11/2024 (11/2024)	11/2026 (06/2027)	2735 (2735)	324.64	11
248	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (617181)	Rajasthan	03/2025 (03/2025)	12/2026 (03/2027)	404 (404)	16.16	1
249	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Tarnsmission Limited] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (616671)	Tamil Nadu	01/2025 (01/2025)	12/2026 (12/2026)	548 (548)	37.86	9
250	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (617269)	Uttar Pradesh	12/2024 (12/2024)	06/2026 (08/2026)	212.81 (212.81)	2.1	0
Total (68)					150796.17	59403.74	
Ministry of Housing & Urban Affairs							
Construction							
251	C/o 184 MS Flats for Hon'ble MPs at BKS Marg, New Delhi <i>(Central Public Works Department [CPWD])</i> (617282)	Delhi	01/2022 (05/2022)	05/2025 (09/2025)	646.53 (646.52)	545.86	100
252	Construction of One Tower of Office Complex and another Tower of Residential quarters consisting of 10Nos. Type-V, 10Nos. Type-VI & 1No.Type-VII Quarters i/c internal water supply, sanitary installation and all development and bulk services, Horticulture works on EPC Mode-I basis i/c comprehensive operation and maintenance of Civil, E&M services for 7 years after completion of original construction work for Ranga Reddy, Secunderabad, Medchal, Auditl, Audit-II Commissionerates of Central Tax at Khajaguda, Serilingampally, Hyderabad. <i>(Central Public Works Department - CPWD)</i> (617412)	Telangana	03/2024 (11/2024)	09/2027 (-)	644 (644)	87.6	6
Total (2)					1290.53	633.46	
Inland Waterways							
253	Chennai Metro Rail Phase-II Development Project <i>(Chennai Metro Rail Limited [CMRL])</i> (702668)	Tamil Nadu	10/2024 (11/2020)	08/2029 (-)	63246 (63246)	28778.98	47
Total (1)					63246	28778.98	
Real Estate							
254	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System <i>(ministry of housing and urban affairs)</i> (707229)	Andaman & Nicobar	07/2021 (11/2021)	05/2023 (-)	209.88 (209.88)	0	70
255	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi <i>(National Buildings Construction Corporation [NBCC])</i> (400188)	Delhi	07/2016 (05/2018)	12/2025 (12/2025)	32850 (32850)	0	0
256	Rehabilitation in Junavadaj Area Smart City Project <i>(ministry of housing and urban affairs)</i> (701719)	Gujarat	02/2016 (06/2016)	07/2022 (-)	539 (539)	39.63	50
257	Green Building Development Project <i>(ministry of housing and urban affairs)</i> (701766)	Uttarakhand	11/2019 (08/2019)	11/2023 (-)	150.97 (150.97)	18.95	31
Total (4)					33749.85	58.58	
Urban Public Transport							
258	Patna Metro Rail Project <i>(Patna Metro Rail Corporation Ltd. [PMRCL])</i> (702627)	Bihar	02/2019 (02/2019)	02/2024 (06/2027)	13365.77 (13365.8)	4039.77	46
259	Delhi Metro Rail Phase-IV [2 Corridors] <i>(Delhi Metro Rail Corporation Limited [DMRC])</i> (617207)	Delhi	03/2024 (03/2024)	03/2029 (-)	8399.81 (8399.81)	55.92	0
260	DMRTS Phase - IV [3 Priority Corridors] <i>(Delhi Metro Rail Corporation Limited [DMRC])</i> (702632)	Delhi	07/2019 (07/2019)	03/2025 (03/2026)	24948.65 (24948.7)	17838.17	71
261	Surat Metro Rail Project <i>(Gujarat Metro Rail Corporation Limited [GMRCL])</i> (702630)	Gujarat	03/2019 (04/2019)	03/2024 (06/2026)	12020.32 (12020.3)	7977.03	72
262	Ahmedabad Metro Rail Project, Phase-II <i>(Gujarat Metro Rail Corporation Limited [GMRCL])</i> (702631)	Gujarat	03/2019 (03/2019)	03/2024 (12/2025)	5384.17 (5384.17)	4308.13	91
263	Ahmedabad Metro Rail Project [Phase-I] <i>(Gujarat Metro Rail Corporation Limited [GMRCL])</i> (702639)	Gujarat	11/2014 (02/2015)	03/2018 (10/2025)	10773 (12924.5)	12212.92	99
264	Construction of Bangalore Metro Rail Project Phase 2. <i>(Bengaluru Metro Rail)</i> (702635)	Karnataka	02/2014 (02/2016)	03/2021 (09/2026)	26405.14 (30695.1)	29617.97	94
265	Construction Bangalore Metro Rail Project Phase-2A & 2B <i>(Bengaluru Metro Rail)</i> (702665)	Karnataka	06/2021 (01/2019)	06/2026 (06/2026)	14788.1 (14788.1)	8915.63	57
266	Kochi Metro Rail Phase 2 Development Project <i>(CSPCC Projects)</i> (702664)	Kerala	11/2022 (11/2022)	11/2026 (11/2026)	1957.05 (1957.05)	425.58	19



All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
267	Bhopal Metro Rail Project (<i>Madhya Pradesh Metro Rail Co Limited [MPMRCL]</i>) (702625)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (06/2028)	6941.4 (6941.4)	3676.19	47
268	Indore Metro Rail Project (<i>Madhya Pradesh Metro Rail Co Limited [MPMRCL]</i>) (702626)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (12/2028)	7500.8 (7500.8)	4223.43	57
269	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 (<i>Maharashtra Metro Rail Corporation Limited [MMRCL]</i>) (617225)	Maharashtra	10/2023 (10/2023)	01/2027 (-)	910.18 (910.18)	147.84	26
270	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj (<i>Maharashtra Metro Rail Corporation Limited [MMRCL]</i>) (617226)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	2954.53 (2954.53)	22.17	3
271	Thane Integral Ring Metro Rail Project (<i>Maharashtra Metro Rail Corporation Limited [MMRCL]</i>) (617327)	Maharashtra	09/2024 (09/2024)	09/2029 (-)	12200.1 (12200.1)	7.77	3
272	New Suburba Station Development Project (<i>ministry of housing and urban affairs</i>) (701745)	Maharashtra	04/2018 (03/2019)	07/2022 (-)	262.76 (262.76)	17.62	6
273	Kalyan Station Precinct Imporvement Project (<i>ministry of housing and urban affairs</i>) (701991)	Maharashtra	04/2018 (07/2020)	07/2023 (-)	600 (600)	272.42	70
274	Mumbai Metro Line 3 (<i>Mumbai Metro Rail Corporation Limited [MMRC]</i>) (702637)	Maharashtra	07/2013 (06/2016)	03/2023 (08/2025)	23136 (37276)	31783.93	96
275	Nagpur Metro Rail Phase II Development Project (<i>Maharashtra Metro Rail Corporation Limited [MMRCL]</i>) (702658)	Maharashtra	12/2022 (12/2022)	12/2027 (-)	6708 (6708)	1259.29	28
276	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] (<i>Delhi Metro Rail Corporation Limited [DMRC]</i>) (617206)	Multi-States (Delhi, Haryana)	01/2025 (01/2025)	01/2029 (-)	6230.99 (6230.99)	72.38	0
277	Delhi-Ghaziabad-Meerut Regional Rapid Transit System [RRTS] corridor (<i>National Capital Region Transport Corporation [NCRTC]</i>) (702633)	Multi-States (Delhi, Uttar Pradesh)	03/2019 (03/2019)	06/2025 (10/2025)	30274 (30274)	26612.45	95
278	Kanpur Metro Rail Project (<i>Uttar Pradesh metro rail corporation [UPMRC]</i>) (702628)	Uttar Pradesh	05/2019 (11/2019)	05/2024 (03/2027)	11076.48 (11076.5)	9093.83	76
279	Agra Metro Rail Project (<i>Uttar Pradesh metro rail corporation [UPMRC]</i>) (702629)	Uttar Pradesh	05/2019 (12/2020)	05/2024 (06/2027)	8379.62 (8379.62)	6067.88	63
	Total (22)				235216.87	168648.32	
	Waste & Water						
280	ESR - 8 nos., distribution system - 216 Km, new house service connections - 38760 nos. upgrading of feeder mains, pumping station etc. - Phase II (<i>Ministry of Housing & Urban Affairs</i>) (702674)	Andhra Pradesh	02/2017 (07/2018)	03/2023 (12/2025)	172.22 (172.22)	799.74	82
281	Dibrugarh Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702682)	Assam	02/2016 (01/2020)	03/2023 (12/2025)	186.8 (186.8)	1664.41	100
282	Muzaffarpur Storm Water Drainage Phase-I Project (<i>Ministry of Housing & Urban Affairs</i>) (702699)	Bihar	11/2016 (02/2019)	10/2023 (12/2025)	158.78 (158.78)	602.5	83
283	Storm water drainag Development Project (<i>ministry of housing and urban affairs</i>) (702355)	Dadra & Nagar Haveli and Daman & Diu	08/2020 (12/2021)	03/2024 (-)	210 (210)	0	20
284	Upgradation of Sewerage system in Gandhinagar City (<i>ministry of housing and urban affairs</i>) (707267)	Gujarat	07/2020 (03/2021)	06/2023 (-)	200 (200)	100	10
285	Sewerage Management Scheme Part-3 Implementation (<i>Ministry of Housing & Urban Affairs</i>) (702734)	Haryana	03/2017 (11/2017)	09/2023 (03/2026)	278.01 (278.01)	2005.13	88
286	Sewerage Management Scheme Part-3 Implementation (<i>Ministry of Housing & Urban Affairs</i>) (702735)	Haryana	03/2017 (10/2018)	03/2023 (12/2025)	213.19 (213.19)	1430.38	91
287	Dhanbad Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702741)	Jharkhand	02/2017 (12/2018)	03/2023 (03/2026)	216.55 (216.55)	1057.8	72
288	SAAP-3 Water Supply Infrastructure SAAP-3 Project (<i>Ministry of Housing & Urban Affairs</i>) (702742)	Jharkhand	02/2017 (12/2018)	10/2023 (03/2026)	159.31 (159.31)	787.5	65
289	Augmentation and Strengthening of Urban Water Supply Phase 1 - SAAP 3 (<i>Ministry of Housing & Urban Affairs</i>) (702746)	Jharkhand	02/2017 (12/2018)	03/2023 (03/2026)	278.28 (278.28)	1410	78
290	Belgavi Improvement in Sewerage System Project (<i>Ministry of Housing & Urban Affairs</i>) (702760)	Karnataka	12/2015 (10/2016)	07/2023 (12/2025)	162.73 (162.73)	721.71	80
291	24/7 water supply under AMRUT for Davanagere (<i>Ministry of Housing & Urban Affairs</i>) (702764)	Karnataka	11/2016 (01/2018)	03/2023 (12/2025)	174.96 (174.96)	923.02	65
292	Indore Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702793)	Madhya Pradesh	12/2016 (11/2017)	03/2023 (12/2025)	287.17 (287.17)	2271	99
293	Jabalpur Sewerage Management and Treatment Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702798)	Madhya Pradesh	10/2018 (12/2017)	03/2023 (12/2025)	362.31 (362.31)	2930.96	93
294	Satna Sewerage Management and Treatment Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702808)	Madhya Pradesh	11/2015 (12/2016)	03/2024 (12/2025)	191.56 (191.56)	1469.73	86
295	Singrauli Sewerage Management and Treatment Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702810)	Madhya Pradesh	05/2016 (11/2017)	03/2023 (12/2025)	402.01 (402.01)	3175.93	90
296	Kalyan-Dombivali Water Supply Infrastructure Project (<i>Ministry of Housing & Urban Affairs</i>) (702833)	Maharashtra	07/2016 (09/2019)	10/2023 (12/2025)	194.2 (194.2)	1055.02	70

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
297	Mira-Bhayandar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702840)	Maharashtra	11/2016 (08/2018)	03/2023 (12/2025)	204.55 (204.55)	1765.97	99
298	Nagpur Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702842)	Maharashtra	12/2015 (08/2018)	03/2023 (12/2025)	273.78 (273.78)	2409.09	99
299	Pune Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702851)	Maharashtra	03/2017 (07/2017)	03/2023 (10/2025)	235.95 (235.95)	1901.3	92
300	Solapur Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702854)	Maharashtra	03/2017 (04/2018)	03/2023 (12/2025)	180.24 (180.24)	1442.29	91
301	Jalandhar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (703021)	Punjab	11/2016 (08/2020)	08/2023 (03/2026)	258.53 (258.53)	1390.73	58
302	Patiala Water Supply Infrastructure Part-2 Project (Ministry of Housing & Urban Affairs) (703057)	Punjab	11/2016 (08/2020)	10/2023 (12/2025)	287 (287)	1416.38	74
303	Jaunpur Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702948)	Uttar Pradesh	03/2017 (08/2019)	06/2023 (12/2025)	235.73 (235.73)	1911.66	87
304	Jhansi Water Supply Infrastructure Phase-II Project (Ministry of Housing & Urban Affairs) (702949)	Uttar Pradesh	03/2017 (06/2019)	07/2023 (12/2025)	561.74 (561.74)	4045.35	91
Total (25)					6085.6	38687.6	
Ministry of Mines							
Construction							
305	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata (Central Public Works Department (CPWD)) (617280)	West Bengal	04/2019 (02/2020)	08/2026 (-)	255.37 (255.37)	85.9	42
Total (1)					255.37	85.9	
Metals & Mining							
306	Rakha Underground Mining Project (Hindustan Copper Limited [HCL]) (611798)	Jharkhand	12/2022 (03/2024)	03/2033 (-)	2705 (2705)	0	0
307	Surda Underground Copper Mining Project (Hindustan Copper Limited [HCL]) (611800)	Jharkhand	02/2022 (03/2024)	03/2028 (-)	665.02 (665.02)	23.43	1
308	Expansion of Malanjkhand Copper Project (Hindustan Copper Limited [HCL]) (400426)	Madhya Pradesh	09/2011 (04/2015)	04/2020 (04/2026)	1856.36 (1856.36)	940.27	81
309	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonne Per Annum (National Aluminium Company Limited [NALCO]) (400141)	Odisha	04/2017 (04/2017)	12/2022 (09/2025)	4103 (5677.4)	4196.32	78
310	Pottangi Bauxite Mines Project (National Aluminium Company Limited [NALCO]) (400299)	Odisha	05/2018 (05/2018)	03/2025 (05/2026)	1381 (1960.77)	650.04	51
311	UTKAL D AND E COAL BLOCK (National Aluminium Company Limited [NALCO]) (709829)	Odisha	NA (02/2016)	03/2025 (-)	1021.97 (1021.97)	0	0
312	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (Ministry of Mines) (709830)	Odisha	NA (04/2017)	11/2026 (-)	355 (581)	0	0
313	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (National Aluminium Company Limited [NALCO]) (709831)	Odisha	11/2017 (11/2019)	05/2025 (06/2026)	483 (483)	411.79	90
314	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (National Aluminium Company Limited [NALCO]) (709832)	Tamil Nadu	09/2017 (12/2017)	03/2025 (03/2026)	166 (166)	135	65
Total (9)					12736.35	6356.85	
Department of Higher Education							
Education							
315	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008)	Andhra Pradesh	09/2019 (12/2023)	06/2027 (-)	305 (305)	19.96	32
316	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (-)	592.61 (592.61)	550.27	80
317	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (10/2025)	153.71 (153.71)	124.33	97
318	Additional Campus of NITPatna (NIT Patna) (606013)	Bihar	07/2022 (08/2022)	07/2024 (01/2026)	499.21 (499.21)	441.47	99
319	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis (National Institute of Technology Delhi) (612851)	Delhi	09/2009 (11/2022)	09/2025 (-)	333.49 (336.42)	291.33	97
320	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886)	Delhi	09/2024 (03/2025)	10/2026 (-)	373 (373)	21.63	16

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
321	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Central University of Gujarat) (612916)	Gujarat	12/2020 (02/2021)	03/2025 (03/2026)	490.63 (490.63)	313.84	80
322	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099)	Himachal Pradesh	09/2018 (08/2020)	10/2023 (02/2026)	392.51 (454.78)	326.24	93
323	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128)	Himachal Pradesh	03/2023 (03/2024)	03/2026 (03/2026)	166.66 (166.66)	85.92	73
324	Construction of Permanent Campus of Central University of Himachal Pradesh at Dehra, District - Kangra, [H.P.] on Engineering. Procurement and Construction [EPC Mode 1] Basis. (Central University, Himachal Pradesh) (612894)	Himachal Pradesh	03/2021 (08/2022)	11/2024 (11/2025)	251.98 (300.45)	183.47	80
325	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098)	Jammu and Kashmir	03/2019 (10/2020)	06/2023 (11/2025)	424.93 (500.91)	484.52	96
326	Additional Infrastructure at IISc Bangalore-RCC Monolithic for Men Hostel S14, Women Hostel S11 , Postdoctoral Hostel S12 2 Block , International Hostel S 12 , D&E Block S 12 2 Block FR. (IISC Bangalore) (610940)	Karnataka	08/2021 (08/2021)	03/2024 (12/2025)	420.41 (420.41)	364.44	99
327	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431)	Kerala	07/2017 (03/2020)	06/2022 (11/2026)	1006.45 (1217.4)	641.73	74
328	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] (Indian Institute of Technology, Indore) (611957)	Madhya Pradesh	12/2023 (04/2024)	02/2027 (-)	496.28 (496.28)	38.62	37
329	Hostel 4 -Earlier Known as Hostel 20 (Indian Institute of Technology, Bombay) (612135)	Maharashtra	09/2022 (12/2023)	09/2025 (12/2025)	182.33 (182.33)	156.51	98
330	Academic Block 1 & 2 (Indian Institute of Technology, Bombay) (612203)	Maharashtra	09/2022 (05/2023)	07/2026 (03/2027)	68 (263.93)	27.4	20
331	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (07/2025)	494.52 (494.52)	419.57	89
332	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (12/2029)	474.23 (474.23)	167.55	4
333	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	261.24	97
334	IISER BERHAMPUR (Indian Institutes of Science Education and Research, Behrampur) (610315)	Odisha	10/2018 (09/2019)	03/2021 (12/2025)	1229.32 (773.76)	838.21	97
335	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] (National Institute of Technology, Puducherry) (612877)	Puducherry	09/2009 (07/2013)	12/2024 (08/2025)	618.34 (544.34)	529.9	96
336	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I (Indian intitue of Management, Amritsar) (605292)	Punjab	10/2019 (07/2020)	06/2023 (12/2025)	348.31 (348.31)	290.39	91
337	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment (Central University of Punjab) (617221)	Punjab	08/2024 (04/2025)	10/2027 (-)	210.99 (210.99)	0	0
338	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (03/2026)	314.06 (314.06)	238.22	85
339	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	121.56	14
340	Construction of Precast housing and hostels at IIT Hyderabad (Indian Institute of Technology, Hyderabad) (609996)	Telangana	09/2022 (11/2022)	10/2024 (01/2026)	262 (262)	186.49	79
341	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] (Banaras Hindu University) (606479)	Uttar Pradesh	06/2020 (06/2020)	09/2022 (03/2026)	246 (246)	198.02	96
342	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal (National Institute of Technology Uttarakhand) (611963)	Uttarakhand	06/2020 (04/2024)	09/2027 (-)	650.85 (650.85)	195.52	33
343	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur (Indian Institute of Technology, Kharagpur) (609019)	West Bengal	06/2018 (04/2019)	03/2023 (03/2026)	500 (442)	390.6	89
	Total (29)				12467.21	7908.95	
	Department of Sports						
	Education						
344	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081)	Manipur	NA (01/2022)	08/2024 (11/2025)	906.47 (611.74)	553.38	94
	Total (1)				906.47	553.38	

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Petroleum & Natural Gas						
	Energy Storage						
345	Construction of Aviation Fuel farm Facilities at Bhogapuram Airport (Ministry of Petroleum & Natural Gas) (616235)	Andhra Pradesh	08/2024 (08/2024)	03/2026 (03/2026)	240 (240)	61.94	77
346	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	63.31	50
347	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	142.28	57
348	Setting up a common user Petroleum Terminal at Jammu, J&K for resitement of existing PSU OMC's Depots from Jammu City (Bharat Petroleum Corporation Limited [BPCL]) (400235)	Jammu and Kashmir	04/2023 (04/2023)	03/2025 (01/2026)	676.89 (715.89)	550.45	84
349	Andheri Residential Towers, Mumbai (Ministry of Petroleum & Natural Gas) (604833)	Maharashtra	06/2017 (06/2017)	05/2025 (06/2026)	281.35 (389.67)	238.39	51
350	Srikakulam Angul Gas Pipeline Project (Ministry of Petroleum & Natural Gas) (701343)	Multi-States (Andhra Pradesh, Odisha)	09/2019 (09/2019)	07/2022 (12/2025)	2658.34 (2810)	2282.98	96
351	Rajasthan Refinery Project (MinistryofPetroleumNaturalGas) (701263)	Multi-States (Arunachal Pradesh, Gujarat, Rajasthan)	10/2017 (10/2017)	10/2022 (03/2026)	43129 (79459)	61926.61	89
352	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Multi-States (Assam, Bihar, Jharkhand, Odisha, West Bengal)	01/2019 (01/2019)	07/2024 (03/2026)	10228 (11407)	9921.29	88
353	New Mundra Panipat Crude Oil Pipeline (Ministry of Petroleum & Natural Gas) (400078)	Multi-States (Gujarat, Haryana, Rajasthan)	12/2021 (12/2021)	12/2024 (12/2025)	9028 (9028)	7292.34	86
354	Kandla Gorakhpur LPG Pipeline (Ministry of Petroleum & Natural Gas) (400012)	Multi-States (Gujarat, Madhya Pradesh, Uttar Pradesh)	12/2018 (12/2018)	12/2021 (12/2025)	10088 (10088)	8059.53	93
355	Multi Product Pipeline from Irugur to Devangonthi (Department of Water Resources, River Development & GR) (400301)	Multi-States (Karnataka, Tamil Nadu)	11/2012 (11/2012)	02/2017 (09/2026)	678 (1732)	800.88	73
356	Petrochemical evacuation marketing terminal at Barmer, Rajasthan (Hindustan Petroleum Corporation Limited [HPCL]) (709759)	Rajasthan	12/2023 (12/2023)	12/2026 (12/2026)	461.05 (461.05)	145.12	64
357	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] (Ministry of Petroleum & Natural Gas) (400043)	Tamil Nadu	01/2022 (01/2022)	05/2026 (05/2026)	829 (829)	327.86	67
358	Grass root POL Terminal at Vallur, Chennai (Indian Oil Corporation Limited [IOCL]) (400077)	Tamil Nadu	01/2022 (01/2022)	12/2024 (03/2026)	827 (887.71)	638.71	89
359	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	06/2022 (06/2022)	09/2025 (06/2026)	656 (656)	509.92	89
360	Grass-root Terminal at Mirzapur, Uttar Pradesh (Ministry of Petroleum & Natural Gas) (604852)	Uttar Pradesh	09/2022 (09/2022)	11/2026 (11/2026)	980.45 (980.45)	227.04	57
	Total (16)				81301.48	93188.65	
	Oil & Gas						
361	KG-DWN-98/2 Cluster - II Development Project - NELP Block (Oil and Natural Gas Corporation Limited [ONGC]) (400120)	Andhra Pradesh	03/2016 (03/2016)	06/2020 (06/2026)	34012 (34012)	32184.03	96
362	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery (Hindustan Petroleum Corporation Limited) (709752)	Andhra Pradesh	09/2021 (09/2021)	06/2024 (03/2026)	160 (220)	92.6	76
363	City Gas Distribution Project at Kurnool, Guntur & Prakasam Districts (MinistryofPetroleumNaturalGas) (709766)	Andhra Pradesh	03/2022 (03/2022)	03/2030 (03/2030)	1420 (1420)	167.02	6
364	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	07/2020 (07/2020)	07/2024 (12/2025)	12366 (22494)	17659.09	78
365	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	01/2018 (01/2018)	02/2020 (12/2025)	682.9 (726.93)	491.64	94
366	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	05/2021 (05/2021)	10/2023 (05/2026)	412.3 (577)	445.73	87
367	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	12/2020 (12/2020)	03/2024 (12/2025)	430.76 (430.76)	330.99	87
368	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (MinistryofPetroleumNaturalGas) (709776)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277 (323.09)	188.04	68
369	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (MinistryofPetroleumNaturalGas) (709779)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768 (740)	123.97	44
370	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2026)	344.99 (344.99)	215.98	48

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
371	Borholla GGS Life Extension Project [BLEP] <i>(Ministry of Petroleum & Natural Gas)</i> (709850)	Assam	09/2023 (09/2023)	05/2026 (05/2026)	198.7 (198.7)	50.26	40
372	DCU Revamp Project <i>(NRL)</i> (709864)	Assam	08/2021 (08/2021)	07/2024 (06/2026)	370 (370)	266.35	64
373	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme <i>(NRL)</i> (709865)	Assam	04/2023 (04/2023)	12/2024 (12/2025)	293.5 (293.5)	97.22	96
374	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar <i>(Ministry of Petroleum Natural Gas)</i> (617304)	Bihar	10/2023 (10/2023)	03/2027 (03/2027)	340.15 (340.15)	107.35	29
375	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (701324)	Bihar	01/2020 (01/2020)	04/2023 (08/2026)	14810 (16724)	12138.96	88
376	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery <i>(Ministry of Petroleum Natural Gas)</i> (709777)	Bihar	01/2022 (01/2022)	04/2025 (10/2026)	389.35 (340)	73.97	47
377	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709792)	Bihar	12/2022 (12/2022)	03/2030 (03/2030)	3638 (3638)	422.37	29
378	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709793)	Bihar	12/2022 (12/2022)	06/2030 (06/2030)	3919 (3919)	421.98	20
379	Redevelopment of Sobhasan Complex <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400087)	Gujarat	08/2021 (08/2021)	02/2026 (02/2026)	885.63 (1286.67)	876.53	79
380	Redevelopment of Santhal Field [Onshore-Mehsana Asset] <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400167)	Gujarat	02/2017 (02/2017)	03/2026 (03/2026)	1162.56 (1162.56)	1139.5	94
381	Redevelopment of Linch Field <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400169)	Gujarat	04/2021 (04/2021)	03/2025 (03/2026)	631.03 (860.04)	572.74	85
382	Petrochemical and Lube Integration Project at Gujarat Refinery <i>(Ministry of Petroleum & Natural Gas)</i> (701329)	Gujarat	09/2020 (09/2020)	08/2024 (06/2026)	18936 (17825)	12779.56	84
383	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery <i>(Ministry of Petroleum Natural Gas)</i> (709778)	Gujarat	01/2022 (01/2022)	08/2025 (09/2026)	328.29 (287)	172.32	65
384	Commercial Polymer Flooding Project in Bechraji field <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709838)	Gujarat	01/2022 (01/2022)	11/2024 (05/2027)	621.4 (739.02)	137.73	24
385	Restoration of Gas Terminal, Phase-I [Part-A], Hazira <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709840)	Gujarat	05/2022 (05/2022)	02/2025 (12/2025)	249.43 (249.43)	210.42	95
386	Old Pipe Line Replacement [OPRP] Group-A <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709841)	Gujarat	07/2021 (07/2021)	07/2025 (03/2026)	173.03 (169.84)	152.39	89
387	Kalol Redevelopment Project, Ahmedabad Asset <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709842)	Gujarat	08/2022 (08/2022)	03/2027 (03/2027)	1487.41 (1487.41)	937.5	62
388	Revamping of SV Stations, Gas Terminal & Kribhco Terminal <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709845)	Gujarat	11/2022 (11/2022)	08/2026 (08/2026)	837.34 (837.34)	288.4	56
389	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad <i>(Ministry of Petroleum & Natural Gas)</i> (604853)	Haryana	06/2019 (06/2019)	12/2022 (10/2026)	2281.94 (3200)	1841.09	64
390	Poly Butadiene Rubber plant at Panipat <i>(Indian Oil Corporation Limited [IOCL])</i> (611917)	Haryana	03/2022 (03/2022)	03/2025 (06/2026)	1459 (2531.44)	1381.16	74
391	Capacity Expansion of Panipat Refinery from 15 to 25 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (701289)	Haryana	02/2021 (02/2021)	09/2024 (06/2026)	34627 (36225)	26555.13	90
392	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. <i>(Ministry of Petroleum Natural Gas)</i> (709783)	Haryana	12/2020 (12/2020)	06/2023 (06/2026)	165.13 (247.69)	138.41	76
393	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts <i>(Ministry of Petroleum Natural Gas)</i> (709773)	Jammu and Kashmir	03/2022 (03/2022)	03/2032 (03/2032)	538 (538)	4.1	0
394	Development of Jharia CBM Block [Phase-1] <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (610984)	Jharkhand	11/2019 (11/2019)	01/2024 (01/2026)	431 (431)	223.39	60
395	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] <i>(Ministry of Petroleum Natural Gas)</i> (709785)	Jharkhand	02/2023 (02/2023)	02/2026 (02/2026)	202.07 (202.07)	60.23	48
396	Power System Upgradation Project <i>(Mangalore Refinery and Petrochemicals Limited)</i> (612790)	Karnataka	10/2023 (10/2023)	11/2025 (05/2026)	385 (385)	155.14	69
397	Demo Bio-ATF Project <i>(Ministry of Petroleum & Natural Gas)</i> (616879)	Karnataka	03/2024 (03/2024)	01/2027 (01/2027)	364 (364)	32.59	19
398	Revamping/ Augmentation of facilities at existing port terminal at Mangalore <i>(Ministry of Petroleum & Natural Gas)</i> (709774)	Karnataka	01/2022 (01/2022)	12/2025 (12/2025)	463 (500.62)	285.36	74
399	Replacement and Extension of Jetty Pipelines [REJP] at KR <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709790)	Kerala	03/2023 (03/2023)	03/2026 (03/2026)	621.87 (621.87)	203.68	88

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
400	Setting up Polypropylene Unit at Kochi Refinery (<i>Ministry of Petroleum & Natural Gas</i>) (709799)	Kerala	12/2023 (12/2023)	10/2027 (10/2027)	4460 (4460)	308.59	17
401	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery (<i>Ministry of Petroleum & Natural Gas</i>) (709798)	Madhya Pradesh	05/2023 (05/2023)	05/2028 (05/2028)	43367 (43367)	1955	16
402	Debottlenecking and Augmentation of Cryogenic facilities at Uran LPG Import Terminal (<i>Department of Water Resources, River Development & GR</i>) (400158)	Maharashtra	04/2021 (04/2021)	02/2024 (12/2025)	1164.69 (1629.86)	958.12	89
403	500 KTA PDHPP Project, Usar (<i>Ministry of Petroleum & Natural Gas</i>) (400168)	Maharashtra	04/2021 (04/2021)	04/2025 (12/2025)	8797 (11256)	7122.88	86
404	Construction of lube oil blending plant at Rasayani (<i>Ministry of Petroleum & Natural Gas</i>) (610985)	Maharashtra	05/2022 (05/2022)	12/2023 (12/2025)	423.39 (526.26)	313	82
405	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery (<i>Ministry of Petroleum and Natural Gas</i>) (616933)	Maharashtra	12/2024 (12/2024)	03/2028 (03/2028)	4679 (4679)	211.77	5
406	HP TDAE Unit in Mumbai Refinery (<i>Hindustan Petroleum Corporation Limited</i>) (709760)	Maharashtra	06/2024 (06/2024)	04/2026 (04/2026)	240 (240)	44.87	54
407	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts (<i>Ministry of Petroleum & Natural Gas</i>) (709771)	Maharashtra	03/2022 (03/2022)	09/2031 (09/2031)	865 (865)	71.43	3
408	Construction of Additional Tankages and Allied Facilities at JNPT Terminal (<i>Ministry of Petroleum & Natural Gas</i>) (709780)	Maharashtra	04/2022 (04/2022)	08/2026 (08/2026)	341.43 (436.14)	289.06	52
409	ATF Pipeline from Jawaharlal Nehru Port Trust to Navi Mumbai International Airport (<i>Indian Oil Corporation Limited [IOCL]</i>) (709782)	Maharashtra	08/2022 (08/2022)	08/2025 (03/2026)	165 (165)	94.21	78
410	Installation of Independent De- Aromatized Solvents [DAS] production facilities at MR (<i>Bharat Petroleum Corporation Limited [BPCL]</i>) (709789)	Maharashtra	03/2023 (03/2023)	07/2025 (12/2025)	405 (343)	214.5	92
411	POL & LOBS Installations with Receipt Pipelines at Rasayani (<i>Bharat Petroleum Corporation Limited [BPCL]</i>) (709797)	Maharashtra	05/2023 (05/2023)	05/2026 (05/2026)	2585 (2585)	711.91	65
412	Part Replacement Pipeline Project [PRPP] (<i>Oil and Natural Gas Corporation Limited [ONGC]</i>) (709846)	Maharashtra	11/2022 (11/2022)	05/2024 (12/2025)	1219.48 (1145.1)	745	90
413	Visakh Raipur Pipeline Project (<i>Ministry of Petroleum and Natural Gas</i>) (616254)	Multi-States (Andhra Pradesh, Chhattisgarh, Odisha)	09/2024 (09/2024)	09/2027 (09/2027)	2212 (2212)	21.1	11
414	North East Gas Grid (<i>Ministry of Petroleum & Natural Gas</i>) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura, West Bengal)	04/2020 (04/2020)	03/2024 (03/2026)	9265 (9265)	6603.95	86
415	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (<i>Ministry of Petroleum & Natural Gas</i>) (701350)	Multi-States (Assam, West Bengal)	06/2021 (06/2021)	12/2024 (12/2025)	860 (860)	615.47	99
416	CGD Project in Banka, Dumka, Godda, Jamtara, Pakur, Sahibganj GA ID 11A.02 (<i>Hindustan Petroleum Corporation Limited</i>) (709757)	Multi-States (Bihar, Jharkhand)	06/2022 (06/2022)	06/2030 (06/2030)	1377 (1377)	345.02	29
417	Mumbai Nagpur Jharsuguda Pipeline Project (<i>Ministry of Petroleum & Natural Gas</i>) (701354)	Multi-States (Chhattisgarh, Madhya Pradesh, Maharashtra, Odisha)	06/2020 (06/2020)	05/2023 (12/2025)	7844.25 (8255)	6661.2	96
418	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (<i>Ministry of Petroleum & Natural Gas</i>) (701330)	Multi-States (Gujarat, Haryana, Punjab, Rajasthan)	07/2011 (07/2011)	06/2024 (12/2025)	7392 (7392)	6308	90
419	Gurdaspur Jammu Pipeline (<i>Gas Authority of India Limited [GAIL]</i>) (612853)	Multi-States (Jammu and Kashmir, Punjab)	07/2023 (07/2023)	07/2026 (07/2026)	521.9 (521.9)	230.2	40
420	Kochi - Kootanad - Bangalore - Mangalore Pipeline Phase-II (<i>Ministry of Petroleum & Natural Gas</i>) (701228)	Multi-States (Karnataka, Kerala, Tamil Nadu)	06/2009 (06/2009)	12/2012 (12/2025)	2915 (5909)	4506.79	95
421	City Gas Distribution Maharashtra Natural Gas Limited (<i>Ministry of Petroleum & Natural Gas</i>) (701338)	Multi-States (Karnataka, Maharashtra)	01/2006 (01/2006)	06/2031 (06/2031)	5535 (5535)	3986.49	0
422	Dhamra Haldia Pipeline Project (<i>Ministry of Petroleum & Natural Gas</i>) (701344)	Multi-States (Odisha, West Bengal)	03/2020 (03/2020)	11/2022 (12/2025)	1030.65 (1125)	879.8	88
423	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (<i>Bharat Petroleum Corporation Limited [BPCL]</i>) (709794)	Multi-States (Punjab, Rajasthan)	12/2022 (12/2022)	06/2030 (06/2030)	3207 (3207)	348.41	25
424	Augmentation/ Revamping of Dimapur Depot, Dimapur (<i>Ministry of Petroleum & Natural Gas</i>) (709786)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 (227.62)	10.8	25
425	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (<i>Ministry of Petroleum & Natural Gas</i>) (604859)	Odisha	07/2020 (07/2020)	01/2024 (08/2026)	13805 (11783)	8422.69	91

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
426	CUF POL Depot at Sadashibpur [Meramundali], Odisha <i>(Ministry of Petroleum Natural Gas)</i> (709800)	Odisha	04/2021 (04/2021)	03/2026 (03/2026)	393.54 (393.54)	110.87	48
427	Life Extension of 48 well platforms of Mumbai High & Heera Fields <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400119)	Offshore	12/2015 (12/2015)	04/2018 (12/2025)	3190.69 (3375.9)	3119.29	89
428	PRP-VIII [Group-A] <i>(Ministry of Petroleum & Natural Gas)</i> (616950)	Offshore	09/2024 (09/2024)	02/2026 (02/2026)	1486.4 (1486.4)	272.3	23
429	Daman Upside Development Project <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709839)	Offshore	06/2022 (06/2022)	10/2025 (02/2026)	4144.41 (6406.9)	4563.85	88
430	MHN TCPP PGC BGC Project [MTPBP] <i>(Ministry of Petroleum & Natural Gas)</i> (709848)	Offshore	06/2022 (06/2022)	05/2026 (05/2026)	2329.45 (2354.23)	1148.9	59
431	PRP-VIII Group B [NH & BS Asset] <i>(Ministry of Petroleum & Natural Gas)</i> (709849)	Offshore	06/2024 (06/2024)	02/2026 (02/2026)	2379.84 (3165.53)	1806.88	64
432	Integrated Development of 4 Contract Areas under DSF-II <i>(Ministry of Petroleum & Natural Gas)</i> (709851)	Offshore	05/2023 (05/2023)	04/2027 (04/2027)	6183.79 (6183.79)	594.28	23
433	2G Ethanol Biorefinery at Bathinda <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (400171)	Punjab	05/2020 (05/2020)	02/2023 (03/2026)	1421.46 (1421.46)	1201.66	95
434	City Gas Distribution Project at Pathankot District <i>(Ministry of Petroleum Natural Gas)</i> (709770)	Punjab	03/2022 (03/2022)	09/2033 (09/2033)	151 (151)	8.75	2
435	CBR 9 MMTPA Project <i>(Chennai Petroleum Corporation Limited [CPCL])</i> (604795)	Tamil Nadu	09/2021 (09/2021)	06/2025 (10/2028)	31580 (36354)	1342.27	10
436	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore <i>(Chennai Petroleum Corporation Limited [CPCL])</i> (709750)	Tamil Nadu	01/2024 (01/2024)	09/2025 (12/2025)	205 (205)	56.22	51
437	City Gas Distribution Projects at the Nilgiris and Erode districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709796)	Tamil Nadu	12/2022 (12/2022)	03/2030 (03/2030)	3685 (3685)	244.45	20
438	Creation of Gas Dehydration Facilities, Tripura Asset <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709837)	Tripura	03/2022 (03/2022)	05/2024 (12/2025)	209.33 (131.51)	70.1	66
439	PP Project, Pata <i>(Gas Authority of India Limited [GAIL])</i> (400161)	Uttar Pradesh	03/2019 (03/2019)	01/2024 (11/2025)	910.56 (1299.02)	1041	98
440	Revamping / Augmentation of Facilities at Mathura Bitumen Plant <i>(Ministry of Petroleum Natural Gas)</i> (709781)	Uttar Pradesh	04/2022 (04/2022)	06/2027 (12/2026)	260.12 (260.12)	8.14	30
441	City Gas Distribution Projects at Lakhimpur Kheri , Sitapur, Bahraich, Shravasti, Balrampur, Siddharth Nagar & Maharajganj districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709795)	Uttar Pradesh	12/2022 (12/2022)	06/2030 (06/2030)	16654 (16654)	595.93	12
442	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] <i>(Ministry of Petroleum & Natural Gas)</i> (617302)	West Bengal	03/2017 (03/2017)	12/2020 (12/2025)	1740 (2493.15)	2285	90
443	Haldia Panagarh Pipeline Project <i>(Hindustan Petroleum Corporation Limited)</i> (709753)	West Bengal	11/2022 (11/2022)	11/2025 (05/2026)	1010 (1010)	692.62	84
444	CGD Project in Malda, Birbhum, Murshidabad, Dakshin Dinajpur GA ID 11A.03 <i>(Hindustan Petroleum Corporation Limited)</i> (709758)	West Bengal	06/2022 (06/2022)	06/2030 (06/2030)	2628 (2628)	348.91	29
445	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts <i>(Ministry of Petroleum Natural Gas)</i> (709772)	West Bengal	03/2022 (03/2022)	06/2031 (06/2031)	609 (609)	58.09	2
446	City Gas Distribution Projects at Alipurduar and Cooch Behar <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709791)	West Bengal	12/2022 (12/2022)	03/2030 (03/2030)	1017 (1017)	194.58	40
	Total (86)				348775.78	185369.27	
	Ministry of Health & Family Welfare						
	Healthcare						
447	AIIMS Majra Rewari Haryana <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701173)	Haryana	12/2023 (02/2019)	02/2023 (12/2026)	1299 (1299)	349.41	28
448	AIIMS Kashmir at Awantipora Jammu & Kashmir <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701167)	Jammu and Kashmir	01/2019 (11/2020)	01/2025 (12/2025)	1828 (1828)	1321.7	68
449	AIIMS Bibinagar <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701171)	Telangana	12/2018 (07/2022)	09/2022 (12/2025)	1028 (1365.95)	806.8	85
	Total (3)				4155	2477.91	
	Ministry of Labour and Employment						
	Healthcare						
450	Construction of 350 beds + 50 Super Specialty beds ESIC Hospital Sheelanagar, Visakhapatnam, Andhra Pradesh <i>(Employee's State Insurance Company [ESIC])</i> (612167)	Andhra Pradesh	02/2021 (04/2023)	10/2025 (01/2026)	384.27 (384.27)	105	40
451	Construction of 200 bedded ESIC Hospital with 62 Nos Staff quarters , Beltola <i>(Employee's State Insurance Company [ESIC])</i> (612201)	Assam	12/2017 (10/2021)	04/2025 (10/2025)	143.23 (154.75)	101.83	93
452	C/o Construction of 200 bedded [Up-gradable to 300 bedded] ESI Hospital at Surat Gujarat. <i>(Employee's State Insurance Company [ESIC])</i> (612185)	Gujarat	06/2019 (03/2021)	06/2025 (05/2025)	209.36 (209.36)	180.54	98

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
453	350 Bedded [Upgradable to 500 beds] ESI Hospital at Sanand (Employee's State Insurance Company [ESIC]) (612186)	Gujarat	06/2022 (04/2023)	03/2026 (02/2026)	558.12 (558.12)	58.36	7
454	Demolition, Construction and upgradation of ESI Hospital, Kalol, Gujarat from 50 beds to 150 beds. (Employee's State Insurance Company [ESIC]) (612211)	Gujarat	08/2022 (10/2023)	10/2025 (06/2026)	205.87 (205.87)	31.49	16
455	Construction of 100 bedded ESIC Hospital & 32 nos. of Staff qtrs at OMPURA J&K. (Employee's State Insurance Company [ESIC]) (612239)	Jammu and Kashmir	09/2019 (12/2021)	09/2024 (05/2025)	131.05 (164.93)	1747.76	99
456	Construction of 200 bed ESI Hospital at Bommasandra, Karnataka (Employee's State Insurance Company [ESIC]) (612745)	Karnataka	02/2015 (10/2024)	01/2027 (-)	278 (278)	27.8	0
457	Construction of 100 bed ESI Hospital and Staff Quarters [32 Nos.] at Harohalli, Karnataka (Employee's State Insurance Company [ESIC]) (612748)	Karnataka	07/2019 (03/2025)	02/2027 (-)	150.92 (150.92)	0	0
458	Construction of 200 Bedded [Upgradable to 500 Bedded including 50 beds of SST] ESIC Hospital at Bibewadi, Pune (Employee's State Insurance Company [ESIC]) (612188)	Maharashtra	05/2018 (03/2023)	09/2025 (02/2026)	429.25 (429.25)	252.06	68
459	Construction of 200 Bedded ESIC Hospital at Butibori, Nagpur, Maharashtra. (Employee's State Insurance Company [ESIC]) (612213)	Maharashtra	10/2013 (08/2022)	08/2025 (08/2025)	194.93 (196.7)	86.6	60
460	Upgradation & Extension of ESIC Hospital and Construction of PG Hostel / Staff Housing for ESIC Hospital at Andheri, Mumbai (Employee's State Insurance Company [ESIC]) (616691)	Maharashtra	NA (06/2009)	08/2025 (12/2025)	260.13 (260.13)	210.12	88
461	Construction of 100 Bedded ESI Hospital at Duburi, Odisha. (Employee's State Insurance Company [ESIC]) (612513)	Odisha	12/2010 (02/2025)	06/2027 (-)	164.6 (164.6)	16.4	1
462	Construction of 100 Bedded ESIC Hospital building and 32 Nos Residential Quarters at Vallam Vadangal, SIPCOT, Sriperumbudur (Employee's State Insurance Company [ESIC]) (612178)	Tamil Nadu	02/2015 (03/2023)	06/2025 (-)	152.95 (152.95)	107.83	98
463	Construction of New OPD Block 200 Bed ward Basement + GF + 6 Floors at the location of old OPD block, at existing ESIC Hospital/ Medical college campus, Sanathnagar, Hyderabad (Employee's State Insurance Company [ESIC]) (612688)	Telangana	11/2017 (10/2021)	06/2024 (06/2025)	211.13 (211.13)	198.95	100
464	CONSTRUCTION OF 300 BEDDED HOSPITAL AT HARIDWAR (Employee's State Insurance Company [ESIC]) (612259)	Uttarakhand	02/2021 (12/2021)	10/2024 (06/2025)	102.4 (297.63)	297.63	68
Total (15)					3576.21	3422.37	
Ministry of Ports, Shipping and Waterways							
Healthcare							
465	Establishment of 600 bed super specialty hospital with optional development of Medical college and further expansion on PPP basis. (Mumbai Port Trust [MPT]) (708662)	Maharashtra	08/2019 (01/2022)	06/2026 (12/2027)	693 (693)	58	0
Total (1)					693	58	
Inland Waterways							
466	Jal Marg Vikas Project (Inland Waterways Authority of India [IWAI]) (701565)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	01/2018 (02/2018)	12/2023 (12/2025)	5369.18 (5061.15)	3526.99	72
467	Fairway Development in West Bengal Farakka - Kahelgaon (Inland Waterways Authority of India [IWAI]) (611142)	Offshore	NA (08/2018)	07/2023 (04/2024)	177 (197)	183.32	100
Total (2)					5546.18	3710.31	
Shipping							
468	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust [DPT]) (609424)	Gujarat	10/2022 (03/2024)	03/2027 (-)	4243.64 (4243.64)	800.04	32
469	Construction of oil jetty No.8 at old kandla through internal resources (Deendayal Port Trust [DPT]) (701568)	Gujarat	NA (02/2021)	02/2023 (07/2024)	100 (225.85)	166.48	90
470	Replacement and revamping of pipeline projects in oil jetty area, Kandla (Deendayal Port Trust [DPT]) (701570)	Gujarat	09/2021 (09/2021)	09/2023 (03/2025)	171 (211.61)	137.51	71
471	Mechanization of Berth No.14 for handling Containers and other cargo on DBFOT basis - Phase II (New Mangalore Port Authority) (617804)	Karnataka	NA (06/2024)	03/2027 (-)	153.23 (153.23)	50.1	33
472	Construction of new dry dock at exisitng Cochin Shipyard Limited premises at Perumanoor, Kochi 682 015 (Cochin Shipyard) (701564)	Kerala	04/2018 (05/2018)	12/2022 (03/2025)	1799 (1799)	1558.39	96
473	Rewas Port Project (Reliance Industries Ltd) (400382)	Maharashtra	NA (01/2020)	03/2023 (-)	6000 (6000)	5999.89	0
474	Setting up of a Floating Storage and Regasification Unit [FSRU] - Mumbai (Mumbai Port Trust [MPT]) (701586)	Maharashtra	NA (04/2021)	11/2026 (11/2026)	900 (900)	65	0
475	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574)	Odisha	05/2022 (01/2023)	12/2027 (10/2028)	3004.63 (3004.63)	1149.79	40
476	Berth No. 2 [previously Berth 3] of HDC Mechanization Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701576)	West Bengal	NA (03/2023)	09/2025 (01/2026)	298.26 (298.26)	438.5	97

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
477	Shalukkhali Liquid Cargo Handling Facility Development Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701577)	West Bengal	NA (08/2022)	08/2025 (-)	253.65 (253.65)	9.28	0
	Total (10)				16923.41	10374.98	
	Tourism, Hospitality & Wellness						
478	National Maritime Heritage Complex [NMHC] Phase-I (Indian Port Rail & Ropeway Corporation Ltd. [IPRCL]) (707215)	Gujarat	02/2019 (01/2022)	03/2024 (09/2025)	573 (1238.05)	496.63	66
	Total (1)				573	496.63	
	Ministry of Steel						
	Metals & Mining						
479	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul (National Mineral Development Corporation Limited [NMDC]) (615202)	Chhattisgarh	08/2021 (07/2022)	12/2028 (03/2028)	1700 (1756.2)	133.22	6
	Total (1)				1700	133.22	
	Steel						
480	Stamp Charge Battery No.12 Battery Proper at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617338)		01/2025 (02/2025)	07/2028 (-)	2518.39 (2518.39)	152.23	4
481	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617243)	Chhattisgarh	07/2024 (08/2024)	07/2026 (-)	198.62 (198.62)	12.21	15
482	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617255)	Chhattisgarh	10/2023 (12/2023)	06/2026 (-)	471.83 (471.83)	158.07	46
483	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617256)	Chhattisgarh	11/2023 (01/2024)	10/2025 (-)	884.1 (884.1)	506.96	80
484	NMDC Slurry Pipeline Project Phase-1 (National Mineral Development Corporation Limited [NMDC]) (706811)	Chhattisgarh	11/2015 (09/2020)	06/2023 (12/2025)	2907 (5427)	3179.93	88
485	SCREENING PLANT-III AT KIRANDUL (National Mineral Development Corporation Limited [NMDC]) (709826)	Chhattisgarh	NA (10/2021)	01/2026 (-)	2718.84 (2718.84)	1384.73	77
486	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (National Mineral Development Corporation Limited [NMDC]) (709827)	Chhattisgarh	NA (10/2022)	12/2025 (-)	349.75 (349.75)	294.65	94
487	New Sinter Plant at BSL, SAIL (Steel Authority of India Limited [SAIL]) (400174)	Jharkhand	03/2015 (10/2015)	10/2017 (06/2027)	1034.01 (1752.3)	885.26	53
488	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617249)	Jharkhand	01/2025 (02/2025)	01/2027 (-)	211.94 (211.94)	16.04	11
489	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617250)	Jharkhand	01/2025 (02/2025)	10/2026 (-)	207.13 (207.13)	15.76	8
490	Revamping of old sub-systems of Blast Furnace 3 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617253)	Jharkhand	08/2023 (03/2023)	07/2025 (11/2025)	513.82 (513.82)	257.89	74
491	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617254)	Jharkhand	03/2024 (04/2024)	06/2026 (-)	260.37 (260.37)	54.89	23
492	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617257)	Jharkhand	11/2023 (12/2023)	11/2026 (-)	627.31 (627.31)	153.32	46
493	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. (National Mineral Development Corporation Limited [NMDC]) (400121)	Karnataka	11/2014 (06/2024)	08/2026 (-)	1043.63 (1043.63)	288.87	35
494	Installation of 4th Slab Caster along with its Auxiliaries and a New Ladle Furnace in SMS-II at Rourkela Steel Plant (Steel Authority of India Limited [SAIL]) (400065)	Odisha	01/2022 (02/2022)	05/2025 (09/2025)	1105.23 (1105.23)	790.11	99
495	Rebuilding of COB 4 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (612781)	West Bengal	09/2023 (09/2023)	12/2026 (-)	916.78 (916.78)	146.64	20
496	Installation of New Bar Mill at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617242)	West Bengal	07/2024 (08/2024)	06/2027 (-)	2115.44 (2115.44)	236.73	32
497	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617246)	West Bengal	09/2024 (08/2024)	06/2026 (-)	758.09 (758.09)	85.89	7
498	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617248)	West Bengal	11/2024 (12/2024)	07/2026 (-)	227.96 (227.96)	27.2	33
499	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617251)	West Bengal	07/2024 (12/2024)	05/2026 (-)	196.4 (196.4)	5.96	5
	Total (20)				19266.64	8653.34	
	Ministry of Railways						
	Railways						
500	Nadikudi - Srikalahasti New Line (South Central Railway [SCR] - II) (400298)	Andhra Pradesh	03/2012 (12/2016)	05/2027 (03/2028)	2312 (5200)	2179	54

All Ongoing Projects

OCTOBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
501	Malugur- Palasamudram New Line Project [17.975 Km] (South Western Railway [SWR] - II) (611615)	Andhra Pradesh	09/2022 (07/2026)	11/2027 (12/2027)	342 (342)	0	0
502	GOOTY-PENDEKALLU DOUBLING 29.225 Km (South Central Railway [SCR] - II) (611752)	Andhra Pradesh	03/2023 (06/2023)	03/2027 (03/2027)	351.83 (351.83)	18	25
503	GUNTAKAL WEST-MALLAPPA GATE RAIL OVER RAIL - ROR TRACK (South Central Railway [SCR] - II) (611754)	Andhra Pradesh	07/2023 (07/2023)	07/2026 (-)	293.3 (293.3)	0	0
504	Kurnool - Setting up facilities for coach midlife rehabilitation workshop (WPO/Patna) (611927)	Andhra Pradesh	01/2014 (10/2017)	12/2023 (-)	560.72 (560.72)	276.66	65
505	Flyover between Pendurthi and Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB 73 of 2023 24 NR (East Coast Railway [ECor] - II) (612827)	Andhra Pradesh	04/2023 (05/2024)	04/2027 (-)	183.65 (183.65)	5.11	11
506	3rd & 4th line between Vadlapudi -Gate Jn. cabin and Tie line between Gate Junction to Gangavaram port (East Coast Railway [ECor] - II) (616697)	Andhra Pradesh	04/2023 (03/2024)	06/2026 (-)	154.28 (154.28)	20.15	21
507	Tiupati Katpadi 104.39 kms (South Central Railway [SCR] - II) (617210)	Andhra Pradesh	04/2025 (04/2025)	03/2029 (-)	1215.56 (1215.56)	0.1	0
508	3rd Line between Gudur Renigunta 83.17 Km (South Central Railway [SCR] - II) (617216)	Andhra Pradesh	10/2024 (10/2024)	03/2027 (-)	877.34 (877.34)	23.35	0
509	Kurnool Coach Midlife Rehabilitation Project (WPO/Patna) (705253)	Andhra Pradesh	05/2016 (07/2014)	12/2020 (-)	563 (563)	120	0
510	Kotapalli - Narasapur New Line (South Central Railway [SCR] - II) (705436)	Andhra Pradesh	03/2009 (09/2013)	03/2028 (03/2028)	2501 (2501)	1318.88	29
511	Guntur-Guntakal Doubling Project (South Central Railway [SCR] - II) (705633)	Andhra Pradesh	03/2017 (11/2017)	12/2025 (12/2026)	3733 (4295)	4475.84	93
512	Vijaywada-Gudur 3rd Line (RVNL - II) (705648)	Andhra Pradesh	08/2016 (04/2018)	11/2024 (12/2025)	6654 (6654)	5922	90
513	Penukonda - Dharmavaram Doubling Project [41.5 Km] (South Western Railway [SWR] - II) (705789)	Andhra Pradesh	06/2018 (12/2018)	03/2026 (03/2026)	307.66 (307.66)	259.52	65
514	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3727.78	93
515	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
516	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
517	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
518	Sakri -Hasanpur [via Harnagar - Kusheshwar Asthan] New Railway line (East Central Railway [ECR] - I) (400254)	Bihar	12/2023 (08/1997)	12/2024 (03/2027)	735.2 (735.2)	588.66	84
519	Construction of Bulb line at Nabinagar Ankorah of East Central Railway (East Central Railway [ECR] - I) (617231)	Bihar	06/2024 (06/2024)	06/2028 (-)	611.74 (611.74)	0	0
520	Jhajha-Batai New Line Project (East Central Railway [ECR] - I) (617373)	Bihar	03/2023 (03/2023)	03/2027 (-)	588.18 (588.18)	3.05	0
521	Khagaria-Kusheshwar Asthan [42Km] new line project (East Central Railway [ECR] - I) (705364)	Bihar	04/2019 (12/1998)	12/2024 (03/2027)	614 (1384)	487.99	55
522	Hajipur-Sagauli New line (East Central Railway [ECR] - I) (705366)	Bihar	10/2007 (10/2004)	03/2020 (12/2026)	2067 (2087)	2013.82	74
523	Araria Supaul New BG Line (East Central Railway [ECR] - I) (705368)	Bihar	06/2018 (03/2009)	03/2024 (01/2027)	1605 (2514)	1547.96	35
524	Fatuha-Islampur incl. MM for extn.of NL from Neora to Daniawan , Daniawan to Biharsharif, Biharsharif to Barbigha , Barbigha to Shekhpura (East Central Railway [ECR] - I) (705373)	Bihar	08/2002 (03/2002)	03/2023 (08/2025)	1473 (2882)	2535.73	94
525	Jogbani-Biratnagar New Rail Line project (Indian Railway Construction International Limited [IRCON]) (705450)	Bihar	06/2010 (01/2011)	03/2022 (12/2026)	402 (486)	367.54	86
526	Samastipur-Darbhanga Doubling Railway Project (East Central Railway [ECR] - I) (705526)	Bihar	11/2015 (12/2015)	03/2025 (10/2025)	519 (519)	367.57	84
527	Sagauli-Valmiknagar (East Central Railway [ECR] - I) (705527)	Bihar	03/2018 (03/2017)	12/2025 (12/2025)	1216 (2222)	2072.37	91
528	Muzaffarpur-Sugauli (East Central Railway [ECR] - I) (705528)	Bihar	03/2018 (03/2017)	06/2024 (02/2026)	1586 (1586)	1470.4	99
529	Rampur Dumra-Tal-Rajendrapul Additional Bridge and Railway Line Doubling (Indian Railway Construction International Limited [IRCON]) (706759)	Bihar	03/2016 (05/2017)	12/2024 (12/2025)	2373.64 (1700.24)	1427.78	97
530	Barauni-Bachwara [16 km] - 3rd & 4th line incl. Barauni yard remodelling [32 km] (East Central Railway [ECR] - I) (706860)	Bihar	10/2022 (08/2025)	08/2025 (10/2026)	645 (645)	7.96	55

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
531	JHAJHA - BATIA (East Central Railway [ECR] - I) (900874)	Bihar	03/2023 (03/2023)	03/2028 (01/2030)	588.18 (588.18)	0.8	0
532	Kharsia-Dharamjaygarh with Spur line [East Corridor-Phase 1] (Indian Railway Construction International Limited [IRCON]) (400220)	Chhattisgarh	03/2016 (01/2014)	09/2018 (03/2026)	3055 (3438)	2594.89	94
533	Doubling of Kirandul-Jagdalpur Line [150 km] (East Coast Railway [ECoR] - II) (400291)	Chhattisgarh	02/2013 (03/2013)	03/2020 (12/2025)	1589 (1798)	1566.97	93
534	Gauge Conversion of Kendri-Dhamtari including Abhanpur - Rajim Branch line 67.20 Kms - 2nd Material Modification to Raipur Titlagarh doubling. (SECR) (602792)	Chhattisgarh	07/2011 (05/2021)	02/2025 (03/2026)	1171 (1171)	376	100
535	4th line between Nipania Bhatapara 14.4 Km (South East Central Railway [SECR] - II) (612815)	Chhattisgarh	12/2022 (05/2024)	03/2027 (-)	170.49 (170.49)	1.34	5
536	Dharamjaigarh-Korba 63 km (CERL) (613003)	Chhattisgarh	08/2023 (07/2022)	08/2026 (-)	1686.26 (1686.26)	288.83	18.5
537	KHARSIA- NAYA RAIPUR-PARMALKASA 5th and 6th Line [278KM] (CAO/C/SECR) (617200)	Chhattisgarh	04/2025 (04/2025)	03/2031 (-)	7853.84 (7853.84)	0	0
538	Dallirajhara - Rowghat New Rail Line Project, Phase-I (Rail Vikas Nigam Limited) (617374)	Chhattisgarh	NA (11/2009)	03/2025 (-)	1516.45 (1516.45)	873.79	92
539	Dallirajhra- Rowghat New Railway Line - Phase I [95 km] (Rail Vikas Nigam Limited) (705433)	Chhattisgarh	07/2009 (12/2009)	09/2025 (12/2025)	1628 (1628)	1440.85	82
540	Gevra Road-Pendra Road New Railway Line [135 km] (Indian Railway Construction International Limited [IRCON]) (705444)	Chhattisgarh	04/2014 (04/2014)	03/2022 (12/2025)	4970 (4970)	4449.99	73
541	Boridand - Ambikapur Doubling Line Project (South East Central Railway [SECR] - II) (706854)	Chhattisgarh	06/2022 (04/2022)	06/2030 (06/2030)	1376 (1576.23)	139.49	21
542	4TH LINE - BHATAPARA-HATHBAND [8.8 KM] [PB-72/NR/2022-23] (SECR) (709815)	Chhattisgarh	09/2022 (05/2024)	01/2027 (12/2027)	177.03 (177.03)	0	3
543	4TH LINE - BHILAI-BHILAI NAGAR [8.8 KM] [PB-72/NR/2022-23] (SECR) (709816)	Chhattisgarh	09/2022 (05/2024)	02/2027 (02/2027)	177.34 (177.34)	1.64	5
544	4TH LINE - DADHAPARA-BELHA [9.2 KM] [PB-72/NR/2022-23] (SECR) (709817)	Chhattisgarh	09/2022 (05/2024)	11/2026 (11/2026)	169.06 (169.06)	17.84	60
545	4TH LINE RAJNANDGAON-DONGARHGARH [31.2 KM] [PB-72/NR/2022-23] (SECR) (709818)	Chhattisgarh	09/2022 (05/2024)	01/2027 (01/2027)	328.34 (328.34)	56.1	26
546	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (709819)	Chhattisgarh	09/2022 (05/2025)	12/2026 (12/2026)	167.64 (167.64)	0.09	4
547	Redevelopment of New Delhi Railway Station and construction of associated infrastructure (Rail Land Development Authority) (613785)	Delhi	01/2023 (06/2024)	12/2028 (-)	4744 (4744)	119.95	1
548	Development of New Bijwasan Railway Terminal (Northern Railways) (617379)	Delhi	02/2008 (03/2013)	03/2020 (-)	446.21 (446.21)	511.94	80
549	North Region Video Surveillance Project (RCIL) (705298)	Delhi	06/2020 (04/2023)	03/2024 (-)	274.39 (274.39)	0	0
550	Anand Vihar-Tilak Bridge 3rd & 4th line (CAO/C/NR) (705583)	Delhi	03/2013 (03/2013)	03/2023 (12/2027)	667 (667)	287.26	62
551	Provision of Work-site Tampers [WST] Railway Project (EDTK[MC]/RB) (705694)	Delhi	01/2016 (01/2016)	12/2023 (01/2026)	187.72 (187.72)	141.91	100
552	WST Machine Procurement Project (EDTK[MC]/RB) (705708)	Delhi	06/2018 (06/2018)	03/2024 (12/2027)	176 (176)	0	0
553	PCT Machine Procurement Project (EDTK[MC]/RB) (705710)	Delhi	04/2019 (04/2019)	04/2024 (06/2027)	336 (336)	74.32	85
554	RBMV Machine Procurement Project (EDTK[MC]/RB) (705712)	Delhi	10/2019 (10/2019)	06/2024 (12/2027)	480 (480)	0.33	7
555	SRGM Machine Procurement Project (EDTK[MC]/RB) (705717)	Delhi	10/2019 (10/2019)	12/2023 (03/2026)	440 (440)	390.03	90
556	WST Machine Procurement Project (EDTK[MC]/RB) (705720)	Delhi	12/2019 (12/2019)	04/2024 (12/2026)	384 (384)	0	0
557	DTS Machine Procurement Project (EDTK[MC]/RB) (705721)	Delhi	12/2019 (12/2019)	12/2024 (12/2026)	447.6 (447.6)	0	0
558	BRM Machine Procurement Project (EDTK[MC]/RB) (705722)	Delhi	09/2019 (09/2019)	06/2024 (12/2027)	210 (210)	0.02	0
559	Track Machine Procurement Project (EDTK[MC]/RB) (705726)	Delhi	04/2020 (04/2020)	03/2025 (01/2028)	6339 (6339)	4166.47	41
560	Kosamba Umapada 70 Km (PCE/WR) (611918)	Gujarat	07/2023 (07/2022)	03/2027 (-)	468 (468)	20.28	8



All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
561	Adraj Moti Vijapur 40 Kms (Western Railway (WR) - II) (611937)	Gujarat	05/2022 (05/2022)	05/2026 (12/2025)	417.53 (417.53)	494.13	90
562	New Broad Gauge line between Naliya to Jakhau Port (Western Railway (WR) - II) (611943)	Gujarat	02/2023 (02/2023)	01/2028 (01/2028)	410.26 (410.26)	6.6	4
563	Quadrupling between Gandhidham Adipur with Y connection at Adipur for providing direct entry towards Mundra Port and Bhuj and high level platform at Gopalpur 11Kms (Western Railway (WR) - II) (611944)	Gujarat	02/2023 (02/2023)	03/2026 (03/2026)	152.44 (152.44)	101.74	75
564	Petlad Bhadran 23 Kms (Western Railway) (611945)	Gujarat	05/2022 (05/2022)	05/2030 (05/2030)	307.11 (307.11)	13.58	17
565	Samlaya Timba Road 54 km (PCE/WR) (611970)	Gujarat	02/2023 (02/2023)	03/2030 (03/2030)	670.17 (670.17)	44.8	12
566	Samni Jambusar 24 km (PCE/WR) (611971)	Gujarat	05/2022 (05/2022)	03/2030 (03/2030)	350 (349.93)	67.73	31
567	Western Railway Samakhiali Gandhidham Quadrupiling 53 Kms (Western Railway (WR) - II) (611974)	Gujarat	08/2023 (08/2023)	12/2026 (06/2027)	1430 (1430)	220.11	20
568	Dahod Creation of Infrastructure facilities for 9000 HP Electric locomotives Manufacturing at (PCE/WR) (611977)	Gujarat	05/2022 (02/2023)	02/2025 (-)	487 (487)	108.69	0
569	Dahod Rolling Stock Workshop Provision of Infrastructure for CBS at (PCE/WR) (611978)	Gujarat	11/2022 (03/2023)	03/2025 (-)	158 (158)	47.31	0
570	Sabarmati Setting up of Maintenance Facilities for Train Sets Phase ii (PCE/WR) (611979)	Gujarat	01/2023 (04/2023)	06/2025 (-)	250 (250)	0	0
571	4th LINE BETWEEN BAREJADI NANDEJ-SANAND-AHMEDABAD BYPASS (Western Railway (WR) - II) (612072)	Gujarat	02/2023 (02/2023)	03/2027 (07/2028)	961.67 (961.67)	335.93	17
572	Redevelopment of Ahmedabad railway station and associated infrastructure on engineering, procurement and construction mode (Rail Land Development Authority) (613786)	Gujarat	01/2023 (11/2023)	03/2028 (-)	2379 (2379)	726.91	19
573	Miyagam-Karjan-Dabhoi-Samlaya [GC] (Western Railway [WR] - II) (705458)	Gujarat	01/2017 (01/2017)	03/2021 (12/2026)	483.88 (1039.13)	621.53	41
574	Modasa-Shamlaji Road Railway Line Project (Western Railway (WR) - II) (706757)	Gujarat	09/2012 (04/2008)	03/2025 (03/2027)	262 (262)	337.45	62
575	Rajkot - Kanalus Doubling Project [111.2 Kms] (Western Railway (WR) - II) (706763)	Gujarat	10/2021 (12/2021)	10/2026 (10/2026)	1080.58 (1080.58)	822.77	77
576	NADIAD-PETLAD [37.26 KM] (Railway) (709812)	Gujarat	05/2022 (10/2023)	06/2030 (06/2030)	461.91 (461.91)	92.88	7
577	NEW BG LINE INTERSECTION [5 NOS] BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD [16.51 KM] (Western Railway (WR) - II) (709813)	Gujarat	10/2022 (07/2025)	06/2028 (10/2027)	437.21 (437.21)	19.06	17
578	Bhiwani - Dobh Bahali Doubling Project [42.30 Km] (North Western Railway [NWR]) (611884)	Haryana	02/2023 (02/2023)	02/2028 (02/2028)	471 (471)	215.11	65
579	Doubling between Pradhankunta-Patherih-Bhojudih of East Central Railway (East Central Railway [ECR] - I) (617372)	Jharkhand	11/2022 (11/2022)	12/2025 (-)	349.22 (349.22)	106.11	70
580	Gomoh - Flyover for DN trains (East Central Railway [ECR] - I) (705765)	Jharkhand	01/2018 (01/2018)	03/2026 (03/2026)	686 (686)	574.14	59
581	Lodhma - Piska - Link Line bypassing Hatia/Ranchi with Y connection (South Eastern Railway [SER] - I) (705785)	Jharkhand	08/2021 (03/2019)	06/2026 (05/2027)	473 (473)	288.59	5
582	Pradhan Kuntha Jn Line Doubling Project (East Central Railway [ECR] - I) (706837)	Jharkhand	11/2022 (11/2022)	11/2027 (11/2027)	349.22 (349.22)	106.11	62
583	Construction of New BG line between Hassan to Belur [27 Km] (South Western Railway [SWR] - II) (400023)	Karnataka	03/2019 (12/2025)	04/2028 (04/2027)	749 (749)	0	0
584	Yeshvanthpur - Channasandra Doubling Project [21.70 Km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703585)	Karnataka	04/2019 (10/2019)	03/2024 (03/2026)	314.1 (683.57)	152.31	53
585	New Railway Line between Ginigera and Raichur [165.57 km] (South Western Railway [SWR] - II) (705434)	Karnataka	03/2008 (05/2009)	03/2019 (03/2027)	2565 (3034.98)	2105.62	66
586	Gadag-Wadi New Railway Line [257 km] (South Western Railway [SWR] - II) (705490)	Karnataka	04/2013 (08/2017)	03/2027 (12/2027)	2842 (6700)	1400.27	30
587	Kadur - Chickamagalur - Sakleshpur [93km] (South Western Railway [SWR] - II) (705492)	Karnataka	01/2014 (11/2016)	06/2025 (12/2025)	825 (825)	699.12	83
588	Bagalkot-Kudachi New Railway Line [142 km] (South Western Railway [SWR] - II) (705495)	Karnataka	10/2013 (11/2012)	03/2027 (01/2027)	1378 (1649)	716.65	35
589	Tumkur-Chitradurga-Davangere New Rail Line Project [191 km] (South Western Railway [SWR] - II) (705496)	Karnataka	10/2013 (01/2017)	03/2019 (12/2027)	1876 (1876)	436.37	13
590	Bangalore-Whitefield-Bangalore City-Krishnarajapuram [23.08 km] - Quadrupling (South Western Railway [SWR] - II) (705663)	Karnataka	02/2018 (06/2022)	02/2026 (02/2026)	493 (493)	252.45	82



All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
591	SHIMOGA - SHIKARIPURA - RANEBENNUR [96 Km] (South Western Railway [SWR] - II) (705761)	Karnataka	09/2019 (02/2023)	12/2027 (06/2028)	1454 (1454)	71.89	11
592	Belgaum-Dharwad via Kittur [73.10Km] (South Western Railway [SWR] - II) (706835)	Karnataka	09/2020 (03/2025)	12/2027 (03/2029)	1591 (1591)	0.38	0
593	Kumbalam-Turavur doubling project [15.59 Km] (Southern Railway [SR] - II) (705638)	Kerala	04/2023 (04/2023)	03/2027 (03/2027)	813 (802.8)	66.7	18
594	Ernakulam-Kumbalam doubling project [7.71 Km] (SR-ERS) (705639)	Kerala	04/2023 (04/2023)	03/2028 (02/2027)	601 (595.39)	289.52	19
595	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho (North Central Railway) (705480)	Madhya Pradesh	01/2007 (03/1998)	03/2027 (12/2027)	8914 (8914)	5013.49	72
596	Katni - Bina Third Railway Line [279 km] (West Central Railway WCR I) (705651)	Madhya Pradesh	06/2016 (01/2017)	03/2022 (12/2025)	2478.23 (4127.23)	3330.66	92
597	Satna-Rewa Railway Line Doubling Project (West Central Railway [WCR] - II) (705659)	Madhya Pradesh	11/2015 (08/2017)	03/2026 (03/2026)	500 (584)	565.61	80
598	Doubling of Katni - Singrauli Railway Line [261 km] (Indian Railway Construction International Limited [IRCON]) (705660)	Madhya Pradesh	03/2016 (03/2017)	12/2025 (12/2025)	2445 (4377)	3234.88	100
599	Katni Grade Separator/Bye Pass (Indian Railway Construction International Limited [IRCON]) (705661)	Madhya Pradesh	03/2016 (09/2017)	09/2024 (03/2026)	1248 (1248)	1651.34	95
600	Indore - Budni New Railway Line [198 kms] (RVNL - II) (705763)	Madhya Pradesh	08/2019 (10/2020)	09/2030 (09/2030)	7474 (7474)	1780.6	25
601	Nimach-Ratlam Doubling [133 Km] (Western Railway [WR] - II) (705933)	Madhya Pradesh	10/2021 (10/2021)	10/2027 (10/2027)	1095.88 (1095.88)	1067.49	89
602	DHULE [BORVIHIR] - NARDANA NEW LINE [50.60 KMS] (Central Railway) (400019)	Maharashtra	01/2019 (04/2023)	12/2026 (09/2027)	492.76 (1170.83)	276.86	16
603	Wardha-Nanded Via Yavatmal New BG Line (Central Railway [CR] - II) (400271)	Maharashtra	12/2017 (04/2008)	03/2028 (03/2028)	3445 (3445)	3002.93	50
604	AURANGABAD-ANKAI - DOUBLING PROJECT 98.25 Km (South Central Railway [SCR] - II) (611751)	Maharashtra	05/2023 (05/2023)	03/2027 (-)	960.64 (960.64)	511.61	1
605	Redevelopment of Chhatrapati Shivaji Maharaj Terminus [CSMT] and construction of associated infrastructure (Rail Land Development Authority) (613015)	Maharashtra	04/2023 (07/2023)	03/2027 (-)	1813 (1813)	600.75	16
606	Gondia-Balharshah [Chanda Fort] Doubling [240 Km] (South East Central Railway) (617201)	Maharashtra	04/2025 (04/2025)	03/2031 (-)	4373.04 (4373.04)	0	0
607	Doubling between Parbhani Parli Vajjanath stations 64.71 Km (South Central Railway [SCR] - II) (617215)	Maharashtra	12/2023 (12/2023)	03/2028 (-)	769.93 (769.93)	20.91	0
608	Babupeth - Sasti New Rail Line [13.114 KMS] (Central Railway [CR] - II) (617361)	Maharashtra	10/2024 (10/2024)	03/2028 (-)	362.81 (362.81)	0	0
609	Double Chord line Between Nilaje-Kopar (Central Railway [CR] - II) (617364)	Maharashtra	01/2025 (01/2025)	07/2028 (-)	338.33 (205)	3.42	0
610	Western Region Video Surveillance Project (RCIL) (705300)	Maharashtra	06/2020 (04/2023)	12/2023 (-)	227.59 (227.59)	0	0
611	Ahmednagar - Beed - Parli - Vajjnath New Broad Gauge Line Railway Project [261.3 km] (Central Railway [CR] - II) (705356)	Maharashtra	01/1999 (10/2002)	03/2026 (03/2026)	2538.67 (4957.27)	5091.94	98
612	Baramati Lonand New Line Project (Central Railway) (705357)	Maharashtra	03/2016 (03/1999)	03/2027 (03/2027)	138.48 (1843.9)	845.56	51
613	Wadsa-Gadchiroli (South East Central Railway) (705479)	Maharashtra	05/2017 (03/2012)	03/2027 (03/2027)	1886 (1886)	727.89	53
614	3rd Line Kalyan - Kasara [67.35 Kilometres] (Central Railway) (705498)	Maharashtra	09/2015 (09/2015)	12/2026 (12/2026)	792.89 (1395.79)	931.97	51
615	3rd Line Wardha - Sewagram - Nagpur (Central Railway [CR] - II) (705500)	Maharashtra	09/2015 (05/2016)	12/2025 (12/2025)	540.02 (944.24)	779.07	83
616	3rd Line Wardha - Ballarshah [132 Kilometres] (Central Railway [CR] - II) (705502)	Maharashtra	03/2016 (12/2016)	12/2025 (02/2026)	1384.72 (2033.59)	1705.4	80
617	Pune - Miraj-Londa [467 Kilometres] (Central Railway) (705503)	Maharashtra	06/2016 (06/2016)	02/2025 (08/2025)	4027.53 (4872.52)	4924.05	85
618	Doubling of Daund Manmad Line [247.6 km] (Central Railway) (705504)	Maharashtra	10/2017 (03/2017)	12/2025 (03/2026)	2081.27 (3267.06)	2861.77	92
619	4th Line Wardha - Nagpur [78.7 Kilometres] (Central Railway [CR] - II) (705505)	Maharashtra	04/2017 (05/2018)	12/2025 (02/2026)	637.95 (1341.28)	1010.3	83
620	3rd Line Manmad - Jalgaon [160 Kilometres] (Central Railway [CR] - II) (705506)	Maharashtra	05/2017 (04/2018)	12/2024 (08/2025)	1035.16 (1558.75)	1726.94	95

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
621	Solapur-tuljapur-Osmanabad (Central Railway) (705735)	Maharashtra	08/2018 (12/2023)	03/2027 (03/2028)	904.92 (3295.74)	1153.7	12
622	Nagpur- Nagbhir Railway Line Gauge Conversion Project (MRIDC) (705799)	Maharashtra	10/2019 (04/2020)	12/2025 (12/2025)	1400 (1400)	1472	80
623	Mumbai Urban Transport Project [MUTP] - PHASE II (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706779)	Maharashtra	05/2008 (04/2008)	03/2014 (12/2027)	8087 (8087)	7364	87
624	Mumbai Urban Transport Project [MUTP] Phase-III A (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706780)	Maharashtra	04/2019 (04/2019)	12/2027 (12/2027)	33690 (33690)	2436.22	16
625	Mumbai Urban Transport Project Phase-III (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706781)	Maharashtra	11/2016 (12/2016)	03/2022 (12/2026)	10947 (10947)	5460.49	65
626	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (709808)	Maharashtra	08/2022 (01/2022)	08/2027 (03/2028)	955.39 (2093.82)	130.42	11
627	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15598.11	69
628	Marikuppam - Kuppam New Line Project [23.70 Km] (South Western Railway [SWR] - II) (705491)	Multi-States (Andhra Pradesh, Karnataka)	04/2012 (10/2018)	06/2026 (06/2026)	297 (297)	134.31	15
629	Rayadurg-Tumkur via Kalyandurg New Line [207 km] (South Western Railway [SWR] - II) (705494)	Multi-States (Andhra Pradesh, Karnataka)	03/2008 (07/2010)	09/2015 (02/2028)	2496 (2496)	1739.53	69
630	Renigunta, Wadi & Gooty Bypass Railway Project (South Central Railway [SCR] - I) (705610)	Multi-States (Andhra Pradesh, Karnataka)	04/2016 (04/2016)	12/2025 (12/2025)	302 (543)	381	50
631	Doubling between Mudkhed Medchal & Mahbubnagar Dhone section 417.88 Km (South Central Railway [SCR] - II) (617212)	Multi-States (Andhra Pradesh, Maharashtra, Telangana)	08/2023 (08/2023)	03/2029 (-)	4686.09 (4686.09)	668.81	1
632	Vizianagaram - Titlagarh 3rd line [272 Km including By - pass line of 7.68 KM] (RVNL - II) (400253)	Multi-States (Andhra Pradesh, Odisha)	06/2016 (11/2016)	12/2026 (12/2026)	4803 (6670)	5722.01	89
633	Doubling of Kottavalasa-Koraput Rail Line [189 KM] (East Coast Railway [ECOR] - II) (705512)	Multi-States (Andhra Pradesh, Odisha)	12/2015 (01/2016)	03/2022 (03/2028)	2500 (2500)	2023.97	71
634	Vizianagaram-Sambhalpur 3rd Line Project (RVNL) (705520)	Multi-States (Andhra Pradesh, Odisha)	06/2016 (12/2016)	03/2025 (-)	4803.16 (4803.16)	2979.23	0
635	Tindivanam-Nagari New Line Project [184.5 km] (Southern Railway [SR] - II) (400275)	Multi-States (Andhra Pradesh, Tamil Nadu)	07/2008 (10/2008)	09/2016 (03/2028)	3631 (3631)	1113.53	18
636	Doubling between Motumari Vishnupuram - 88.81 Km and Rail over Rail - RoR at Motumari - 10.877 Km (South Central Railway [SCR] - II) (616857)	Multi-States (Andhra Pradesh, Telangana)	02/2024 (03/2025)	03/2029 (-)	1595.55 (1595.55)	14.27	1
637	Doubling of Guntur Bibinagar 239 Km (South Central Railway [SCR] - II) (617211)	Multi-States (Andhra Pradesh, Telangana)	08/2023 (08/2023)	03/2029 (-)	2853.23 (2853.23)	62.29	1
638	Rail Connectivity to Errupalem Amravati Namburu 57 Km (South Central Railway [SCR] - II) (617214)	Multi-States (Andhra Pradesh, Telangana)	11/2024 (11/2024)	03/2027 (-)	2047.4 (2047.4)	14.49	0
639	Kazipet-Vijayawada 3rd line with electrification [220 km] (South Central Railway [SCR] - II) (705612)	Multi-States (Andhra Pradesh, Telangana)	03/2013 (08/2014)	02/2025 (12/2025)	1953 (3363)	3436.15	94
640	Vijayawada - Kazipet Bypass line (South Central Railway [SCR] - II) (705632)	Multi-States (Andhra Pradesh, Telangana)	04/2016 (04/2016)	01/2025 (12/2025)	647 (904)	945.51	92
641	Murkongselek-Pasighat (Northeast Frontier Railway (NFR) - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (03/2023)	03/2025 (05/2026)	435 (1250)	542.07	61
642	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
643	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5571.82	81
644	New Delhi- Howrah Speed Booster[160Kmph] Project (PCE/NCR) (705794)	Multi-States (Bihar, Delhi, Jharkhand, Uttar Pradesh, West Bengal)	09/2019 (09/2019)	03/2024 (-)	6684.81 (6684.81)	127.03	0
645	Third Railway Line between Patratu-Sonnagar [281 kms] (RVNL - II) (400234)	Multi-States (Bihar, Jharkhand)	11/2016 (08/2018)	03/2026 (07/2026)	8975 (8975)	4950	88
646	Multi tracking of Son Nagar-Andal 374.53 rkm & 814.38 tkm (East Central Railway [ECR] - I) (616699)	Multi-States (Bihar, Jharkhand)	08/2023 (08/2023)	03/2028 (-)	12333.57 (12333.6)	520.39	13
647	Koderma-Tilaiya New Line (East Central Railway [ECR] - I) (705375)	Multi-States (Bihar, Jharkhand)	11/2004 (03/2002)	02/2025 (02/2026)	1626 (2486.62)	2113.82	93
648	Pirpainti - Jasidih [100.52 Km] New BG line (Eastern Railway [ER] - I) (705385)	Multi-States (Bihar, Jharkhand)	03/2014 (03/2022)	03/2028 (03/2028)	2555 (2555)	780.18	49
649	NER Provision of Automatic Block Signalling on Gorakhpur Cantt[Excl] Chhapra Gramin & Burhwal Jn [Excl] Sitapur Jn section of high density routes (North Eastern Railway [NER]) (611669)	Multi-States (Bihar, Uttar Pradesh)	NA (06/2023)	03/2027 (-)	380.47 (380.47)	24.53	0

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
650	Gorakhpur-Valmikinagar Doubling project (NER) (617224)	Multi-States (Bihar, Uttar Pradesh)	08/2023 (03/2024)	12/2027 (-)	1120 (1120)	247.46	26
651	Chhapra-Ballia Patch Doubling (North Eastern Railway [NER]) (705562)	Multi-States (Bihar, Uttar Pradesh)	03/2013 (12/2015)	02/2025 (03/2026)	963 (1046)	911.66	95
652	Katihar - Kumedpur Doubling Line Project (GM/C/ NFR) (706844)	Multi-States (Bihar, West Bengal)	08/2022 0	08/2027 (08/2027)	942 (942)	356	45
653	Rajnandgaon - Nagpur [Kalumna] Third Railway Line [228.30 km] (South East Central Railway [SECR] - II) (705617)	Multi-States (Chhattisgarh, Maharashtra)	09/2016 (12/2016)	12/2024 (06/2026)	3545 (3545)	3507.04	96
654	Sardega -Bhalumuda New Double line [37.24 Km] (SECR) (617390)	Multi-States (Chhattisgarh, Odisha)	09/2024 (09/2024)	03/2028 (-)	1281.81 (1281.81)	128	1
655	Jagdulpur-Koraput (East Coast Railway [ECoR] - II) (705511)	Multi-States (Chhattisgarh, Odisha)	12/2015 (03/2016)	03/2024 (12/2026)	1547 (1547)	1329.73	90
656	Jharsuguda-Bilaspur Fourth Railway Line [206 km] (SECR) (705616)	Multi-States (Chhattisgarh, Odisha)	09/2016 (09/2016)	10/2024 (12/2025)	2140 (2979)	2196.74	93
657	Mumbai-Ahmedabad High Speed Rail Project- 508 km (National High Speed Rail Corporation [NHSRC]) (705728)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	03/2015 (09/2017)	08/2027 (12/2029)	108000 (108000)	82967.89	55
658	New Delhi- Mumbai Speed Booster[160Kmph] Project (PCE/WR) (705793)	Multi-States (Delhi, Gujarat, Madhya Pradesh, Maharashtra, Rajasthan)	09/2019 (09/2019)	03/2024 (-)	6806.44 (6806.44)	135.65	0
659	Hospet - Tinaighat - Vasco Rail Doubling Project (RVNL - II) (705650)	Multi-States (Goa, Karnataka)	03/2010 (07/2012)	03/2027 (12/2027)	5060 (5060)	5246.91	86
660	Hospet-Hubli-Vasco da Gama Line Electrification Project (RVNL) (706950)	Multi-States (Goa, Karnataka)	07/2015 (05/2018)	03/2023 (03/2024)	744.49 (1122.62)	969.05	95
661	Western Dedicated Freight Corridor (DFCCIL) (705237)	Multi-States (Gujarat, Haryana, Maharashtra, Rajasthan, Uttar Pradesh)	02/2008 (01/2012)	03/2022 (12/2025)	51101 (124005)	124623	96
662	New line Dahod-Indore via Sardarpur, Jabuwa and Dhar (Western Railway [WR] - II) (705453)	Multi-States (Gujarat, Madhya Pradesh)	06/2012 (06/2012)	02/2027 (02/2027)	456.07 (3516.77)	3633.27	49
663	Chhota Udaipur - Dhar New Line Project [157 km] (Western Railway [WR] - II) (705454)	Multi-States (Gujarat, Madhya Pradesh)	11/2008 (01/2014)	12/2025 (12/2025)	1794 (1794)	1815.94	80
664	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (Western Railway) (611452)	Multi-States (Gujarat, Maharashtra)	09/2019 (03/2023)	12/2025 (06/2025)	311 (311)	208	92
665	Taranga Hill-Abu Road via Ambaji (North Western Railway [NWR]) (400022)	Multi-States (Gujarat, Rajasthan)	07/2022 (07/2022)	07/2030 (07/2030)	2798 (2798)	2014.6	17
666	LUNI- SAMDARI- BHILDI DOUBLING (North Western Railway [NWR]) (616842)	Multi-States (Gujarat, Rajasthan)	02/2024 (02/2024)	07/2027 (-)	3085.59 (3085.59)	329.31	13
667	Chandigarh-Baddi New Rail Line- 36 km (Northern Railway [NR]) (705424)	Multi-States (Haryana, Himachal Pradesh)	02/2018 (02/2018)	12/2026 (12/2026)	1540 (1540.13)	527.66	34
668	Rewari - Kathuwas Doubling Project [27.72 Km] (North Western Railway [NWR]) (611861)	Multi-States (Haryana, Rajasthan)	02/2023 (12/2022)	06/2027 (06/2027)	352 (352)	271.93	65
669	Nangal Dam-Talwara New Broad Gauge Line [84 KM] and Taking Over Siding Mukerian-Talwara [29 KM] (Northern Railway [NR]) (705410)	Multi-States (Himachal Pradesh, Punjab)	03/1983 (05/1985)	12/2025 (01/2027)	2018 (2018)	2053.9	45
670	Bhanupalli-Bilaspur-Beri New Railway Line Project (RVNL - II) (705428)	Multi-States (Himachal Pradesh, Punjab)	03/2009 (04/2015)	12/2026 (12/2027)	13447 (13447)	6928.81	61
671	Doubling of Hatia [Ranchi]-Bondamunda Rail Line - 159 km (South Eastern Railway - JH) (705628)	Multi-States (Jharkhand, Odisha)	03/2016 (02/2017)	06/2025 (06/2026)	3029 (3029.04)	2501.09	86
672	Buramara-Chakulia new line [59.96 km] (South Eastern Railway [SER] - I) (616588)	Multi-States (Jharkhand, Odisha, West Bengal)	08/2024 (12/2024)	12/2029 (-)	1459.13 (1459.13)	3.32	0
673	KHARAGPUR-ADITYAPUR THIRD RAIL LINE- 132 KM (RVNL - I) (705668)	Multi-States (Jharkhand, West Bengal)	09/2016 (01/2018)	03/2025 (12/2025)	3250 (3250)	3176.46	97
674	Hotgi-Kudgi-Gadag Doubling Project (South Western Railway [SWR] - II) (705662)	Multi-States (Karnataka, Maharashtra)	04/2014 (01/2016)	12/2024 (03/2026)	1878 (2459)	2684.66	92
675	Baiyyappanahalli - Hosur Doubling Project [48 km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703586)	Multi-States (Karnataka, Tamil Nadu)	04/2019 (02/2019)	03/2024 (01/2026)	498.7 (748.7)	630.41	86
676	Trivandrum- Kanyakumari (Southern Railway (SR) - I) (705635)	Multi-States (Kerala, Tamil Nadu)	08/2017 (03/2016)	03/2025 (12/2026)	1432 (3785.45)	2505.8	50
677	Ratlam-Mhow-Khandwa-Akola Gauge Conversion (Western Railway [WR] - II) (705457)	Multi-States (Madhya Pradesh, Maharashtra)	04/2008 (03/2010)	03/2027 (09/2028)	1656.25 (6499.86)	4445.82	81

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
678	Itarsi - Nagpur Third Railway Line [280 km] (Central Railway (CR) - II) (705507)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016 (09/2016)	03/2027 (03/2027)	2449.91 (2506.68)	1850.73	51
679	RATLAM- DUNGARPUR VIA BANSWARA NEW LINE PROJECT (North Western Railway [NWR]) (617406)	Multi-States (Madhya Pradesh, Rajasthan)	10/2015 (05/2023)	03/2028 (-)	2417.24 (2417.24)	5.66	7
680	Gwalior - Seopurkala with extension to Kota [Gauge Conversion] (North Central Railway) (705419)	Multi-States (Madhya Pradesh, Rajasthan)	03/2011 (07/2018)	03/2025 (02/2026)	2913 (2913)	2109.86	84
681	Ramganjmandi-Bhopal New Line Project [262 km] (West Central Railway [WCR] - II) (705481)	Multi-States (Madhya Pradesh, Rajasthan)	03/2001 (10/2004)	12/2025 (12/2027)	3032 (5073)	3723.61	70
682	Nimach-Badi Sadri New Rail Line Project (Western Railway [WR] - II) (705764)	Multi-States (Madhya Pradesh, Rajasthan)	04/2017 (09/2021)	03/2026 (06/2026)	495 (825)	123.77	57
683	Mathura-Jhansi Third Railway Line [274 Km] (RVNL - II) (705667)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	12/2015 (03/2018)	12/2024 (12/2026)	5961 (5961)	4964.19	94
684	Jhansi - Bina Third Railway Line [153 Km] (CAO/C/NCR) (705598)	Multi-States (Madhya Pradesh, Uttar Pradesh)	09/2016 (03/2018)	03/2022 (03/2026)	2002 (2002)	1806.86	93
685	Jhansi-Khairar-Manikpur & Khirar-Bhimsen (North Central Railway) (705608)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2018 (04/2019)	03/2026 (03/2026)	4330 (4330)	2417.11	60
686	Third Line [new] between Kazipet - Balharshah with electrification [201.04 Km] (South Central Railway [SCR] - II) (705613)	Multi-States (Maharashtra, Telangana)	09/2016 (10/2016)	01/2025 (11/2025)	2595 (3071)	3396.31	94
687	Narayangarh-Bhadrak 3rd line (South Eastern Railway [SER] - I) (705629)	Multi-States (Odisha, West Bengal)	03/2019 (03/2017)	12/2025 (06/2026)	2400 (2400)	2311.95	66
688	Nagapattinam-Tiruturaipundi and Karaikal-Peralam New Line (Southern Railway [SR] - II) (400223)	Multi-States (Puducherry, Tamil Nadu)	07/2008 (01/2019)	03/2026 (03/2027)	713 (981)	598.38	80
689	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Multi-States (Sikkim, West Bengal)	10/2009 (05/2010)	05/2015 (12/2027)	7877 (12133)	9039.91	84
690	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass Line Project (Eastern Railway [ER] - I) (602797)	Multi-States (Uttar Pradesh, West Bengal)	08/2017 (12/2017)	03/2027 (03/2027)	461.64 (461.64)	192.72	8
691	Proposed 6 nos Road Over Bridge [ROB] at different locations under MCL Talcher Under Deposit Scheme. (East Coast Railway [ECoR] - II) (400045)	Odisha	08/2022 (07/2022)	03/2025 (01/2025)	168.32 (168.32)	69.85	82
692	Brundamal-Jharsuguda- flyover connection for joining downline (East Coast Railway [ECoR] - II) (400232)	Odisha	01/2014 (01/2014)	12/2026 (12/2026)	297 (297)	193.22	30
693	3rd & 4th line between Sarla - Sason [8 km] [PB 73/2023-24/NR] (East Coast Railway [ECoR] - II) (612834)	Odisha	04/2023 (04/2023)	12/2025 (-)	252 (252)	88.95	48
694	Bangriposi-Gorumahisani new line [85.60 km] (CAO/C/SER) (616586)	Odisha	08/2024 (09/2025)	12/2029 (-)	2269.49 (2269.49)	3.06	0
695	Badampahar-Kendujhargarh new line [82.06 km] (CAO/C/SER) (616587)	Odisha	08/2024 (09/2025)	12/2029 (-)	1875.72 (1875.72)	0.91	0
696	Paradeep - Badabandha 3rd & 4th Line / 18.51kms (East Coast Railway [ECoR] - II) (616695)	Odisha	08/2023 (04/2025)	11/2028 (-)	300.15 (300.15)	0	0
697	Jeypore - Malkangiri New BG Line Project (Indian Railways) (617290)	Odisha	NA (02/2018)	12/2030 (-)	2343.64 (2343.64)	630.83	13
698	New B.G Railway Line between Jeypore & Navarangpur [38 Km] with Electrification (Indian Railway and Govt of Odisha) (617320)	Odisha	07/2017 (09/2022)	09/2025 (-)	747.91 (747.91)	7.21	0
699	Khurda-Bolangir New Broad Gauge Rail Link [301km] (East Coast Railway [ECoR] - II) (705358)	Odisha	03/1994 (03/2001)	12/2026 (12/2026)	3792 (5089)	5147.89	89
700	Talcher-Bimlagarh New Railway Line (East Coast Railway [ECoR] - II) (705359)	Odisha	03/2004 (12/2004)	03/2025 (03/2027)	1928 (1928)	1955.9	48
701	Bhadrak-Nergundi Third Line (East Coast Railway [ECoR] - II) (705510)	Odisha	10/2015 (04/2015)	11/2024 (01/2026)	1284 (1284)	1298	80
702	Koraput - Singapur Railway Doubling (East Coast Railway [ECoR] - II) (705513)	Odisha	12/2015 (12/2015)	12/2027 (03/2028)	2362 (2362)	1825.42	70
703	Jarapada- Budhapank with flyover at Talcher road 3rd and 4th Line (East Coast Railway [ECoR] - II) (705514)	Odisha	11/2015 (12/2015)	11/2018 (03/2026)	1000 (810.02)	415.46	58
704	3rd & 4th Railway Line Project from Salegaon to Budhapank via Rajathgarh. (East Coast Railway [ECoR] - II) (705515)	Odisha	07/2013 (12/2015)	03/2026 (03/2026)	1173 (2092)	1971	80
705	Jeypore-Navarangpur New Rail Line Project (East Coast Railway [ECoR] - II) (705741)	Odisha	07/2017 (04/2023)	07/2028 (12/2029)	748 (748)	12.06	1
706	Jeypore-Malkanagiri New Railway Line Project (East Coast Railway [ECoR] - II) (705742)	Odisha	02/2018 (12/2023)	07/2033 (07/2033)	2344 (2344)	489.57	20
707	Khurda Road - Balangir Electrification of Railway Track Project (Ministry of Railways) (706898)	Odisha	09/2018 (09/2019)	03/2021 (-)	267.61 (267.61)	0	0



All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
708	Godhani-Kalumna Chord 13.7 km (Ministry of Railways) (617321)	Offshore	07/2018 (07/2018)	07/2028 (-)	150000 (150000)	1940	11
709	Jaynagar-Bijalpura, incl. extn. Bet, Bijalpura-Bardibas [Nepal] (East Central Railway [ECR] - I) (705362)	Offshore	08/2015 (03/2011)	03/2022 (03/2026)	819 (819)	580.51	75
710	Ludhiana- Killa Raipur Railway Doubling Project (Railway) (705783)	Punjab	03/2019 (12/2022)	03/2025 (03/2026)	237.64 (238)	134.48	50
711	Dedicated Test Track for RDSO Phase II (North Western Railway [NWR]) (611614)	Rajasthan	11/2021 (11/2021)	11/2026 (11/2026)	819.48 (967.06)	471	86
712	Devgarh Madariya - Nathdwara Gauge Conversion [82.54 Km] part of Marwar - Mavli Gauge Conversion [152 Km] (North Western Railway [NWR]) (611849)	Rajasthan	01/2023 (01/2023)	06/2028 (06/2028)	968.92 (968.92)	137.16	51
713	Maintenance cum workshop depot for Vande Bharat Sleeper Trains as per conditions under WTA 527 (WPO/Patna) (611929)	Rajasthan	09/2022 (06/2023)	12/2024 (-)	166.86 (166.86)	0	0
714	PUSHKAR- MERTA CITY NEW LINE (North Western Railway [NWR]) (616841)	Rajasthan	02/2024 (02/2024)	12/2026 (-)	799.64 (799.64)	14.64	4
715	AJMER- CHANDERIYA DOUBLING (North Western Railway [NWR]) (616843)	Rajasthan	02/2024 (02/2024)	06/2027 (-)	1634.79 (1634.79)	123.05	7
716	SADULPUR - CHURU DOUBLING PROJECT (North Western Railway [NWR]) (617403)	Rajasthan	01/2024 (01/2024)	06/2026 (-)	468.64 (468.64)	125.08	50
717	POKHRAN - RAMDEVRA New Line (North Western Railway [NWR]) (617404)	Rajasthan	04/2025 (04/2025)	03/2028 (-)	189.21 (189.21)	0	0
718	NATHDWARA- NATHDWARA TOWN NL (North Western Railway [NWR]) (617408)	Rajasthan	03/2019 (04/2024)	03/2027 (-)	166.33 (166.33)	81.41	1
719	Dholpur - Sirmuttra Gauge Conversion (North Central Railway) (705482)	Rajasthan	03/2022 (04/2020)	02/2019 (02/2027)	747 (747)	378.05	44
720	Gudha-Thatha Mithri Construction of Railway Track Project (North Western Railway [NWR]) (705752)	Rajasthan	04/2019 (04/2019)	11/2026 (11/2026)	819.48 (967.06)	384.28	99
721	Sawai Madhopur-Jaipur Railway Line Project (North Western Railway [NWR]) (705912)	Rajasthan	02/2024 (04/2023)	03/2027 (-)	1203.89 (1203.89)	94.76	12
722	Agra Fort-Bandikui Doubling Line Project (CAO/C/NCR) (705919)	Rajasthan	06/2022 (02/2021)	06/2027 (06/2027)	1390 (1390)	123	25
723	Sawaimadhopur Bye Pass Line Project (North Western Railway [NWR]) (706866)	Rajasthan	12/2022 (01/2023)	03/2026 (05/2027)	304 (304)	51.64	45
724	Ph II extension of MRTS from Velachery to St Thomas Mount (Southern Railways [SR] - construction) (400280)	Tamil Nadu	11/2007 (11/2008)	07/2024 (08/2025)	734 (982)	475.73	99
725	Redevelopment of Chennai Egmore Station (Railway) (613002)	Tamil Nadu	05/2022 (10/2022)	03/2026 (-)	842 (842)	340	0
726	Coach Production Factory Upgradation Project (CPM/ICF) (705244)	Tamil Nadu	12/2017 (07/2018)	12/2021 (-)	520 (520)	192.25	0
727	Doubling between Bhadrachalam Road and Dornakal (South Central Railway [SCR] - II) (616856)	Telangana	08/2023 (04/2025)	04/2029 (-)	770.12 (770.12)	16.34	0
728	Railway Manufacturing Unit (South Central Railway [SCR] - II) (617409)	Telangana	07/2016 (02/2023)	12/2026 (-)	521.36 (521.36)	420	58
729	Kazipet Wagon Overhauling Project (RVNL) (705252)	Telangana	09/2017 (07/2017)	12/2023 (-)	385 (385)	0	0
730	Manoharabad-Kothapalli New Rail Line [151 km] (South Central Railway [SCR] - II) (705437)	Telangana	07/2016 (01/2017)	03/2027 (12/2027)	1160 (2781)	1985.73	71
731	Bahraich-Shravasti-Balrampur-Siddharthnagar -Santkabar nagar (North Eastern Railway [NER]) (400204)	Uttar Pradesh	10/2018 (03/2017)	10/2030 (10/2030)	4939.78 (4939.78)	1251.81	8
732	Sahjanwa-Dohrighat (North Eastern Railway [NER]) (400205)	Uttar Pradesh	08/2019 (03/2017)	03/2029 (03/2029)	1319.75 (1319.75)	475.67	3
733	Anandnagar - Ghugli via Maharajganj New line 52.7 km (Construction NER) (617252)	Uttar Pradesh	10/2023 (11/2023)	03/2028 (-)	958.27 (958.27)	449.37	23
734	Chunar-Chopan doubling project (North Central Railway) (617284)	Uttar Pradesh	08/2023 (01/2025)	03/2028 (-)	1423.96 (1423.96)	53.81	4
735	Surface triangle line bet. Bhadura stn and new crossing stn Karma (East Central Railway [ECR] - I) (617333)	Uttar Pradesh	10/2022 (05/2024)	02/2027 (-)	199.96 (199.96)	0	0
736	Doubling between Jaunpur Jn - Zaffarabad 6.28 km (M/S SRC company Infra Private Limited) (617370)	Uttar Pradesh	03/2023 (02/2025)	01/2027 (-)	180.66 (180.66)	4	11
737	Burhwal Gonda 3rd line (North Eastern Railway [NER]) (705567)	Uttar Pradesh	11/2017 (07/2019)	03/2025 (01/2026)	1016 (1118)	1410.08	88

All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
738	Janghai-Pratapgarh- Amethi (CAO/C/II/INR) (705588)	Uttar Pradesh	11/2017 (03/2017)	03/2025 (03/2026)	722 (1194)	1567	70
739	Lalitpur-Birari with flyover at Lalitpur- 16 Km (North Central Railway) (705766)	Uttar Pradesh	03/2017 (11/2017)	12/2024 (01/2026)	304.44 (356)	231.37	78
740	Allahabad-Bamhraulii Flyover Construction & 4th Railway Line Project (North Central Railway) (705771)	Uttar Pradesh	04/2019 (10/2020)	03/2026 (03/2026)	494 (494)	333	70
741	Mughalsarai-Allahabad, 3rd line (North Central Railway) (705772)	Uttar Pradesh	12/2015 (03/2016)	12/2026 (03/2027)	2649 (2649.44)	1561.89	62
742	Aligarh -Daud Khan Flyover Construction & 3rd Railway Line Project (CAO/C/NCR) (705774)	Uttar Pradesh	04/2019 (09/2020)	01/2025 (03/2027)	758 (779.49)	387.73	69
743	Bhandai - Flyover for Etawah bound down train- 10 Km (North Central Railway (NCR) - II) (705777)	Uttar Pradesh	07/2020 (04/2021)	02/2026 (02/2027)	250.18 (250.18)	115.05	8
744	Phephna-Indara, Mau-Shahganj doubling excluding Indara-Mau (RVNL - I) (705779)	Uttar Pradesh	05/2017 (10/2019)	12/2024 (03/2026)	1178 (1777)	1489.5	85
745	Bhatni-Aurnihar with electrification excluding Indara-Mau (RVNL - I) (705780)	Uttar Pradesh	03/2018 (03/2017)	12/2024 (10/2025)	2529 (2529.46)	2051.69	94
746	Barabanki-Malhaur 3rd & 4th Railway Line Project (CAO/C/INR) (705782)	Uttar Pradesh	01/2019 (04/2017)	03/2025 (03/2026)	407 (407)	317	75
747	Janghai-Phaphamau Doubling Rail Line Project (RVNL) (705784)	Uttar Pradesh	11/2018 (03/2020)	03/2025 (03/2025)	357 (978.77)	579	95
748	Rishikesh-Karnaprayag New Rail Line- 125 km (RVNL - I) (705429)	Uttarakhand	11/2016 (08/2018)	12/2025 (03/2027)	38953 (38953)	24645.15	65
749	Kalinarayanpur-Krishnanagar Doubling Alongwith Krishnanagar - Chapra New Line And Naihati-Ranaghat 3rd Line. (Eastern Railway [ER] - I) (400247)	West Bengal	07/2015 (11/2005)	02/2027 (02/2027)	1000 (1000)	1053.4	69
750	Tarakeshwar-Bishnupur New Line [82.47 km] (Eastern Railway [ER] - I) (400273)	West Bengal	03/2001 (02/2008)	03/2019 (02/2026)	1189 (1542)	1323.68	91
751	Dum Dum Airport-New Garia via Rajarhat-Construction of Metro Railway (RVNL - II) (400277)	West Bengal	03/2010 (10/2011)	12/2025 (03/2026)	8964 (8964)	8316.32	81
752	Construction of Balurghat-Hilli new BG Line (Northeast Frontier Railway [NFR]) (612096)	West Bengal	12/2010 (12/2010)	03/2027 (03/2025)	1209 (1209)	405.31	9
753	SER Upgradation of maintenance infrastructure at Shalimar into Vande Bharat Chair Car maintenance cum workshop depot. (South Eastern Railway - JH) (617345)	West Bengal	NA (12/2024)	10/2026 (-)	226.87 (226.87)	0.21	5
754	Joka-BBD Bag new metro project (RVNL - II) (705730)	West Bengal	03/2010 (04/2010)	12/2026 (12/2029)	4835 (10362)	4634.68	59
755	Noapara-Barasat via Bimanbandar - Construction of Metro railway [18 km] (Metro Railway, Kolkata) (706776)	West Bengal	11/2010 (03/2010)	08/2026 (03/2029)	4830 (4830)	2764.13	32
756	Baranagar-Barrackpore and Dakshineshwar- Construction of Metro Railway (RVNL - II) (706777)	West Bengal	03/2010 (03/2010)	12/2026 (12/2025)	2298 (2734)	393.01	17
Total (257)					839222.35	536735.17	
Department for Promotion of Industry & Internal Trade							
Real Estate							
757	Krishnapatnam Node - Phase 1 - Roads and Services Development (National Industrial Corridor Development Corporation) (701658)	Andhra Pradesh	12/2020 (02/2024)	02/2028 (-)	2139.44 (2139.44)	472.8	21
758	Tumakuru Node - Phase 1 - Roads and Services Development (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (701657)	Karnataka	12/2020 (02/2023)	09/2026 (-)	1701.81 (1701.81)	117.35	10
Total (2)					3841.25	590.15	
Department of Telecommunications							
Telecommunication							
759	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance (Erstwhile NICF)) (709859)	Delhi	10/2014 (04/2018)	02/2020 (10/2025)	248.2 (248.2)	236.91	98
760	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (03/2026)	971.96 (971.96)	208.25	99
761	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase 1 Upgradation (Department of Telecommunications [DoT]) (617413)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	04/2022 (05/2024)	05/2025 (11/2025)	1884.6 (1884.6)	100	67

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
762	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 (Department of Telecommunications [DoT]) (701599)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	NA (09/2021)	03/2023 (11/2025)	1577.57 (1577.57)	600.6	87
763	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha (Department of Telecommunications [DoT]) (701602)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	11/2021 (05/2022)	11/2023 (11/2025)	3685 (3685)	1135.28	81
764	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (03/2026)	1255.49 (1255.49)	284.04	91
765	354 Uncovered Villages Scheme (Department of Telecommunications [DoT]) (701600)	Multi-States (Bihar, Gujarat, Himachal Pradesh, Jammu and Kashmir, Ladakh, Rajasthan, Uttar Pradesh)	12/2019 (04/2020)	10/2021 (08/2025)	336.89 (301.13)	227.82	97
766	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajasthan and Uttar Pradesh (Department of Telecommunications [DoT]) (704495)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	NA (03/2021)	03/2022 (12/2025)	421.65 (228.94)	142.01	96
767	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (709749)	Multi-States (Maharashtra, Telangana)	03/2020 (03/2020)	06/2021 (12/2025)	461.42 (461.42)	166.02	81
768	Saturation 4G mobile coverage of Uncovered Villages through USOF (Department of Telecommunications [DoT]) (400013)	PAN India	07/2022 (07/2022)	06/2024 (03/2026)	26316 (30620)	9791.8	76
769	4G Services by BSNL (Department of Telecommunications [DoT]) (701593)	PAN India	11/2020 (11/2020)	03/2024 (03/2026)	28466 (19592)	8419.04	96
770	BharatNet (Department of Telecommunications [DoT]) (706775)	PAN India	07/2017 (10/2011)	08/2023 (03/2027)	61109 (188000)	46431.54	81
771	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (709856)	PAN India	05/2023 (05/2023)	08/2024 (10/2025)	645.13 (645.13)	377.27	92
772	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. (BSNL) (709857)	PAN India	05/2023 (06/2023)	06/2025 (03/2026)	24544.55 (24544.5)	8448.06	97
773	OPTICAL TRANSPORT NETWORK [OTN] PH-4 IN BSNL (BSNL) (709858)	PAN India	02/2024 (02/2024)	08/2025 (11/2025)	810.99 (810.99)	786.3	100
	Total (15)				152734.45	77354.94	
	Department of Water Resources, River Development & GR						
	Waste & Water						
774	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616600)	Bihar	10/2017 (03/2022)	02/2025 (12/2025)	413.29 (413.29)	126.67	97
775	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616611)	Bihar	08/2017 (07/2019)	12/2025 (-)	824 (824)	396.71	56
776	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616612)	Bihar	08/2017 (07/2019)	12/2025 (-)	578.89 (578.89)	171.79	54
777	Sewer Network, SPS and STP at Begusarai (National Mission for Clean Ganga) (616615)	Bihar	03/2010 (03/2018)	04/2025 (12/2025)	230.06 (230.06)	261.82	97
778	Sewer Networks, SPS and STP at Hajipur (National Mission for Clean Ganga) (616616)	Bihar	03/2010 (03/2018)	06/2025 (12/2025)	305.19 (305.19)	346.46	95
779	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme (National Mission for Clean Ganga) (616594)	Uttar Pradesh	05/2020 (04/2023)	04/2025 (12/2025)	842.25 (842.25)	208.64	75
780	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP (National Mission for Clean Ganga) (616605)	Uttar Pradesh	05/2020 (11/2024)	12/2024 (05/2027)	690.71 (690.71)	34.79	34
781	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP (National Mission for Clean Ganga) (616604)	West Bengal	05/2018 (12/2021)	03/2025 (12/2025)	154.73 (154.73)	96.17	92
	Total (8)				4039.12	1643.05	



All Ongoing Projects

OCTOBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Water Resources						
782	Sardar Gouthu Latchanna Thotapalli Barrage Project (<i>Water Resources-AP</i>) (400100)	Andhra Pradesh	04/2005 (01/2006)	12/2019 (06/2026)	353.05 (1023.24)	869.11	95
783	Gundlakamma project (<i>Water Resources-AP</i>) (400101)	Andhra Pradesh	04/2005 (04/2005)	12/2019 (03/2027)	397.41 (697.39)	619.09	98
784	Polavaram Irrigation Project (<i>Water Resources-AP</i>) (701415)	Andhra Pradesh	01/2009 (11/2009)	04/2022 (03/2026)	10151.04 (55548.9)	24837.97	84
785	Borolia Irrigation Project (<i>Department of Water Resources, River Development & GR</i>) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55
786	Punpun Barrage Project (<i>Water Resources-BR</i>) (400104)	Bihar	04/2007 (04/2007)	12/2019 (03/2026)	571.07 (658.12)	447.68	44
787	Kelo Irrigation Project (<i>Water Resources-CT</i>) (400111)	Chhattisgarh	04/2008 (04/2008)	12/2019 (06/2026)	459.97 (727.04)	616.93	72
788	Kudali Irrigation Project (<i>Department of Water Resources, River Development & GR</i>) (701399)	Chhattisgarh	04/2009 (12/2009)	12/2025 (-)	382.29 (382.29)	239.03	86
789	Sardar Sarovar CADWM Project (<i>Narmada and Water Resources, Water Supply and Kalpsar Department-GJ</i>) (400097)	Gujarat	04/2017 (04/2017)	12/2019 (03/2026)	5021.76 (6670.31)	4954.99	90
790	Sardar Sarovar Project (<i>Narmada and Water Resources, Water Supply and Kalpsar Department-GJ</i>) (701372)	Gujarat	04/1996 (04/1996)	12/2019 (03/2026)	20718.17 (33412.5)	31860.86	93
791	Subernarekha Multipurpose Project, Jharkhand (<i>Department of Water Resources-JH</i>) (701376)	Jharkhand	04/2011 (01/2012)	12/2019 (03/2026)	3807.77 (9579.58)	5790.29	70
792	Upper Tunga Irrigation Project (<i>Water Resources-KA</i>) (701377)	Karnataka	04/2014 (04/2014)	12/2019 (03/2026)	770.16 (1606.07)	1515.32	99
793	Omkareshwar CADWM Project (<i>Water resource-mp</i>) (400096)	Madhya Pradesh	04/2017 (04/2017)	12/2019 (03/2026)	648.09 (648.09)	172.56	3
794	Bargi Diversion Project Phase - IV [km. 154 to km 197] (<i>Water Resources-MP</i>) (400115)	Madhya Pradesh	04/2008 (01/2009)	12/2019 (03/2026)	751.03 (893.35)	783.1	75
795	Bargi Diversion Project Phase - III [km. 104 to km 154] (<i>Water Resources-MP</i>) (400116)	Madhya Pradesh	04/2007 (04/2007)	12/2019 (03/2026)	1229.15 (1399.7)	1937.25	80
796	Gosikhurd CADWM Project (<i>Department of water resources-MH - II</i>) (400095)	Maharashtra	04/2017 (04/2017)	12/2019 (06/2026)	743.73 (743.73)	295.12	52
797	Urmodi Irrigation Project (<i>Department of water resources-MH - II</i>) (400105)	Maharashtra	04/2017 (04/2018)	06/2022 (12/2026)	580.79 (895.81)	713.46	76
798	Sulwade-Jamphal-Kanoli Lift Irrigation Scheme (<i>Department of water resources-MH - II</i>) (400107)	Maharashtra	04/2017 (02/2019)	06/2023 (06/2027)	2407.67 (2407.67)	2570.94	80
799	Purna Barrage-2 [Ner Dhamana] Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (400109)	Maharashtra	04/2017 (04/2018)	06/2020 (06/2026)	848.07 (888.43)	690.49	69
800	Jigaon Irrigation Project (<i>Department of water resources-MH - II</i>) (400112)	Maharashtra	04/2017 (04/2018)	06/2028 (-)	7222.95 (7222.95)	8722.81	90
801	Bodwad Parisar Sinchan Yojna (<i>Department of Water Resources-MH</i>) (617422)	Maharashtra	05/2002 (01/2017)	07/2027 (-)	1923.81 (1923.81)	1770.13	49
802	Waghur Project (<i>Department of water resources-MH - II</i>) (701383)	Maharashtra	04/1996 (04/1996)	12/2019 (03/2026)	1058.99 (1758.51)	1557.45	89
803	Gosikhurd Project (<i>Department of water resources-MH - II</i>) (701386)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2028)	7196.47 (12770.1)	13765.22	72
804	Aruna Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (701391)	Maharashtra	04/2009 (01/2010)	12/2019 (12/2025)	210.45 (1472.14)	1697.94	97
805	Lower Pedhi Project (<i>Department of water resources-MH - II</i>) (701396)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2026)	255.97 (1480.7)	1324.98	65
806	Nardave Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (701398)	Maharashtra	04/2009 (04/2009)	12/2019 (06/2026)	211.46 (781.85)	623.5	72
807	Thoubal Multipurpose Project (<i>Water Resources Department-MN</i>) (701400)	Manipur	04/1997 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
808	North Koel Reservoir Project (<i>Department of Water Resources, River Development & GR</i>) (701412)	Multi-States (Bihar, Jharkhand)	08/2017 (01/2021)	03/2021 (03/2026)	1622.27 (2430.76)	151.04	32
809	Integrated Anandpur Barrage Project (<i>Water Resources-OR</i>) (603945)	Odisha	04/1997 (01/1998)	12/2019 (06/2026)	567.03 (2990.05)	2629.74	62
810	Kanupur Irrigation Project (<i>Irrigation and CAD-TG</i>) (701404)	Odisha	04/2003 (01/2004)	12/2019 (06/2026)	989.43 (2301.28)	2712.75	79
811	Relining of Rajasthan feeder and Sirhind Feeder canal (<i>Department of Water Resources-PB</i>) (701410)	Punjab	02/2016 (04/2018)	06/2021 (06/2026)	1441.26 (2462.16)	3012.69	80

All Ongoing Projects							OCTOBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
812	Shahpur Kandi Dam Project (Department of Water Resources-PB) (701411)	Punjab	02/2010 (04/2018)	06/2022 (10/2025)	2285.81 (2715.7)	2169.72	88
813	Sri Ram Sagar Project Stage - II (Irrigation and CAD-TG) (400102)	Telangana	04/2005 (04/2005)	12/2019 (03/2026)	736.13 (949.87)	940.7	96
814	Indiramma Flood Flow Canal Project (Irrigation and CAD-TG) (400103)	Telangana	04/2005 (01/2006)	12/2019 (12/2026)	1331.3 (5940.09)	4491.08	92
815	J. Chokka Rao Devadula Lift Irrigation Scheme (Irrigation and CAD-TG) (701405)	Telangana	04/2006 (04/2006)	12/2019 (12/2025)	8200.71 (14730)	4664.8	87
816	Rajiv Bhima Lift Irrigation Scheme (Irrigation and CAD-TG) (701406)	Telangana	04/2007 (01/2008)	12/2019 (03/2026)	1402 (2509.66)	1839.76	100
817	Saryu Nahar CADWM Project (Irrigation & Water Resources-UP) (400093)	Uttar Pradesh	04/2017 (04/2017)	12/2019 (03/2026)	1672.7 (1672.7)	22.24	1
818	Morna [Gureghar] Irrigation Project (Department of Water Resources, River Development & GR) (701395)	Uttar Pradesh	04/2007 (12/2007)	12/2025 (-)	219.9 (219.9)	115.2	31
819	Madhya Ganga canal Phase-II (Irrigation & Water Resources-UP) (701408)	Uttar Pradesh	04/2008 (04/2008)	12/2019 (12/2025)	1060.67 (4417.21)	4552.44	82
820	Jamrani Dam Multipurpose Project (Irrigation-UK) (613787)	Uttarakhand	10/2023 (11/2023)	06/2029 (-)	2584.1 (2584.1)	968.52	16
Total (39)					93740.23	138529.51	



सत्यमेव जयते

**Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.ipm.mospi.gov.in>**
