



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation



482th Flash Report on Central Sector Infrastructure Projects



Scan the QR code to access the
PAIMANA Portal.

(Rs. 150 crore
& above)

DECEMBER 2025

www.mospi.gov.in @GoIStats /GoIStats GoIStats Ministry of Statistics & PI




CONTENTS

I. Overview*	2-4
II. North Eastern Region	5-6
III. As per Harmonized Master List (HML) 2022	7-13
IV. Major Infrastructure Central Ministries & Departments	14-19
V. Appendix : <i>List of Tables</i>	20 onwards
Table 1: Ministry-wise Ongoing Projects	
Table 2: State-wise Ongoing Projects	
Table 3: Completed Projects	
Table 4: Newly Added Projects	
Table 5: Ongoing Projects of North Eastern Region	
Table 6: All Ongoing Projects	

**Note: This report is web-generated from the PAIMANA portal (ipm.mospi.gov.in) as of December 2025, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies on the IPM portal (indiainvestmentgrid.gov.in) latest by 27th January 2026.*





Overview




Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above


DECEMBER 2025

<p>1392 17 Ongoing Projects Line Ministries & Departments</p>	<p>₹ 29,68,248 Original Cost (crores)</p>	<p>₹ 35,10,920 Revised Cost (crores)</p>	<p>₹ 19,01,163 (54.15% of Revised Cost) Expenditure (crores)</p>
<p>17 Commissioned during month</p>	<p>20 Newly Added during month</p>		


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

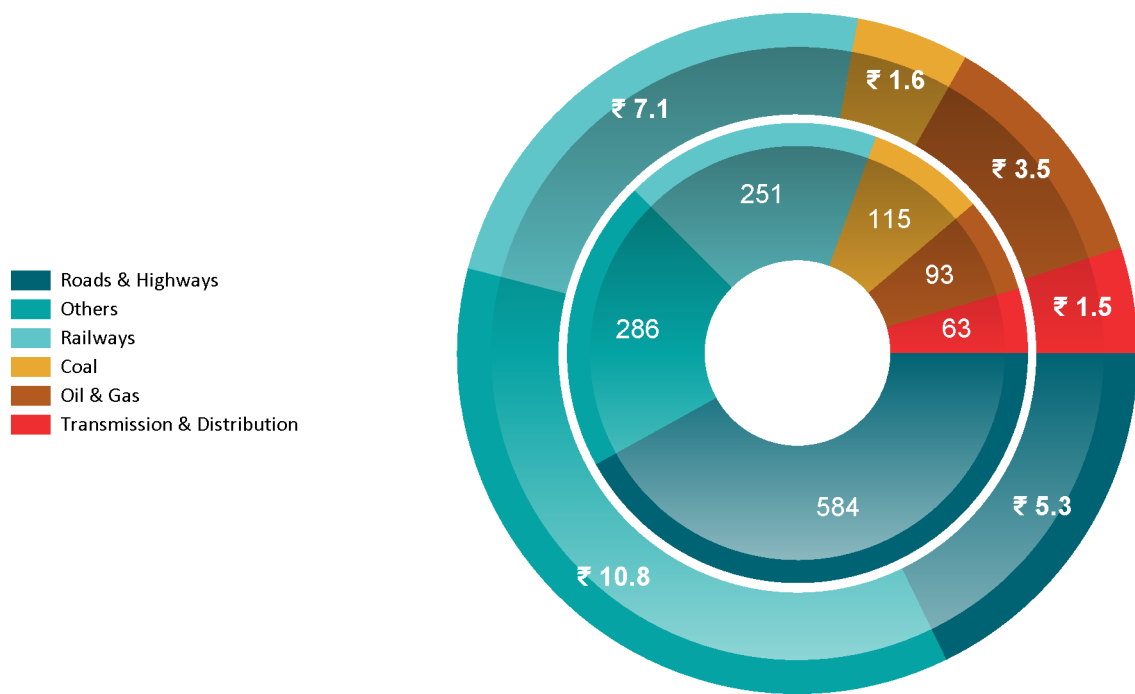


Ministry Comparison : Major Ministries*
[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

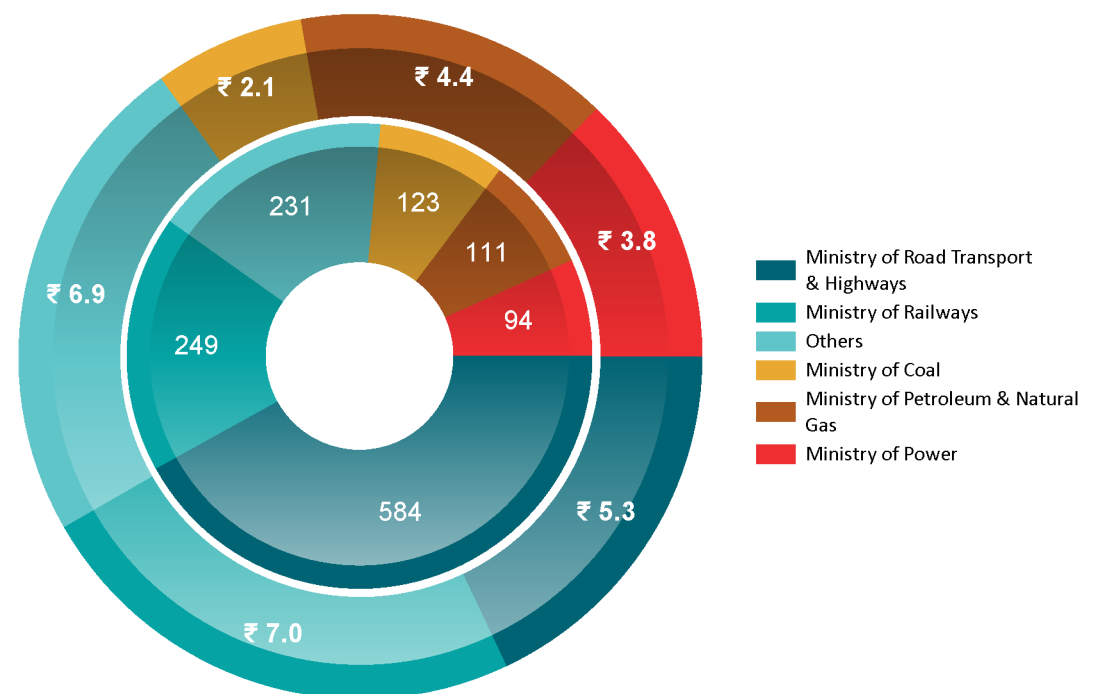

Cost Analytics : Major Sectors*

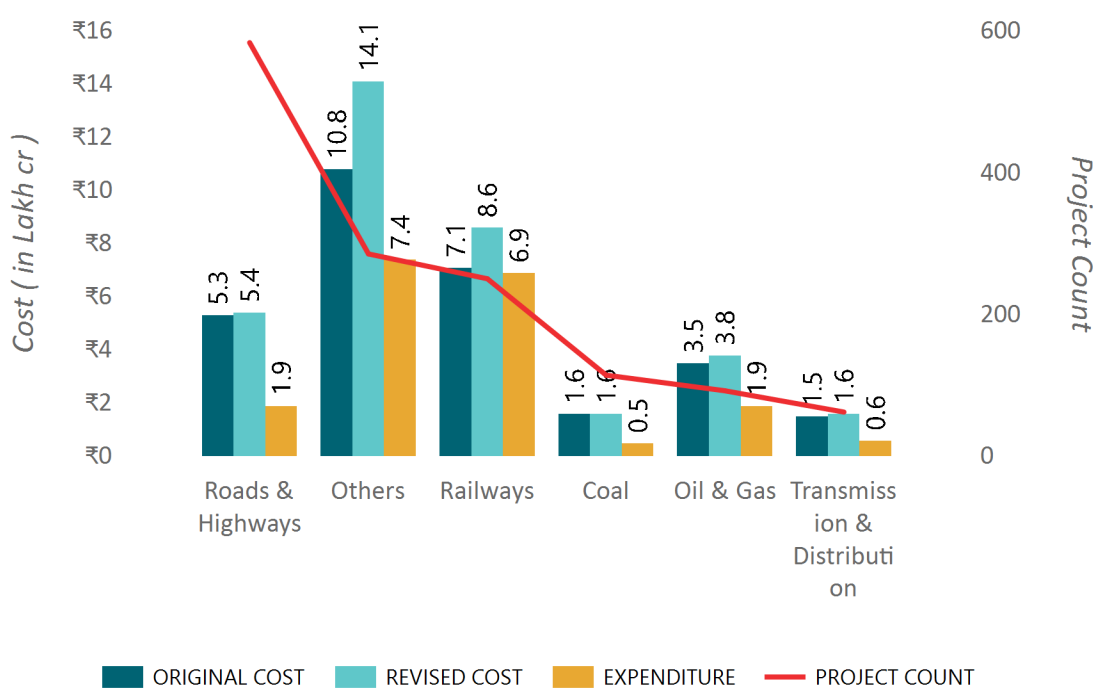


Cost Analytics : Major Ministries*

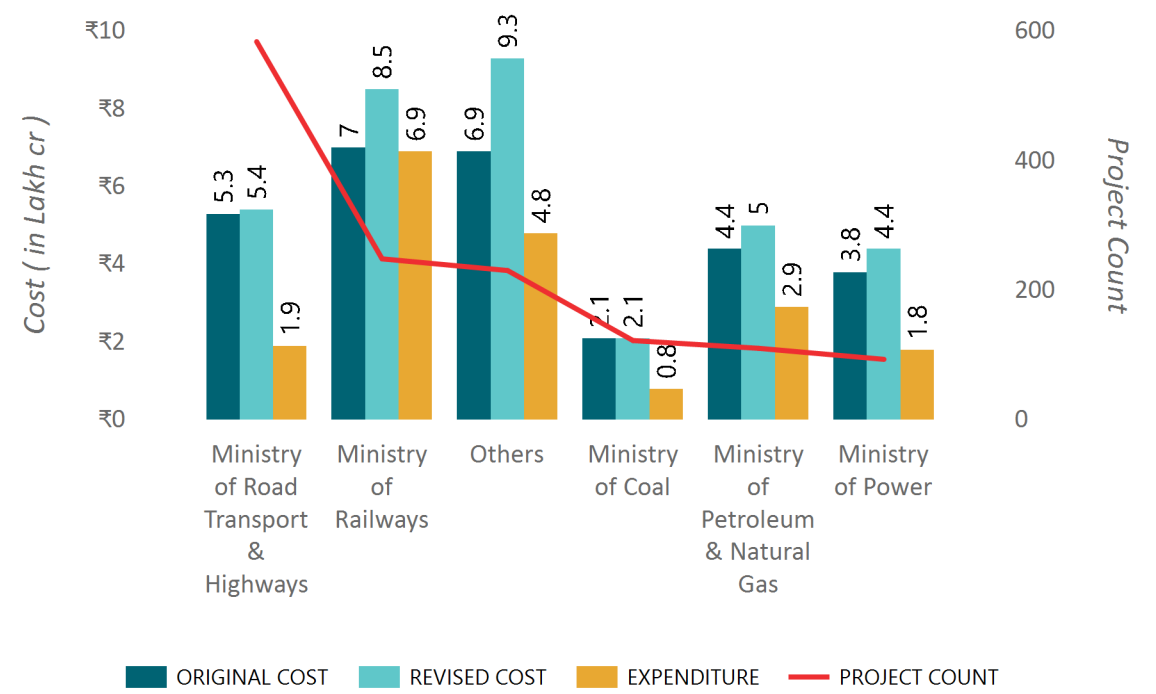


Note: * as per Project Count

Analytics: as per HML

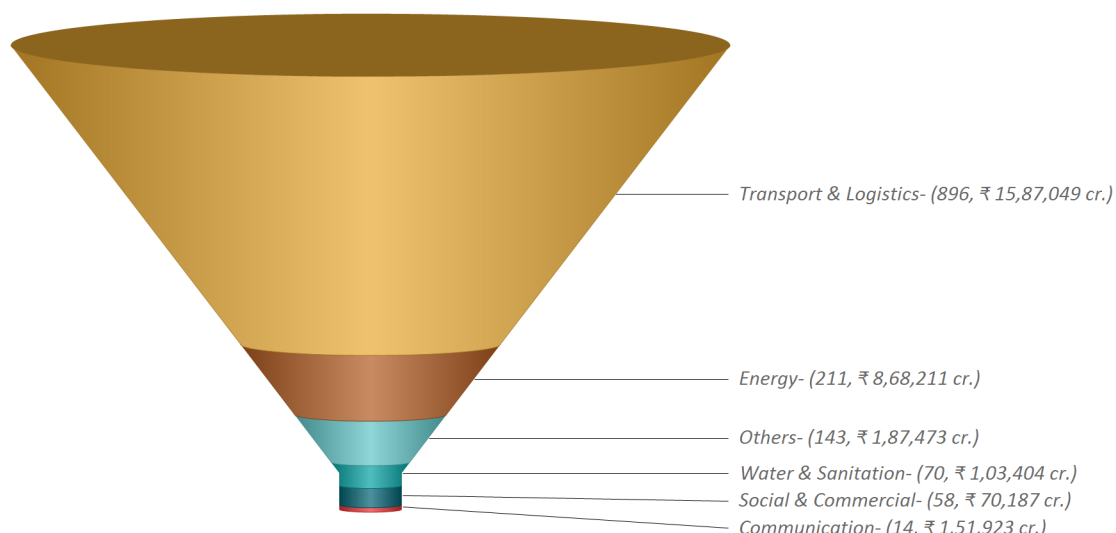


Note: all indicated legends are in format (Project count, Original Cost in crores)

Physical & Financial progress (%) : Project count

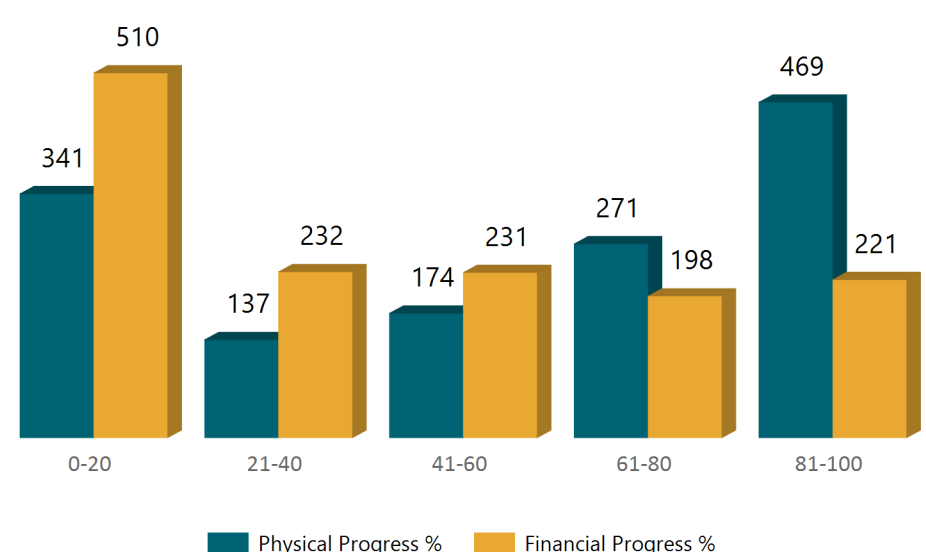


State Comparison : Major States*

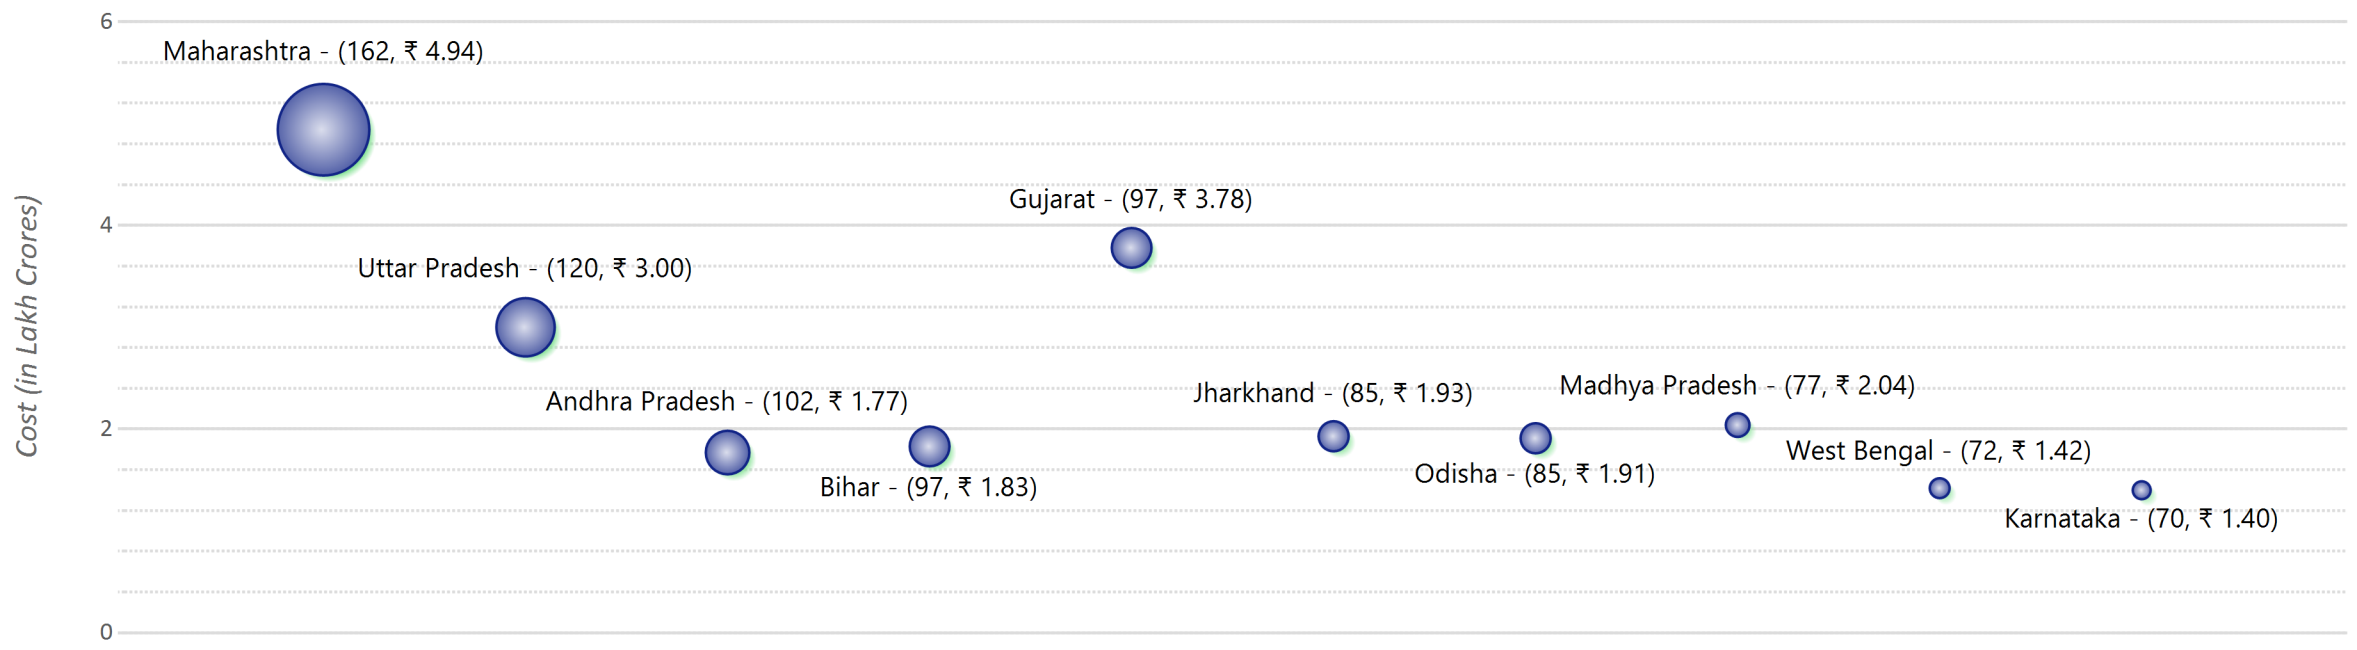


Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count


Ministry-wise Distribution of total 469 projects with reported Physical Progress between 81-100%

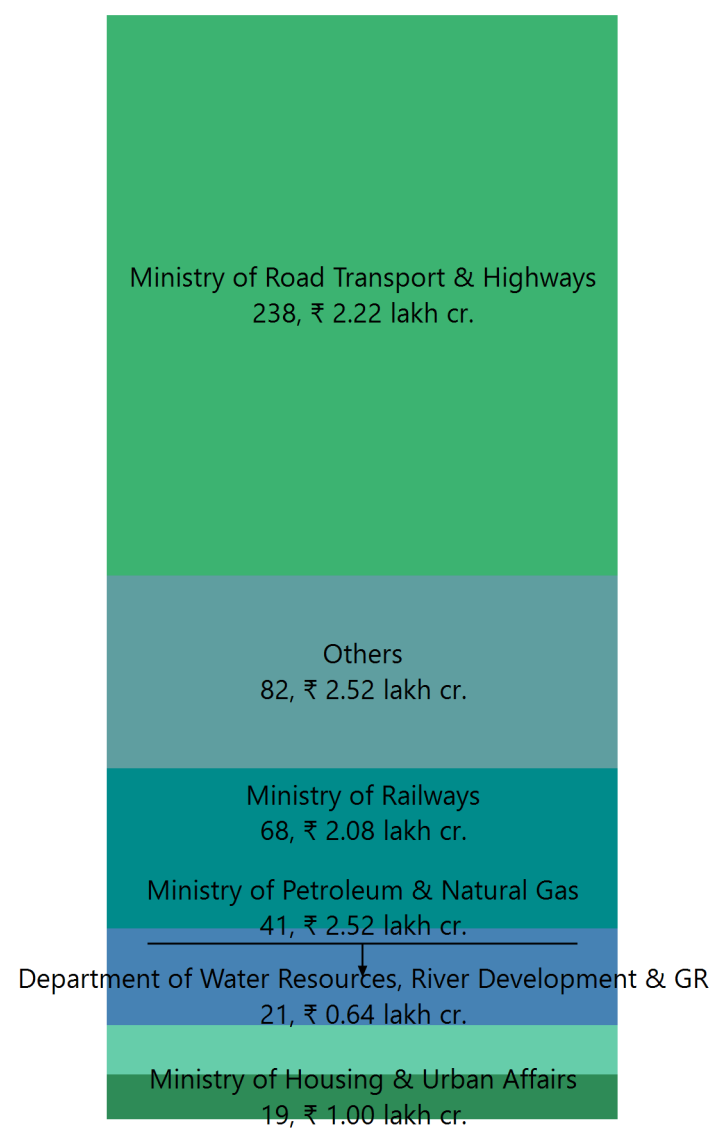

Total Ongoing Projects: Mega & Major

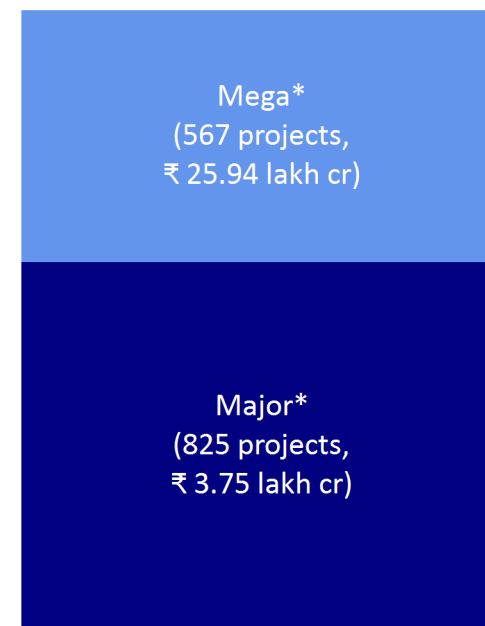


Total North East Region Ongoing Projects: Mega & Major




Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost >= 1000 crore
* Major project if having original cost < 1000 crore


Project volume (nos.)

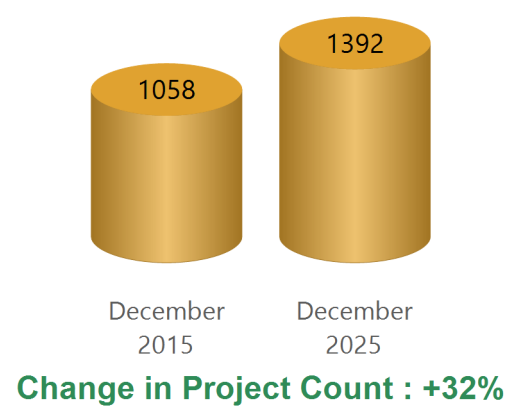

Total Project value (in lakh crore)

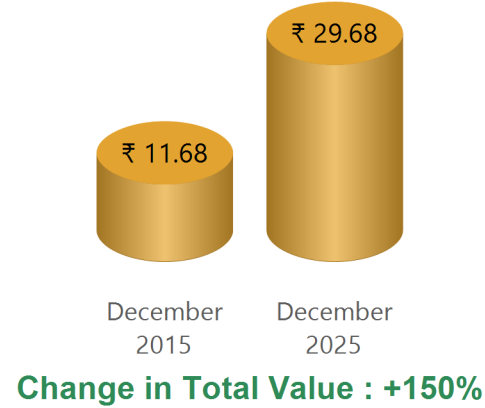


Cumulative Expenditure (in lakh crore)

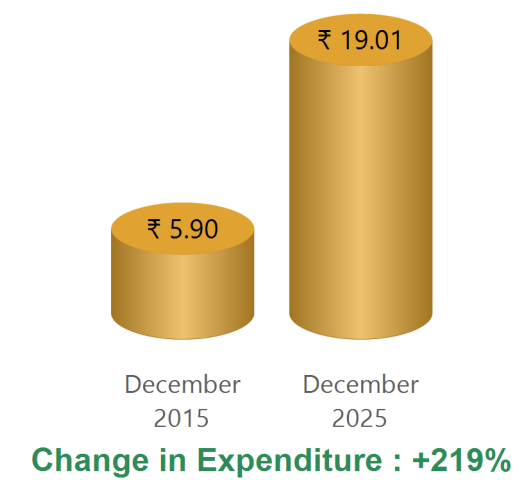



North Eastern Region





Special Focus : North Eastern Region

DECEMBER 2025

170 | 11

Ongoing Projects |
Line Ministries & Departments

₹ 2,12,025

Original Cost
(crores)

₹ 2,64,185

Revised Cost
(crores)

₹ 1,39,479

(52.8% of Revised Cost)
Expenditure
(crores)

0


Commissioned during month

1


Newly Added during month

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

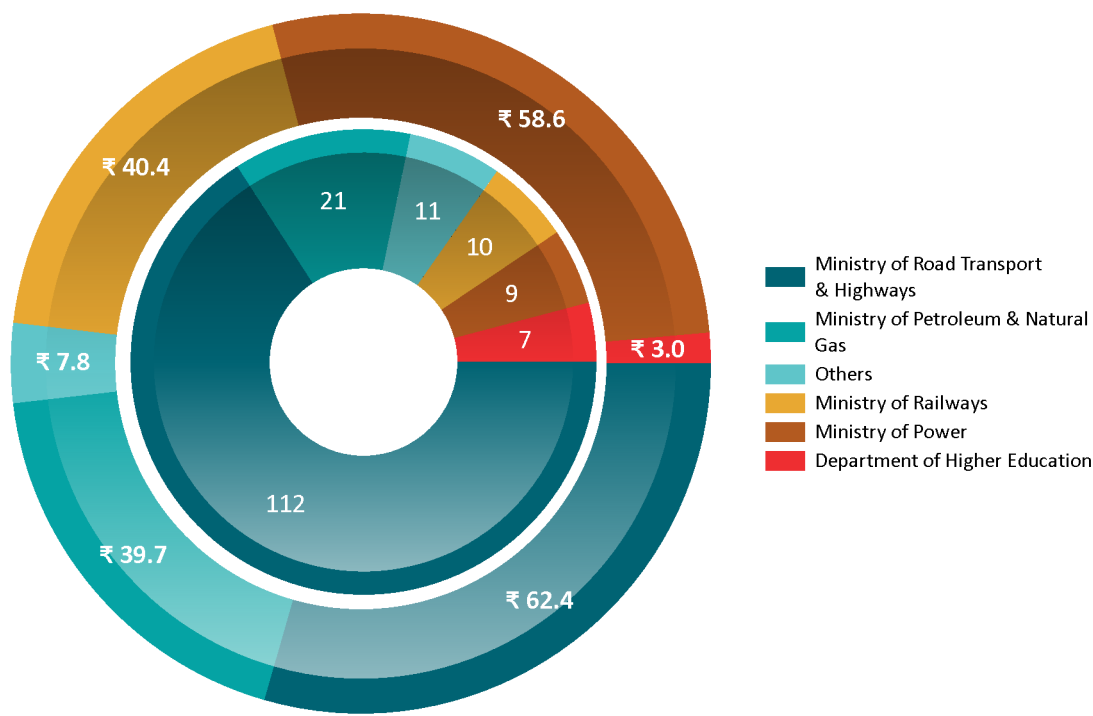


Cost Analytics : Major Ministries*

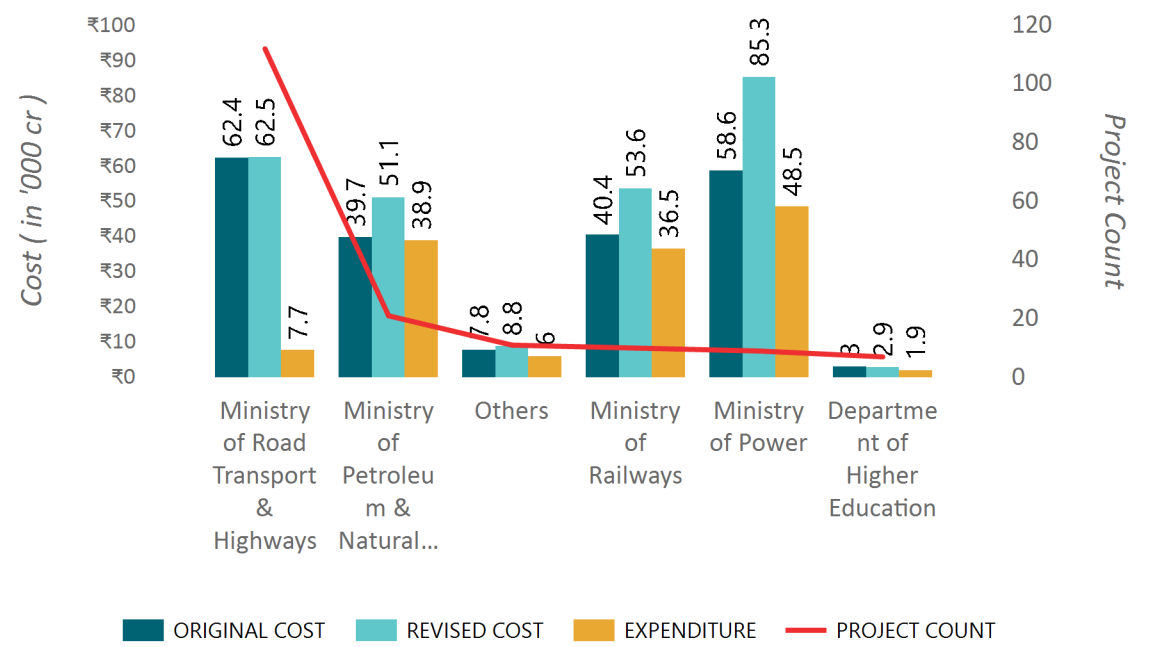


Note: * as per Project Count

Analytics: as per HML

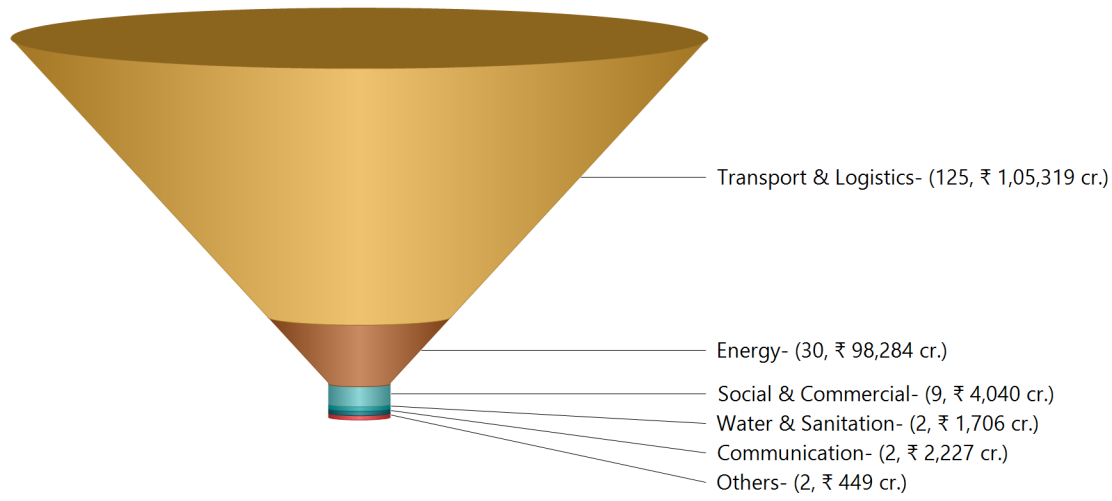


Physical & Financial progress (%) : Project count

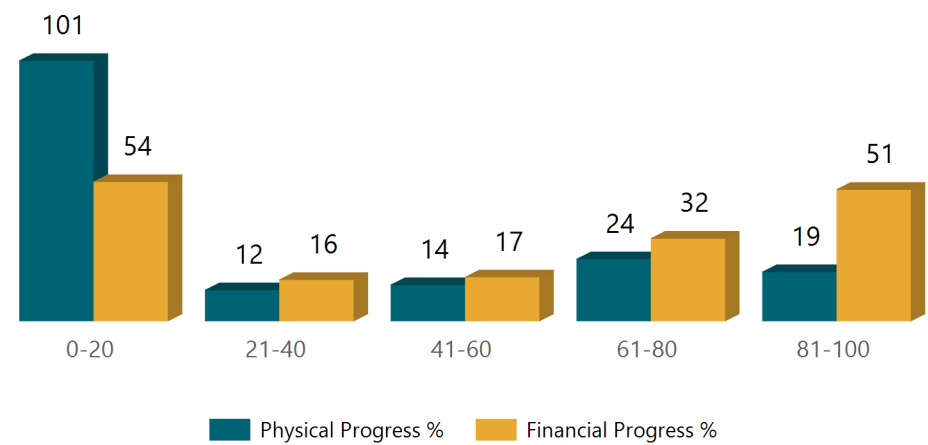

Note: all indicated legends are in format (Project count, Original Cost in crores)

State Comparison : All States

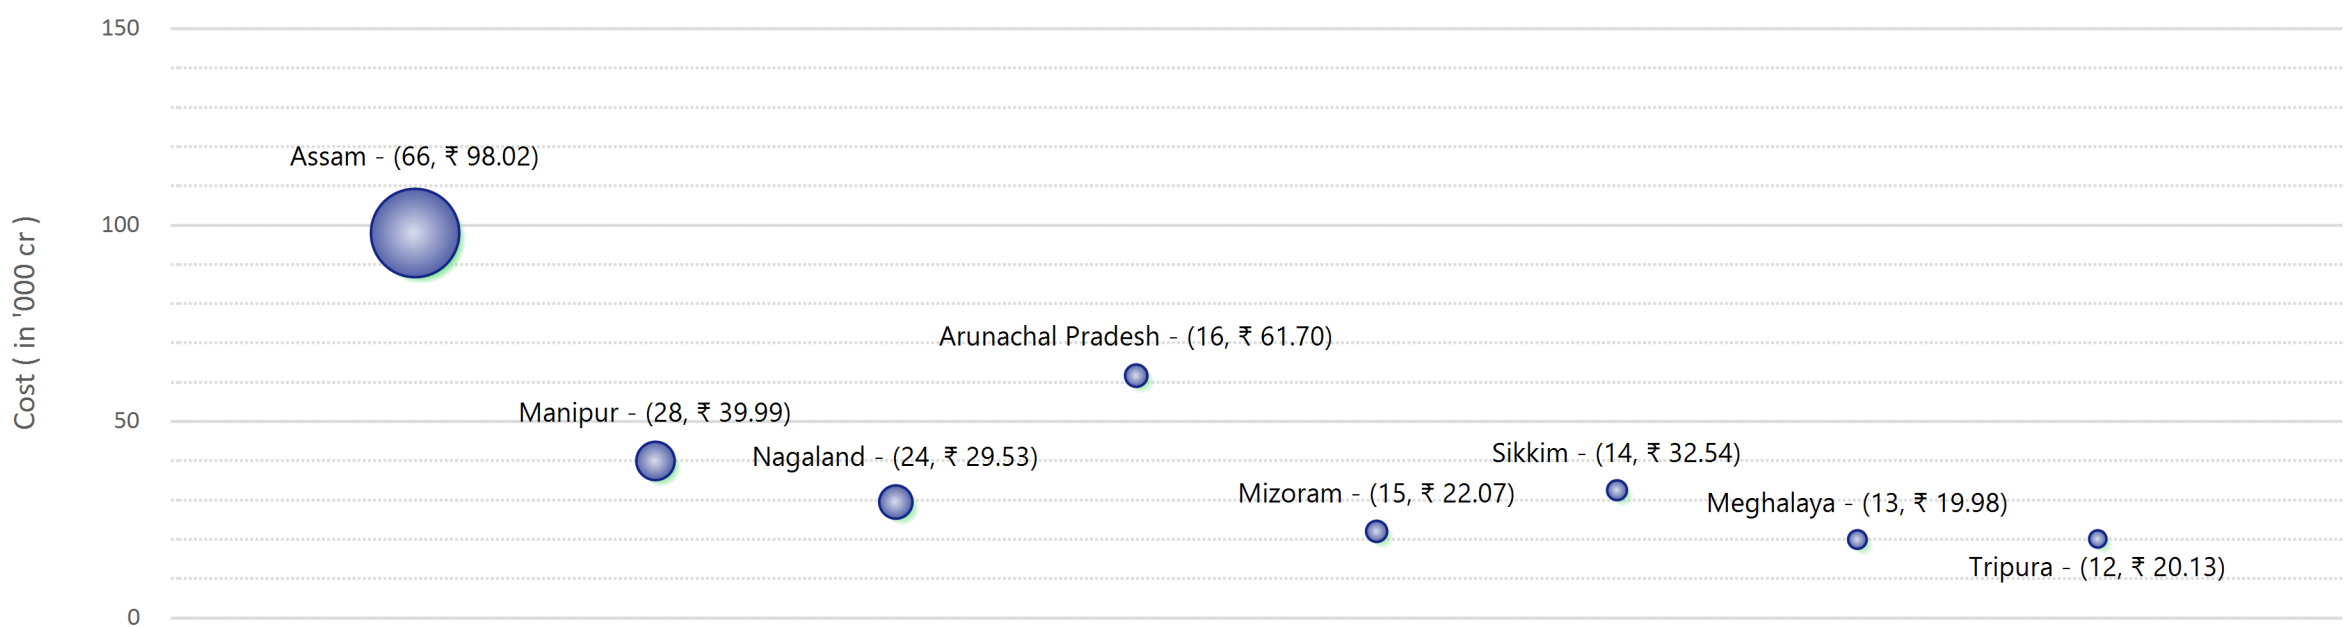

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022





HML Category 1 : Transport & Logistics

DECEMBER 2025

896
Ongoing Projects

₹ 15,87,049
Original Cost
(crores)


₹ 17,70,182
Revised Cost
(crores)

₹ 11,00,207
(62.15% of Revised Cost)
Expenditure
(crores)


5
Commissioned during month

13
Newly Added during month

Cost Analytics : All Sectors

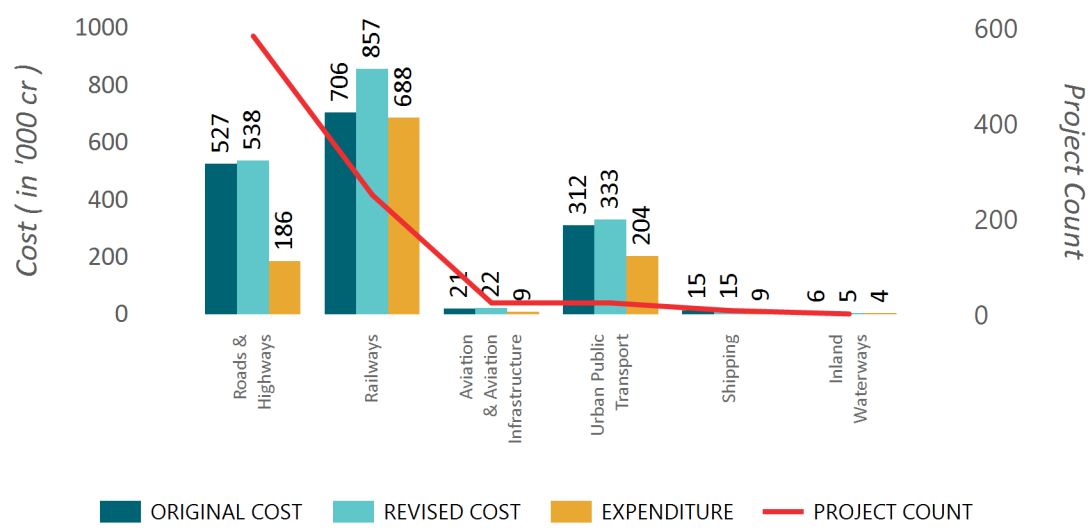

Physical & Financial progress (%) : Project count

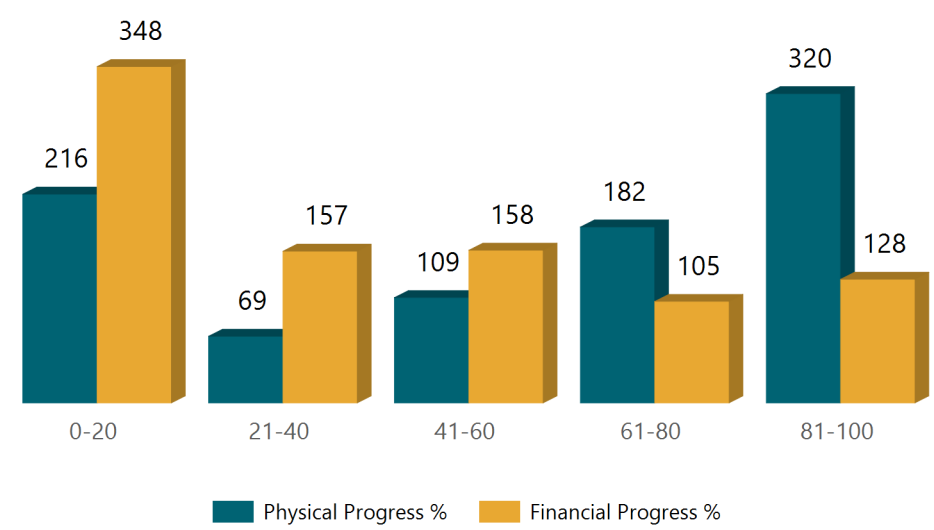

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Roads & Highways	584	527,441	537,799	185,964
2	Railways	251	705,753	856,854	688,175
3	Aviation & Aviation Infrastructure	25	21,238	22,452	9,261
4	Urban Public Transport	25	311,947	332,528	203,575
5	Shipping	9	15,124	15,291	9,131
6	Inland Waterways	2	5,546	5,258	4,100

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	85,338	56
2	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		30,211	48
3	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
4	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	26,841	72
5	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,922	20



HML Category 2 : Energy

DECEMBER 2025

211

Ongoing Projects

₹ 8,68,211

Original Cost
(crores)

₹ 10,00,245

Revised Cost
(crores)

₹ 4,97,761

(49.76% of Revised Cost)
Expenditure
(crores)


5

Commissioned during month


3

Newly Added during month

Cost Analytics : All Sectors

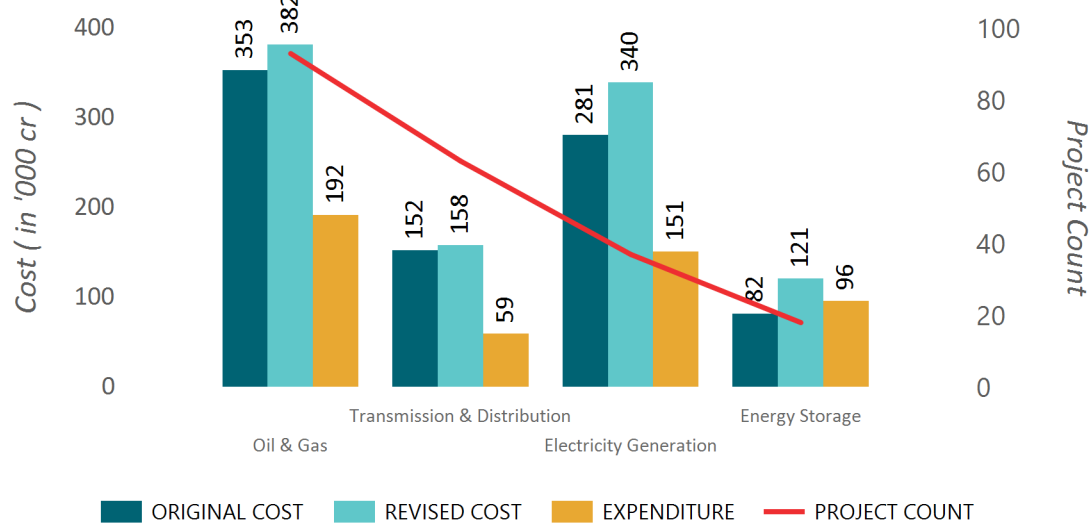

Physical & Financial progress (%) : Project count

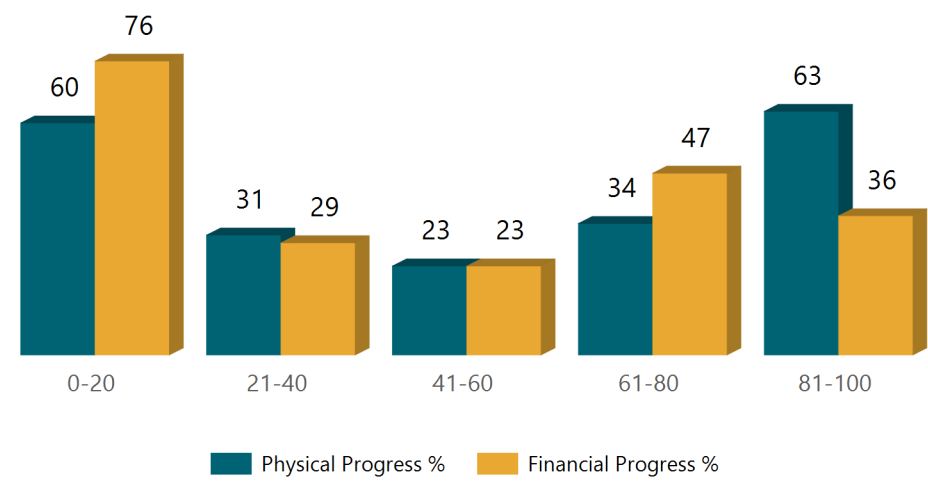

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	93	353,463	381,881	191,901
2	Transmission & Distribution	63	152,121	158,085	59,381
3	Electricity Generation	37	280,742	339,525	150,606
4	Energy Storage	18	81,884	120,754	95,874

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	2,593	18
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	63,572	90
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA	34,627	36,225	27,829	91
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	32,374	96
5	602182	DIBANG MULTIPURPOSE PROJECT	31,876		3,862	16



HML Category 3 : Water & Sanitation

DECEMBER 2025

70
Ongoing Projects

₹ 1,03,404
Original Cost
(crores)


₹ 2,03,283
Revised Cost
(crores)

₹ 1,46,362
(72% of Revised Cost)
Expenditure
(crores)


1
Commissioned during month

0
Newly Added during month

Cost Analytics : All Sectors

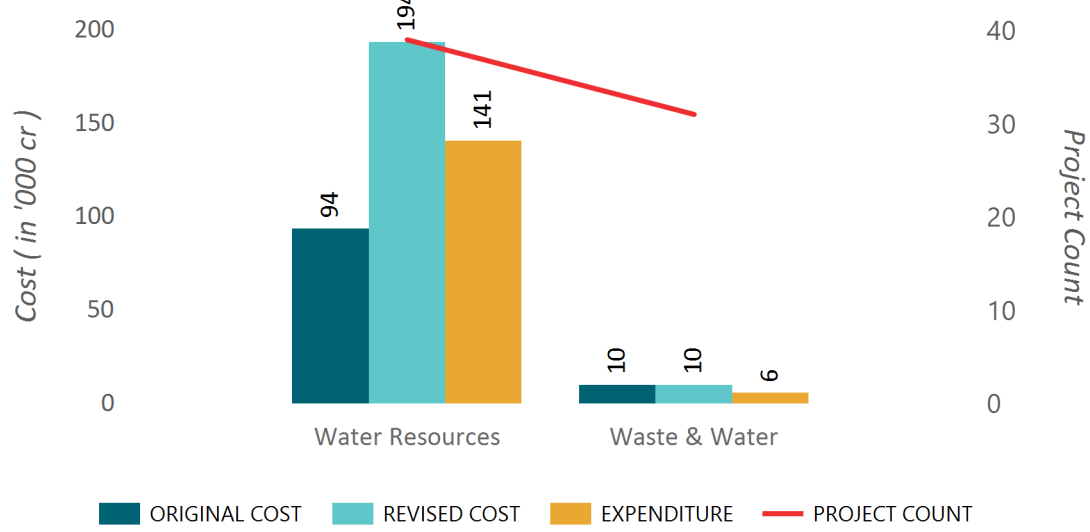

Physical & Financial progress (%) : Project count

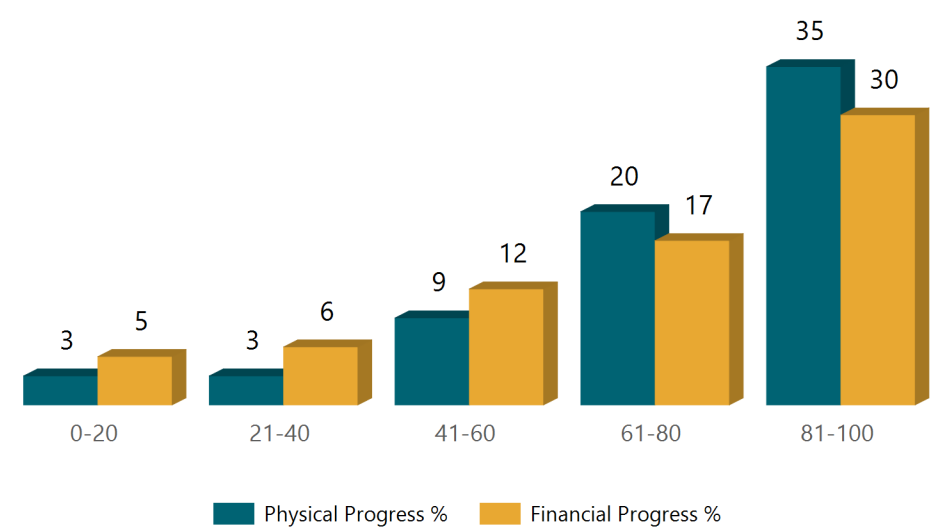

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	39	93,740	193,594	140,622
2	Waste & Water	31	9,664	9,688	5,739

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,861	93
2	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	25,834	84
3	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,665	87
4	400112	JIGAON IRRIGATION PROJECT	7,223		9,349	91
5	701386	GOSIKHURD PROJECT	7,196	12,770	13,898	72



HML Category 4 : Communication

DECEMBER 2025

14
Ongoing Projects

₹ 1,51,923
Original Cost
(crores)


₹ 2,74,016
Revised Cost
(crores)

₹ 77,211
(28.18% of Revised Cost)
Expenditure
(crores)


1
Commissioned during month

0
Newly Added during month

Cost Analytics : All Sectors

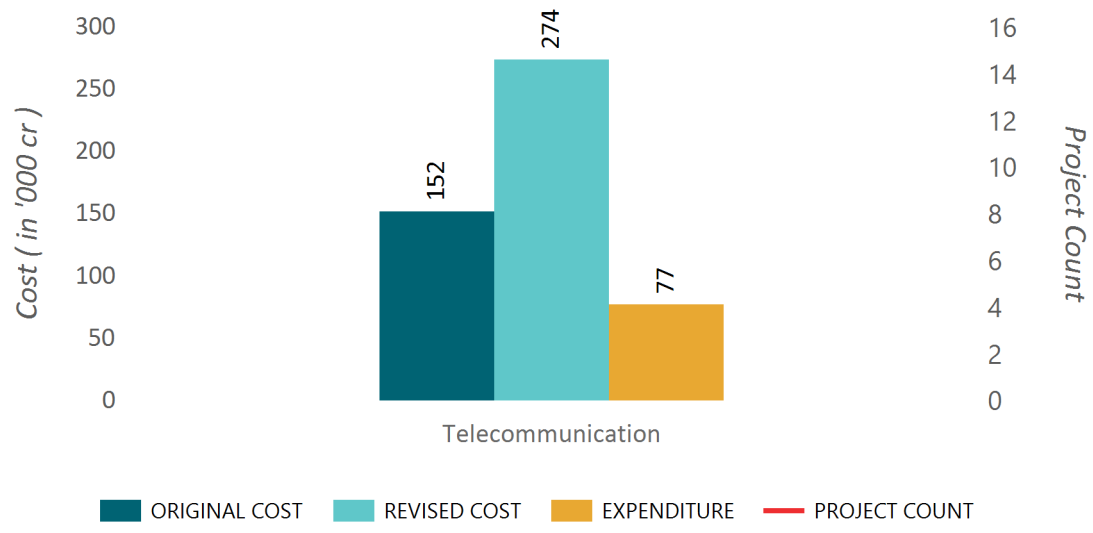

Physical & Financial progress (%) : Project count

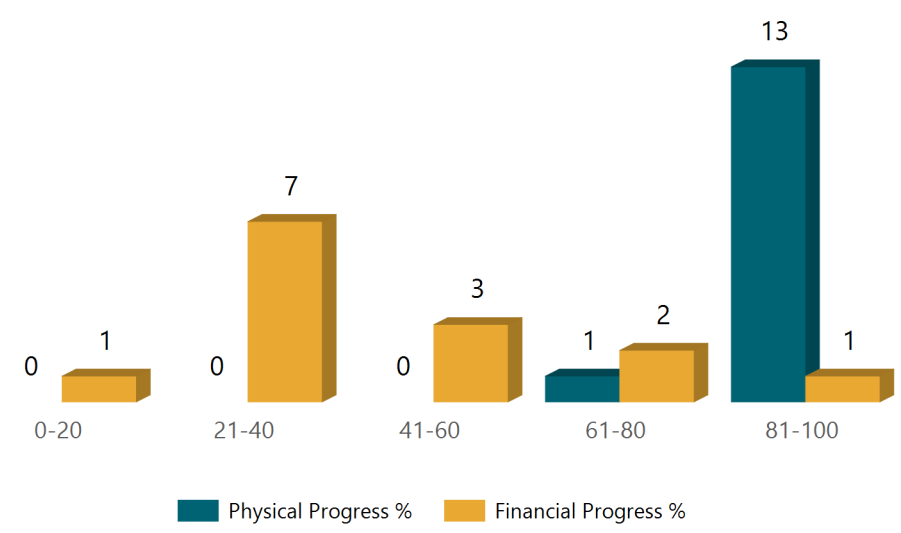

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	14	151,923	274,016	77,211

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	706775	BHARATNET	61,109	188,000	46,432	81
2	701593	4G SERVICES BY BSNL	28,466	19,592	8,471	97
3	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	30,620	9,792	80
4	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		8,472	97
5	701602	PROVISION OF 4G BASED MOBILE SERVICES IN 7,287 UNCOVERED VILLAGES OF 44 ASPIRATIONAL DISTRICT ACROSS 5 STATES OF ANDHRA PRADESH, CHHATTISGARH, JHARKHAND, MAHARASHTRA & ODISHA	3,685		1,332	82



HML Category 5 : Social & Commercial

DECEMBER 2025

58

Ongoing Projects

₹ 70,187

Original Cost
(crores)

₹ 72,308

Revised Cost
(crores)

₹ 15,609

(21.59% of Revised Cost)
Expenditure
(crores)


3

Commissioned during month


3

Newly Added during month

Cost Analytics : All Sectors

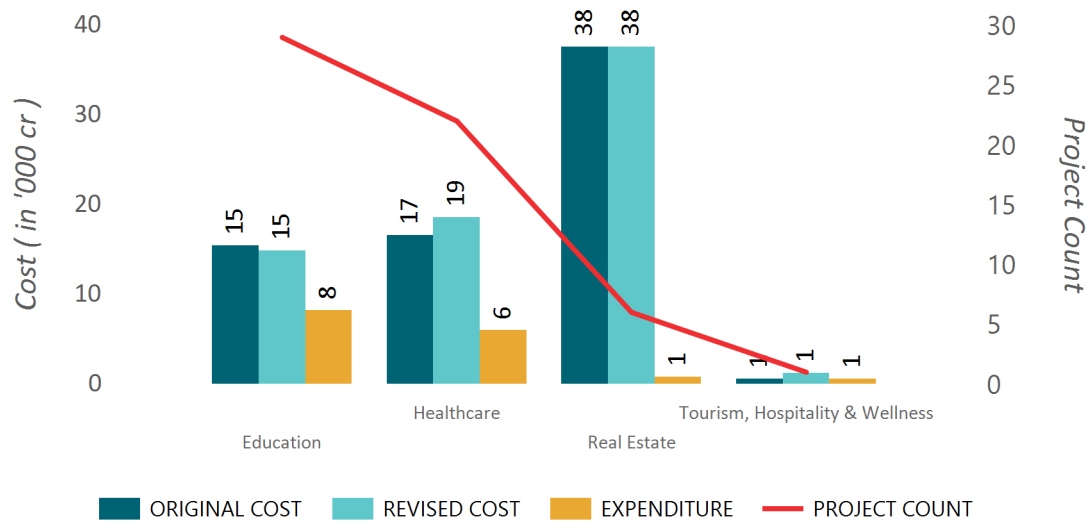

Physical & Financial progress (%) : Project count

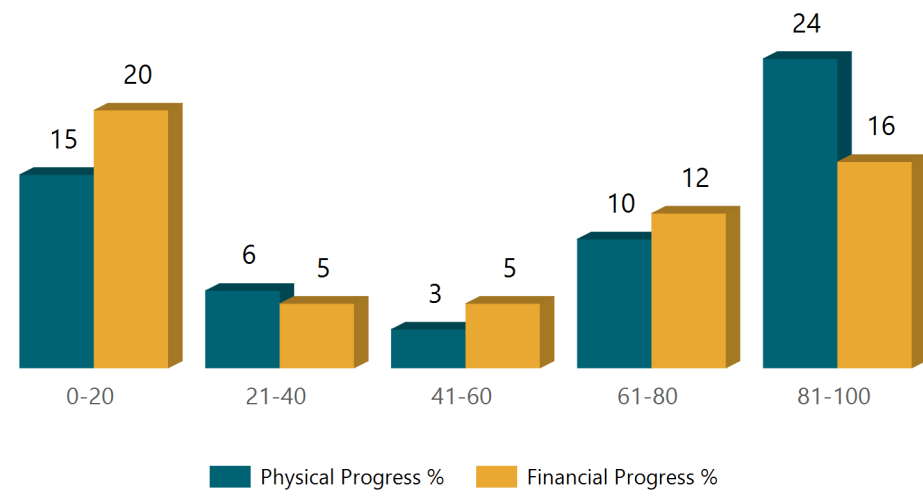

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Education	29	15,419	14,867	8,254
2	Healthcare	22	16,604	18,613	5,998
3	Real Estate	6	37,591	37,591	811
4	Tourism, Hospitality & Wellness	1	573	1,238	546

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850		0	0
2	617883	REDEVELOPMENT OF RESIDENTIAL COLONIES AT AYUR VIGYAN NAGAR AND WEST ANSARI NAGAR CAMPUSES OF AIIMS, NEW DELHI	4,441		25	61
3	701658	KRISHNAPATNAM NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	2,139		568	27
4	701167	AIIMS KASHMIR AT AWANTIPORA JAMMU & KASHMIR	1,828	2,161	1,492	72
5	701657	TUMAKURU NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	1,702		184	17



Other Sectors

DECEMBER 2025

143

Ongoing Projects

₹ 1,87,473

Original Cost
(crores)

₹ 1,90,885

Revised Cost
(crores)

₹ 64,013

(33.53% of Revised Cost)

Expenditure
(crores)


2

Commissioned during month

1

Newly Added during month

Physical & Financial progress (%) : Project count

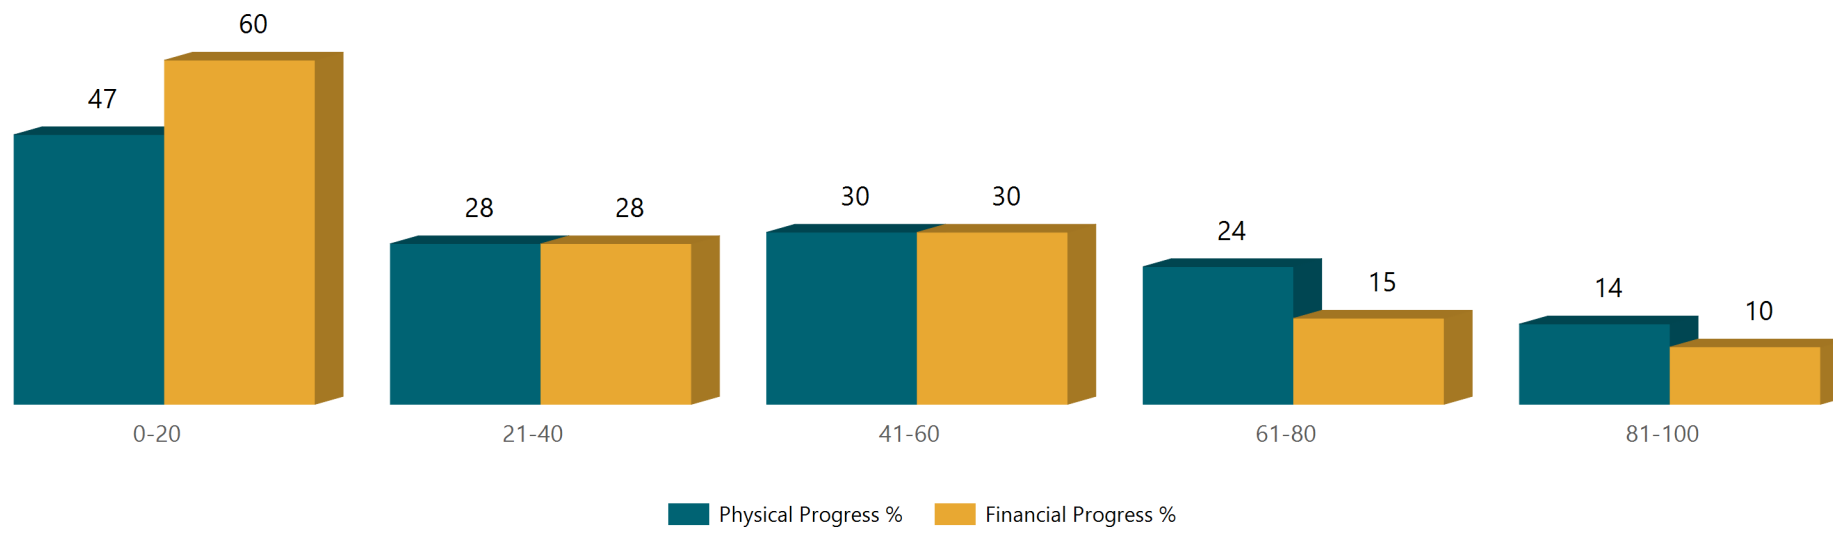

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	115	158,368	156,106	48,265
2	Steel	19	18,161	21,400	8,618
3	Metals & Mining	7	10,044	12,481	6,921
4	Construction	2	899	899	210

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400424	GEVRA OC [70 MTY]	11,816		6,813	78
2	400185	GOPALJI KANIHA OCP [10 TO 30 M]	8,416	6,108	1,746	17
3	400150	RPR MAGADH EXP OCP	7,254		1,599	38
4	617416	REVISED JHARIA MASTER PLAN FOR DEALING WITH FIRE, SUBSIDENCE & REHABILITATION OF AFFECTED FAMILIES IN JHARIA COALFIELD- REG.	5,940		26	19
5	616253	BLOCK E OCP	5,851		20	3



Major Infrastructure Central Ministries & Departments






Ministry of Road Transport & Highways

DECEMBER 2025

584 Ongoing Projects	₹ 5,27,441 Original Cost (crores)	₹ 5,37,799 Revised Cost (crores)	₹ 1,85,964 (34.58% of Revised Cost) Expenditure (crores)
195 ₹ 348,461 Mega Projects Count Original Cost (crores)	389 ₹ 178,980 Major Projects Count Original Cost	0 Commissioned during month	0 Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

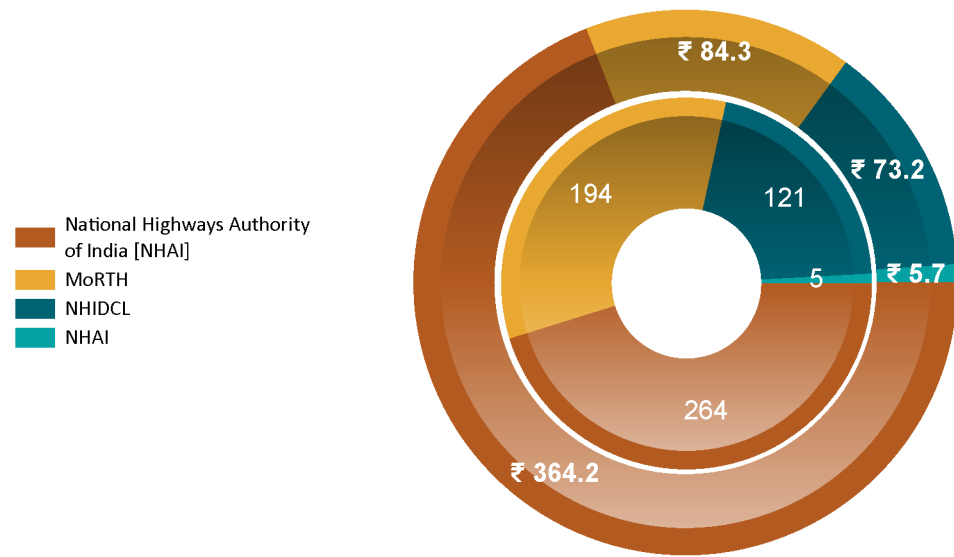


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Physical & Financial progress (%) : Project count

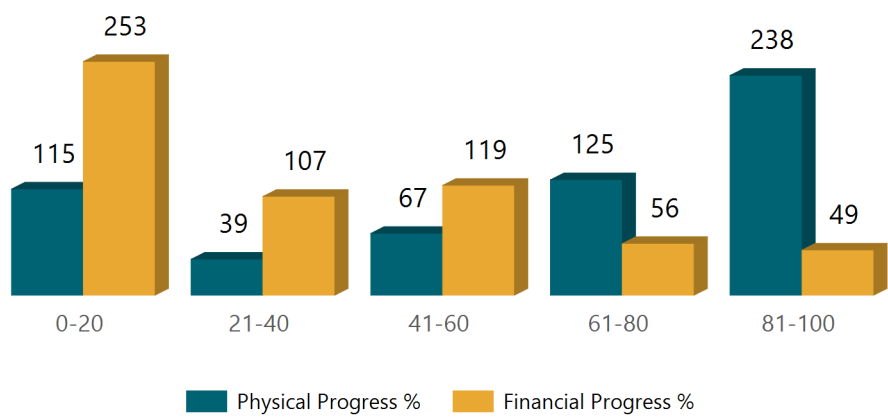

Cost Analytics : Major Sectors*

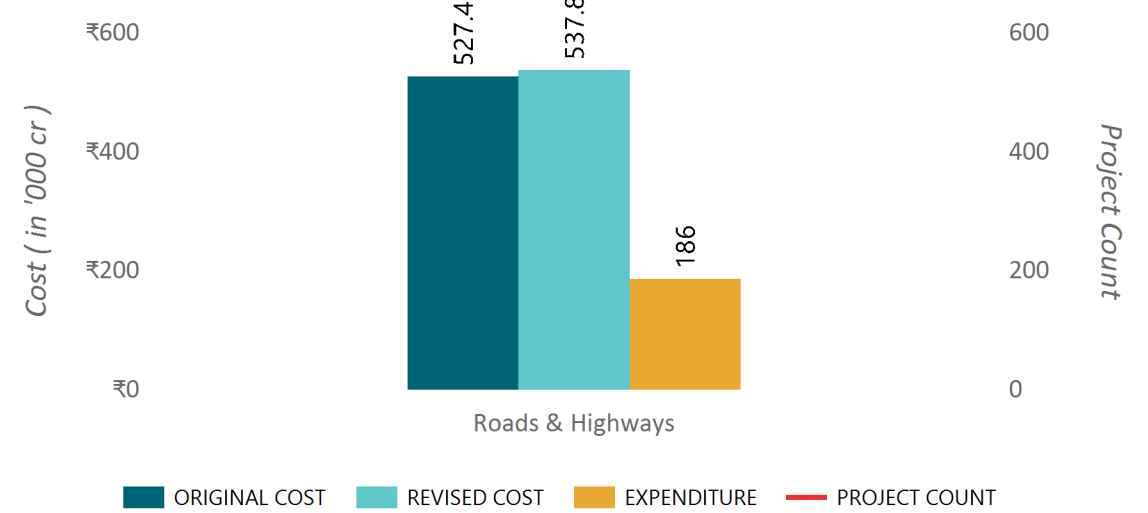

State Comparison : Major States*

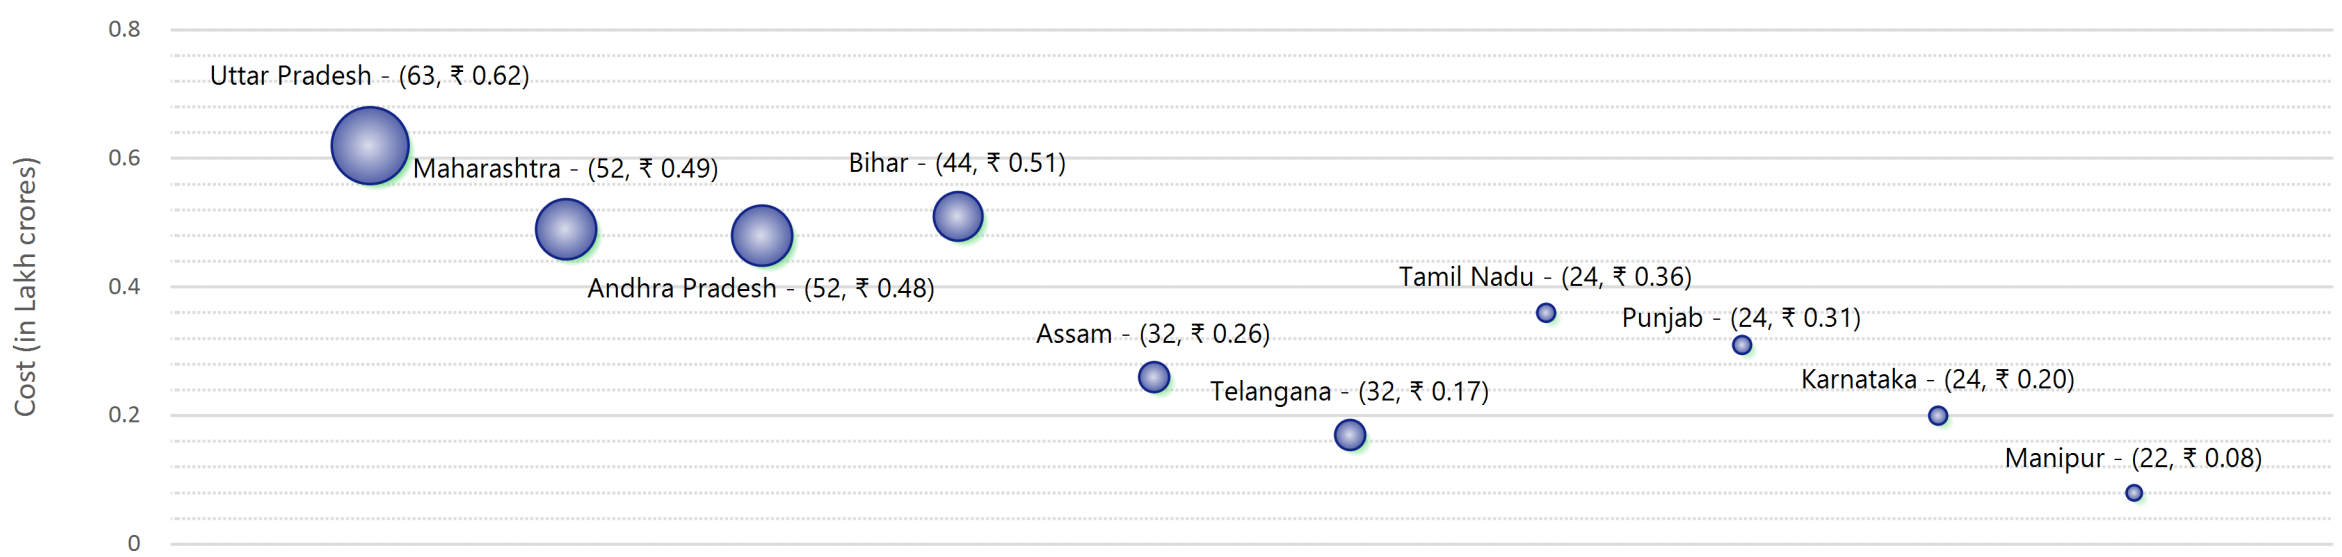

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count



Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	618412	CONSTRUCTION OF I CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL ROAD LENGTH 18.475KM AND II 14.150 KM LONG 2-L BI-DIRECTIONAL SINGLE TUBE ZOJI-LA TUNNEL ACROSS ZOJILA PASS ON SONAMARG - KARGIL SECTION FROM KM 82 TO KM 118 OF NH-01 UNDER PMDP	6,809	6,809		0
2	618738	6L BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD NH-131G STARTING FROM KM 8.480 NEAR SHERPUR TO KM 23.000 NEAR DIGHWARA	6,292	3,352	421	13
3	618373	CONSTRUCTION OF 4-LANE BRIDGE INCLUDING APPROACHES OVER RIVER BRAHMAPUTRA BETWEEN DHUBRI ON NORTH BANK, ASSAM AND PHULBARI ON SOUTH BANK, MEGHALAYA ON NH-127B UNDER JICA ODA LOAN ASSISTANCE PHASE-III	4,997	4,997		67
4	618599	6L OF RAMANATUKKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66	4,924	4,919	1,669	99
5	618602	6L OF THALIKULAM TO KODUGALLUR SECTION FROM KM 369.015 TO KM 397.850 OF NH - 66 OLD NH-17	4,302	4,302	618	80



Ministry of Railways

DECEMBER 2025

249
Ongoing Projects

₹ 7,02,267
Original Cost
(crores)

₹ 8,52,603
Revised Cost
(crores)

₹ 6,86,201
(80.48% of Revised Cost)
Expenditure
(crores)

133 | ₹ 646,960
Mega Projects
Count | Original Cost (crores)


116 | ₹ 55,307
Major Projects
Count | Original Cost

4
Commissioned during month

11
Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

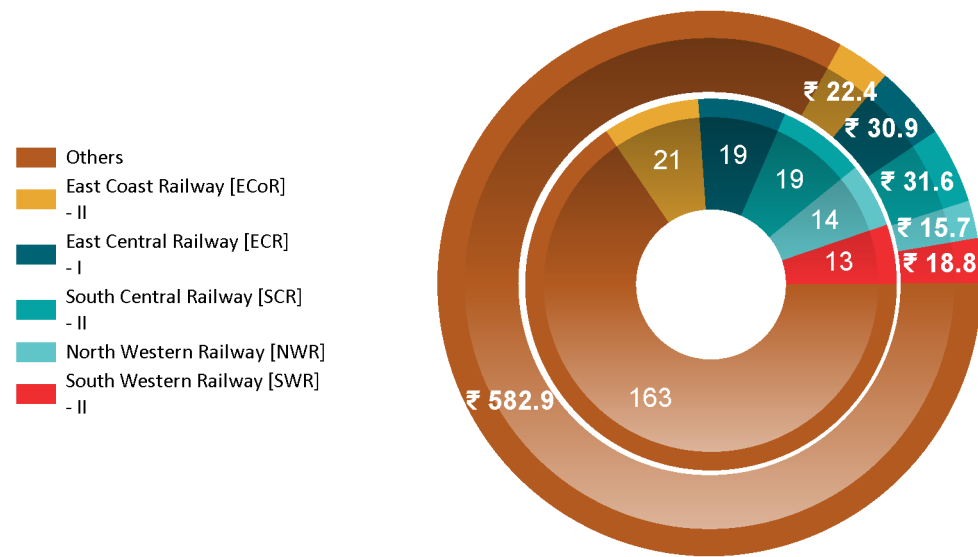


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Physical & Financial progress (%) : Project count

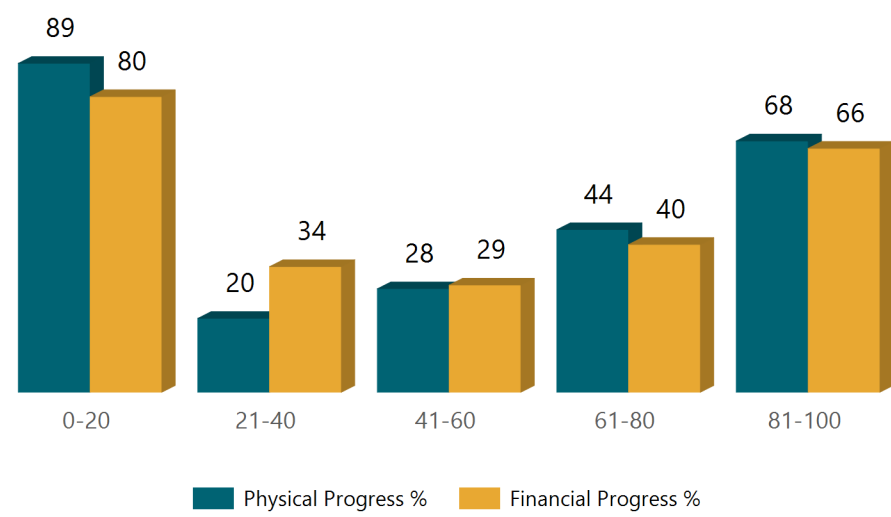

Cost Analytics : Major Sectors*

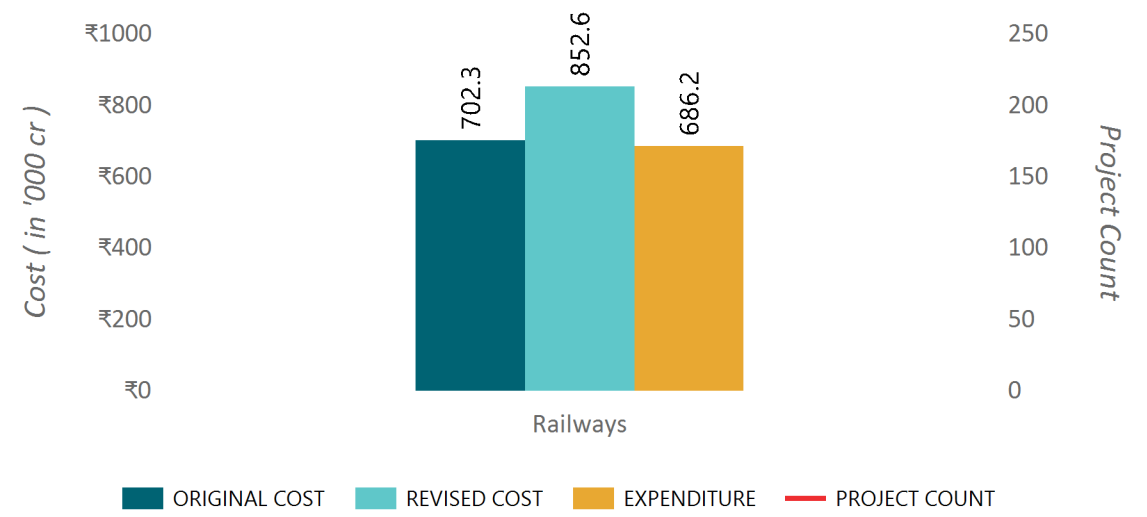

State Comparison : Major States*

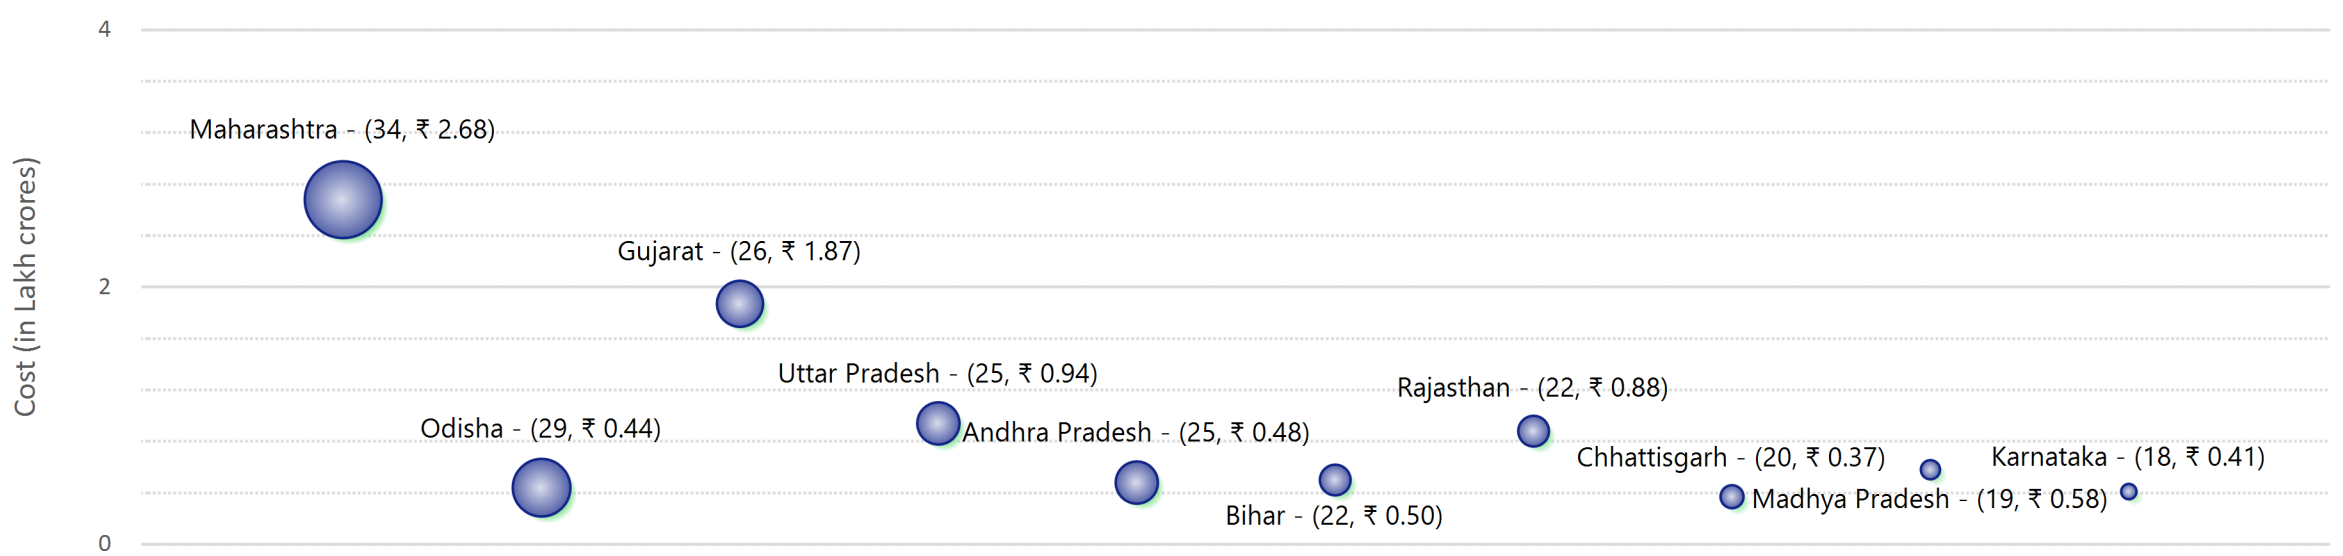

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	85,338	56
2	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
3	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	26,841	72
4	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,922	20
5	705941	BANGALORE SUBURBAN RAILWAY PROJECT	15,767	15,767	2,321	19



Ministry of Coal

DECEMBER 2025

123
Ongoing Projects

₹ 2,11,674
Original Cost
(crores)

₹ 2,14,438
Revised Cost
(crores)

₹ 75,927
(35.41% of Revised Cost)
Expenditure
(crores)

40 | ₹ 170,706
Mega Projects
Count | Original Cost (crores)


83 | ₹ 40,968
Major Projects
Count | Original Cost

1
Commissioned during month

3
Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

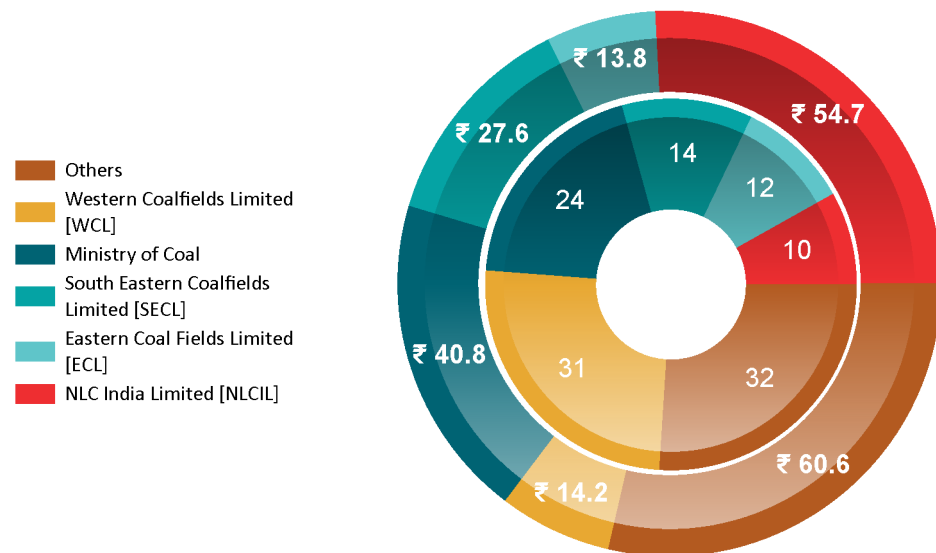


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

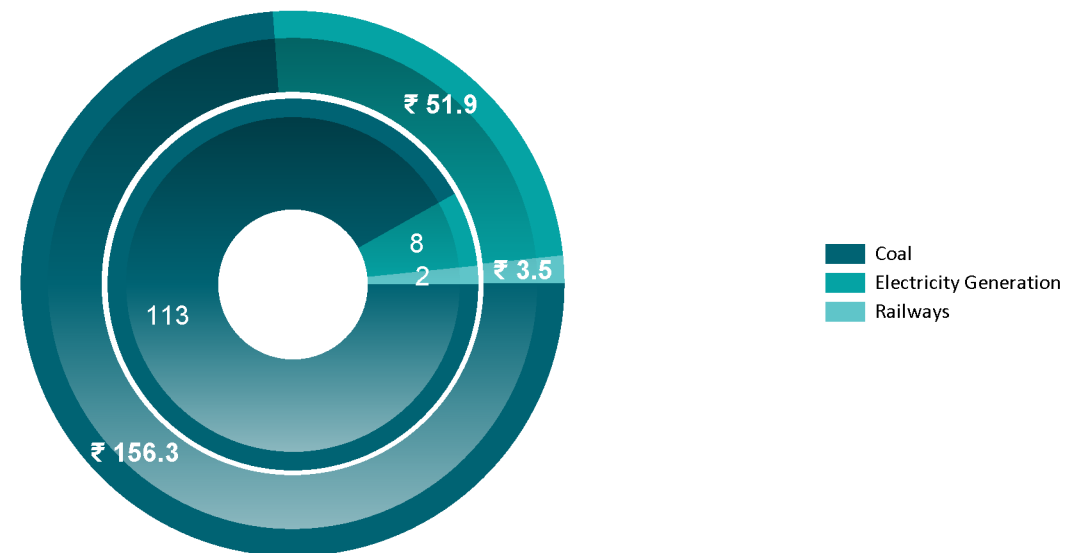


Physical & Financial progress (%) : Project count

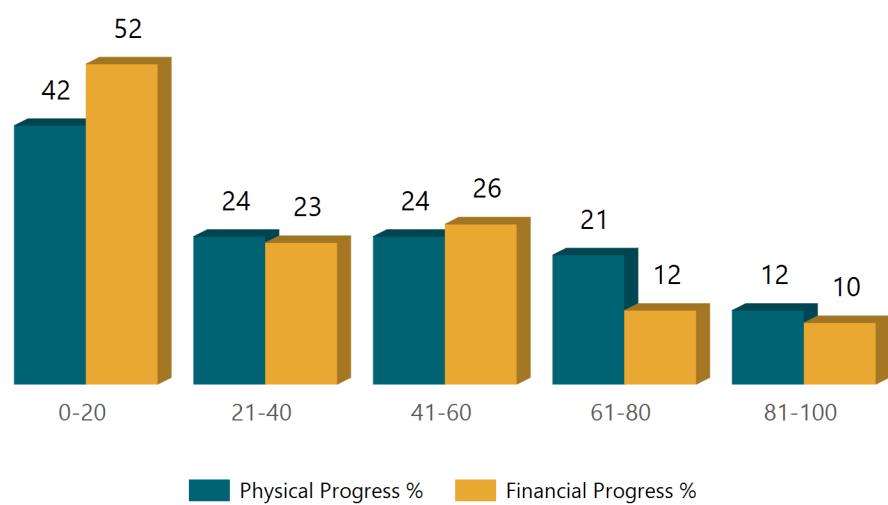

Cost Analytics : Major Sectors*

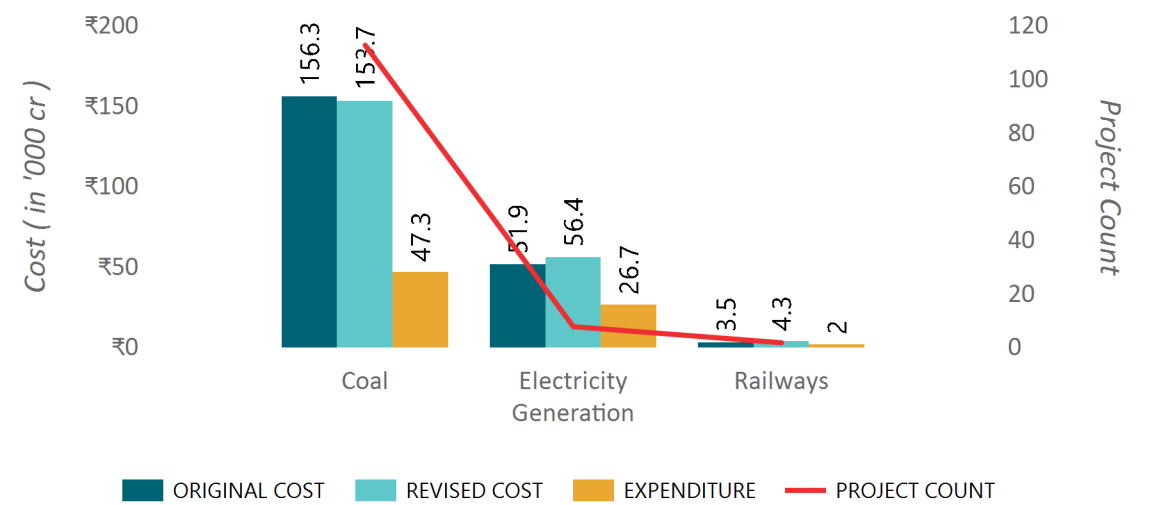

State Comparison : Major States*

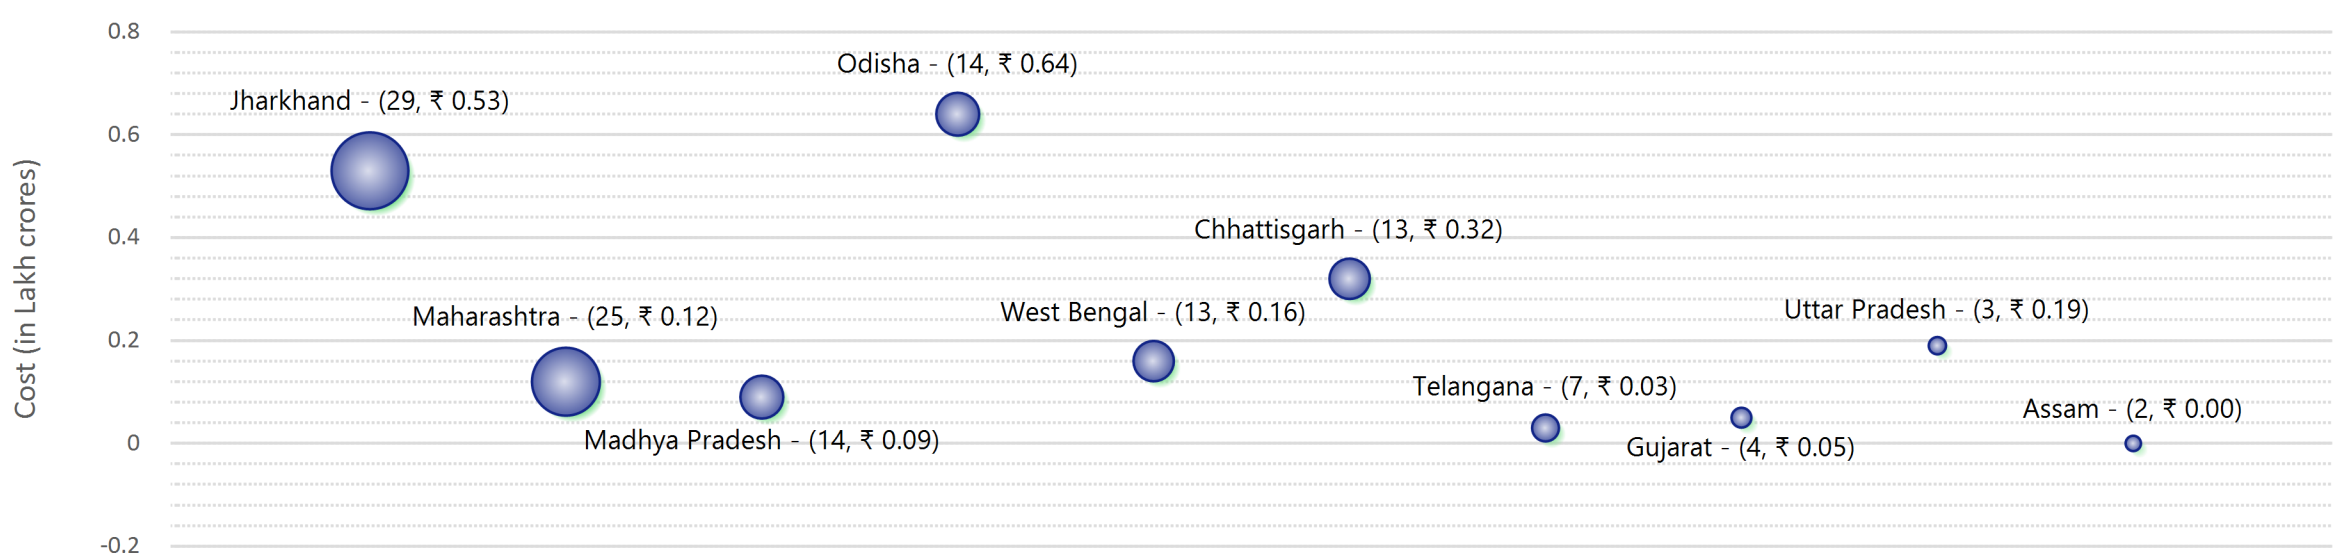

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	2,608	1
2	400259	GHATAMPUR THERMAL POWER PLANT 3 X 660 MW	17,238	21,781	20,744	94
3	400424	GEVRA OC [70 MTY]	11,816	11,816	6,813	78
4	400185	GOPALJI KANIHA OCP [10 TO 30 M]	8,416	6,108	1,746	17
5	400150	RPR MAGADH EXP OCP	7,254	7,254	1,599	38



Ministry of Petroleum & Natural Gas

DECEMBER 2025

111
Ongoing Projects

₹ 4,35,347
Original Cost
(crores)

₹ 5,02,635
Revised Cost
(crores)

₹ 2,87,775
(57.25% of Revised Cost)
Expenditure
(crores)

49 | ₹ 407,313
Mega Projects
Count | Original Cost (crores)


62 | ₹ 28,034
Major Projects
Count | Original Cost

2
Commissioned during month

0
Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

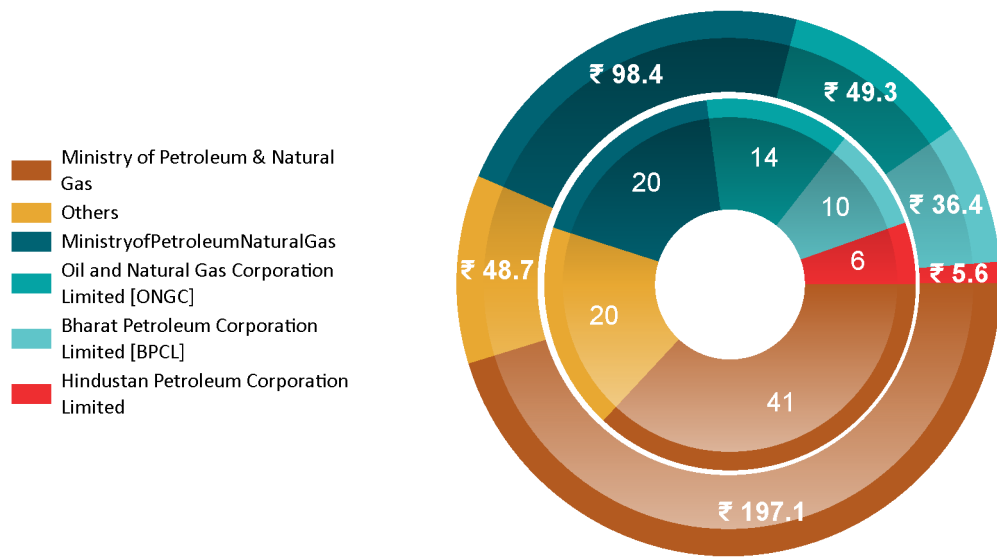


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

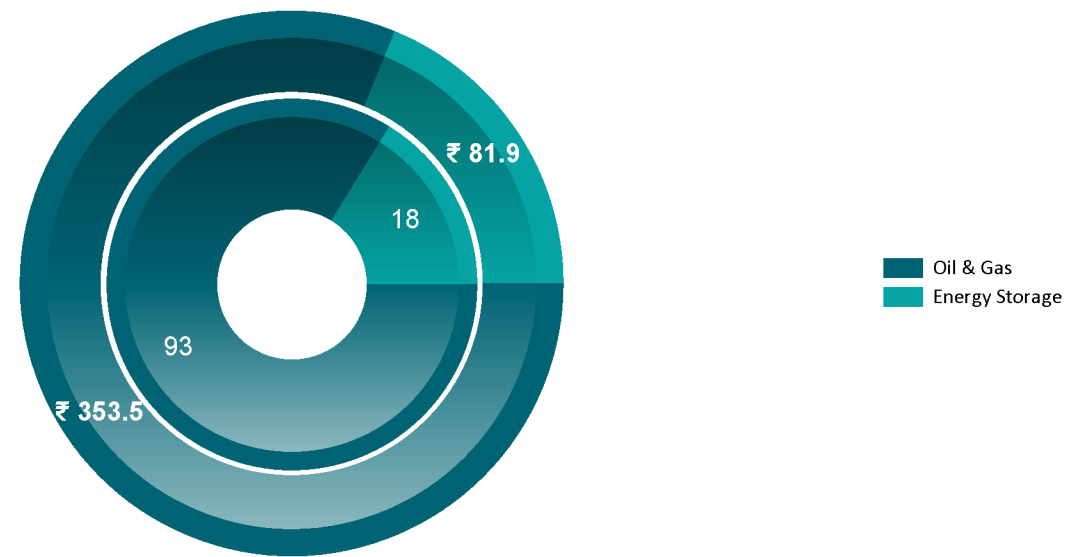


Physical & Financial progress (%) : Project count

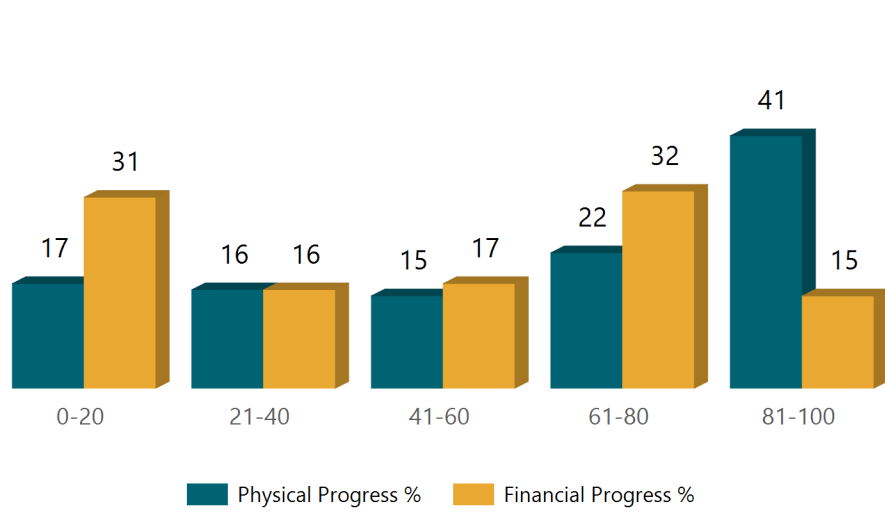

Cost Analytics : Major Sectors*

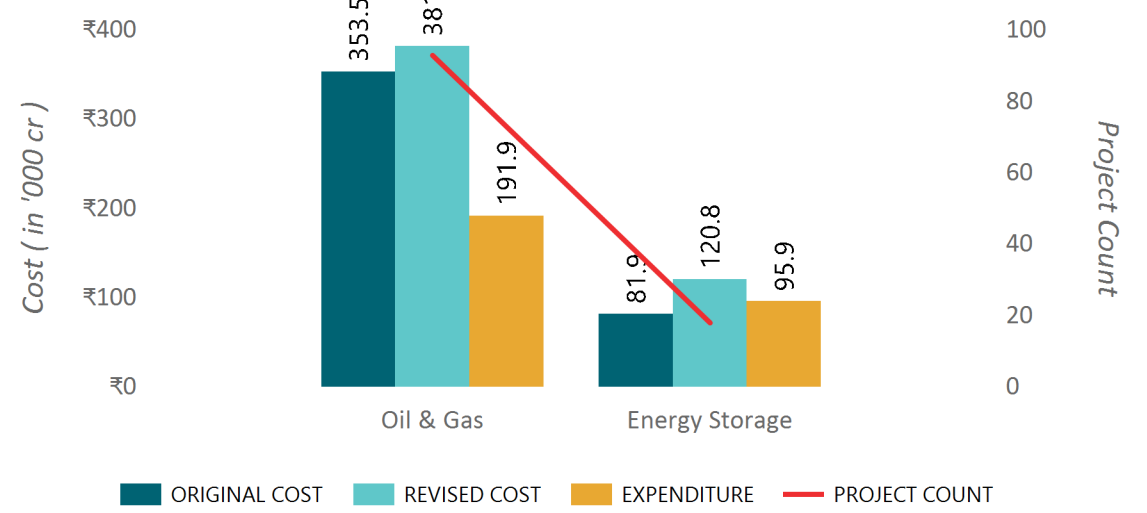

State Comparison : Major States*

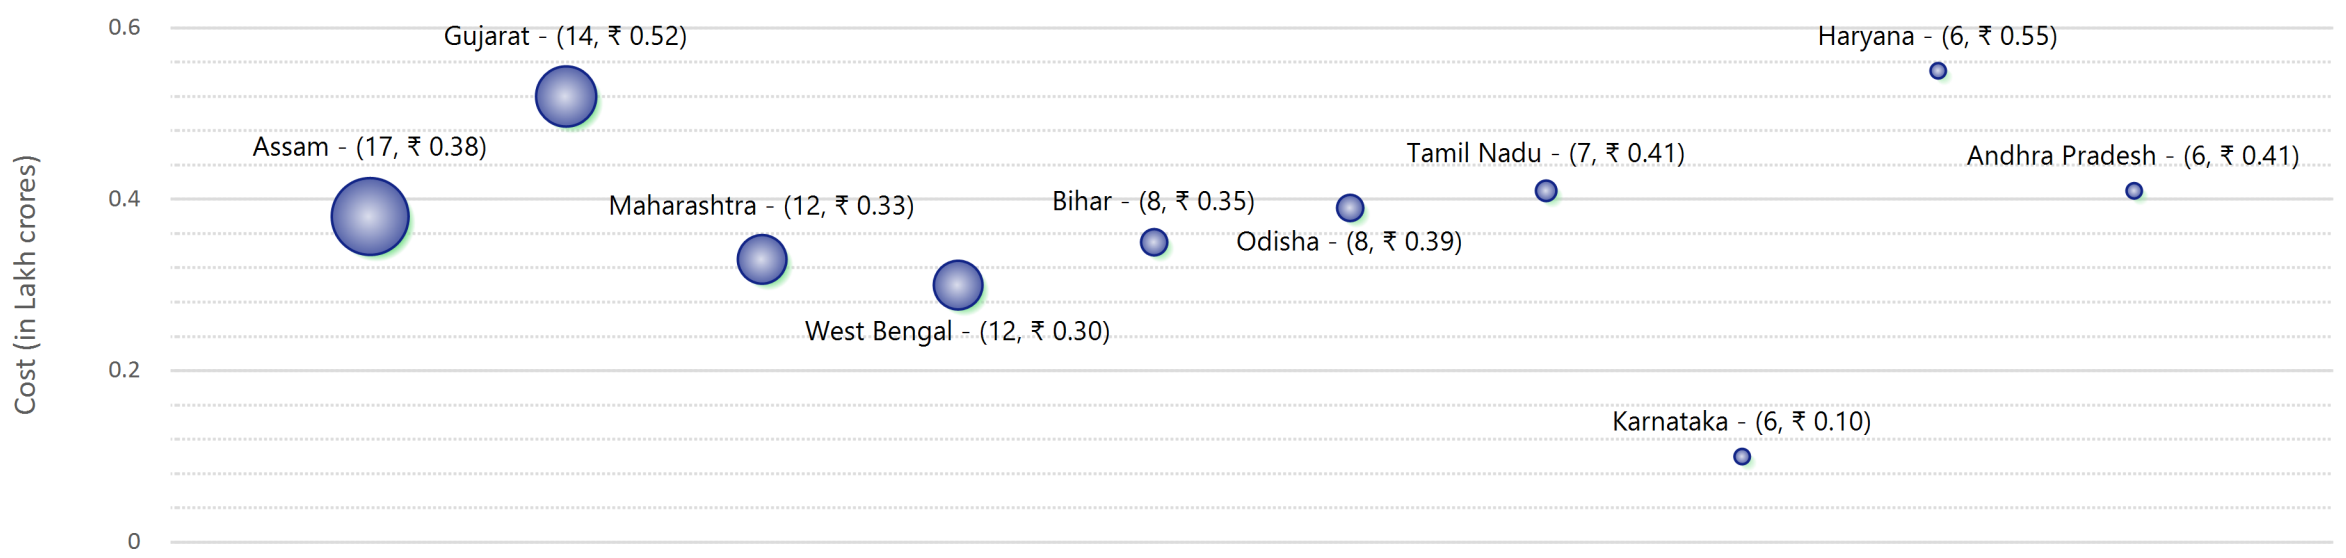

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	2,593	18
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	63,572	90
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	27,829	91
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	32,374	96
5	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,405	10



Ministry of Power

DECEMBER 2025

94

Ongoing Projects

₹ 3,83,043

Original Cost (crores)

₹ 4,43,529

Revised Cost (crores)

₹ 1,84,298

(41.55% of Revised Cost)

Expenditure (crores)

64 | ₹ 370,561

Mega Projects Count | Original Cost (crores)

30 | ₹ 12,482

Major Projects Count | Original Cost

3


Commissioned during month

1

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

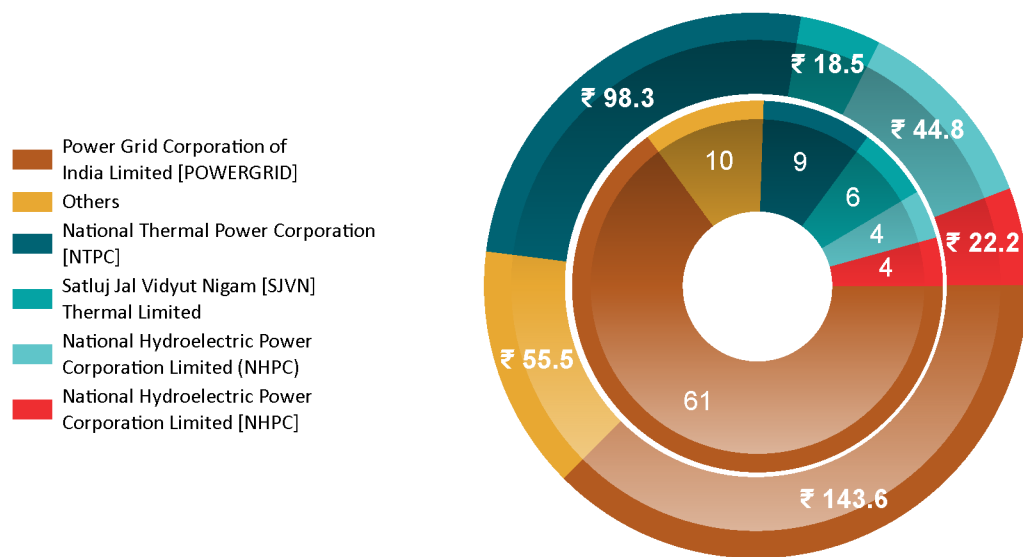


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

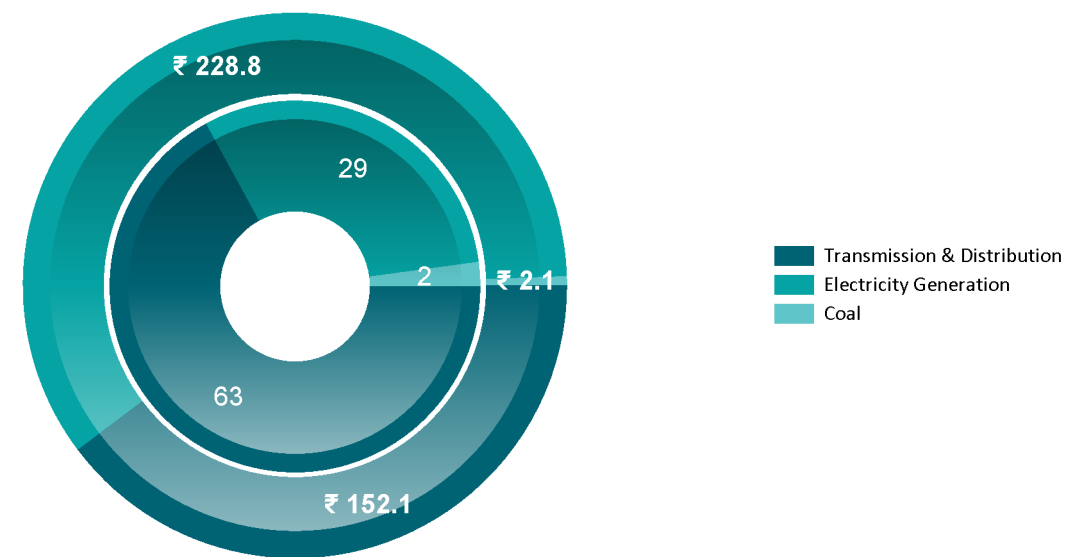


Physical & Financial progress (%) : Project count

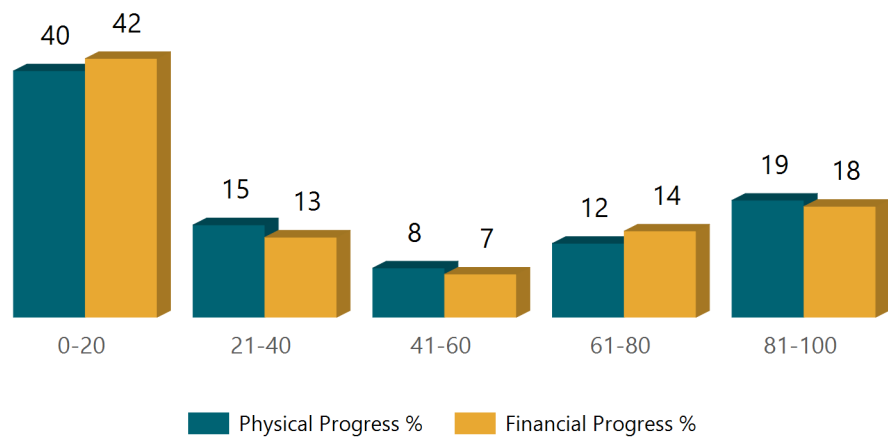

Cost Analytics : Major Sectors*

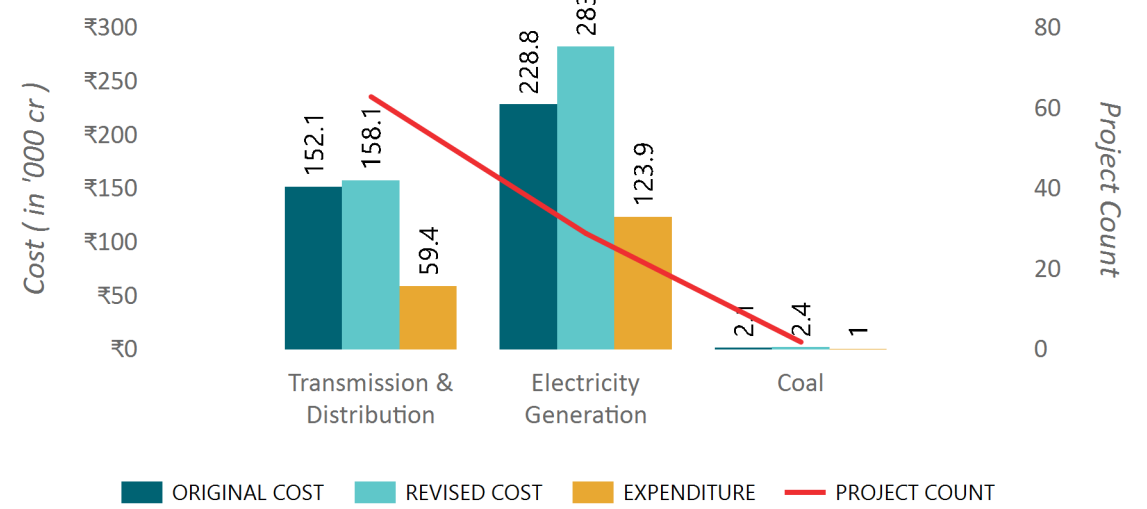

State Comparison : Major States*

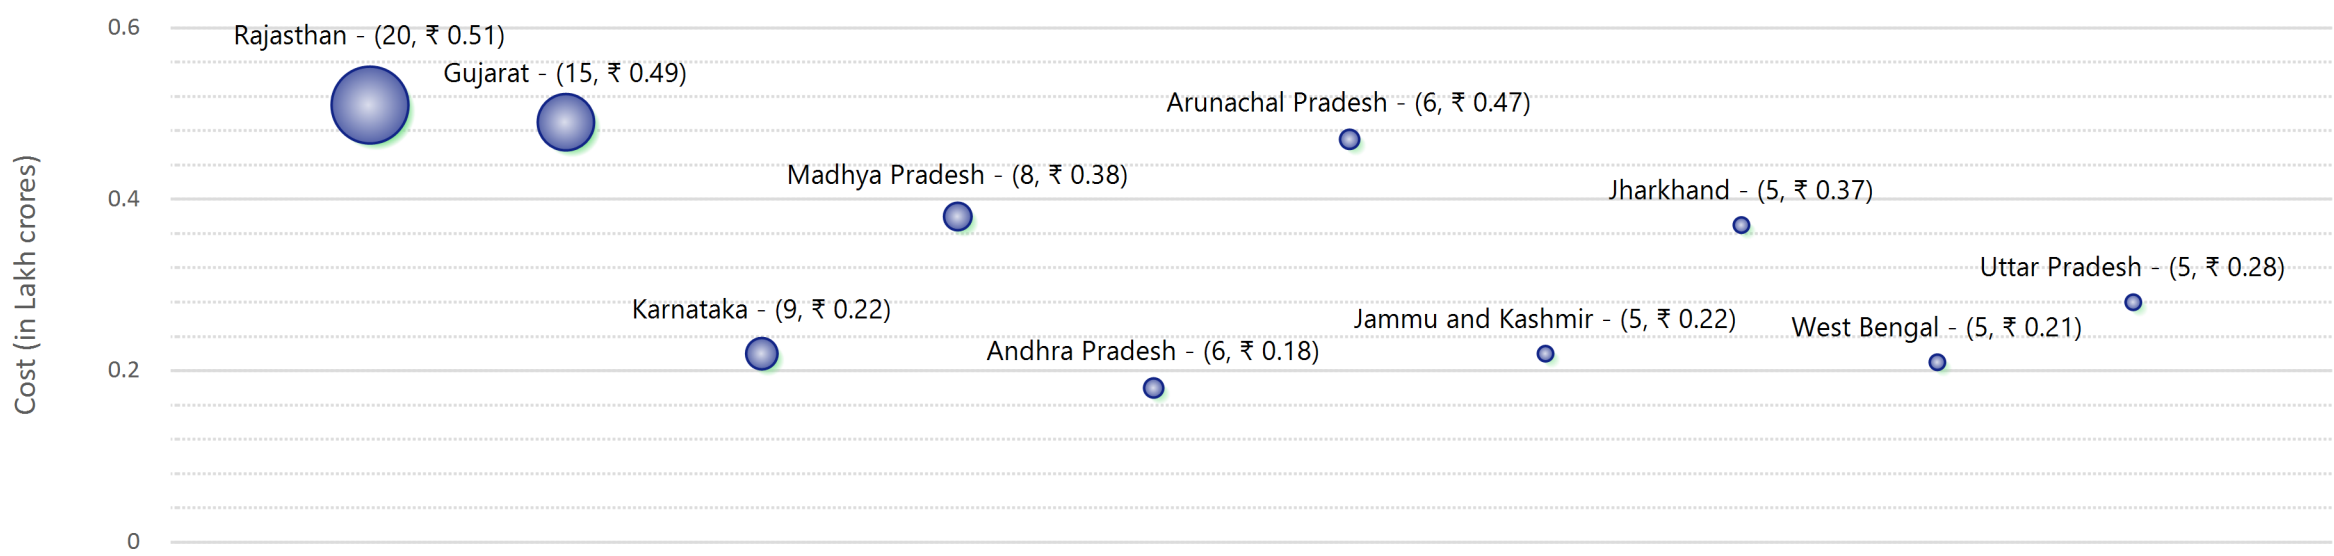

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	3,862	16
2	615347	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV NAME POWERGRID WEST CENTRAL TRANSMISSION LIMITED]	24,819	24,819	1,986	5
3	618976	GADARWARA SUPER THERMAL POWER PROJECT, STAGE-II [3X800 MW]	20,446	20,446	1,146	4
4	400261	PATRATU THERMAL POWER STATION EXPANSION PROJECT PHASE-I [3X800 MW]	18,668	20,302	18,166	86
5	400062	RAGHUNATHPUR THERMAL POWER STATION PHASE II [2X660 MW] AT RAGHUNATHPUR, PURULIA, WEST BENGAL	17,673	17,673	1,480	4



List of Tables






Table 1: Ministry-wise Ongoing Projects





Ministry-wise Ongoing Projects

DECEMBER 2025

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Real Estate	2	3841.25 3841.25	752.38
		Total	2	3,841.25	752.38
2	Department of Higher Education	Education	28	14512.44 14255	7689.22
		Total	28	14,512.44	7,689.22
3	Department of Sports	Education	1	906.47 611.74	565.17
		Total	1	906.47	565.17
4	Department of Telecommunications	Telecommunication	14	151923.46 274016	77210.7
		Total	14	151,923.46	77,210.70
5	Department of Water Resources, River Development & GR	Waste & Water	8	4039.12 4039.12	1643.05
		Water Resources	39	93740.23 193594	140622
		Total	47	97,779.35	142,265.05
6	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	25	21237.66 22451.7	9260.93
		Total	25	21,237.66	9,260.93
7	Ministry of Coal	Coal	113	156284.68 153741	47277.8
		Electricity Generation	8	51903.57 56446.7	26675.7
		Railways	2	3485.86 4250.56	1974
		Total	123	211,674.11	75,927.50
8	Ministry of Health & Family Welfare	Healthcare	8	12677.19 14452.9	4077.54
		Total	8	12,677.19	4,077.54
9	Ministry of Housing & Urban Affairs	Construction	1	644 644	116.18
		Real Estate	4	33749.85 33749.8	58.58
		Urban Public Transport	25	311946.96 332528	203575
		Waste & Water	23	5625.02 5649.35	4096.26
		Total	53	351,965.83	207,846.02
10	Ministry of Labour and Employment	Healthcare	13	3234.03 3466.61	1862.5
		Total	13	3,234.03	1,862.50
11	Ministry of Mines	Construction	1	255.37 255.37	93.39
		Metals & Mining	6	8344.36 10724.5	6765.91
		Total	7	8,599.73	6,859.30
12	Ministry of Petroleum & Natural Gas	Energy Storage	18	81884.05 120754	95874.3
		Oil & Gas	93	353462.93 381881	191901
		Total	111	435,346.98	287,775.30
13	Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58
		Inland Waterways	2	5546.18 5258.15	4100.49
		Shipping	9	15124.41 15290.9	9130.93
		Tourism, Hospitality & Wellness	1	573 1238.05	545.51
		Total	13	21,936.59	13,834.93
14	Ministry of Power	Coal	2	2083 2365	987.47
		Electricity Generation	29	228838.76 283079	123930
		Transmission & Distribution	63	152121.4 158085	59380.8
		Total	94	383,043.16	184,298.27
15	Ministry of Railways	Railways	249	702266.73 852603	686201
		Total	249	702,266.73	686,201.00
16	Ministry of Road Transport & Highways	Roads & Highways	584	527441.16 537799	185964
		Total	584	527,441.16	185,964.00
17	Ministry of Steel	Metals & Mining	1	1700 1756.2	155.07
		Steel	19	18161.41 21399.7	8617.56
		Total	20	19,861.41	8,772.63
Total			1392	2,968,247.55	1,901,162.44



Table 2: State-wise Ongoing Projects





Ongoing Projects State-Wise

DECEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	6	19714.58 22972.8	12511.42
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	177 197	383.41
		Ministry of Railways	Railways	1	819 819	580.51
	PAN India	Department of Telecommunications	Telecommunication	5	141080.68 263402	73544.16
		Ministry of Railways	Railways	1	274.39 274.39	0.00
Total				14	162065.65	87019.50
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 209.88	0.00
		Total				1
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	2139.44 2139.44	568.22
		Department of Higher Education	Education	1	305 305	51.33
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	2369.02
		Department of Water Resources, River Development & GR	Water Resources	3	10901.5 57269.5	27321.88
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1224.86 1224.86	741.32
		Ministry of Housing & Urban Affairs	Waste & Water	1	172.22 172.22	88.86
		Ministry of Labour and Employment	Healthcare	1	384.27 384.27	167.37
		Ministry of Petroleum & Natural Gas	Energy Storage	2	2898.34 3050	2417.92
			Oil & Gas	4	37804 37864	32778.98
		Ministry of Power	Transmission & Distribution	6	17931.23 17931.2	5796.55
		Ministry of Railways	Railways	25	47518.61 55475.5	33329.05
Ministry of Road Transport & Highways	Roads & Highways	52	48187.47 47907.5	16351.06		
Total				102	176614.11	121981.56
4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 592.61	550.61
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	299.02
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6622.00
		Ministry of Power	Electricity Generation	4	41850.64 61640.8	29708.73
			Transmission & Distribution	2	4963.8 9338.7	7809.26
		Ministry of Railways	Railways	1	435 1250	805.31
		Ministry of Road Transport & Highways	Roads & Highways	6	3335.98 3296.08	457.02
Total				16	61698.52	46251.95
5	Assam	Department of Higher Education	Education	1	153.71 153.71	125.03
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	299.02
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 256.16	44.70
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1712 2520	2514.59
		Ministry of Coal	Coal	2	449.23 449.23	187.08
		Ministry of Labour and Employment	Healthcare	1	143.23 154.75	116.08
		Ministry of Petroleum & Natural Gas	Energy Storage	3	10768.4 11947.4	10513.11
			Oil & Gas	14	27584.43 37939.2	27750.59
		Ministry of Power	Electricity Generation	1	6285.33 26075.5	25718.57
			Transmission & Distribution	1	5111.33 6700	5442.41
		Ministry of Railways	Railways	8	18227.15 19942.2	10778.28
Ministry of Road Transport & Highways	Roads & Highways	32	26070.92 25618.5	1812.54		
Total				66	98017.38	85302.00
6	Bihar	Department of Higher Education	Education	1	499.21 499.21	445.97
		Department of Telecommunications	Telecommunication	4	4220.71 3992.24	1417.07
		Department of Water Resources, River Development & GR	Waste & Water	5	2351.43 2351.43	1303.45
			Water Resources	2	2193.34 3088.88	614.84



Ongoing Projects State-Wise

DECEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3541.56 3541.56	1425.64
		Ministry of Health & Family Welfare	Healthcare	1	1264 1264	0.00
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	13365.77 13365.8	4670.21
			Waste & Water	1	158.78 158.78	69.52
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	10270.18
			Oil & Gas	7	25153.5 27018.2	13941.35
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3717.08
		Ministry of Power	Electricity Generation	1	10439.09 13756.6	12911.13
			Transmission & Distribution	3	3119.63 3119.63	10.25
		Ministry of Railways	Railways	22	50016.25 54484.6	76561.12
Ministry of Road Transport & Highways	Roads & Highways	44	50936.38 48685.1	13684.01		
Total				97	182856.83	141041.82
7	Chhattisgarh	Department of Higher Education	Education	1	1188.97 1188.97	0.00
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	2369.02
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 1109.33	855.96
		Ministry of Coal	Coal	12	30153.29 30153.3	12431.78
			Railways	1	1686.22 1686.22	484.26
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	10613.29 11024	6993.27
		Ministry of Power	Electricity Generation	2	25321 25897	4552.60
		Ministry of Railways	Railways	20	36771.79 41215.9	20642.99
		Ministry of Road Transport & Highways	Roads & Highways	11	8367.23 9174.44	3554.30
		Ministry of Steel	Metals & Mining	1	1700 1756.2	155.07
Steel	6		7530.14 10050.1	5830.53		
Total				62	131321.36	57869.78
8	Dadra & Nagar Haveli and Daman & Diu	Ministry of Housing & Urban Affairs	Waste & Water	1	210 210	0.00
		Ministry of Power	Transmission & Distribution	1	4546.26 4546.26	4358.49
		Ministry of Railways	Railways	1	108000 108000	85337.89
Total				3	112756.26	89696.38
9	Delhi	Department of Higher Education	Education	2	706.49 709.42	325.28
		Department of Telecommunications	Telecommunication	1	248.2 248.2	236.91
		Ministry of Health & Family Welfare	Healthcare	2	4799.19 4799.19	24.68
		Ministry of Housing & Urban Affairs	Real Estate	1	32850 32850	0.00
			Urban Public Transport	4	69853.45 69853.4	45842.54
		Ministry of Power	Transmission & Distribution	2	2331 2331	1708.24
		Ministry of Railways	Railways	5	19348.46 19348.5	1225.05
		Ministry of Road Transport & Highways	Roads & Highways	2	3557.38 4713.79	3143.96
Total				19	133694.17	52506.66
10	Goa	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	255.69 255.69	154.30
		Ministry of Railways	Railways	2	5804.49 6182.62	6420.85
		Ministry of Road Transport & Highways	Roads & Highways	2	868.22 790.9	102.44
Total				5	6928.4	6677.59
11	Gujarat	Department of Higher Education	Education	1	490.63 490.63	316.05
		Department of Telecommunications	Telecommunication	1	336.89 301.13	237.19
		Department of Water Resources, River Development & GR	Water Resources	2	25739.93 40082.8	36817.84
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1305 1551	739.77
		Ministry of Coal	Electricity Generation	4	5421.78 5421.78	1531.38



Ongoing Projects State-Wise

DECEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
11	Gujarat	Ministry of Health & Family Welfare	Healthcare	1	1195 1195	774.60
		Ministry of Housing & Urban Affairs	Real Estate	1	539 539	39.63
			Urban Public Transport	3	28177.49 30329	25315.14
			Waste & Water	1	200 200	100.00
		Ministry of Labour and Employment	Healthcare	3	973.35 973.35	290.30
		Ministry of Petroleum & Natural Gas	Energy Storage	3	19472.86 19420.4	15702.67
			Oil & Gas	11	32704.12 32296.3	24180.17
		Ministry of Ports, Shipping and Waterways	Shipping	3	4514.64 4681.1	1287.01
			Tourism, Hospitality & Wellness	1	573 1238.05	545.51
		Ministry of Power	Electricity Generation	1	339.35 339.35	317.59
			Transmission & Distribution	14	48255.1 48255.1	13027.50
		Ministry of Railways	Railways	26	186558.1 263078	222820.90
		Ministry of Road Transport & Highways	Roads & Highways	20	21459.77 26094.4	15619.11
Total				97	378256.01	359662.36
12	Haryana	Ministry of Health & Family Welfare	Healthcare	1	1299 1646.43	479.98
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	6230.99 6230.99	72.43
			Waste & Water	2	491.2 491.2	387.03
		Ministry of Petroleum & Natural Gas	Energy Storage	1	9028 9028	7394.54
			Oil & Gas	5	45925.07 49596.1	37642.94
		Ministry of Power	Transmission & Distribution	3	11696 11696	1644.80
		Ministry of Railways	Railways	4	53464 126368	125687.83
		Ministry of Road Transport & Highways	Roads & Highways	8	9252 9548.4	4122.25
Total				25	137386.26	177431.80
13	Himachal Pradesh	Department of Higher Education	Education	3	811.15 921.89	652.55
		Department of Telecommunications	Telecommunication	1	336.89 301.13	237.19
		Ministry of Power	Electricity Generation	4	7728.04 13783.7	4389.81
		Ministry of Railways	Railways	3	17005 17005.1	97254.21
		Ministry of Road Transport & Highways	Roads & Highways	13	9084.05 10926.2	3825.83
Total				24	34965.13	106359.59
14	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 500.91	484.52
		Department of Telecommunications	Telecommunication	1	336.89 301.13	237.19
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 861.37	248.88
		Ministry of Health & Family Welfare	Healthcare	1	1828 2160.84	1491.97
		Ministry of Petroleum & Natural Gas	Energy Storage	1	676.89 715.89	576.69
			Oil & Gas	2	1059.9 1059.9	253.81
		Ministry of Power	Electricity Generation	4	22207.77 27945.1	13958.90
			Transmission & Distribution	1	218.6 218.6	2.71
Ministry of Road Transport & Highways	Roads & Highways	21	23044.71 22716.7	8785.51		
Total				33	50659.06	26040.18
15	Jharkhand	Department of Telecommunications	Telecommunication	3	7147.17 7147.17	2369.02
		Department of Water Resources, River Development & GR	Water Resources	2	5430.04 12010.3	5957.45
		Ministry of Coal	Coal	28	51354.95 51119.3	10763.01
			Railways	1	1799.64 2564.34	1489.74
		Ministry of Housing & Urban Affairs	Waste & Water	3	654.14 654.14	403.16
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	10270.18



Ongoing Projects State-Wise

DECEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
15	Jharkhand	Ministry of Petroleum & Natural Gas	Oil & Gas	3	2010.07 2010.07	640.90
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3717.08
		Ministry of Power	Coal	2	2083 2365	987.47
			Electricity Generation	2	33026 34660	19704.88
			Transmission & Distribution	1	1842.25 1842.25	1648.05
		Ministry of Railways	Railways	14	46589.07 47449.7	15276.82
		Ministry of Road Transport & Highways	Roads & Highways	18	22680.79 22167.5	10121.82
		Ministry of Steel	Steel	6	2854.58 3572.87	1559.19
Total				85	193068.88	84908.77
16	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1701.81 1701.81	184.16
		Department of Water Resources, River Development & GR	Water Resources	1	770.16 1606.07	1515.32
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1143.4 1143.4	599.57
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	41193.24 45483.2	39001.19
			Waste & Water	2	337.69 337.69	178.89
		Ministry of Labour and Employment	Healthcare	2	428.92 428.92	235.37
		Ministry of Petroleum & Natural Gas	Energy Storage	1	678 1732	893.48
			Oil & Gas	5	9662 12693.6	9114.41
		Ministry of Ports, Shipping and Waterways	Shipping	1	153.23 153.23	24.00
		Ministry of Power	Transmission & Distribution	9	21604 21604	4676.94
		Ministry of Railways	Railways	18	41130.29 47548.9	20460.00
		Ministry of Road Transport & Highways	Roads & Highways	24	20248.82 19697.4	10444.14
Ministry of Steel	Steel	1	1043.63 1043.63	375.39		
Total				70	140095.19	87702.86
17	Kerala	Department of Higher Education	Education	2	2533.45 2744.4	673.20
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	484.57 484.57	116.14
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1957.05 1957.05	516.92
		Ministry of Petroleum & Natural Gas	Oil & Gas	4	9126.87 11871	5597.60
		Ministry of Railways	Railways	3	2846 5183.64	2930.14
		Ministry of Road Transport & Highways	Roads & Highways	15	41724.33 44771.7	13485.33
Total				26	58672.27	23319.33
18	Ladakh	Department of Telecommunications	Telecommunication	1	336.89 301.13	237.19
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480 640	484.60
		Ministry of Road Transport & Highways	Roads & Highways	3	1184.27 1184.27	0.00
Total				5	2001.16	721.79
19	Madhya Pradesh	Department of Higher Education	Education	1	496.28 496.28	56.35
		Department of Telecommunications	Telecommunication	3	3883.82 3691.11	1179.88
		Department of Water Resources, River Development & GR	Water Resources	3	2628.27 2941.14	2982.68
		Ministry of Coal	Coal	14	8634.02 8634.02	3543.56
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	14442.2 14442.2	8262.56
			Waste & Water	4	1243.05 1267.38	1124.28
		Ministry of Mines	Metals & Mining	1	1856.36 1856.36	950.94
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10088 10088	8217.69
			Oil & Gas	3	53003.25 53414	9840.10
		Ministry of Power	Electricity Generation	1	20446 20446	1145.83
Transmission & Distribution	7		17765 17765	4705.14		



Ongoing Projects State-Wise

DECEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
19	Madhya Pradesh	Ministry of Railways	Railways	19	58468.02 72465.1	46251.50
		Ministry of Road Transport & Highways	Roads & Highways	18	11067.7 11053.4	4005.01
		Total		77	204021.97	92265.52
20	Maharashtra	Department of Telecommunications	Telecommunication	4	7608.59 7608.59	2535.04
		Department of Water Resources, River Development & GR	Water Resources	11	22660.36 32345.7	34616.74
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	348.09
		Ministry of Coal	Coal	25	12455.88 12455.9	2875.77
		Ministry of Housing & Urban Affairs	Urban Public Transport	9	60255.66 74395.7	34603.37
			Waste & Water	4	814.94 814.94	662.68
		Ministry of Labour and Employment	Healthcare	3	884.31 886.08	606.60
		Ministry of Petroleum & Natural Gas	Energy Storage	1	281.35 389.67	249.50
			Oil & Gas	11	32676.16 35504.2	20955.37
		Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58.00
			Shipping	2	6900 6900	6064.89
		Ministry of Power	Transmission & Distribution	4	30596.67 30596.7	6459.46
		Ministry of Railways	Railways	34	267898.34 358579	272544.48
Ministry of Road Transport & Highways	Roads & Highways	52	49332.36 49549.1	14283.95		
Total		162	493558.1	396863.94		
21	Manipur	Department of Sports	Education	1	906.47 611.74	565.17
		Department of Water Resources, River Development & GR	Water Resources	1	1449.44 1822.24	1837.91
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499 499	160.06
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6622.00
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5442.41
		Ministry of Railways	Railways	1	14323 21885.9	15824.48
		Ministry of Road Transport & Highways	Roads & Highways	22	8432.41 8432.41	4453.04
Total		28	39986.65	34905.07		
22	Meghalaya	Department of Higher Education	Education	1	494.52 429.7	426.07
		Department of Telecommunications	Telecommunication	1	971.96 971.96	215.36
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6622.00
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5442.41
		Ministry of Road Transport & Highways	Roads & Highways	9	4138.06 4138.06	182.58
Total		13	19980.87	12888.42		
23	Mizoram	Department of Higher Education	Education	1	474.23 474.23	167.55
		Ministry of Petroleum & Natural Gas	Energy Storage	1	225.71 225.71	16.32
			Oil & Gas	1	9265 9265	6622.00
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5442.41
		Ministry of Road Transport & Highways	Roads & Highways	11	6992.95 7137.51	587.89
Total		15	22069.22	12836.17		
24	Nagaland	Department of Higher Education	Education	1	275.63 275.63	261.70
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	9492.62 9492.62	6637.85
			Transmission & Distribution	1	5111.33 6700	5442.41
		Ministry of Railways	Railways	2	8786.7 8786.7	5842.09
		Ministry of Road Transport & Highways	Roads & Highways	18	5867.05 6421.1	228.62
Total		24	29533.33	18412.67		
25	Odisha	Department of Higher Education	Education	1	1229.32 843.09	835.60
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	2369.02



Ongoing Projects State-Wise

DECEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
25	Odisha	Department of Water Resources, River Development & GR	Water Resources	2	1556.46 5291.33	5427.87
		Ministry of Coal	Coal	13	37048.73 34740.4	13642.46
			Electricity Generation	1	27212.96 27213	2607.89
		Ministry of Labour and Employment	Healthcare	1	164.6 164.6	16.40
		Ministry of Mines	Metals & Mining	4	6322 8702.17	5679.97
		Ministry of Petroleum & Natural Gas	Energy Storage	2	12886.34 14217	12553.16
			Oil & Gas	6	25800.35 24283.5	16656.64
		Ministry of Ports, Shipping and Waterways	Shipping	1	3004.63 3004.63	1277.52
		Ministry of Power	Electricity Generation	1	11843.75 12543	5347.06
			Transmission & Distribution	1	342.69 342.69	6.85
		Ministry of Railways	Railways	28	43414.1 49171.3	31196.37
			Railways	1	267.61 267.61	0.00
		Ministry of Road Transport & Highways	Roads & Highways	20	12259.74 14260.5	5144.48
Total				85	190500.45	102761.29
26	Puducherry	Department of Higher Education	Education	1	618.34 544.34	530.45
		Ministry of Railways	Railways	1	713 981	633.24
		Ministry of Road Transport & Highways	Roads & Highways	2	4488.17 4315.67	1288.86
Total				4	5819.51	2452.55
27	Punjab	Department of Higher Education	Education	2	559.3 559.3	320.39
		Department of Water Resources, River Development & GR	Water Resources	2	3727.07 5177.86	5182.41
		Ministry of Housing & Urban Affairs	Waste & Water	2	545.53 545.53	374.66
		Ministry of Petroleum & Natural Gas	Oil & Gas	5	12693.36 12693.4	8191.03
		Ministry of Power	Transmission & Distribution	1	5969 5969	837.04
		Ministry of Railways	Railways	3	15702.64 15703	96835.77
		Ministry of Road Transport & Highways	Roads & Highways	24	31275.39 34504.4	16008.20
Total				39	70472.29	127749.50
28	Rajasthan	Department of Telecommunications	Telecommunication	2	758.54 530.07	380.25
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	2874 2874	803.08
		Ministry of Coal	Electricity Generation	1	1813 1813	1627.06
		Ministry of Petroleum & Natural Gas	Energy Storage	3	52618.05 88948.1	71132.20
			Oil & Gas	2	10599 10599	6714.28
		Ministry of Power	Transmission & Distribution	20	50547.23 50547.2	19497.19
		Ministry of Railways	Railways	22	87820.03 163243	140848.77
		Ministry of Road Transport & Highways	Roads & Highways	16	10383.1 9938.64	5813.09
Total				69	217412.95	246815.92
29	Sikkim	Department of Higher Education	Education	2	999.82 924.82	409.78
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 323.26	51.21
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6622.00
		Ministry of Power	Electricity Generation	2	6686.33 7576.15	5503.93
			Transmission & Distribution	1	4754.42 9129.32	7809.22
		Ministry of Railways	Railways	1	7877 11775	9861.45
		Ministry of Road Transport & Highways	Roads & Highways	6	2629.21 2525.29	1.91
Total				14	32535.04	30259.50
30	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1207 1207	208.06
		Ministry of Coal	Electricity Generation	1	218.03 218.03	165.50
		Ministry of Health & Family Welfare	Healthcare	1	1264 2021.51	366.59



Ongoing Projects State-Wise

DECEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
30	Tamil Nadu	Ministry of Housing & Urban Affairs	Urban Public Transport	1	63246 63246	30211.38
		Ministry of Labour and Employment	Healthcare	1	152.95 177.01	107.83
		Ministry of Mines	Metals & Mining	1	166 166	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	2334 3448.71	1882.97
			Oil & Gas	4	38385 46153	6290.91
		Ministry of Power	Transmission & Distribution	1	548 548	102.46
		Ministry of Railways	Railways	7	8370.7 11242.2	6033.89
		Ministry of Road Transport & Highways	Roads & Highways	24	36073.87 35226.7	12743.31
Total				45	151965.55	58247.90
31	Telangana	Department of Higher Education	Education	1	262 262	194.37
		Department of Telecommunications	Telecommunication	3	3923.59 3923.59	1202.84
		Department of Water Resources, River Development & GR	Water Resources	4	11670.14 24129.6	11936.34
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	348.09
		Ministry of Coal	Coal	7	2986.57 2986.57	1721.56
		Ministry of Health & Family Welfare	Healthcare	1	1028 1365.95	939.72
		Ministry of Housing & Urban Affairs	Construction	1	644 644	116.18
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	215 215	38.16
		Ministry of Power	Transmission & Distribution	2	5694.56 5694.56	5125.94
		Ministry of Railways	Railways	11	19213.75 22977.8	12716.38
		Ministry of Road Transport & Highways	Roads & Highways	32	17213.24 18825	6692.74
Total				64	63351.33	41032.32
32	Tripura	Ministry of Petroleum & Natural Gas	Energy Storage	1	656 656	526.86
			Oil & Gas	2	9474.33 9396.51	6693.95
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5442.41
		Ministry of Road Transport & Highways	Roads & Highways	8	4890.7 4915.23	0.00
Total				12	20132.36	12663.22
33	Uttar Pradesh	Department of Higher Education	Education	1	246 246	199.71
		Department of Telecommunications	Telecommunication	4	4220.71 3992.24	1417.07
		Department of Water Resources, River Development & GR	Waste & Water	2	1532.96 1532.96	243.43
			Water Resources	3	2953.27 6309.81	4689.88
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3949.13 3949.13	892.25
		Ministry of Coal	Coal	2	1328.09 1328.09	1087.06
			Electricity Generation	1	17237.8 21780.9	20743.86
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	49730.1 49730.1	42464.09
			Waste & Water	2	797.47 797.47	707.18
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11068.45 11068.5	8468.24
			Oil & Gas	3	17824.68 18213.1	1718.69
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3717.08
		Ministry of Power	Electricity Generation	1	17195 17195	2418.36
			Transmission & Distribution	4	10482.81 10482.8	2394.58
		Ministry of Railways	Railways	25	93620.38 167255	146306.15
Ministry of Road Transport & Highways	Roads & Highways	63	62299 57497.2	24085.68		
Total				120	299855.03	261553.31
34	Uttarakhand	Department of Higher Education	Education	1	650.85 650.85	261.11
		Department of Water Resources, River Development & GR	Water Resources	1	2584.1 2584.1	987.61



Ongoing Projects State-Wise

DECEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
34	Uttarakhand	Ministry of Housing & Urban Affairs	Real Estate	1	150.97 150.97	18.95
		Ministry of Labour and Employment	Healthcare	1	102.4 297.63	322.55
		Ministry of Power	Electricity Generation	3	11663.95 25651.4	19943.55
		Ministry of Railways	Railways	1	38953 38953	26840.95
		Ministry of Road Transport & Highways	Roads & Highways	10	6925.68 6926.79	2526.34
Total			18	61030.95	50901.06	
35	West Bengal	Department of Higher Education	Education	1	500 442	401.60
		Department of Telecommunications	Telecommunication	2	3462.17 3462.17	1036.82
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 154.73	96.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1877.3 1877.3	469.55
		Ministry of Coal	Coal	13	15863.74 15863.7	2905.50
		Ministry of Mines	Construction	1	255.37 255.37	93.39
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	10270.18
			Oil & Gas	11	19590.65 20535.2	12100.56
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3717.08
			Shipping	2	551.91 551.91	477.51
		Ministry of Power	Electricity Generation	3	20091.84 21644.6	4027.48
			Transmission & Distribution	2	751.63 751.63	7.25
		Ministry of Railways	Railways	16	49559.1 60771	35486.52
		Ministry of Road Transport & Highways	Roads & Highways	10	7013.9 7267.45	1980.82
		Ministry of Steel	Steel	6	6733.06 6733.06	852.45
Total			72	142002.58	73922.88	



Table 3: Completed Projects





Completed Projects During Month

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
Department of Higher Education						
Education						
1	Additional Infrastructure at IISc Bangalore-RCC Monolithic for Men Hostel S14, Women Hostel S11, Postdoctoral Hostel S12 2 Block, International Hostel S 12, D&E Block S 12 2 Block FR. (IISc Bangalore) 610940	Karnataka	08/2021 (08/2021)	12/2025 (03/2024) (12/2025)	420.41 (420.41)	367.92
2	Hostel 4 -Earlier Known as Hostel 20 (Indian Institute of Technology, Bombay) 612135	Maharashtra	09/2022 (12/2023)	12/2025 (09/2025) (12/2025)	182.33 (-)	178.17
Total (2)					602.74	546.09
Department of Telecommunications						
Telecommunication						
3	OPTICAL TRANSPORT NETWORK [OTN] PH-4 IN BSNL (BSNL) 709858	PAN India	02/2024 (02/2024)	10/2025 (08/2025) (10/2025)	810.99 (-)	786.86
Total (1)					810.99	786.86
Ministry of Civil Aviation						
Aviation & Aviation Infrastructure						
4	Construction of New Terminal Building, Second Link Taxi Track, Apron Expansion, and associated works at Prayagraj Airport- On Design & Build Basis. (Airport Authority of India [AAI]) 612063	Uttar Pradesh	(08/2023)	10/2025 (11/2024) (10/2025)	219.18 (274.38)	215.51
Total (1)					219.18	215.51
Ministry of Coal						
Coal						
5	CHHAL OC SEAM III [6 MTY] (South Eastern Coalfields Limited [SECL]) 400145	Chhattisgarh	12/2013 (12/2013)	12/2025 (03/2022) (01/2026)	610.63 (-)	583.26
Total (1)					610.63	583.26
Ministry of Housing & Urban Affairs						
Waste & Water						
6	Nagpur Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) 702842	Maharashtra	12/2015 (08/2018)	01/2026 (03/2023) (01/2026)	273.78 (271.86)	267.57
Total (1)					273.78	267.57
Ministry of Labour and Employment						
Healthcare						
7	Construction of 100 bedded ESIC Hospital & 32 nos. of Staff qtrs at OMPURA J&K. (Employee's State Insurance Company [ESIC]) 612239	Jammu and Kashmir	09/2019 (12/2021)	12/2025 (09/2024) (12/2025)	131.05 (164.93)	162.05
Total (1)					131.05	162.05
Ministry of Petroleum & Natural Gas						
Oil & Gas						
8	Debottlenecking and Augmentation of Cryogenic facilities at Uran LPG Import Terminal (Department of Water Resources, River Development & GR) 400158	Maharashtra	04/2021 (04/2021)	12/2025 (02/2024) (12/2025)	1164.69 (1629.86)	1048.74
9	Construction of lube oil blending plant at Rasayani (Ministry of Petroleum & Natural Gas) 610985	Maharashtra	05/2022 (05/2022)	12/2025 (12/2023) (12/2025)	423.39 (526.26)	333.48
Total (2)					1588.08	1382.22
Ministry of Power						
Electricity Generation						
10	BIKANER SOLAR POWER PROJECT (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) 709748	Rajasthan	10/2021 (05/2022)	12/2025 (04/2024) (12/2025)	5491.89 (-)	5523.11
11	Khurja super Thermal Power Plant [2X660 MW] (THDC India Limited) 602194	Uttar Pradesh	03/2019 (08/2019)	09/2025 (02/2024) (09/2025)	11089.42 (13276.2)	12888.23
Total (2)					16581.31	18411.34
Transmission & Distribution						
12	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan[8.1 GW] under phase-II- Part E (Power Grid Corporation of India Limited [POWERGRID]) 611659	Rajasthan	03/2023 (03/2023)	01/2026 (09/2024) (01/2026)	1433.28 (1433)	1433
Total (1)					1433.28	1433
Ministry of Railways						
Railways						
13	Adraj Moti Vijapur 40 Kms (Western Railway (WR) - II) 611937	Gujarat	05/2022 (05/2022)	12/2025 (05/2026) (12/2025)	417.53 (417.53)	513.61
14	Western Region Video Surveillance Project (RCIL) 705300	PAN India	06/2020 (04/2023)	01/2026 (12/2023) (07/2026)	227.59 (-)	0
15	Phephna-Indara, Mau-Shahganj doubling excluding Indara-Mau (RVNL - I) 705779	Uttar Pradesh	05/2017 (10/2019)	12/2025 (12/2024) (12/2025)	1178 (2215)	2217.85



Completed Projects During Month

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	Janghai-Phaphamau Doubling Rail Line Project (RVNL) 705784	Uttar Pradesh	11/2018 (03/2020)	01/2025 (03/2025) (01/2025)	357 (978.77)	844.84
	Total (4)				2180.12	3576.3
	Ministry of Steel					
	Steel					
17	Installation of 4th Slab Caster along with its Auxiliaries and a New Ladle Furnace in SMS-II at Rourkela Steel Plant (Steel Authority of India Limited [SAIL]) 400065	Odisha	01/2022 (02/2022)	NA (05/2025) (09/2025)	1105.23 (-)	809.53
	Total (1)				1105.23	809.53

Note: Cumulative Expenditure is as per last reporting by Central Line Ministries/ Departments on the IPM portal, this may not be the actual completion cost.




Table 4: Newly Added Projects





Newly Added Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
Ministry of Civil Aviation					
Aviation & Aviation Infrastructure					
1	Development of New Greenfield Airport at Bundi, Kota Rajasthan. (Airport Authority of India [AAI]) (618977)	Rajasthan	08/2025 (10/2025)	10/2027 (-)	1507 (-)
Total (1)					1507
Ministry of Coal					
Coal					
2	Talabira II & III OCP - FMC (NLC India Limited [NLCIL]) (618982)	Odisha	10/2022 (05/2023)	06/2026 (-)	522.45 (-)
Total (1)					522.45
Electricity Generation					
3	200 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (618991)	Gujarat	07/2022 (03/2024)	12/2026 (-)	1221.41 (-)
4	100 MW SPP part of SECI 150 MW Hybrid (NLC India Limited [NLCIL]) (618992)	Gujarat	07/2022 (04/2024)	12/2026 (-)	480.68 (-)
Total (2)					1702.09
Ministry of Health & Family Welfare					
Healthcare					
5	AIIMS Darbhanga (PMSSY AND Institute of NATIONAL Importance) (701172)		(09/2020)	09/2024 (-)	1264 (-)
6	AIIMS Rajkot (PMSSY AND Institute of NATIONAL Importance) (701170)	Gujarat	01/2019 (01/2019)	03/2026 (03/2026)	1195 (-)
7	ALL India Institute of Medical Sciences-AIIMS Madurai (PMSSY AND Institute of NATIONAL Importance) (701168)	Tamil Nadu	12/2018 (12/2018)	08/2022 (10/2026)	1264 (2021.51)
Total (3)					3723
Ministry of Housing & Urban Affairs					
Urban Public Transport					
8	Pune Metro Rail Project Phase-2 Line-4 Kharadi to Khadakwasla with Spur Line 4A Nal Stop - Warje - Manikbaug (Maharashtra Metro Rail Corporation Limited [MMRCL]) (618985)	Maharashtra	12/2025 (12/2025)	12/2030 (-)	9857.85 (-)
Total (1)					9857.85
Ministry of Power					
Electricity Generation					
9	Gadarwara Super Thermal Power Project, Stage-II [3x800 MW] (National Thermal Power Corporation [NTPC]) (618976)	Madhya Pradesh	11/2024 (05/2025)	03/2030 (-)	20446 (-)
Total (1)					20446
Ministry of Railways					
Railways					
10	Furkating-New Tinsukia[194 Km] (Northeast Frontier Railway [NFR]) (618986)	Assam	09/2025 (09/2025)	06/2029 (-)	3633.58 (-)
11	Devbhumi Dwarka [Okha] - Kanalus Doubling (Western Railway [WR] - II) (618972)	Gujarat	12/2025 (12/2025)	12/2028 (-)	1456.77 (-)
12	Bangalore Suburban Railway Project (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (705941)	Karnataka	10/2020 (10/2020)	12/2026 (03/2030)	15767 (-)
13	Katihar Kumedpur & Katihar Mukuria BG Doubling Project (Northeast Frontier Railway [NFR]) (617245)	Multi-States (Bihar, West Bengal)	08/2022 (08/2022)	08/2026 (02/2027)	942.64 (-)
14	Gondia - Dongargarh 4th line [84 Km] (South Eastern Central Railway) (618978)	Multi-States (Chhattisgarh, Maharashtra)	10/2025 (10/2025)	10/2030 (-)	2222.53 (-)
15	Jharsuguda-Barpali-Sardega Ph II Works- Rail Connectivity for Coal Loading Bulb at Barpali. (South Eastern Railway [SER] - I) (400006)	Odisha	10/2021 (10/2021)	10/2025 (12/2025)	808.99 (-)
16	Doubling of Lingaraj SILO connectivity of NTPC line and augmentation of NTPC exchange yard and NTPC Block Cabin. (East Coast Railway [ECoR] - II) (400047)	Odisha	08/2022 (06/2022)	12/2024 (07/2024)	210 (-)
17	Doubling of lines connecting the loading spurs in Talcher Yard. (East Coast Railway [ECoR] - II) (400048)	Odisha	09/2022 (06/2022)	12/2024 (09/2024)	186.21 (-)
18	Flyover between Siju and Paradeep coaching Yard to avoid Surface crossing of trains (East Coast Railway [ECoR] - II) (616694)	Odisha	04/2023 (10/2025)	07/2028 (-)	200.77 (-)
19	New Line between Junagarh - Nabarangpur [116.21 Km] (Indian Railway) (618995)	Odisha	08/2024 (08/2025)	08/2030 (-)	2864.51 (-)
20	Varanasi-Pt. Deen Dayal Upadhya multitracking 15km including construction of new Rail-cum-Road Bridge across Ganga River. (Northern Railways) (617213)	Uttar Pradesh	10/2024 (10/2025)	10/2029 (-)	2464.46 (-)
Total (11)					30757.46




Table 5: Ongoing Projects North Eastern Region





Ongoing Projects of North-East Region

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Civil Aviation							
Aviation & Aviation Infrastructure							
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (03/2026)	1712 (2520)	2514.59	96
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	160.06	42
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	51.21	22
Total (3)					2534.26	2725.86	
Ministry of Coal							
Coal							
4	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	81.47	88
5	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.61	3
Total (2)					449.23	187.08	
Department of Higher Education							
Education							
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (08/2024)	592.61 (592.61)	550.61	80
7	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 (153.71)	125.03	97
8	Construction and Development of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (10/2026)	494.52 (429.7)	426.07	91
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (03/2022)	474.23 (474.23)	167.55	4
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	261.7	97
11	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	171.56	24
12	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (03/2026)	314.06 (314.06)	238.22	85
Total (7)					2990.52	1940.74	
Department of Sports							
Education							
13	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081)	Manipur	NA (01/2022)	08/2024 (08/2026)	906.47 (611.74)	565.17	95
Total (1)					906.47	565.17	
Ministry of Power							
Electricity Generation							
14	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited (NHPC)) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3861.98	16
15	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	66.73	3
16	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	61.45	2
17	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited (NHPC)) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	25718.57	97
18	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited (NHPC)) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	3972.89	71
19	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited (NHPC)) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (12/2025)	938.29 (1828.11)	1531.04	94
Total (6)					48536.97	35212.66	
Transmission & Distribution							
20	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	0.04	0



Ongoing Projects of North-East Region

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
21	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Mizoram, Nagaland, Tripura, Manipur, Meghalaya)	12/2014 (03/2016)	12/2018 (03/2026)	5111.33 (6700)	5442.41	96
22	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Sikkim, Arunachal Pradesh)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	7809.22	82
Total (3)					10075.13	13251.67	
Ministry of Petroleum & Natural Gas							
Energy Storage							
23	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	74.46	55
24	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	168.47	67
25	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Assam	01/2019 (01/2019)	07/2024 (06/2026)	10228 (11407)	10270.18	89
26	LPG Bottling Plant at Mualkhang (Ministry of Petroleum & Natural Gas) (617829)	Mizoram	07/2024 (07/2024)	10/2028 (11/2027)	225.71 (225.71)	16.32	26
27	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	06/2022 (06/2022)	09/2025 (06/2026)	656 (656)	526.86	92
Total (5)					11650.11	11056.29	
Oil & Gas							
28	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	05/2021 (05/2021)	10/2023 (05/2026)	412.3 (577)	458.56	89
29	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	07/2020 (07/2020)	07/2024 (09/2026)	12366 (22494)	18147.42	80
30	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	01/2018 (01/2018)	02/2020 (06/2026)	682.9 (726.93)	493.53	94
31	Coke Drum Structure Package (Ministry of Petroleum & Natural Gas) (617836)	Assam	12/2022 (12/2022)	12/2025 (09/2026)	635.28 (635.28)	80.32	51
32	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	12/2020 (12/2020)	03/2024 (03/2026)	430.76 (430.76)	334.6	89
33	Pipeline Rehabilitation Project, Phase-II (Ministry of Petroleum & Natural Gas) (617827)	Assam	12/2024 (12/2024)	12/2029 (12/2029)	680 (680)	2.32	17
34	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Assam	06/2021 (06/2021)	12/2024 (03/2026)	860 (860)	636.92	99
35	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Ministry of Petroleum & Natural Gas) (709776)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277 (323.09)	192.31	74
36	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Ministry of Petroleum & Natural Gas) (709779)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768 (740)	130.46	49
37	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2026)	344.99 (344.99)	220.37	50
38	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	09/2023 (09/2023)	05/2026 (05/2026)	198.7 (198.7)	59.75	45
39	DCU Revamp Project (NRL) (709864)	Assam	08/2021 (08/2021)	07/2024 (06/2026)	370 (370)	274.81	68
40	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	04/2023 (04/2023)	12/2024 (09/2026)	293.5 (293.5)	97.22	98
41	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Meghalaya, Mizoram, Tripura, Assam, Manipur, Sikkim, Nagaland, Arunachal Pradesh)	04/2020 (04/2020)	03/2024 (03/2026)	9265 (9265)	6622	86
42	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum & Natural Gas) (709786)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 (227.62)	15.85	28
43	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022 (03/2022)	05/2024 (05/2026)	209.33 (131.51)	71.95	66
Total (16)					28021.38	27838.39	



Ongoing Projects of North-East Region

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Labour and Employment							
Healthcare							
44	Construction of 200 bedded ESIC Hospital with 62 Nos Staff quarters , Beltola (Employee's State Insurance Company [ESIC]) (612201)	Assam	12/2017 (10/2021)	04/2025 (02/2026)	143.23 (154.75)	116.08	96
Total (1)					143.23	116.08	
Ministry of Railways							
Railways							
45	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
46	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
47	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
48	Furkating-New Tinsukia[194 Km] (Northeast Frontier Railway [NFR]) (618986)	Assam	09/2025 (09/2025)	06/2029 (-)	3633.58 (3633.58)	0	0
49	Doubling of New Bonggaigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3739.15	93
50	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15824.48	72
51	Murkongselek-Pasighat (Northeast Frontier Railway (NFR) - II) (705401)	Multi-States (Assam, Arunachal Pradesh)	02/2011 (03/2023)	03/2025 (05/2026)	435 (1250)	805.31	65
52	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway (NFR) - II) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5828.35	81
53	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Nagaland, Assam)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
54	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Sikkim	10/2009 (05/2010)	05/2015 (12/2027)	7877 (11775)	9861.45	90
Total (10)					40427.15	36464.21	
Ministry of Road Transport & Highways							
Roads & Highways							
55	Construction of 2-Laning with hard shoulders of Hayuliang Hawaii bypass Road on EPC basis from design Km. 51.825 to Km. 63.131 Existing Km 45.050 of HayuliangHawaii road to Hawaii Town under SARDP-NE -Balance work Pkg - IV (NHIDCL) (618424)	Arunachal Pradesh	01/2017 (05/2021)	05/2023 (07/2026)	256.66 (216.76)	0	93
56	Construction of Balance work of 2-Lane with PS of Joram-Koloriang Road NH-713 on EPC basis from Design Km 44.989 to Km 61.547 Existing Km 50.050 to Km 70.000 in the state of Arunachal Pradesh under SARDP-NE Pkg-3 (NHIDCL) (618432)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (07/2023)	228.72 (228.72)	0	99
57	Construction of Balance work of 2-Lane with PS of Joram Koloriang Road from existing Km122.600 to km138.00 [Design Km108.724 to Km123.714] in Arunachal Pradesh on EPC Mode under SARDP-NE Pkg-7 (NHIDCL) (618433)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (07/2023)	184.89 (184.89)	0	98
58	Roing-Hunli Road Greenfield Alignment Project (NHIDCL) (618434)	Arunachal Pradesh	02/2017 (03/2018)	03/2022 (04/2025)	1718.59 (1718.59)	0	77
59	Construction of 2-lane road of Potin to Pangin section of NH-13 from Km 163.59 to Km 206.66 Package-5 on EPC Mode in the State of Arunachal Pradesh under Arunachal Pradesh Package of Roads and Highways of SARDP-NE [Job No SARDP-NE/P-P/Pkg-A/NH-13/Ar.Pr./PWD/2018-19/116] (MoRTH) (617892)	Arunachal Pradesh	03/2019 (11/2020)	11/2023 (07/2024)	450.65 (450.65)	303.39	96
60	4-Laning of Itanagar to Banderdewa section of NH-415from km 40430 to km 51735 Package-Bon EPC Mode in the state of Arunachal Pradesh Job NO. 415/Ar. P/2020-21/031 (MoRTH) (618033)	Arunachal Pradesh	06/2020 (12/2021)	12/2024 (-)	496.47 (496.47)	153.63	48
61	Construction of Mangaldoi Bypass NH-15 starting at Ch 26400 and terminating at Ch 41505 under Rangia NH Division L 15.105 Km in the State of Assam. Job No. 15/AS/2021-22/234 (MoRTH) (617895)	Assam	03/2022 (04/2023)	04/2025 (-)	535.03 (535.03)	104.57	55
62	4-L Bilasipara-Guwahati Package-10 (NHIDCL) (618282)	Assam	03/2023 (12/2023)	06/2026 (-)	1264.9 (1264.9)	0	39
63	4-L Bilasipara-Guwahati Package-9 (NHIDCL) (618283)	Assam	03/2023 (12/2023)	06/2026 (-)	1000.27 (1000.27)	0	40
64	Widening/Improvement to 4-Lane with paved shoulder from Km 99930 to Km 143680 Design Chainage 96000 to 139750 of Paikan to Dhupdhara Sahar of Bilasipura-Guwahati Road on NH-17 in the state of Assam on EPC mode under Bharatmala Pariyojana in Economic Corridors Project Length 43.750km under NHO-NE Package-8 (NHIDCL) (618284)	Assam	03/2023 (12/2023)	12/2026 (-)	1457.59 (1457.59)	0	56



Ongoing Projects of North-East Region

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
65	Widening/Improvement to 4-Lane with Paved Shoulder from Ch. 88.000km to Ch.99.930 km Design Ch.84.100km to Ch.96.000 km of Sagunbashi forest near Nichinta to starting of Krishnai Bypass Section of Bilasipura Guwahati road NH 17 on EPC Package-7 (NHIDCL) (618285)	Assam	03/2021 (10/2023)	10/2025 (-)	286.72 (286.72)	0	100
66	Construction of New 2-Lane Bridge with its approaches from km 0000 to Km 4385 across River Brahmaputra on NH-17 at Jogighopa in Assam on EPC mode (NHIDCL) (618286)	Assam	09/2021 (11/2021)	11/2024 (06/2026)	746.76 (746.76)	0	0
67	Construction and up gradation to 4-Lane of existing two lane with paved shoulder from Hapachara to Tulungia road of NH-117 of existing Km 0.00 to km 14.050 and Design Km 0.000 to km 14.660 under BMP on EPC mode (NHIDCL) (618289)	Assam	03/2020 (06/2020)	12/2022 (06/2024)	224.85 (224.85)	204.19	0
68	Construction of 4-Lane Panchgram Bypass from Design Chainage km 15500 on NH-37 Old NH-53 at Kalinagar Pt.-I Village to Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Package-2 (NHIDCL) (618308)	Assam	03/2023 (08/2024)	02/2027 (-)	676.18 (728.97)	0	46
69	4-Laning of Dhanehari Lailapur / Vairengte section from Existing Chainage km 12920 to km 43000 of NH 306 Design Chainage km 20000 to km 49360 on Silchar - Vairengte Sairang road in the State of Assam under Bharatmala Pariyojana on EPC mode. Project Length 29.360 km under NHO-NE Package-2 (NHIDCL) (618314)	Assam	03/2023 (02/2024)	08/2026 (-)	1716.21 (1716.21)	848.23	64
70	4-Laning of Silchar - Dhanehari section from Existing Chainage km 263800 of NH 37 to km 12920 of NH 306 Design Chainage km 0000 to km 20000 on Silchar - Vairengte - Sairang road in the State of Assam under Bharatmala Pariyojana on EPC mode Package-1 (NHIDCL) (618315)	Assam	02/2023 (01/2024)	07/2026 (-)	1256.9 (1256.9)	0	0
71	Dillai to Lahorijan Package-7 (NHIDCL) (618325)	Assam	11/2021 (01/2023)	07/2024 (12/2025)	204.1 (204.1)	0	0
72	Widening/Improvement to 4-Lane with Paved Shoulder from KM 38500 to Km 51246 Design Chainage 38500 to 50959 with proposed Daboka Bypass of Daboka-Parokhaowa of NH 29 on EPC under NHO-NE Package-1 (NHIDCL) (618326)	Assam	01/2023 (11/2023)	11/2025 (-)	516.88 (516.88)	0	0
73	Widening/Improvement to 4-Lane with Paved Shoulder from KM 113300 to Km 146230 Design Chainage 113830 to 145712 of Kwaram Taro Village - Dillai Section in Assam on EPC Package-6 (NHIDCL) (618327)	Assam	09/2021 (07/2022)	07/2024 (03/2025)	625.64 (625.64)	0	0
74	Construction of 4/6 Laning from existing Km 159.400 of NH-36 to existing Km 102.500 of NH-39 and upto end point of Assam portion [Design Km 118.050 to design Km 132.375] Total New Alignment length of 14.325 Km of Daboka - Dimapur Section Dimapur Bypass in the state of Assam under SARDP-NE 'Phase-A' on EPC mode Assam Portion (NHIDCL) (618330)	Assam	03/2018 (11/2019)	11/2022 (08/2024)	511.02 (511.02)	0	0
75	Widening/Improvement to 2-Lane Lane with Paved Shoulder from km 16900 Bogapani to km 27150 Golai Goan on existing Dibrugarh to Ledo section with proposed Digboi Bypass Green Field and Brownfield 2-LanePS of NH-315 OLD NH-38 in Tinsukia District under NHO- NE Package-4 (NHIDCL) (618339)	Assam	01/2023 (12/2023)	12/2026 (-)	356.65 (356.65)	0	20
76	Widening/Improvement to 4-Lane with Paved Shoulder from km 626030 Nalani hulla Gaon to km 650450 Chotahapjan on existing Tinsukhia -Makum Bypass of NH-15 OLD NH-37 and Strengthening of existing NH-315 OLD NH-38 from Km 0000 Chotahapjan to Km 16900 Bogapani section 2-Lane PS in Assam on EPCMode under NHO-NE Package-3 (NHIDCL) (618340)	Assam	01/2023 (05/2023)	09/2025 (-)	458.59 (458.59)	0	68
77	4-Laning from Rangagara to Kaliabor Tinali from km 297.00 to km 315.315 of NH-37 on EPC basis under SARDP-NE in state of Assam (NHIDCL) (618435)	Assam	01/2016 (10/2017)	04/2020 (03/2025)	386.51 (386.51)	0	0
78	4-Laning of Jamugurihat to end of Biswanath Chariali By-Pass from Km 182.000 to Km 208.000 of NH-52 on EPC mode in state of Assam under SARDP-NE (NHIDCL) (618436)	Assam	03/2015 (12/2016)	06/2019 (03/2025)	599 (599)	0	0
79	Construction of Balance Work of 4-Laning of NH-37 Section between End of Moran Bypass to Bogibeel junction near Lapetketa Km. 561.700-Km. 580.875 under SARDP-NE, Phase 'A' in the State of Assam on EPC mode Pkg-I Road works & Toll Plaza (NHIDCL) (618437)	Assam	01/2016 (09/2024)	08/2025 (-)	274.34 (274.34)	0	100
80	4-Laning of NH-37 Section between Demow to End of Moran Bypass From Km. 534.800 to Km. 561.700 including Emergency Landing Facility ELF under SARDP-NE, Phase 'A' in the State of Assam on EPC mode (NHIDCL) (618438)	Assam	01/2016 (01/2023)	08/2025 (01/2025)	385.57 (385.57)	0	0
81	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 501.800 11.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618441)	Assam	01/2016 (10/2024)	09/2025 (-)	467.79 (476.5)	72.13	0
82	Development of External Trunk Connectivity and Internal Infrastructure Works at Multi Model Logistics ParkMMLP at Jogighopa in the State of Assam on EPC Mode Package-I Road and Utility Works (NHIDCL) (618455)	Assam	02/2020 (09/2020)	09/2024 (10/2024)	693.97 (693.97)	0	0



Ongoing Projects of North-East Region

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
83	6L Standalone Flyovers at Bongaigaon, Chapaguri, Pathsala, Simlaguri chowk and Baihata Bypass Junctions on stretches of NH-31 and NH-27 (National Highways Authority of India [NHAI]) (618575)	Assam	03/2022 (01/2023)	07/2024 (-)	457.72 (412.15)	371.63	100
84	6L Standalone Flyovers at Raha, Demow, Borghat, Kathiatiali junctions and ROB at Jagiroad on stretches of NH 36 and NH 27 (National Highways Authority of India [NHAI]) (618576)	Assam	03/2022 (12/2022)	06/2024 (-)	280.75 (255.53)	211.79	99
85	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 156.489 near P. Leikul to km 176.410 near Borowapu on EPC mode under NHO-NE Assam portion Package-10 (NHIDCL) (618351)	Assam	03/2023 (08/2023)	08/2025 (-)	890.33 (693.15)	0	0
86	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 136.500 near Hejaichak to km 156.489 near P. Leikul Package-9 on EPC mode under NHO-NE Package-9 (NHIDCL) (618352)	Assam	03/2023 (08/2023)	08/2025 (-)	860.37 (614.43)	0	0
87	Widening & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 116.480 near Hangrum to km 136.500 near Hejaichak Package-8 on EPC mode under NHO-NE Package 8 (NHIDCL) (618353)	Assam	03/2023 (08/2023)	08/2025 (-)	904.04 (904.04)	0	0
88	Wideinig & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 96.870 near Jiri River to km 116.550 near Hangrum Package-7 on EPC mode Package7 (NHIDCL) (618354)	Assam	12/2023 (03/2024)	03/2026 (-)	846.82 (846.82)	0	71
89	Widening/Improvement to 4-Lane with Paved Shoulder from km 55000 Nagabang Gamsuk to km 82514 Oyan in the State of Assam and Arunachal Pradesh on EPC mode under Bharatmala Pariyojna of Length 27.514 Km Package-3 (NHIDCL) (618359)	Assam	03/2023 (09/2024)	08/2025 (-)	665.47 (665.47)	0	54
90	Widening/Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Srirampur near Bhairiguri Village to Kachukhana Harichara Paglagaunj Package-I of Srirampur - Dhubri Section of NH-127B from existing Km 0.000 to Km 28.050 Design Km 0.000 to Km 27.650, Design Length 27.650 Km under JICA ODA Loan assistance Phase-V -Balance work (NHIDCL) (618371)	Assam	03/2022 (11/2024)	11/2026 (-)	613.89 (613.89)	0	43
91	Widening / Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Kachukhana Harichara Paglagaunj to Dhubri - Phulbari Bridge approach Package-II of Srirampur - Dhubri Section of NH-127B from existing Km 28.050 to Km 55.060 Design Km 27.650 to Km 54.154, Design Length 26.504 Km under JICA ODA Loan assistance Phase-V [Srirampur - Dhubri Pkg-2] (NHIDCL) (618372)	Assam	03/2022 (01/2023)	06/2025 (-)	909.02 (909.02)	0	100
92	Construction of 4-Lane Bridge including approaches over River Brahmaputra between Dhubri on North Bank, Assam and Phulbari on south Bank, Meghalaya on NH-127B under JICA ODA Loan assistance Phase-III (NHIDCL) (618373)	Assam	05/2019 (12/2020)	09/2028 (12/2028)	4997.04 (4997.04)	0	67
93	Construction of 2-laning with Hard shoulder of Ukhrul Tolloi - Tadubi section of NH-102A from Design Chainage km 9450 to km 50850 in the State of Manipur on EPC mode under NHO-NE Package-2 (NHIDCL) (618387)	Manipur	03/2023 (03/2024)	03/2026 (-)	578.98 (578.98)	234.11	77
94	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 50.850 km to 81.870 km in the State of Manipur on EPC mode under NHO-TSP Package -3 (NHIDCL) (618388)	Manipur	09/2021 (07/2023)	01/2025 (03/2025)	315.56 (315.56)	227.97	90
95	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 81.870 km to 105.825 km in the State of Manipur on EPC mode under NHO-TSP Package -4 (NHIDCL) (618389)	Manipur	09/2021 (08/2022)	02/2024 (10/2025)	310.76 (310.76)	247	96
96	Improvement of existing road to 2 laning with Hard Shoulders of Maram-Peren section Package-1B, length- 17.660 km from Design Chainage 22.340 km to 40.000 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618415)	Manipur	02/2021 (06/2021)	12/2022 (08/2023)	188.36 (188.36)	0	99
97	Improvement of existing road to 2 laning with Hard Shoulders of Maram -Peren section Package-1A, length- 22.340Km from Design Chainage 0.000 km to 22.340 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618416)	Manipur	02/2021 (06/2021)	12/2022 (02/2023)	226.32 (226.32)	0	0
98	Construction of 2 -Lane with paved shoulders road from Tamenglong-Tousem-Lisang-Mahur Road NH-137 starting near Dialong Village from km 10.000 at Dialong to km 31.430 near Old Tamenglong , near Barak River on EPC Mode Package-2 (NHIDCL) (618355)	Manipur	07/2021 (09/2021)	03/2023 (12/2025)	483.87 (483.87)	351.99	92
99	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur in the state of Manipur from km 31.430 at Old Tamenglong to km 43.480 ending near Phelong on EPC Mode Package-3 (NHIDCL) (618356)	Manipur	03/2021 (06/2021)	12/2022 (12/2025)	234.08 (234.08)	0	94
100	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 in Manipur starting from km 54.180 near Azuram to km 80.630 near Mandeu on EPC Mode Package 5 (NHIDCL) (618357)	Manipur	09/2021 (11/2021)	05/2023 (04/2025)	477.86 (477.86)	330.1	84



Ongoing Projects of North-East Region

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
101	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 starting from km 80.630 near Mandeu to km 96.870 near Jiri River on EPC Mode Package-6 (NHIDCL) (618358)	Manipur	09/2021 (11/2021)	05/2023 (07/2027)	311.18 (311.18)	223.12	84
102	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from Design Chainage 69.875 Km to 121.769 Km in the State of Manipur on EPC mode Package-3 (NHIDCL) (618344)	Manipur	03/2021 (08/2021)	08/2023 (04/2025)	673.27 (673.27)	480.59	50
103	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section from Km 48.587 to Km 69.875 in the State of Manipur on EPC mode under NHO Package-2B (NHIDCL) (618345)	Manipur	06/2020 (08/2020)	08/2022 (02/2023)	365.53 (365.53)	168.23	64
104	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 32.835 to km 48.587 in the State of Manipur on EPC mode under NHO Package-2A (NHIDCL) (618346)	Manipur	04/2020 (07/2020)	06/2022 (02/2023)	232.99 (232.99)	127.15	81
105	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 13.747 to km 32.835 in the State of Manipur on EPC mode under NHO Package-1B (NHIDCL) (618347)	Manipur	04/2020 (07/2020)	06/2022 (04/2025)	241.52 (241.52)	0	45
106	Widening to 2 lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 169570 Near Nungkao village under Tamenglong District to km 205974 near Jiribam Bridge under Jiribam district under NHO-NE PKG-7 (NHIDCL) (618333)	Manipur	01/2023 (12/2023)	12/2025 (-)	760.16 (760.16)	365.34	75
107	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 131.280 to km 169.570 on EPC mode in Manipur under NHO-TSP PKG-6 (NHIDCL) (618334)	Manipur	12/2021 (02/2023)	02/2025 (05/2025)	504.76 (504.76)	269.89	0
108	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from Km 101280 Near Khongsang Village to Km 131280 near Puilon Kambiron Village on EPC Mode in Manipur PKG-5 (NHIDCL) (618335)	Manipur	12/2021 (11/2022)	05/2024 (02/2026)	410.68 (410.68)	309.93	80
109	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 66.110 km to 101.280 Km Existing Chainage km 67.496 to km 103.557 on EPC Mode in Manipur PKG-4 (NHIDCL) (618336)	Manipur	09/2021 (06/2022)	12/2023 (08/2025)	579.63 (579.63)	355.94	79
110	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 33.000 km to 66.390 Km Existing Chainage from km 33.395 to km 67.496 on EPC Mode in Manipur PKG-3 (NHIDCL) (618337)	Manipur	03/2021 (09/2021)	03/2023 (07/2025)	467 (467)	552.2	82
111	Widening/Improvement of existing 2-Lane road to 4-Lane Divided Highway from Sekmai to Nilakuthi section of Imphal-Kohima Road Design Chainage from Km 297700 to Km 308729 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5B (NHIDCL) (618298)	Manipur	03/2021 (07/2021)	01/2023 (06/2025)	211.7 (211.7)	209.48	78
112	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Taphukuki to Daili section of Imphal-Kohima road NH-02 Design Chainage from Km 262175 to Km 274610 in the state of Manipur on EPC mode Pkg-4A (NHIDCL) (618300)	Manipur	09/2020 (10/2020)	04/2022 (07/2025)	379.39 (379.39)	0	78
113	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 16.900 to Km 30.970 of NH-202 in the state of Manipur on EPC mode Package-2 (NHIDCL) (618302)	Manipur	03/2020 (07/2020)	06/2022 (12/2025)	256.04 (256.04)	0	35
114	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 0.000 to Km 16.900 of NH-202 in the state of Manipur on EPC mode Package-1 (NHIDCL) (618303)	Manipur	03/2020 (07/2020)	06/2022 (04/2025)	222.77 (222.77)	0	37
115	Rehabilitation and Up-gradation of Nongstoin Wahkaji section of Project Road Km 0000 to Km 43060 to Intermediate Lane with earthen shoulder under SARDP-NE Phase-A in the State of Meghalaya on EPC mode. Job No- SARDP-NE/Nong-Don-Maw/MG/2020-21/294 (MoRTH) (617885)	Meghalaya	08/2020 (02/2022)	08/2023 (07/2024)	302.88 (302.88)	182.58	98
116	Improvement/Widening to 2-L with Paved Shoulder/ 4-Laning of NH-40 section from Km 151330 to Km 163400 design Km 63.530 to Km 71.520 including Dawki Bridge of length 368 m between Shillong-Dawki under JICA ODA Loan assistance Phase-II Pkg-5 -Balance work (NHIDCL) (618374)	Meghalaya	07/2020 (05/2024)	11/2026 (11/2027)	284.21 (284.21)	0	32
117	Improvement/Widening to 2-Lane with Paved Shoulder from design Km 45.760 to Km 63.530 between Shillong-Dawki under JICA ODA Loan assistance Phase-II - Balance work Pkg-4 (NHIDCL) (618375)	Meghalaya	07/2020 (04/2024)	04/2026 (07/2026)	445.51 (445.51)	0	37
118	Improvement/Widening to 2-Lane with Paved Shoulder between Shillong-Dawki road up to Bangladesh Border from design Km 10.670 to Km 37.550 under JICA ODA Loan assistance Phase-II -Balance Work-Pkg-2 (NHIDCL) (618376)	Meghalaya	07/2020 (02/2024)	08/2026 (07/2026)	525.67 (525.67)	0	41



Ongoing Projects of North-East Region

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
119	Improvement/Widening to 2-L with Paved Shoulder/4-L from Km 81740 to Km 93490 design Km 0000 to Km 10670 of NH-40 New NH-106 & 206 section & 4-L from design Km 0.00 to Km 0.930 of NH-44 section between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance Work Pkg-1 (NHIDCL) (618377)	Meghalaya	07/2020 (10/2023)	10/2025 (-)	351.12 (351.12)	0	78
120	Rehabilitation and up gradation of Nongstoin-Rambrai-Kyrshai road up to Meghalaya-Assam border from Km 0.335 to km 34.039 to 2-Lane under NHO - NE in the State of Meghalaya Package-1 (NHIDCL) (618418)	Meghalaya	09/2021 (05/2022)	05/2024 (06/2025)	359.86 (359.86)	0	69
121	Construction of 2-Lane with paved shoulders of Shillong Western Bypass starting from NH-06 near Ladumsaw existing Km 60.900 of old NH40 to NH106 old NH 44E Package-III, from km 24700 to km 38256 under SARDP-NE PHASE A in the state of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618419)	Meghalaya	03/2023 (09/2024)	09/2026 (-)	562.48 (562.48)	0	33
122	Construction of 2 lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw existing km 60.900 of old NH-40 to NH-106 old NH-44E, Package-II km 12800 to km 24700 under SARDP-NE Phase A in the State of Meghalaya on EPC Mode (NHIDCL) (618420)	Meghalaya	03/2023 (09/2024)	09/2026 (-)	686.03 (686.03)	0	0
123	Construction of 2-Lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw Existing km 60.900 of old NH-40 to NH106 old NH-44E, km 0000 to km 12800 Package-I under SARDP-NE PHASE A in the State of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618421)	Meghalaya	03/2023 (09/2024)	09/2026 (-)	620.3 (620.3)	0	46
124	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 208. 000 to Km 250.000 Package-5 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-5 (NHIDCL) (618379)	Mizoram	09/2019 (10/2019)	04/2023 (-)	752.89 (752.89)	125.62	95
125	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 125. 000 to Km 166 Package-3 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-3 (NHIDCL) (618380)	Mizoram	09/2019 (10/2019)	04/2023 (11/2024)	867.09 (867.09)	0	0
126	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 250.00 Lunglei to km 298.00 on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-6 (NHIDCL) (618381)	Mizoram	09/2019 (12/2019)	06/2023 (03/2025)	768.76 (768.76)	168.78	98
127	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 298.00 to km 339.00 on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-7 (NHIDCL) (618382)	Mizoram	09/2019 (10/2020)	04/2024 (03/2025)	605.76 (750.32)	0.01	100
128	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 339.00 to km 380.00 Siaha on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-8 (NHIDCL) (618383)	Mizoram	09/2019 (03/2020)	09/2023 (05/2025)	637.06 (637.06)	101.89	99
129	Widening and up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 166. 000 to Km 208.000 Package-4 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-4 (NHIDCL) (618384)	Mizoram	09/2019 (10/2019)	04/2023 (09/2024)	899.45 (899.45)	191.59	99
130	Construction of 2-laning with hard shoulder of Lunglei to Chhumkhum from Design Chainage Km 0.000 to Km 37.420 of NH-302 [Lunglei-Tlabung] Package-A (NHIDCL) (618362)	Mizoram	03/2021 (06/2021)	12/2022 (05/2025)	698.45 (698.45)	0	0
131	Construction of 2-laning with hard shoulder configuration of Chhumkhum to Tlabung from Design Chainage Km 37.420 to Km 74.950 of NH-302 in Mizoram under Bharatmala Pariyojana on EPC mode [Pkg-B] (NHIDCL) (618363)	Mizoram	06/2021 (07/2021)	01/2023 (05/2025)	740.58 (740.58)	0	0
132	Up-gradation to 2-lane with paved shoulders of Ngopa - Pawrang section of NH 102B of Aizawl - Imphal Economic Corridor from Existing Chainage km 32.796 to km 72.030 [Design Chainage km 31.280 to km 68.170] in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-2 Keifang-Tuivai Pkg-2 (NHIDCL) (618341)	Mizoram	09/2021 (09/2023)	02/2025 (06/2026)	523.78 (523.78)	0	64
133	Rehabilitation and upgradation to 2 Lane with Paved shoulder of Economic corridor of NH-6 from Design chainage Km 0.000 to Km 13.510 Package-1 in the state of Mizoram under Bharatmala Pariyojana on EPC mode (NHIDCL) (618342)	Mizoram	03/2020 (07/2020)	06/2022 (06/2024)	206.9 (206.9)	0	0
134	Rehabilitation and Up gradation to 2-lane with paved shoulder of Keifang Section Economic Corridor of NH-06 from Existing Chainage Km 30050 Keifang to Km 50360 Keifang, Design Chainage Km 27400 to Km 45040 PkgIII in the State of Mizoram under Bharatmala Pariyojna on EPC Mode Seling-Dulte - III (NHIDCL) (618343)	Mizoram	03/2020 (07/2020)	06/2022 (12/2024)	292.23 (292.23)	0	0
135	4-Laning of Balance work of Dimapur-Kohima Road from design km 152.490 to km 166.700 Existing km 156.000 to km 172.900 Excluding Dimapur & Kohima Bypass under SARDP-NE Package-III (NHIDCL) (618328)	Nagaland	03/2016 (09/2023)	09/2025 (-)	562.98 (794.75)	0	0
136	Construction of 4/6 Laning from Km 132.375 to Km 153.058 Total New Alignment length of 20.683 Km of Daboka-Dimapur Section Dimapur Bypass Nagaland Portion of NH-36 & 39 in the State of Nagaland on EPC basis under PhaseA of SARDP-NE (NHIDCL) (618329)	Nagaland	02/2017 (09/2017)	09/2020 (02/2023)	819.39 (819.39)	0	0



Ongoing Projects of North-East Region

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
137	Construction of 2-lane with Paved shoulder of Kohima- Bypass Road Connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29, NH-39New NH-02 from Design Km 32.00 to Design Km 43.454Design Length-11.454 Km in the State of Nagaland under SARDP-NE on EPC Mode Package-IV (NHIDCL) (618290)	Nagaland	07/2020 (10/2020)	04/2022 (02/2025)	202.36 (202.36)	0	0
138	Construction of 2-lane with Paved shoulder of Kohima-Bypass Road connecting NH- 39 New NH-02, NH150New NH-02, NH7-61 New NH-29 and NH-39 New NH-02 from Design km 21.000 to km 32.268 [Design length11.268 km] in the state of Nagaland Under SARDP-NE on EPC Mode Package- 3 (NHIDCL) (618291)	Nagaland	07/2020 (06/2023)	06/2025 (-)	159.85 (342.29)	0	0
139	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting New NH-02 and New NH-29 from Design Km 10.500 to design Km 21.000 [Design Length- 10.500 km] including TUNNEL of 500m at Ch. 11.000 in the state of Nagaland Under SARDP-NE on EPC Mode Package-2 (NHIDCL) (618292)	Nagaland	07/2020 (10/2020)	10/2022 (01/2024)	277.44 (277.44)	0	0
140	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29 and NH-39New NH-02 from design Km 0.00 to Km 10.500 in the State of Nagaland under SARDP-NE on EPC Mode Package-1 -Balance work (NHIDCL) (618293)	Nagaland	07/2020 (11/2023)	11/2026 (-)	232.29 (350.88)	0	20
141	Balance work of Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 old NH-150 from existing km 98.380 near Chizami vill. to km120.367 Nagaland/Manipur Border [Design km 95.700 to design km 117.200] [Design Length 21.500 km] in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode Package-V under NHO (NHIDCL) (618296)	Nagaland	03/2020 (11/2023)	11/2025 (-)	330.8 (330.8)	0	91
142	Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 Old NH-150 from existing Km 30.474 Near Kidwema road Chakahabama to existing Km 53.220 Near Kikruma Village Design Km 29.60 to Km 51.50 Design length-21.90 Km in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode under NHO Package-II -Balance work (NHIDCL) (618297)	Nagaland	03/2020 (01/2024)	01/2026 (-)	355.79 (355.79)	0	29
143	Widening of existing Single lane / Intermediate lane road to 2 lane from Km 101 to Km 125 of NH 61 (MoRTH) (617886)	Nagaland	06/2020 (06/2024)	06/2026 (-)	252.2 (252.2)	0	41
144	Widening of existing single lane to intermediate lane road from Mokochung to Chare via Dikhu in the state of Nagaland on EPC mode (MoRTH) (618002)	Nagaland	02/2021 (06/2023)	06/2025 (-)	192.93 (192.93)	99.65	0
145	Widening to Existing single lane /intermediate lane to 2 lane from Km185.00 to Km 220.00 of NH-61 New NH-02 in the state of Nagaland. (MoRTH) (618072)	Nagaland	03/2021 (07/2022)	07/2024 (03/2025)	297.25 (297.25)	128.97	85
146	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-I Design Chainage 0000 Km to 34795 Km, in the State of Nagaland on EPC mode under NH O-NE (NHIDCL) (618364)	Nagaland	12/2022 (08/2023)	02/2026 (-)	430.24 (430.24)	0	78
147	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-III Design Chainage 69875 Km to 106816 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618365)	Nagaland	12/2022 (08/2023)	02/2026 (-)	497.18 (497.18)	0	80
148	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-II Design Chainage 34795 Km to 69875 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618366)	Nagaland	12/2022 (08/2023)	02/2026 (-)	442.54 (442.54)	0	38
149	Construction of 2 laning with Hard shoulder of Peren-Dimapur section on NH 129A from Design Km 146.208 to Km 163.592 Length- 17.384 km in the state of Nagaland on EPC mode under NHO-TSP Package-III (NHIDCL) (618413)	Nagaland	02/2021 (06/2023)	06/2025 (11/2025)	177.77 (199.02)	0	76
150	Construction of Balance work for 2-lane with hard shoulder of Peren- Dimapur section on NH-129A from Design Km 126.775 to Km 146.208 Length 19.433 Km in the state of Nagaland on EPC mode under NHO-TSP Package-II (NHIDCL) (618414)	Nagaland	01/2021 (09/2023)	09/2025 (-)	258.52 (258.52)	0	0
151	Construction of 2-lane with hard shoulders of Merangkong-Tamlu-Mon road Wakching Twon portion on EPC basis from existing Chainage Km 59000 to Km 73640 [Design Km. 59000 to Km, 72450] Design length - 13.450 Km under SARDP-NE package-V Balance work (NHIDCL) (618422)	Nagaland	03/2021 (09/2023)	09/2025 (-)	161.73 (161.73)	0	0
152	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon MTM Road from existing Km 20.456 to Km 41.065 Design Km. 20 to Km. 40.0 Design Length-20.000 Km in the State of Nagaland under SARDP-NE Phase-A Pkg-2 Balance work (NHIDCL) (618423)	Nagaland	03/2018 (08/2023)	08/2025 (-)	215.79 (215.79)	0	0
153	Construction & Upgradation of existing road to 2-lane with paved shoulder from New Rolep Bridge at km 37.600 to Chochepheri at km 52.00 in the section of Rongli to Chochepheri of NH 717B Pkg-II C (NHIDCL) (618446)	Sikkim	10/2020 (05/2021)	05/2024 (02/2025)	493.42 (478.79)	0	64
154	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Helipad near Menla at Km 82000 to Menla at Km 94030 of Rhenock-Menla Spur NH-717B Package-IIIB on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618447)	Sikkim	01/2021 (02/2021)	02/2024 (11/2025)	410.6 (379.3)	0	33



Ongoing Projects of North-East Region

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
155	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Chochenpheri at Km 52000 to Helipad near Menla at Km 82000 of Rhenock-Menla Spur NH-717B Package-IIIa on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618448)	Sikkim	10/2020 (12/2020)	12/2023 (09/2025)	816.79 (786.6)	0	0
156	Construction & Upgradation of existing road to 2-lane with paved shoulder from km27.200 End of Rongli bypass to km37.600New Rolep Bridge of Rhenok-Menla spur NH-717B on EPC Mode under SARDP-NE Phase-A in Sikkim Pkg-II B (NHIDCL) (618449)	Sikkim	07/2020 (10/2020)	04/2023 (02/2025)	230.45 (244.91)	0	64
157	Rehabilitation & Upgradation of existing road to 2-lane with paved shoulder including geometric improvement of section from start of Rabangla km33.600 to km58.840 under SARDP-NE Phase A Pkg- IV (NHIDCL) (618450)	Sikkim	07/2020 (10/2020)	05/2022 (04/2025)	292.8 (292.8)	1.91	18
158	Construction of two lane with paved shoulder Gangtok Bypass Road from Ranipool to Burtuk Ch 0.00 Km to 23.316 L23.316 Km in the State of Sikkim (MORTH) (618071)	Sikkim	10/2021 (05/2022)	05/2024 (01/2025)	385.15 (342.89)	0	78
159	Rehabilitation and up-gradation of road from km 16.077 to km 43.935 total length 27.858 km of Lalchara-Kanchanpur section via Shivbari on NH-44A to 2 lane with paved shoulder in the state of Tripura on EPC Mode Pkg-2 under BharatMala Pariyojana Manu-Simlung -2 (NHIDCL) (618307)	Tripura	02/2022 (01/2023)	01/2025 (04/2025)	456.88 (456.88)	0	0
160	Construction of 4-Lane with paved shoulder Agartala bypass Western side, length 25.402 km connecting NH-8 near Amtali to NH-108B near Lembuchhera in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618417)	Tripura	03/2023 (03/2024)	03/2027 (-)	2026.05 (2026.05)	0	0
161	Melaghar-Srimantapur section on NH-08 Spur from Km 23 to Km 34.500 11.5 Km and overlay from Km 20.30 to Km 22.00 1.7 Km Total Length 13.2 Km (NHIDCL) (618411)	Tripura	01/2023 (05/2023)	11/2024 (12/2025)	195.95 (195.95)	0	0
162	Rehabilitation and up-gradation of road from design km 25.250 to km 36.460 Total length 11.210 km of Kailashahar-Kurti Bridge section on NH-208A to 2-lane with paved shoulder on EPC basis under NHO Package-III- Balance Work (NHIDCL) (618385)	Tripura	02/2020 (09/2024)	09/2025 (-)	174.43 (174.43)	0	0
163	Rehabilitation & Upgradation of Road from Km 0.00 to Km 18.600 Total length-18.600 km of Kumarghat-Kailashahar section on NH-208 to 2-lane with Paved shoulder on EPC basis under NHO (NHIDCL) (618386)	Tripura	02/2020 (07/2020)	01/2022 (10/2024)	277.5 (302.03)	0	0
164	Improvement and Widening to 2-lane with paved shoulder of road from design Km 36.000 Rangamati to design Km 72.000 Pati Chhari Total length 36.000 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-3 (NHIDCL) (618368)	Tripura	01/2024 (09/2024)	09/2026 (-)	670.9 (670.9)	0	6
165	Improvement and Widening to 2-lane with paved shoulder of road from existing Km 438.170 Khowai Chowmuhani to existing Km 439.410 South Pulinpur of NH-08 and from design Km 0.000 South Pulinpur to design Km 36.00 near Rangamati of NH 208 on Khowai Teliamura- Harina section Total length 37.24 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-2 (NHIDCL) (618369)	Tripura	01/2024 (09/2024)	09/2026 (-)	657.21 (657.21)	0	42
166	Improvement and Widening to 2-lane with paved shoulder of road from Km 101.300 to km 127.319 Total Length 26.019 Km i.e. the Khowai Teliamura-Amarpur-Harina-Sabroom section of NH 208 in the state of Tripura on EPC under JICA ODA Loan Phase VI Package-1 (NHIDCL) (618370)	Tripura	01/2024 (07/2024)	07/2026 (-)	431.78 (431.78)	0	0
Total (112)					62357.28	7723.6	
Department of Telecommunications							
Telecommunication							
167	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (03/2026)	971.96 (971.96)	215.36	99
168	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Assam, Arunachal Pradesh)	12/2020 (10/2021)	04/2023 (03/2026)	1255.49 (1255.49)	299.02	99
Total (2)					2227.45	514.38	
Department of Water Resources, River Development & GR							
Water Resources							
169	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55
170	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
Total (2)					1705.6	1882.61	



Table 6: All Ongoing Projects





All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Civil Aviation							
Aviation & Aviation Infrastructure							
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport (Airport Authority of India [AAII]) (612786)	Andhra Pradesh	03/2023 (01/2024)	01/2026 (03/2026)	265.91 (265.91)	88.87	46
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. (Airport Authority of India [AAII]) (701107)	Andhra Pradesh	06/2020 (09/2020)	09/2022 (03/2026)	611.8 (611.8)	523.14	87
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. (Airport Authority of India [AAII]) (701121)	Andhra Pradesh	12/2022 (08/2023)	08/2025 (03/2026)	347.15 (347.15)	129.31	68
4	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (03/2026)	1712 (2520)	2514.59	96
5	Development of New Civil Enclave at Bihta (Airport Authority of India [AAII]) (612183)	Bihar	08/2024 (03/2025)	03/2027 (-)	1413 (1413)	0	1
6	Development of New Civil Enclave and associated works at Darbhanga Airport (Airport Authority of India [AAII]) (612194)	Bihar	07/2024 (07/2024)	07/2026 (-)	911.66 (911.66)	258.93	48
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna (Airport Authority of India [AAII]) (701101)	Bihar	12/2018 (10/2018)	07/2023 (05/2026)	1216.9 (1216.9)	1166.71	97
8	Goa Airport Terminal Building Extension Project (Airport Authority of India [AAII]) (701105)	Goa	11/2017 (12/2019)	12/2021 (01/2026)	255.69 (255.69)	154.3	98
9	Development of Dholera International Greenfield Airport , Gujarat (Airport Authority of India [AAII]) (701126)	Gujarat	06/2022 (07/2022)	06/2026 (06/2026)	1305 (1551)	739.77	72
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. (Airport Authority of India [AAII]) (611047)	Jammu and Kashmir	07/2022 (07/2023)	06/2026 (06/2026)	861.37 (861.37)	248.88	42
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport (Airport Authority of India [AAII]) (612787)	Karnataka	06/2023 (01/2024)	01/2026 (03/2026)	320.47 (320.47)	99.39	59
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. (Airport Authority of India [AAII]) (612788)	Karnataka	06/2023 (02/2024)	01/2026 (04/2026)	322.45 (322.45)	152.09	67
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 (Airport Authority of India [AAII]) (612789)	Kerala	06/2023 (02/2024)	09/2025 (06/2026)	484.57 (484.57)	116.14	31
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh (Airport Authority of India [AAII]) (400010)	Ladakh	07/2018 (09/2018)	09/2021 (07/2026)	480 (640)	484.6	78
15	C/o NITB Imphal Airport (Airport Authority of India [AAII]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	160.06	42
16	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, Jewar [earlier MOPA, without ASMGCS], HIAL & BIAL (Airport Authority of India [AAII]) (611570)	Multi-States (Karnataka, Maharashtra, Telangana, Uttar Pradesh)	12/2020 (10/2022)	09/2025 (08/2026)	500.48 (500.48)	348.09	76
17	Development of New Greenfield Airport at Bundi, Kota Rajasthan. (Airport Authority of India [AAII]) (618977)	Rajasthan	08/2025 (10/2025)	10/2027 (-)	1507 (1507)	10.05	1
18	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. (Airport Authority of India [AAII]) (701127)	Rajasthan	05/2022 (04/2023)	11/2024 (01/2026)	480 (480)	330.65	93
19	Construction of New Integrated Passenger Terminal Building at Udaipur Airport (Airport Authority of India [AAII]) (701128)	Rajasthan	06/2023 (11/2023)	03/2026 (09/2026)	887 (887)	462.38	57
20	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAII]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	51.21	22
21	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAII]) (611602)	Tamil Nadu	05/2018 (06/2023)	07/2025 (06/2026)	1207 (1207)	208.06	27
22	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAII]) (701113)	Uttar Pradesh	07/2024 (07/2024)	07/2027 (07/2027)	2869.65 (2869.65)	410.36	21
23	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAII]) (701122)	Uttar Pradesh	06/2024 (07/2024)	07/2026 (-)	579 (579)	133.8	28
24	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAII]) (611495)	West Bengal	08/2024 (09/2024)	01/2027 (01/2027)	1549 (1549)	359.56	16
25	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCBI Airport Kolkata. (Airport Authority of India [AAII]) (612791)	West Bengal	04/2023 (12/2023)	02/2025 (08/2026)	328.3 (328.3)	109.99	49



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Total (25)					21237.66	9260.93	
Ministry of Coal							
Coal							
26	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	81.47	88
27	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.61	3
28	PORDA CHIMTAPANI OCP [10 MTY] (South Eastern Coalfields Limited [SECL]) (400144)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	2310.12 (2310.12)	91.43	10
29	BAROUD OC EXPANSION [3.0-10.0M] (South Eastern Coalfields Limited [SECL]) (400149)	Chhattisgarh	08/2020 (08/2020)	03/2029 (-)	2309.8 (2309.8)	956.88	50
30	DIPKA EXPANSION OCP [40 MTY] (South Eastern Coalfields Limited [SECL]) (400354)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	5241.4 (5241.4)	2862.43	37
31	GEVRA OC [70 MTY] (South Eastern Coalfields Limited [SECL]) (400424)	Chhattisgarh	03/2016 (03/2016)	03/2023 (03/2027)	11816.4 (11816.4)	6813.01	78
32	AMERA OC RCE [1.0 MTY] (South Eastern Coalfields Limited [SECL]) (613798)	Chhattisgarh	02/2015 (02/2015)	03/2026 (-)	335.97 (335.97)	88.28	42
33	AMGAON OC RCE [1.0 MTY] (South Eastern Coalfields Limited [SECL]) (613799)	Chhattisgarh	07/2015 (07/2015)	03/2026 (-)	316.11 (316.11)	188.72	78
34	JAGANNATHPUR OC RCE PROJECT (South Eastern Coalfields Limited [SECL]) (613800)	Chhattisgarh	07/2016 (07/2016)	03/2025 (03/2026)	459.49 (459.49)	274.35	96
35	MAHAMAYA OCP [1.50 MTY] (South Eastern Coalfields Limited [SECL]) (613801)	Chhattisgarh	05/2018 (05/2018)	03/2026 (03/2028)	410.26 (410.26)	183.37	54
36	KATKONA RO UG MINE (South Eastern Coalfields Limited [SECL]) (615191)	Chhattisgarh	01/2023 (01/2023)	03/2029 (-)	329.21 (329.21)	61.34	2
37	PELMA OC MDO (South Eastern Coalfields Limited [SECL]) (616234)	Chhattisgarh	10/2022 (10/2022)	03/2033 (-)	1725.04 (1725.04)	15.66	40
38	KUSMUNDA OC EXPANSION PROJECT (SECL - CIL) (617287)	Chhattisgarh	11/2024 (11/2024)	03/2030 (-)	4516.88 (4516.88)	783.28	21
39	MANIKPUR OC EXPANSION PROJECT (South Eastern Coalfields Limited [SECL]) (617288)	Chhattisgarh	01/2025 (01/2025)	03/2029 (-)	382.61 (382.61)	113.03	21
40	HURA C OCP (ECL - CIL) (400018)	Jharkhand	08/2022 (08/2022)	03/2029 (-)	859.41 (859.41)	453	62
41	KONAR EXPANSION OCP (Ministry of Coal) (400073)	Jharkhand	01/2022 (01/2022)	03/2032 (-)	799.34 (799.34)	429.33	45
42	KARO EXPANSION OCP (Ministry of Coal) (400074)	Jharkhand	01/2022 (01/2022)	03/2029 (-)	908.47 (908.47)	269.26	22
43	SANGHMITRA OC (Ministry of Coal) (400136)	Jharkhand	03/2024 (03/2024)	03/2032 (-)	2660 (2660)	6.61	16
44	CHANDRAGUPT OCP (Ministry of Coal) (400138)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	973.5 (973.5)	440.75	24
45	KOTRE BASANTPUR PACHMO OCP (Ministry of Coal) (400139)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	861.06 (625.4)	455.95	42
46	Pachwara South Coal Block (NLC India Limited [NLCL]) (400142)	Jharkhand	03/2016 (11/2019)	09/2028 (-)	2242.9 (2242.9)	1253.92	74
47	RPR MAGADH EXP OCP (Ministry of Coal) (400150)	Jharkhand	08/2020 (08/2020)	03/2028 (-)	7254.37 (7254.37)	1599.39	38
48	NORTH URIMARI EXPANSION OCP (Ministry of Coal) (400151)	Jharkhand	07/2021 (07/2021)	03/2029 (-)	778.8 (778.8)	696.05	68
49	EPR ROHINI - KARKETTA OCP (Ministry of Coal) (400153)	Jharkhand	01/2021 (01/2021)	03/2028 (-)	1020.42 (1020.42)	84.74	21
50	EPR PUNDI OCP (Ministry of Coal) (400154)	Jharkhand	11/2020 (11/2020)	03/2027 (-)	713.35 (713.35)	236.58	10
51	EPR ASHOK OC (Ministry of Coal) (400155)	Jharkhand	05/2021 (05/2021)	03/2031 (-)	2898.28 (2898.28)	185.04	24
52	EPR AMRAPALI OCP (Ministry of Coal) (400156)	Jharkhand	02/2020 (02/2020)	03/2028 (-)	5136.15 (5136.15)	1257.44	42
53	RAJRAPPA RCE OCP (Ministry of Coal) (400160)	Jharkhand	12/2009 (12/2009)	03/2016 (03/2027)	510.85 (510.85)	488.69	76
54	CHITRA EAST OC (Eastern Coal Fields Limited [ECL]) (400172)	Jharkhand	08/2018 (08/2018)	03/2026 (03/2028)	513.99 (513.99)	230.87	51



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
55	JHARKHAND-LAIYO OCP (Ministry of Coal) (400352)	Jharkhand	08/2020 (08/2020)	03/2031 (-)	764.57 (764.57)	145.81	29
56	MOONIDIH XV SEAM UG (Ministry of Coal) (400425)	Jharkhand	08/2011 (08/2011)	03/2019 (05/2026)	1230.27 (1230.27)	635.78	82
57	2.5 MTPA PATHERDIH NLW WASHERY (Ministry of Coal) (611017)	Jharkhand	10/2015 (04/2016)	04/2018 (03/2026)	334.27 (334.27)	151.09	49
58	AMALGAMATED NTST KUJAMA OCP 8.5MTY (Ministry of Coal) (611864)	Jharkhand	01/2023 (01/2023)	03/2030 (-)	4011.85 (4011.85)	414.41	28
59	MURAI DIH UG PROJECT (Ministry of Coal) (613808)	Jharkhand	02/2011 (02/2011)	04/2014 (12/2026)	339.87 (339.87)	191	70
60	TAPIN SOUTH EXPN (Ministry of Coal) (615349)	Jharkhand	11/2020 (11/2020)	03/2028 (-)	230.41 (230.41)	22.02	21
61	SIRKA OC (Ministry of Coal) (615822)	Jharkhand	05/2020 (05/2020)	03/2028 (-)	222.82 (222.82)	140.58	53
62	TETARIAKHAR OC (Ministry of Coal) (615843)	Jharkhand	11/2019 (11/2019)	03/2025 (03/2027)	243.52 (243.52)	49.54	29
63	CHUPERBHITA SIMLONG OCP MDO 6 (Eastern Coal Fields Limited [ECL]) (616225)	Jharkhand	12/2023 (12/2023)	03/2037 (-)	979.08 (979.08)	0	0
64	JARANGDIH EXPN. OCP 1.5 MTY (CCL - CIL) (616236)	Jharkhand	02/2020 (02/2020)	03/2029 (-)	414.37 (414.37)	85.6	33
65	BLOCK E OCP (Ministry of Coal) (616253)	Jharkhand	03/2024 (03/2024)	03/2029 (-)	5850.83 (5850.83)	20.32	3
66	Revised Jharia Master Plan for Dealing with Fire, Subsidence & Rehabilitation of affected families in Jharia Coalfield- Reg. (Bharat Coking Coal Limited (BCCL)) (617416)	Jharkhand	06/2025 (07/2025)	12/2028 (-)	5940.47 (5940.47)	26.31	19
67	AMADAND OCP[4.0MTY] (Ministry of Coal) (400148)	Madhya Pradesh	03/2016 (03/2016)	03/2021 (03/2027)	869.44 (869.44)	278.78	75
68	RAMPUR BATURA OCP [4.0MTY] (South Eastern Coalfields Limited [SECL]) (400152)	Madhya Pradesh	07/2019 (07/2019)	03/2026 (-)	1248.93 (1248.93)	498.6	44
69	BLOCK B EXPANSION [3.5 TO 8.0 (Northern Coalfields Limited [NCL]) (400162)	Madhya Pradesh	07/2019 (07/2019)	03/2023 (03/2027)	998.71 (998.71)	488.66	48
70	NIGAH EXPANSION [15 TO 25 MTP (Northern Coalfields Limited [NCL]) (400321)	Madhya Pradesh	11/2020 (11/2020)	03/2025 (03/2028)	1729.68 (1729.68)	859.8	48
71	KANCHAN OC EXP (South Eastern Coalfields Limited [SECL]) (613802)	Madhya Pradesh	12/2014 (12/2014)	03/2026 (03/2028)	371.04 (371.04)	144.61	58
72	JHIRIA WEST OCP [1.5 MTY] (South Eastern Coalfields Limited [SECL]) (613803)	Madhya Pradesh	01/2024 (01/2024)	03/2029 (-)	366.94 (366.94)	34.12	41
73	RPR TAWA-III UG 0.84 MTY (Western Coalfields Limited [WCL]) (613804)	Madhya Pradesh	12/2021 (12/2021)	03/2027 (-)	314.09 (314.09)	6.08	17
74	AMALGAMATED DHANKASA & JAMUNIA (Western Coalfields Limited [WCL]) (615185)	Madhya Pradesh	09/2022 (09/2022)	03/2027 (-)	399.2 (399.2)	96.21	66
75	RPR OF VISHNUPURI UG TO OC (Western Coalfields Limited [WCL]) (615187)	Madhya Pradesh	11/2022 (11/2022)	03/2029 (-)	220.62 (220.62)	0	11
76	URDHAN EXPANSION OC COST PLUS (Western Coalfields Limited [WCL]) (615194)	Madhya Pradesh	07/2022 (01/2023)	03/2031 (-)	206.88 (206.88)	27.19	0
77	SHARDA UG MINE (Western Coalfields Limited [WCL]) (615195)	Madhya Pradesh	07/2022 (09/2023)	03/2028 (-)	166.25 (166.25)	4.41	9
78	GANDHIGRAM UG MINE (Western Coalfields Limited [WCL]) (615206)	Madhya Pradesh	08/2019 (08/2019)	03/2026 (-)	414.15 (414.15)	18.04	56
79	BHATADI EXPANSION OC (Western Coalfields Limited [WCL]) (400033)	Maharashtra	02/2020 (05/2022)	03/2028 (-)	580.61 (580.61)	84.73	31
80	AMALGAMATED YEKONA I & YEKONA (Western Coalfields Limited [WCL]) (400177)	Maharashtra	08/2015 (08/2015)	03/2025 (03/2026)	727.28 (727.28)	539.9	80
81	DINESH[MAKARDHOKRA-III] OC (Western Coalfields Limited [WCL]) (400178)	Maharashtra	02/2020 (02/2020)	03/2027 (-)	822.88 (822.88)	623.1	34
82	DHUPTALA OC [SASTI UG TO OC] (Western Coalfields Limited [WCL]) (400353)	Maharashtra	02/2019 (10/2021)	03/2028 (-)	711.01 (711.01)	169.79	19
83	SAONER UG MINE -1 EXPANSION 1. (Western Coalfields Limited [WCL]) (615184)	Maharashtra	01/2022 (01/2022)	03/2028 (-)	228.64 (228.64)	146.08	68
84	SASTI EXPANSION OPENCAST (Western Coalfields Limited [WCL]) (615186)	Maharashtra	08/2020 (08/2020)	03/2026 (-)	319.04 (319.04)	91.82	20
85	NEW MAJRI UG TO OC 3 MTY COST (Western Coalfields Limited [WCL]) (615188)	Maharashtra	05/2019 (09/2022)	03/2027 (-)	402.27 (402.27)	60.25	24



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
86	MAKARDHOKRA EXPN OC 4.9 MTY (Western Coalfields Limited [WCL]) (615189)	Maharashtra	06/2022 (06/2022)	03/2026 (-)	361.87 (361.87)	85.39	11
87	SINGHORI DEEP OC MIN 2.0 MTY (Western Coalfields Limited [WCL]) (615190)	Maharashtra	05/2022 (05/2022)	03/2029 (-)	335.75 (335.75)	35.89	6
88	GOKUL EXTENSION OC MINE (Western Coalfields Limited [WCL]) (615192)	Maharashtra	04/2021 (04/2021)	03/2026 (-)	309.58 (309.58)	46.56	8
89	KOLGAON EXPANSION DEEP OC MINE (Western Coalfields Limited [WCL]) (615199)	Maharashtra	01/2023 (09/2023)	03/2027 (-)	198.71 (198.71)	12.89	2
90	BALLARPUR NORTH WEST OC MINE (Western Coalfields Limited [WCL]) (615330)	Maharashtra	12/2022 (12/2022)	03/2029 (-)	360.81 (360.81)	0.02	4
91	GADEGAON OC 3 MTY (Western Coalfields Limited [WCL]) (615331)	Maharashtra	10/2023 (10/2023)	03/2030 (-)	497.41 (497.41)	0.08	0
92	GHONSA EXPANSION DEEP OC MINE (Western Coalfields Limited [WCL]) (615914)	Maharashtra	03/2021 (03/2021)	03/2029 (-)	184.71 (184.71)	14.88	5
93	AMLG GAURI PAUNI EXPANSION OC (Western Coalfields Limited [WCL]) (615916)	Maharashtra	04/2024 (04/2024)	03/2030 (-)	1225.21 (1225.21)	80.14	2
94	GAURIDEEP/GAURI CENTRAL OCP 7. (Western Coalfields Limited [WCL]) (615917)	Maharashtra	08/2023 (06/2024)	03/2030 (-)	973.07 (973.07)	0.67	0
95	RPR OF BHANEGAON OC (Western Coalfields Limited [WCL]) (615918)	Maharashtra	02/2017 (09/2022)	03/2028 (-)	405.2 (405.2)	12.64	7
96	N. EXTN. MUNGOLI NIRGUDA D OCP (Western Coalfields Limited [WCL]) (615919)	Maharashtra	06/2024 (06/2024)	03/2029 (-)	1024.91 (1024.91)	175.86	0
97	NILJAI EXPANSION DEEP OCP (Western Coalfields Limited [WCL]) (615982)	Maharashtra	08/2016 (08/2016)	03/2022 (03/2026)	319.75 (319.75)	187.1	79
98	UKNI DEEP OC MINE -COST PLUS (Western Coalfields Limited [WCL]) (616044)	Maharashtra	11/2018 (01/2019)	03/2021 (03/2026)	237.06 (237.06)	165.81	87
99	AMALGAMATED INDER-KAMPTEE DEEP (Western Coalfields Limited [WCL]) (616050)	Maharashtra	09/2018 (09/2018)	03/2024 (03/2026)	235.9 (235.9)	132.25	98
100	ADASA UG TO OC MINE (Western Coalfields Limited [WCL]) (616223)	Maharashtra	11/2018 (11/2018)	03/2024 (03/2026)	316 (316)	208.73	86
101	AMAL GONDEGAON GHATROHANA EXPN (Western Coalfields Limited [WCL]) (616229)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	668.54 (668.54)	1.19	0
102	WAGHODA UG MINE [1.02 MTY] (Western Coalfields Limited [WCL]) (617233)	Maharashtra	01/2024 (01/2025)	03/2030 (-)	379.3 (379.3)	0	0
103	KOLARPIMPRI EXPANSION OC [2.5 (Western Coalfields Limited [WCL]) (617278)	Maharashtra	06/2024 (02/2025)	03/2030 (-)	630.37 (630.37)	0	0
104	Master Plan for Jharia and Raniganj Coalfields (Bharat Coking Coal Limited [BCCL]) (400313)	Multi-States (Jharkhand, West Bengal)	08/2009 (08/2009)	08/2019 (12/2028)	2661.73 (2661.73)	792.93	43
105	BINA KAKRI AMALGAMATION EXPANS (Northern Coalfields Limited [NCL]) (400369)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020 (08/2020)	03/2024 (03/2027)	836.42 (836.42)	829.04	89
106	KHADIA EXPANSION [10 TO 16 MTP (Northern Coalfields Limited [NCL]) (615183)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021 (06/2021)	03/2025 (03/2027)	491.67 (491.67)	258.02	52
107	SUBHADRA OCP (Mahanadi Coalfields Limited [MCL]) (400165)	Odisha	05/2021 (05/2021)	04/2032 (-)	1693.81 (1693.81)	1326.59	42
108	SIARMAL OCP (Mahanadi Coalfields Limited [MCL]) (400166)	Odisha	02/2021 (02/2021)	03/2029 (-)	5194.95 (5194.95)	3462.73	57
109	BALARAM EXPANSION OCP (Mahanadi Coalfields Limited [MCL]) (400183)	Odisha	08/2020 (08/2020)	03/2029 (-)	3504.21 (3504.21)	927.17	53
110	GOPALJI KANIHA OCP [10 TO 30 M (MCL - CIL) (400185)	Odisha	04/2022 (04/2022)	03/2030 (-)	8416.19 (6107.87)	1745.72	17
111	INTEGRATED LAKHANPUR-BELPAHAR- (Mahanadi Coalfields Limited [MCL]) (400187)	Odisha	05/2018 (05/2018)	03/2027 (-)	2434.75 (2434.75)	1859.96	71
112	BHARATPUR RE-ORGANIZATION OCP (Mahanadi Coalfields Limited [MCL]) (400392)	Odisha	11/2018 (11/2018)	03/2029 (-)	2838.86 (2838.86)	1676.51	48
113	BASUNDHARA WEST EXTENSION OPEN (MCL - CIL) (615193)	Odisha	05/2014 (05/2014)	03/2019 (03/2029)	479.15 (479.15)	275.1	65
114	Naini Coal Mine (Singareni Collieries Company Limited [SCCL]) (615857)	Odisha	03/2020 (03/2020)	03/2026 (-)	494.3 (494.3)	491.33	80
115	INTEGRATED KULDA GARJANBAHAL O (Mahanadi Coalfields Limited [MCL]) (616226)	Odisha	04/2023 (04/2023)	03/2033 (-)	3563.5 (3563.5)	604.11	3
116	BHUBANESWARI EXPN OCP 50 MTY (MCL - CIL) (616231)	Odisha	03/2024 (03/2024)	03/2033 (-)	5366.27 (5366.27)	472.43	29



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
117	HINGULA II OC EXPN PH III 15 M (MCL - CIL) (616232)	Odisha	11/2022 (11/2022)	03/2029 (-)	1561.85 (1561.85)	274.97	24
118	BALABHADRA OCP (MCL - CIL) (616233)	Odisha	04/2023 (04/2023)	03/2030 (-)	978.44 (978.44)	214.56	12
119	Talabira II & III OCP - FMC (NLC India Limited [NLCIL]) (618982)	Odisha	10/2022 (05/2023)	06/2026 (-)	522.45 (522.45)	311.28	68
120	Jawahar Khani Open Cast Mine (Singareni Collieries Company Limited [SCCL]) (615818)	Telangana	12/2021 (12/2021)	03/2025 (03/2027)	297.88 (297.88)	47.06	20
121	Kalyanikhani Opencast Project (Singareni Collieries Company Limited [SCCL]) (615858)	Telangana	03/2016 (05/2017)	03/2026 (-)	384.32 (384.32)	284.94	75
122	Godavarikhani Coal Mine - 5 (Singareni Collieries Company Limited [SCCL]) (615860)	Telangana	07/2019 (05/2019)	03/2025 (03/2026)	607.04 (607.04)	196.67	71
123	Indaram Opencast Project (Singareni Collieries Company Limited [SCCL]) (615861)	Telangana	08/2017 (12/2022)	03/2025 (03/2026)	424.81 (424.81)	405.12	80
124	Goleti Opencast Mine (Singareni Collieries Company Limited [SCCL]) (615862)	Telangana	07/2021 (08/2021)	03/2026 (-)	345.6 (345.6)	80.24	21
125	Venkatesh Khani Coal Mine (Singareni Collieries Company Limited [SCCL]) (615863)	Telangana	10/2020 (06/2020)	03/2026 (-)	484.5 (484.5)	477.14	97
126	Kakatiyakhani OC - 2 Project (Singareni Collieries Company Limited [SCCL]) (615865)	Telangana	08/2017 (09/2017)	03/2025 (03/2026)	442.42 (442.42)	230.39	63
127	MOHANPUR EXPANSION OC - PHASE I (Eastern Coal Fields Limited [ECL]) (400173)	West Bengal	11/2020 (11/2020)	03/2026 (03/2030)	888.99 (888.99)	119.09	30
128	BONJEMEHARI EXPANSION OCP (Eastern Coal Fields Limited [ECL]) (400180)	West Bengal	08/2021 (08/2021)	03/2026 (03/2030)	570.11 (570.11)	83.36	16
129	NAKRAKONDA KUMARDIH- B OCP (Eastern Coal Fields Limited [ECL]) (400181)	West Bengal	08/2018 (08/2018)	03/2029 (-)	502.68 (502.67)	71.85	26
130	SIDULI [OC & UG] (ECL - CIL) (400182)	West Bengal	05/2018 (05/2018)	03/2027 (03/2030)	535.18 (535.17)	5.32	14
131	TILABONI UG (Eastern Coal Fields Limited [ECL]) (400186)	West Bengal	01/2023 (01/2023)	03/2029 (-)	749.08 (749.07)	52.89	10
132	JHANJRA EXPANSION UG (Eastern Coal Fields Limited [ECL]) (400312)	West Bengal	04/2020 (04/2020)	03/2029 (-)	1210.12 (1210.12)	550.2	44
133	SONEPUR BAZARI EXPANSION OCP [] (Eastern Coal Fields Limited [ECL]) (400315)	West Bengal	07/2021 (07/2021)	03/2029 (-)	5365.88 (5365.88)	596.74	17
134	2.0 MTPA BHOJUDIH NLW WASHERY (Ministry of Coal) (611016)	West Bengal	12/2015 (03/2019)	09/2020 (12/2025)	384.57 (384.57)	358.11	97
135	ITAPARA OCP (Eastern Coal Fields Limited [ECL]) (612816)	West Bengal	12/2023 (12/2023)	03/2030 (-)	929.1 (929.1)	69.88	7
136	SHYAMSUNDARPUR UG INCLUDING SA (Eastern Coal Fields Limited [ECL]) (613793)	West Bengal	04/2020 (04/2020)	03/2026 (03/2028)	483.65 (483.65)	61.75	16
137	PARASEA-BELBAID UG PROJECT (Eastern Coal Fields Limited [ECL]) (613794)	West Bengal	01/2023 (01/2023)	03/2028 (-)	389.1 (389.1)	132.48	21
138	PARASCOLE JAMBAD OCP (Eastern Coal Fields Limited [ECL]) (616230)	West Bengal	11/2024 (11/2024)	03/2037 (-)	1193.55 (1193.55)	10.9	0
Total (113)					156284.68	47277.79	
Electricity Generation							
139	50 MW Wind Power Project (NLC India Limited [NLCIL]) (617299)	Gujarat	07/2022 (01/2024)	06/2025 (01/2026)	383.84 (383.84)	323.92	51
140	600 MW Khavda Solar Power Project (NLC India Limited [NLCIL]) (617730)	Gujarat	08/2023 (06/2024)	06/2026 (-)	3335.85 (3335.85)	1143.13	25
141	200 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (618991)	Gujarat	07/2022 (03/2024)	12/2026 (-)	1221.41 (1221.41)	61.81	0
142	100 MW SPP part of SECI 150 MW Hybrid (NLC India Limited [NLCIL]) (618992)	Gujarat	07/2022 (04/2024)	12/2026 (-)	480.68 (480.68)	2.52	1
143	NLC Talabira Thermal Power Project (NLC India Limited [NLCIL]) (400231)	Odisha	01/2017 (01/2024)	03/2030 (-)	27212.96 (27213)	2607.89	1
144	300 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (612819)	Rajasthan	07/2022 (03/2023)	09/2024 (12/2025)	1813 (1813)	1627.06	93
145	50 MW Solar PP Minedout Area (NLC India Limited [NLCIL]) (615327)	Tamil Nadu	08/2023 (02/2024)	03/2025 (12/2025)	218.03 (218.03)	165.5	85
146	Ghatampur Thermal Power Plant 3 X 660 MW (NLC India Limited [NLCIL]) (400259)	Uttar Pradesh	07/2016 (08/2016)	11/2020 (03/2026)	17237.8 (21780.9)	20743.86	94



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Total (8)					51903.57	26675.69	
Railways							
147	Dharamjaigarh-Korba (Railway) (400203)	Chhattisgarh	05/2018 (03/2017)	12/2026 (08/2026)	1686.22 (1686.22)	484.26	42
148	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] (Ministry of Coal) (400416)	Jharkhand	02/2018 (05/2022)	06/2025 (06/2026)	1799.64 (2564.34)	1489.74	64
Total (2)					3485.86	1974	
Ministry of Power							
Coal							
149	Tubed Coal Mine (Damodar Valley Corporation) (400192)	Jharkhand	07/2016 (10/2016)	05/2026 (05/2026)	1581 (1581)	599.18	36
150	Badam Coal Mining project of NTPC (National Thermal Power Corporation [NTPC]) (603293)	Jharkhand	02/2019 (09/2019)	12/2056 (04/2027)	502 (784)	388.29	59
Total (2)					2083	987.47	
Electricity Generation							
151	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited (NHPC)) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3861.98	16
152	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	66.73	3
153	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	61.45	2
154	Buxar Thermal Power Project [1320 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602579)	Bihar	03/2019 (06/2019)	01/2024 (12/2025)	10439.09 (13756.6)	12911.13	93
155	Lara Super Thermal Power Project Stage-II [2 x 800 MW] (National Thermal Power Corporation [NTPC]) (611930)	Chhattisgarh	08/2023 (08/2023)	06/2028 (09/2028)	15530 (16106)	3498.35	21
156	Sipat Super Thermal Power Project, Stage-III [1x800 MW] (National Thermal Power Corporation [NTPC]) (617188)	Chhattisgarh	09/2024 (09/2024)	09/2029 (-)	9791 (9791)	1054.25	8
157	Bagodara Solar Power Project (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709747)	Gujarat	03/2021 (05/2021)	12/2025 (12/2025)	339.35 (339.35)	317.59	51
158	Dhulasidh Hydro Electric Project [66 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602582)	Himachal Pradesh	10/2020 (05/2021)	11/2025 (03/2027)	687.97 (1561.21)	1027.23	72
159	Luhri Stage-I Hydro Electric Project [210 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602593)	Himachal Pradesh	11/2020 (11/2020)	01/2026 (02/2030)	1810.56 (4681.64)	1841.71	51
160	382 MW Sunni Dam HEP (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602633)	Himachal Pradesh	NA (04/2018)	03/2027 (-)	2615 (2615)	495.57	0.5
161	Sunni Dam Hydro Electric Project [382 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (611586)	Himachal Pradesh	01/2023 (01/2023)	04/2028 (12/2029)	2614.51 (4925.87)	1025.3	31
162	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW (National Hydroelectric Power Corporation Limited [NHPC]) (602525)	Jammu and Kashmir	10/2014 (02/2018)	04/2020 (12/2026)	8112.12 (12728)	8057.69	77
163	Kiru HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (602532)	Jammu and Kashmir	03/2019 (02/2020)	09/2023 (12/2026)	4287.59 (5409)	3313.59	75
164	Rattle HE Project - 850 MW, Rattle Hydroelectric Power Corporation Limited. (National Hydroelectric Power Corporation Limited [NHPC]) (602535)	Jammu and Kashmir	02/2021 (01/2022)	02/2026 (11/2028)	5281.94 (5281.94)	1384.07	26
165	Kwar HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (605155)	Jammu and Kashmir	05/2022 (11/2022)	11/2026 (03/2028)	4526.12 (4526.12)	1203.55	26
166	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] (National Thermal Power Corporation [NTPC]) (400261)	Jharkhand	11/2017 (11/2017)	03/2023 (02/2027)	18668 (20302)	18166	86
167	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand (Damodar Valley Corporation) (611509)	Jharkhand	04/2023 (11/2024)	03/2029 (-)	14358 (14358)	1538.88	6
168	Gadarwara Super Thermal Power Project, Stage-II [3x800 MW] (National Thermal Power Corporation [NTPC]) (618976)	Madhya Pradesh	11/2024 (05/2025)	03/2030 (-)	20446 (20446)	1145.83	4
169	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited (NHPC)) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	25718.57	97
170	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion (National Thermal Power Corporation [NTPC]) (602961)	Odisha	08/2022 (09/2022)	05/2027 (03/2028)	11843.75 (12543)	5347.06	44
171	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited (NHPC)) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	3972.89	71
172	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited (NHPC)) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (12/2025)	938.29 (1828.11)	1531.04	94
173	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] (National Thermal Power Corporation [NTPC]) (612142)	Uttar Pradesh	03/2024 (03/2024)	02/2030 (-)	17195 (17195)	2418.36	13



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
174	Tapovan-Vishnugad HEP [4x130 MW] (National Thermal Power Corporation [NTPC]) (602185)	Uttarakhand	NA (11/2006)	03/2013 (04/2029)	2978 (10907.3)	6769.58	77
175	Tehri Pumped Storage Plant Project [4x250 MW] (THDC India Limited) (602193)	Uttarakhand	07/2006 (06/2011)	06/2022 (03/2026)	4825.6 (8339)	8169.51	98
176	Vishnugad Pipalkoti Hydro Electric Project [444 MW] (THDC India Limited) (602195)	Uttarakhand	08/2008 (01/2014)	12/2022 (09/2027)	3860.35 (6405.08)	5004.46	74
177	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal (Damodar Valley Corporation) (400062)	West Bengal	01/2023 (02/2025)	06/2029 (-)	17673 (17673)	1479.89	4
178	Rammam-III HEPP [3x40 MW] (National Thermal Power Corporation [NTPC]) (602184)	West Bengal	09/2014 (09/2014)	09/2019 (03/2029)	1381.84 (2865.56)	1431.94	52
179	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 (Damodar Valley Corporation) (602538)	West Bengal	06/2019 (02/2021)	01/2024 (12/2025)	1037 (1106)	1115.65	93
Total (29)					228838.76	123929.85	
Transmission & Distribution							
180	Transmission Scheme for Solar Energy Zone in Ananthpuram 2500MW and Kurnool 1000MW (Power Grid Corporation of India Limited [POWERGRID]) (611967)	Andhra Pradesh	09/2023 (09/2023)	09/2025 (03/2026)	1248.69 (1248.69)	1077.61	91
181	Augmentation of 1x1500 MVA 3rd 765/400 kV transformation capacity at Kurnool New Substation (Power Grid Corporation of India Limited [POWERGRID]) (612856)	Andhra Pradesh	05/2023 (12/2023)	09/2025 (03/2026)	163.61 (163.61)	111.04	82
182	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617183)	Andhra Pradesh	03/2025 (03/2025)	12/2027 (-)	2886 (2886)	155.84	4
183	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	0.04	0
184	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part C (Power Grid Corporation of India Limited [POWERGRID]) (611657)	Gujarat	03/2023 (03/2023)	03/2025 (01/2026)	2820.99 (2820.99)	2783.19	98
185	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (612139)	Gujarat	12/2023 (12/2023)	12/2025 (12/2026)	3751.82 (3751.82)	2101.02	38
186	Transmission System for Evacuation of Power from potential Renewable Energy zone in Khavda Area of Gujarat under Phase IV [7 GW] Part E3 (Power Grid Corporation of India Limited [POWERGRID]) (612151)	Gujarat	07/2023 (07/2023)	07/2025 (03/2026)	334 (334)	236.17	78
187	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (612855)	Gujarat	05/2024 (05/2024)	05/2026 (06/2026)	679 (679)	176.54	31
188	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615342)	Gujarat	10/2024 (10/2024)	07/2026 (-)	329 (329)	14.67	5
189	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] (Power Grid Corporation of India Limited [POWERGRID]) (615343)	Gujarat	11/2024 (11/2024)	11/2026 (-)	501 (501)	8.11	2
190	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345)	Gujarat	10/2024 (10/2024)	10/2026 (03/2027)	4766 (4766)	1048.56	12
191	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069)	Gujarat	02/2025 (02/2025)	02/2027 (-)	466 (466)	23.99	1
192	Augmentation of Banaskantha [Raghnesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182)	Gujarat	03/2025 (03/2025)	03/2027 (-)	172 (172)	20.64	19
193	Augmentation of Transformation Capacity at Bhuj-II PS [GIS] (Power Grid Corporation of India Limited [POWERGRID]) (617391)	Gujarat	02/2025 (02/2025)	11/2026 (03/2027)	488.29 (488.29)	0.98	0
194	Jamnagar Transmission Limited (Adani Transmission Limited) (617405)	Gujarat	NA (10/2024)	10/2026 (-)	4000 (4000)	268	16
195	Provision of ICT Augmentation & Bus Reactor at Bhuj-II PS (Power Grid Corporation of India Limited [POWERGRID]) (617801)	Gujarat	03/2025 (03/2025)	12/2026 (03/2027)	581.74 (581.74)	1.16	0
196	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272)	Haryana	06/2024 (06/2024)	12/2026 (-)	370 (370)	22.2	6
197	Transmission Scheme for evacuation of Power from Ratle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179)	Jammu and Kashmir	07/2024 (07/2024)	07/2026 (03/2027)	218.6 (218.6)	2.71	0



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
198	Implementation of Transmission Systems in the State of Jharkhand consisting of 400/220/132/33 kV transmission lines and substations under Jharkhand Consultancy Project (Power Grid Corporation of India Limited [POWERGRID]) (617326)	Jharkhand	02/2012 (02/2012)	03/2026 (08/2026)	1842.25 (1842.25)	1648.05	95
199	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140)	Karnataka	12/2023 (12/2023)	12/2025 (06/2026)	2889.39 (2889.39)	1841.69	68
200	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672)	Karnataka	01/2025 (01/2025)	06/2027 (-)	1354 (1354)	49.15	6
201	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068)	Karnataka	02/2025 (02/2025)	06/2027 (-)	288 (288)	7.41	3
202	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184)	Karnataka	03/2025 (03/2025)	09/2027 (-)	3453 (3453)	69.06	3
203	Transmission System Strengthening at Davanagere for Integration of RE Generation [SPV Name - POWERGRID Davanagere Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617803)	Karnataka	09/2025 (09/2025)	09/2027 (-)	379 (379)	7.58	0
204	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344)	Madhya Pradesh	10/2024 (10/2024)	10/2026 (03/2027)	3674 (3674)	1099.98	24
205	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346)	Madhya Pradesh	08/2024 (08/2024)	08/2026 (12/2026)	2708 (2708)	1110.22	47
206	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279)	Madhya Pradesh	06/2025 (06/2025)	12/2027 (-)	558 (558)	33.48	2
207	Augmentation of Transformation Capacity and Implementation of Line Bays at Mandsaur S/S for RE Interconnection [SPV Name- POWERGRID Mandsaur I RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617802)	Madhya Pradesh	10/2025 (10/2025)	03/2028 (-)	319 (319)	1.1	0
208	Transmission System for Evacuation of power from Potential RE Zone in Khavda Area of Gujarat under phase IV 7GW-Part E4 (Power Grid Corporation of India Limited [POWERGRID]) (611966)	Maharashtra	11/2023 (11/2023)	07/2025 (03/2026)	224.41 (224.41)	109.96	49
209	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185)	Multi-States (Andhra Pradesh, Karnataka)	03/2025 (03/2025)	03/2027 (-)	5550 (5550)	610	4
210	Transmission System for Integration of Ananthapur 2 REZ Phase 1 for 4.5 GW. SPV Name Anantapuram 2 REZ Transmission Ltd (Sterlite Power) (617806)	Multi-States (Andhra Pradesh, Karnataka)	08/2024 (03/2025)	03/2027 (-)	4535.99 (4535.99)	401.57	32
211	Transmission System for Kurnool Wind Energy Zone/ Solar Energy Zone Part-A and Part-B (Power Grid Corporation of India Limited [POWERGRID]) (900808)	Multi-States (Andhra Pradesh, Telangana)	11/2022 (03/2023)	11/2024 (03/2026)	3546.94 (3546.94)	3440.49	98
212	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	7809.22	82
213	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (03/2026)	5111.33 (6700)	5442.41	96
214	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271)	Multi-States (Bihar, Odisha, West Bengal)	09/2024 (09/2024)	03/2026 (06/2026)	342.69 (342.69)	6.85	4
215	Inter-regional [NR-WR] Transmission System strengthening to relieve the loading of 765 kV Vindhyachal-Varanasi D/c line (Power Grid Corporation of India Limited [POWERGRID]) (617807)	Multi-States (Bihar, Uttar Pradesh)	10/2025 (10/2025)	10/2027 (-)	2368 (2368)	3	0
216	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270)	Multi-States (Bihar, West Bengal)	11/2024 (11/2024)	05/2026 (03/2027)	408.94 (408.94)	0.4	0
217	Transmission Network Expansion in Gujarat to increase its ATC from ISTS Part B (Power Grid Corporation of India Limited [POWERGRID]) (400005)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	01/2022 (07/2022)	06/2023 (03/2026)	4546.26 (4546.26)	4358.49	95
218	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735)	Multi-States (Delhi, Rajasthan)	12/2022 (12/2022)	03/2025 (07/2026)	331 (331)	142.84	42
219	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132)	Multi-States (Delhi, Rajasthan)	02/2024 (02/2024)	08/2025 (06/2026)	2000 (2000)	1565.4	76



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
220	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347)	Multi-States (Gujarat, Maharashtra)	11/2024 (11/2024)	05/2029 (-)	24819 (24819)	1985.98	5
221	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5969 (5969)	837.04	14
222	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Siwani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340)	Multi-States (Haryana, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5357 (5357)	785.56	21
223	Inter-Regional Strengthening between SR Grid and WR Grid (Power Grid Corporation of India Limited [POWERGRID]) (617808)	Multi-States (Karnataka, Maharashtra)	10/2025 (10/2025)	10/2027 (-)	1007 (1007)	5.03	0
224	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138)	Multi-States (Karnataka, Telangana)	02/2024 (02/2024)	02/2026 (06/2026)	2147.62 (2147.62)	1685.45	79
225	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (-)	2227 (2227)	846.22	29
226	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (03/2027)	3251 (3251)	1202.85	32
227	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [Rajasthan V Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025 (03/2025)	03/2027 (-)	5028 (5028)	411.29	9
228	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023 (12/2023)	12/2025 (06/2026)	2056 (2056)	1644.8	66
229	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024 (12/2024)	12/2026 (03/2027)	5846 (5846)	744.68	15
230	Transmission System for Evacuation of Power from REZ in Rajasthan 20GW under Phase III- Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (611947)	Rajasthan	11/2023 (11/2023)	06/2025 (03/2026)	428.3 (428.3)	334.08	82
231	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part H (Power Grid Corporation of India Limited [POWERGRID]) (611948)	Rajasthan	10/2023 (10/2023)	04/2025 (03/2026)	2211.29 (2211.29)	2081.24	94
232	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949)	Rajasthan	10/2023 (10/2023)	04/2025 (03/2026)	1796.02 (1796.02)	1621.79	94
233	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part B1 (Power Grid Corporation of India Limited [POWERGRID]) (611950)	Rajasthan	09/2023 (09/2023)	04/2025 (01/2026)	2190.54 (2190.54)	2079.44	98
234	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part E1 (Power Grid Corporation of India Limited [POWERGRID]) (611951)	Rajasthan	12/2021 (08/2023)	02/2025 (01/2026)	688.74 (688.74)	685.29	99
235	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134)	Rajasthan	12/2023 (12/2023)	12/2025 (06/2026)	2998.34 (2998.34)	2158.8	62
236	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332)	Rajasthan	08/2024 (08/2024)	08/2026 (12/2026)	3279 (3279)	1260.05	32
237	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615335)	Rajasthan	08/2024 (08/2024)	08/2026 (12/2026)	1382 (1382)	290.08	18
238	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615337)	Rajasthan	08/2024 (08/2024)	02/2026 (03/2026)	369 (369)	129.49	38
239	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615338)	Rajasthan	11/2024 (11/2024)	11/2026 (06/2027)	2735 (2735)	656.05	22
240	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617181)	Rajasthan	03/2025 (03/2025)	12/2026 (03/2027)	404 (404)	20.2	2
241	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616671)	Tamil Nadu	01/2025 (01/2025)	12/2026 (12/2026)	548 (548)	102.46	12



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
242	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex (Power Grid Corporation of India Limited [POWERGRID]) (617269)	Uttar Pradesh	12/2024 (12/2024)	06/2026 (08/2026)	212.81 (212.81)	2.1	0
Total (63)					152121.4	59380.79	
Ministry of Housing & Urban Affairs							
Construction							
243	Construction of One Tower of Office Complex and another Tower of Residential quarters consisting of 10Nos. Type-V, 10Nos. Type-VI & 1No.Type-VII Quarters i/c internal water supply, sanitary installation and all development and bulk services, Horticulture works on EPC Mode-I basis i/c comprehensive operation and maintenance of Civil, E&M services for 7 years after completion of original construction work for Ranga Reddy, Secunderabad, Medchal, Auditl, Audit-II Commissionerates of Central Tax at Khajaguda, Serilingampally, Hyderabad. (Central Public Works Department - CPWD) (617412)	Telangana	03/2024 (11/2024)	09/2027 (-)	644 (644)	116.18	10
Total (1)					644	116.18	
Real Estate							
244	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System (ministry of housing and urban affairs) (707229)	Andaman & Nicobar	07/2021 (11/2021)	05/2023 (-)	209.88 (209.88)	0	70
245	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi (National Buildings Construction Corporation [NBCC]) (400188)	Delhi	07/2016 (05/2018)	12/2025 (12/2025)	32850 (32850)	0	0
246	Rehabilitation in Junavadaj Area Smart City Project (ministry of housing and urban affairs) (701719)	Gujarat	02/2016 (06/2016)	07/2022 (-)	539 (539)	39.63	50
247	Green Building Development Project (ministry of housing and urban affairs) (701766)	Uttarakhand	11/2019 (08/2019)	11/2023 (-)	150.97 (150.97)	18.95	31
Total (4)					33749.85	58.58	
Urban Public Transport							
248	Patna Metro Rail Project (Patna Metro Rail Corporation Ltd. [PMRCL]) (702627)	Bihar	02/2019 (02/2019)	02/2024 (06/2027)	13365.77 (13365.8)	4670.21	48
249	Delhi Metro Rail Phase-IV [2 Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (617207)	Delhi	03/2024 (03/2024)	03/2029 (-)	8399.81 (8399.81)	67.13	0
250	DMRTS Phase - IV [3 Priority Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (702632)	Delhi	07/2019 (07/2019)	03/2025 (03/2026)	24948.65 (24948.7)	18390.81	74
251	Surat Metro Rail Project (Gujarat Metro Rail Corporation Limited [GMRCL]) (702630)	Gujarat	03/2019 (04/2019)	03/2024 (06/2026)	12020.32 (12020.3)	8232.16	75
252	Ahmedabad Metro Rail Project, Phase-II (Gujarat Metro Rail Corporation Limited [GMRCL]) (702631)	Gujarat	03/2019 (03/2019)	03/2024 (12/2025)	5384.17 (5384.17)	4816.5	97
253	Ahmedabad Metro Rail Project [Phase-I] (Gujarat Metro Rail Corporation Limited [GMRCL]) (702639)	Gujarat	11/2014 (02/2015)	03/2018 (01/2026)	10773 (12924.5)	12266.48	99
254	Construction of Bangalore Metro Rail Project Phase 2. (Bengaluru Metro Rail) (702635)	Karnataka	02/2014 (02/2016)	03/2021 (09/2026)	26405.14 (30695.1)	29687.97	95
255	Construction Bangalore Metro Rail Project Phase-2A & 2B (Bengaluru Metro Rail) (702665)	Karnataka	06/2021 (01/2019)	06/2026 (06/2026)	14788.1 (14788.1)	9313.22	60
256	Kochi Metro Rail Phase 2 Development Project (CSPCC Projects) (702664)	Kerala	11/2022 (11/2022)	11/2026 (11/2026)	1957.05 (1957.05)	516.92	24
257	Bhopal Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702625)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (06/2028)	6941.4 (6941.4)	3846.45	51
258	Indore Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702626)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (12/2028)	7500.8 (7500.8)	4416.11	58
259	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617225)	Maharashtra	10/2023 (10/2023)	01/2027 (-)	910.18 (910.18)	196.77	32
260	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617226)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	2954.53 (2954.53)	25.24	4
261	Thane Integral Ring Metro Rail Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617327)	Maharashtra	09/2024 (09/2024)	09/2029 (-)	12200.1 (12200.1)	8.98	5
262	Pune Metro Rail Project Phase-2 Corridor 2A Vanaz to Chandani Chowk and Corridor 2B Ramwadi to Wagholi/Vitthalwadi (Maharashtra Metro Rail Corporation Limited [MMRCL]) (618971)	Maharashtra	07/2025 (07/2025)	07/2029 (-)	3626.24 (3626.24)	0.41	0
263	Pune Metro Rail Project Phase-2 Line-4 Kharadi to Khadakwasla with Spur Line 4A Nal Stop - Warje - Manikbaug (Maharashtra Metro Rail Corporation Limited [MMRCL]) (618985)	Maharashtra	12/2025 (12/2025)	12/2030 (-)	9857.85 (9857.85)	0	0
264	New Suburba Station Development Project (ministry of housing and urban affairs) (701745)	Maharashtra	04/2018 (03/2019)	07/2022 (-)	262.76 (262.76)	17.62	6
265	Kalyan Station Precinct Improvement Project (ministry of housing and urban affairs) (701991)	Maharashtra	04/2018 (07/2020)	07/2023 (-)	600 (600)	272.42	70



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
266	Mumbai Metro Line 3 (Mumbai Metro Rail Corporation Limited [MMRC]) (702637)	Maharashtra	07/2013 (06/2016)	03/2023 (08/2025)	23136 (37276)	32609.9	97
267	Nagpur Metro Rail Phase II Development Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (702658)	Maharashtra	12/2022 (12/2022)	12/2027 (-)	6708 (6708)	1472.03	31
268	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] (Delhi Metro Rail Corporation Limited [DMRC]) (617206)	Multi-States (Delhi, Haryana)	01/2025 (01/2025)	01/2029 (-)	6230.99 (6230.99)	72.43	0
269	Delhi-Ghaziabad-Meerut Regional Rapid Transit System [RRTS] corridor (National Capital Region Transport Corporation [NCRTC]) (702633)	Multi-States (Delhi, Uttar Pradesh)	03/2019 (03/2019)	06/2025 (01/2026)	30274 (30274)	27312.17	96
270	Chennai Metro Rail Phase-II Development Project (Chennai Metro Rail Limited [CMRL]) (702668)	Tamil Nadu	10/2024 (11/2020)	08/2029 (-)	63246 (63246)	30211.38	48
271	Kanpur Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702628)	Uttar Pradesh	05/2019 (11/2019)	05/2024 (03/2027)	11076.48 (11076.5)	9089.89	76
272	Agra Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702629)	Uttar Pradesh	05/2019 (12/2020)	05/2024 (06/2027)	8379.62 (8379.62)	6062.03	65
Total (25)					311946.96	203575.23	
Waste & Water							
273	ESR - 8 nos., distribution system - 216 Km, new house service connections - 38760 nos. upgrading of feeder mains, pumping station etc. - Phase II (Ministry of Housing & Urban Affairs) (702674)	Andhra Pradesh	02/2017 (07/2018)	03/2023 (03/2026)	172.22 (172.22)	88.86	82
274	Muzaffarpur Storm Water Drainage Phase-I Project (Ministry of Housing & Urban Affairs) (702699)	Bihar	11/2016 (02/2019)	10/2023 (03/2026)	158.78 (158.78)	69.52	83
275	Storm water drainag Development Project (ministry of housing and urban affairs) (702355)	Dadra & Nagar Haveli and Daman & Diu	08/2020 (12/2021)	03/2024 (-)	210 (210)	0	20
276	Upgradation of Sewerage system in Gandhinagar City (ministry of housing and urban affairs) (707267)	Gujarat	07/2020 (03/2021)	06/2023 (-)	200 (200)	100	10
277	Sewerage Management Scheme Part-3 Implementation (Ministry of Housing & Urban Affairs) (702734)	Haryana	03/2017 (11/2017)	09/2023 (03/2026)	278.01 (278.01)	218.89	88
278	Sewerage Management Scheme Part-3 Implementation (Ministry of Housing & Urban Affairs) (702735)	Haryana	03/2017 (10/2018)	03/2023 (01/2026)	213.19 (213.19)	168.14	91
279	Dhanbad Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702741)	Jharkhand	02/2017 (12/2018)	03/2023 (03/2026)	216.55 (216.55)	129.16	74
280	SAAP-3 Water Supply Infrastructure SAAP-3 Project (Ministry of Housing & Urban Affairs) (702742)	Jharkhand	02/2017 (12/2018)	10/2023 (03/2026)	159.31 (159.31)	87.5	66
281	Augmentation and Strengthening of Urban Water Supply Phase 1 - SAAP 3 (Ministry of Housing & Urban Affairs) (702746)	Jharkhand	02/2017 (12/2018)	03/2023 (03/2026)	278.28 (278.28)	186.5	79
282	Belgavi Improvement in Sewerage System Project (Ministry of Housing & Urban Affairs) (702760)	Karnataka	12/2015 (10/2016)	07/2023 (03/2026)	162.73 (162.73)	85.71	80
283	24/7 water supply under AMRUT for Davanagere (Ministry of Housing & Urban Affairs) (702764)	Karnataka	11/2016 (01/2018)	03/2023 (03/2026)	174.96 (174.96)	93.18	65
284	Indore Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702793)	Madhya Pradesh	12/2016 (11/2017)	03/2023 (01/2026)	287.17 (287.17)	252.5	99
285	Jabalpur Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702798)	Madhya Pradesh	10/2018 (12/2017)	03/2023 (01/2026)	362.31 (362.31)	322.31	96
286	Satna Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702808)	Madhya Pradesh	11/2015 (12/2016)	03/2024 (03/2026)	191.56 (215.89)	191.79	88
287	Singrauli Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702810)	Madhya Pradesh	05/2016 (11/2017)	03/2023 (03/2026)	402.01 (402.01)	357.68	90
288	Kalyan-Dombivali Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702833)	Maharashtra	07/2016 (09/2019)	10/2023 (03/2026)	194.2 (194.2)	136.56	75
289	Mira-Bhayandar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702840)	Maharashtra	11/2016 (08/2018)	03/2023 (02/2026)	204.55 (204.55)	186.13	99
290	Pune Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702851)	Maharashtra	03/2017 (07/2017)	03/2023 (03/2026)	235.95 (235.95)	184.98	95
291	Solapur Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702854)	Maharashtra	03/2017 (04/2018)	03/2023 (03/2026)	180.24 (180.24)	155.01	91
292	Jalandhar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (703021)	Punjab	11/2016 (08/2020)	08/2023 (03/2026)	258.53 (258.53)	161.02	58
293	Patiala Water Supply Infrastructure Part-2 Project (Ministry of Housing & Urban Affairs) (703057)	Punjab	11/2016 (08/2020)	10/2023 (02/2026)	287 (287)	213.64	99
294	Jaunpur Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702948)	Uttar Pradesh	03/2017 (08/2019)	06/2023 (02/2026)	235.73 (235.73)	221.27	99
295	Jhansi Water Supply Infrastructure Phase-II Project (Ministry of Housing & Urban Affairs) (702949)	Uttar Pradesh	03/2017 (06/2019)	07/2023 (02/2026)	561.74 (561.74)	485.91	93



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Total (23)					5625.02	4096.26	
Ministry of Mines							
Construction							
296	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata (Central Public Works Department (CPWD)) (617280)	West Bengal	04/2019 (02/2020)	08/2026 (-)	255.37 (255.37)	93.39	50
Total (1)					255.37	93.39	
Metals & Mining							
297	Expansion of Malanjkhand Copper Project (Hindustan Copper Limited [HCL]) (400426)	Madhya Pradesh	09/2011 (04/2015)	04/2020 (04/2026)	1856.36 (1856.36)	950.94	82
298	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonne Per Annum (National Aluminium Company Limited [NALCO]) (400141)	Odisha	04/2017 (04/2017)	12/2022 (09/2025)	4103 (5677.4)	4449.07	80
299	Pottangi Bauxite Mines Project (National Aluminium Company Limited [NALCO]) (400299)	Odisha	05/2018 (05/2018)	03/2025 (05/2026)	1381 (1960.77)	650.04	51
300	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (Ministry of Mines) (709830)	Odisha	NA (04/2017)	11/2026 (-)	355 (581)	163.55	12
301	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (National Aluminium Company Limited [NALCO]) (709831)	Odisha	11/2017 (11/2019)	05/2025 (06/2026)	483 (483)	417.31	91
302	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (National Aluminium Company Limited [NALCO]) (709832)	Tamil Nadu	09/2017 (12/2017)	03/2025 (03/2026)	166 (166)	135	66
Total (6)					8344.36	6765.91	
Department of Higher Education							
Education							
303	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008)	Andhra Pradesh	09/2019 (12/2023)	06/2027 (-)	305 (305)	51.33	38
304	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (08/2024)	592.61 (592.61)	550.61	80
305	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 (153.71)	125.03	97
306	Additional Campus of NITPatna (NIT Patna) (606013)	Bihar	07/2022 (08/2022)	07/2024 (01/2026)	499.21 (499.21)	445.97	97
307	Phase B of Construction of Permanent Campus of IIT Bhilai (Indian Institute of Technology, Bhilai) (617877)	Chhattisgarh	05/2025 (01/2026)	10/2028 (-)	1188.97 (1188.97)	0	0
308	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis (National Institute of Technology Delhi) (612851)	Delhi	09/2009 (11/2022)	09/2025 (01/2026)	333.49 (336.42)	297.65	97
309	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886)	Delhi	09/2024 (03/2025)	10/2026 (-)	373 (373)	27.63	10
310	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Central University of Gujarat) (612916)	Gujarat	12/2020 (02/2021)	03/2025 (03/2026)	490.63 (490.63)	316.05	83
311	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099)	Himachal Pradesh	09/2018 (08/2020)	10/2023 (02/2026)	392.51 (454.78)	328.83	95
312	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128)	Himachal Pradesh	03/2023 (03/2024)	03/2026 (03/2026)	166.66 (166.66)	102.52	76
313	Construction of Permanent Campus of Central University of Himachal Pradesh at Dehra, District - Kangra, [H.P.] on Engineering. Procurement and Construction [EPC Mode 1] Basis. (Central University, Himachal Pradesh) (612894)	Himachal Pradesh	03/2021 (08/2022)	11/2024 (03/2026)	251.98 (300.45)	221.2	82
314	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098)	Jammu and Kashmir	03/2019 (10/2020)	06/2023 (11/2025)	424.93 (500.91)	484.52	96
315	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431)	Kerala	07/2017 (03/2020)	06/2022 (06/2026)	1006.45 (1217.4)	663.4	79
316	Phase B of Construction of Permanent Campus of IIT Palakkad (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (617878)	Kerala	05/2025 (01/2026)	10/2028 (-)	1527 (1527)	9.8	0
317	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] (Indian Institute of Technology, Indore) (611957)	Madhya Pradesh	12/2023 (04/2024)	02/2027 (-)	496.28 (496.28)	56.35	37



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
318	Construction and Development of National Institute of Technology Meghalaya Permanent Campus at Sohra <i>(National Institute of Technology, Meghalaya)</i> (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (10/2026)	494.52 (429.7)	426.07	91
319	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl <i>(NIT Mizoram)</i> (612876)	Mizoram	09/2009 (06/2014)	12/2029 (03/2022)	474.23 (474.23)	167.55	4
320	Establishment of NIT Nagaland <i>(NIT Nagaland)</i> (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	261.7	97
321	IISER BERHAMPUR <i>(Indian Institutes of Science Education and Research, Behrampur)</i> (610315)	Odisha	10/2018 (09/2019)	03/2021 (06/2026)	1229.32 (843.09)	835.6	98
322	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] <i>(National Institute of Technology, Puducherry)</i> (612877)	Puducherry	09/2009 (07/2013)	12/2024 (08/2025)	618.34 (544.34)	530.45	97
323	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I <i>(Indian Institute of Management, Amritsar)</i> (605292)	Punjab	10/2019 (07/2020)	06/2023 (12/2025)	348.31 (348.31)	290.39	91
324	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment <i>(Central University of Punjab)</i> (617221)	Punjab	08/2024 (04/2025)	10/2027 (-)	210.99 (210.99)	30	19
325	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim <i>(Sikkim University)</i> (609736)	Sikkim	08/2020 (01/2022)	01/2025 (03/2026)	314.06 (314.06)	238.22	85
326	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District <i>(NIT Sikkim)</i> (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	171.56	24
327	Construction of Precast housing and hostels at IIT Hyderabad <i>(Indian Institute of Technology, Hyderabad)</i> (609996)	Telangana	09/2022 (11/2022)	10/2024 (01/2026)	262 (262)	194.37	83
328	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] <i>(Banaras Hindu University)</i> (606479)	Uttar Pradesh	06/2020 (06/2020)	09/2022 (03/2026)	246 (246)	199.71	97
329	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal <i>(National Institute of Technology Uttarakhand)</i> (611963)	Uttarakhand	06/2020 (04/2024)	09/2027 (-)	650.85 (650.85)	261.11	40
330	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur <i>(Indian Institute of Technology, Kharagpur)</i> (609019)	West Bengal	06/2018 (04/2019)	03/2023 (03/2026)	500 (442)	401.6	92
Total (28)					14512.44	7689.22	
Department of Sports							
Education							
331	National Sports University [NSU], Imphal [Manipur] <i>(Department of Sports & Youth Affairs)</i> (400081)	Manipur	NA (01/2022)	08/2024 (08/2026)	906.47 (611.74)	565.17	95
Total (1)					906.47	565.17	
Ministry of Petroleum & Natural Gas							
Energy Storage							
332	Construction of Aviation Fuel farm Facilities at Bhogapuram Airport <i>(Ministry of Petroleum & Natural Gas)</i> (616235)	Andhra Pradesh	08/2024 (08/2024)	03/2026 (03/2026)	240 (240)	134.94	89
333	Construction of LPG Facilities at Kamardanga, Assam <i>(Hindustan Petroleum Corporation Limited)</i> (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	74.46	55
334	Setting up of new rail fed POL facility at Kamardanga, Assam <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	168.47	67
335	Capacity Augmentation of Kandla LPG Import Terminal [KLIT] from 0.6 MMTPA to 2.5 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (617839)	Gujarat	05/2023 (05/2023)	07/2026 (07/2026)	356.86 (304.4)	90.44	60
336	Setting up a common user Petroleum Terminal at Jammu, J&K for resitment of existing PSU OMC's Depots from Jammu City <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (400235)	Jammu and Kashmir	04/2023 (04/2023)	03/2025 (01/2026)	676.89 (715.89)	576.69	91
337	Andheri Residential Towers, Mumbai <i>(Ministry of Petroleum & Natural Gas)</i> (604833)	Maharashtra	06/2017 (06/2017)	05/2025 (06/2026)	281.35 (389.67)	249.5	56
338	LPG Bottling Plant at Mualkhang <i>(Ministry of Petroleum & Natural Gas)</i> (617829)	Mizoram	07/2024 (07/2024)	10/2028 (11/2027)	225.71 (225.71)	16.32	26
339	Srikakulam Angul Gas Pipeline Project <i>(Ministry of Petroleum & Natural Gas)</i> (701343)	Multi-States (Andhra Pradesh, Odisha)	09/2019 (09/2019)	07/2022 (06/2026)	2658.34 (2810)	2282.98	96
340	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip <i>(Ministry of Petroleum & Natural Gas)</i> (701349)	Multi-States (Assam, Bihar, Jharkhand, Odisha, West Bengal)	01/2019 (01/2019)	07/2024 (06/2026)	10228 (11407)	10270.18	89
341	New Mundra Panipat Crude Oil Pipeline <i>(Ministry of Petroleum & Natural Gas)</i> (400078)	Multi-States (Gujarat, Haryana, Rajasthan)	12/2021 (12/2021)	12/2024 (06/2026)	9028 (9028)	7394.54	88
342	Kandla Gorakhpur LPG Pipeline <i>(Ministry of Petroleum & Natural Gas)</i> (400012)	Multi-States (Gujarat, Madhya Pradesh, Uttar Pradesh)	12/2018 (12/2018)	12/2021 (03/2026)	10088 (10088)	8217.69	94



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
343	Multi Product Pipeline from Irugur to Devangonchi <i>(Department of Water Resources, River Development & GR)</i> (400301)	Multi-States (Karnataka, Tamil Nadu)	11/2012 (11/2012)	02/2017 (09/2026)	678 (1732)	893.48	74
344	Rajasthan Refinery Project <i>(Ministry of Petroleum & Natural Gas)</i> (701263)	Rajasthan	10/2017 (10/2017)	10/2022 (03/2026)	43129 (79459)	63571.54	90
345	Petrochemical evacuation marketing terminal at Barmer, Rajasthan <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (709759)	Rajasthan	12/2023 (12/2023)	12/2026 (12/2026)	461.05 (461.05)	166.12	72
346	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] <i>(Ministry of Petroleum & Natural Gas)</i> (400043)	Tamil Nadu	01/2022 (01/2022)	05/2026 (05/2026)	829 (829)	339.98	69
347	Grass root POL Terminal at Vallur, Chennai <i>(Indian Oil Corporation Limited [IOCL])</i> (400077)	Tamil Nadu	01/2022 (01/2022)	12/2024 (03/2026)	827 (887.71)	649.51	90
348	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot <i>(Indian Oil Corporation Limited [IOCL])</i> (400035)	Tripura	06/2022 (06/2022)	09/2025 (06/2026)	656 (656)	526.86	92
349	Grass-root Terminal at Mirzapur, Uttar Pradesh <i>(Ministry of Petroleum & Natural Gas)</i> (604852)	Uttar Pradesh	09/2022 (09/2022)	11/2026 (11/2026)	980.45 (980.45)	250.55	62
Total (18)					81884.05	95874.25	
Oil & Gas							
350	KG-DWN-98/2 Cluster - II Development Project - NELP Block <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400120)	Andhra Pradesh	03/2016 (03/2016)	06/2020 (06/2026)	34012 (34012)	32374.37	96
351	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery <i>(Hindustan Petroleum Corporation Limited)</i> (709752)	Andhra Pradesh	09/2021 (09/2021)	06/2024 (03/2026)	160 (220)	106.27	80
352	City Gas Distribution Project at Kurnool, Guntur & Prakasam Districts <i>(Ministry of Petroleum & Natural Gas)</i> (709766)	Andhra Pradesh	03/2022 (03/2022)	03/2030 (03/2030)	1420 (1420)	170.7	6
353	Numaligarh Refinery Expansion Project <i>(Ministry of Petroleum & Natural Gas)</i> (604791)	Assam	07/2020 (07/2020)	07/2024 (09/2026)	12366 (22494)	18147.42	80
354	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija <i>(Ministry of Petroleum & Natural Gas)</i> (604863)	Assam	01/2018 (01/2018)	02/2020 (06/2026)	682.9 (726.93)	493.53	94
355	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery <i>(Ministry of Petroleum & Natural Gas)</i> (607701)	Assam	05/2021 (05/2021)	10/2023 (05/2026)	412.3 (577)	458.56	89
356	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field <i>(Ministry of Petroleum & Natural Gas)</i> (616858)	Assam	12/2020 (12/2020)	03/2024 (03/2026)	430.76 (430.76)	334.6	89
357	Coke Drum Structure Package <i>(Ministry of Petroleum & Natural Gas)</i> (617836)	Assam	12/2022 (12/2022)	12/2025 (09/2026)	635.28 (635.28)	80.32	51
358	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi <i>(Ministry of Petroleum & Natural Gas)</i> (709776)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277 (323.09)	192.31	74
359	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (709779)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768 (740)	130.46	49
360	Pipeline Network Project Rudrasagar <i>(Ministry of Petroleum & Natural Gas)</i> (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2026)	344.99 (344.99)	220.37	50
361	Borholla GGS Life Extension Project [BLEP] <i>(Ministry of Petroleum & Natural Gas)</i> (709850)	Assam	09/2023 (09/2023)	05/2026 (05/2026)	198.7 (198.7)	59.75	45
362	DCU Revamp Project <i>(NRL)</i> (709864)	Assam	08/2021 (08/2021)	07/2024 (06/2026)	370 (370)	274.81	68
363	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme <i>(NRL)</i> (709865)	Assam	04/2023 (04/2023)	12/2024 (09/2026)	293.5 (293.5)	97.22	98
364	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar <i>(Ministry of Petroleum & Natural Gas)</i> (617304)	Bihar	10/2023 (10/2023)	03/2027 (03/2027)	340.15 (340.15)	124.9	39
365	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (701324)	Bihar	01/2020 (01/2020)	04/2023 (08/2026)	14810 (16724)	12484.41	89
366	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery <i>(Ministry of Petroleum & Natural Gas)</i> (709777)	Bihar	01/2022 (01/2022)	04/2025 (10/2026)	389.35 (340)	84.81	52
367	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709792)	Bihar	12/2022 (12/2022)	03/2030 (03/2030)	3638 (3638)	437.06	30
368	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709793)	Bihar	12/2022 (12/2022)	06/2030 (06/2030)	3919 (3919)	457.23	23
369	City Gas Distribution [CGD] Project in Kondagaon, Bastar, Sukma, Narayanpur, Bijapur & Dantewada GA <i>(GAIL Gas)</i> (617819)	Chhattisgarh	06/2022 (06/2022)	06/2030 (06/2030)	557.04 (557.04)	8.33	2



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
370	Redevelopment of Sobhasan Complex (Oil and Natural Gas Corporation Limited [ONGC]) (400087)	Gujarat	08/2021 (08/2021)	02/2026 (02/2026)	885.63 (1286.67)	911.57	85
371	Redevelopment of Santhal Field [Onshore-Mehsana Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (400167)	Gujarat	02/2017 (02/2017)	03/2026 (03/2026)	1162.56 (1162.56)	1145.85	95
372	Redevelopment of Linch Field (Oil and Natural Gas Corporation Limited [ONGC]) (400169)	Gujarat	04/2021 (04/2021)	03/2025 (03/2026)	631.03 (860.04)	600.07	88
373	Petrochemical and Lube Integration Project at Gujarat Refinery (Ministry of Petroleum & Natural Gas) (701329)	Gujarat	09/2020 (09/2020)	08/2024 (06/2026)	18936 (17825)	13229.31	85
374	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery (Ministry of Petroleum Natural Gas) (709778)	Gujarat	01/2022 (01/2022)	08/2025 (09/2026)	328.29 (287)	183.45	72
375	Commercial Polymer Flooding Project in Bechradi field (Oil and Natural Gas Corporation Limited [ONGC]) (709838)	Gujarat	01/2022 (01/2022)	11/2024 (05/2027)	621.4 (739.02)	144.19	25
376	Restoration of Gas Terminal, Phase-I [Part-A], Hazira (Oil and Natural Gas Corporation Limited [ONGC]) (709840)	Gujarat	05/2022 (05/2022)	02/2025 (04/2026)	249.43 (249.43)	210.45	95
377	Old Pipe Line Replacement [OPRP] Group-A (Oil and Natural Gas Corporation Limited [ONGC]) (709841)	Gujarat	07/2021 (07/2021)	07/2025 (03/2026)	173.03 (169.84)	154.84	89
378	Kalol Redevelopment Project, Ahmedabad Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709842)	Gujarat	08/2022 (08/2022)	03/2027 (03/2027)	1487.41 (1487.41)	938.5	63
379	Revamping of SV Stations, Gas Terminal & Kribhco Terminal (Oil and Natural Gas Corporation Limited [ONGC]) (709845)	Gujarat	11/2022 (11/2022)	08/2026 (08/2026)	837.34 (837.34)	325.04	59
380	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad (Ministry of Petroleum & Natural Gas) (604853)	Haryana	06/2019 (06/2019)	12/2022 (10/2026)	2281.94 (3200)	1885.39	64
381	Poly Butadiene Rubber plant at Panipat (Indian Oil Corporation Limited [IOCL]) (611917)	Haryana	03/2022 (03/2022)	03/2025 (06/2026)	1459 (2531.44)	1435.65	79
382	Capacity Expansion of Panipat Refinery from 15 to 25 MTPA (Ministry of Petroleum & Natural Gas) (701289)	Haryana	02/2021 (02/2021)	09/2024 (06/2026)	34627 (36225)	27829.24	91
383	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. (Ministry of Petroleum Natural Gas) (709783)	Haryana	12/2020 (12/2020)	06/2023 (06/2026)	165.13 (247.69)	155.76	79
384	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts (Ministry of Petroleum Natural Gas) (709773)	Jammu and Kashmir	03/2022 (03/2022)	03/2032 (03/2032)	538 (538)	4.11	0
385	Development of Jharia CBM Block [Phase-1] (Oil and Natural Gas Corporation Limited [ONGC]) (610984)	Jharkhand	11/2019 (11/2019)	01/2024 (03/2026)	431 (431)	228.44	61
386	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] (Ministry of Petroleum Natural Gas) (709785)	Jharkhand	02/2023 (02/2023)	02/2026 (03/2027)	202.07 (202.07)	61.84	50
387	Power System Upgradation Project (Mangalore Refinery and Petrochemicals Limited) (612790)	Karnataka	10/2023 (10/2023)	11/2025 (05/2026)	385 (385)	178.36	74
388	Demo Bio-ATF Project (Ministry of Petroleum & Natural Gas) (616879)	Karnataka	03/2024 (03/2024)	01/2027 (01/2027)	364 (364)	49.39	26
389	Revamping/ Augmentation of facilities at existing port terminal at Mangalore (Ministry of Petroleum & Natural Gas) (709774)	Karnataka	01/2022 (01/2022)	12/2025 (06/2027)	463 (500.62)	301.09	76
390	Augmentation of CCKPL and IDPL Pipelines capacity along with setting up of Palakkad TOP (Ministry of Petroleum & Natural Gas) (617838)	Kerala	09/2024 (09/2024)	08/2028 (08/2028)	1130 (1130)	189.61	20
391	Replacement and Extension of Jetty Pipelines [REJP] at KR (Bharat Petroleum Corporation Limited [BPCL]) (709790)	Kerala	03/2023 (03/2023)	03/2026 (03/2026)	621.87 (372)	459.74	93
392	Setting up Polypropylene Unit at Kochi Refinery (Ministry of Petroleum Natural Gas) (709799)	Kerala	12/2023 (12/2023)	10/2027 (10/2027)	4460 (4460)	399.96	20
393	C2/C3 Vijaipur Pata Pipeline (Ministry of Petroleum & Natural Gas) (617830)	Madhya Pradesh	05/2024 (05/2024)	01/2027 (01/2027)	1792 (1792)	390.2	46
394	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery (Ministry of Petroleum Natural Gas) (709798)	Madhya Pradesh	05/2023 (05/2023)	05/2028 (05/2028)	43367 (43367)	2592.6	18
395	500 KTA PDHPP Project, Usar (Ministry of Petroleum & Natural Gas) (400168)	Maharashtra	04/2021 (04/2021)	04/2025 (06/2026)	8797 (11256)	7371.46	88
396	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery (Ministry of Petroleum and Natural Gas) (616933)	Maharashtra	12/2024 (12/2024)	03/2028 (03/2028)	4679 (4679)	222.44	7
397	HP TDAE Unit in Mumbai Refinery (Hindustan Petroleum Corporation Limited) (709760)	Maharashtra	06/2024 (06/2024)	04/2026 (04/2026)	240 (240)	77.58	70
398	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts (Ministry of Petroleum Natural Gas) (709771)	Maharashtra	03/2022 (03/2022)	09/2031 (09/2031)	865 (865)	74.35	3



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
399	Construction of Additional Tankages and Allied Facilities at JNPT Terminal (Ministry of Petroleum & Natural Gas) (709780)	Maharashtra	04/2022 (04/2022)	08/2026 (08/2026)	341.43 (436.14)	293.12	55
400	ATF Pipeline from Jawaharlal Nehru Port Trust to Navi Mumbai International Airport (Indian Oil Corporation Limited [IOCL]) (709782)	Maharashtra	08/2022 (08/2022)	08/2025 (03/2026)	165 (165)	96.61	83
401	Installation of Independent De-Aromatized Solvents [DAS] production facilities at MR (Bharat Petroleum Corporation Limited [BPCL]) (709789)	Maharashtra	03/2023 (03/2023)	07/2025 (02/2026)	405 (343)	244.2	97
402	POL & LOBS Installations with Receipt Pipelines at Rasayani (Bharat Petroleum Corporation Limited [BPCL]) (709797)	Maharashtra	05/2023 (05/2023)	05/2026 (05/2026)	2585 (2585)	936.03	80
403	Part Replacement Pipeline Project [PRPP] (Oil and Natural Gas Corporation Limited [ONGC]) (709846)	Maharashtra	11/2022 (11/2022)	05/2024 (01/2026)	1219.48 (1145.1)	745	90
404	Visakh Raipur Pipeline Project (Ministry of Petroleum & Natural Gas) (616254)	Multi-States (Andhra Pradesh, Chhattisgarh, Odisha)	09/2024 (09/2024)	09/2027 (09/2027)	2212 (2212)	127.64	21
405	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura, West Bengal)	04/2020 (04/2020)	03/2024 (03/2026)	9265 (9265)	6622	86
406	Pipeline Rehabilitation Project, Phase-II (Ministry of Petroleum & Natural Gas) (617827)	Multi-States (Assam, Bihar, West Bengal)	12/2024 (12/2024)	12/2029 (12/2029)	680 (680)	2.32	17
407	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Multi-States (Assam, West Bengal)	06/2021 (06/2021)	12/2024 (03/2026)	860 (860)	636.92	99
408	CGD Project in Banka, Dumka, Godda, Jamtara, Pakur, Sahibganj GA ID 11A.02 (Hindustan Petroleum Corporation Limited) (709757)	Multi-States (Bihar, Jharkhand)	06/2022 (06/2022)	06/2030 (06/2030)	1377 (1377)	350.62	32
409	Mumbai Nagpur Jharsuguda Pipeline Project (Ministry of Petroleum & Natural Gas) (701354)	Multi-States (Chhattisgarh, Madhya Pradesh, Maharashtra, Odisha)	06/2020 (06/2020)	05/2023 (02/2026)	7844.25 (8255)	6857.3	97
410	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (Ministry of Petroleum & Natural Gas) (701330)	Multi-States (Gujarat, Haryana, Punjab, Rajasthan)	07/2011 (07/2011)	06/2024 (03/2026)	7392 (7392)	6336.9	90
411	Gurdaspur Jammu Pipeline (Gas Authority of India Limited [GAIL]) (612853)	Multi-States (Jammu and Kashmir, Punjab)	07/2023 (07/2023)	07/2026 (07/2026)	521.9 (521.9)	249.7	43
412	Kochi - Kootanad - Bangalore - Mangalore Pipeline Phase-II (Ministry of Petroleum & Natural Gas) (701228)	Multi-States (Karnataka, Kerala, Tamil Nadu)	06/2009 (06/2009)	12/2012 (03/2026)	2915 (5909)	4548.29	95
413	City Gas Distribution Maharashtra Natural Gas Limited (Ministry of Petroleum & Natural Gas) (701338)	Multi-States (Karnataka, Maharashtra)	01/2006 (01/2006)	06/2031 (06/2031)	5535 (5535)	4037.28	0
414	Dhamra Haldia Pipeline Project (Ministry of Petroleum & Natural Gas) (701344)	Multi-States (Odisha, West Bengal)	03/2020 (03/2020)	11/2022 (03/2026)	1030.65 (1125)	885.2	91
415	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (Bharat Petroleum Corporation Limited [BPCL]) (709794)	Multi-States (Punjab, Rajasthan)	12/2022 (12/2022)	06/2030 (06/2030)	3207 (3207)	377.38	27
416	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum & Natural Gas) (709786)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 (227.62)	15.85	28
417	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (Ministry of Petroleum & Natural Gas) (604859)	Odisha	07/2020 (07/2020)	01/2024 (08/2026)	13805 (11783)	8613.21	92
418	City Gas Distribution [CGD] Project in Gajapati, Kandhamal, Boudh, & Sonepur GA (GAIL Gas) (617818)	Odisha	02/2022 (02/2022)	02/2030 (02/2030)	514.91 (514.91)	19.92	4
419	CUF POL Depot at Sadashibpur [Meramundali], Odisha (Ministry of Petroleum & Natural Gas) (709800)	Odisha	04/2021 (04/2021)	03/2026 (03/2026)	393.54 (393.54)	153.37	54
420	Life Extension of 48 well platforms of Mumbai High & Heera Fields (Oil and Natural Gas Corporation Limited [ONGC]) (400119)	Offshore	12/2015 (12/2015)	04/2018 (03/2026)	3190.69 (3375.9)	3123.2	90
421	PRP-VIII [Group-A] (Ministry of Petroleum & Natural Gas) (616950)	Offshore	09/2024 (09/2024)	02/2026 (05/2026)	1486.4 (1486.4)	394.85	30
422	Daman Upside Development Project (Oil and Natural Gas Corporation Limited [ONGC]) (709839)	Offshore	06/2022 (06/2022)	10/2025 (02/2026)	4144.41 (6406.9)	4833.7	93
423	MHN TCPP PGC BGC Project [MTPBP] (Ministry of Petroleum & Natural Gas) (709848)	Offshore	06/2022 (06/2022)	05/2026 (05/2026)	2329.45 (2354.23)	1148.9	66
424	PRP-VIII Group B [NH & BS Asset] (Ministry of Petroleum & Natural Gas) (709849)	Offshore	06/2024 (06/2024)	02/2026 (05/2026)	2379.84 (3165.53)	2115.21	77
425	Integrated Development of 4 Contract Areas under DSF-II (Ministry of Petroleum & Natural Gas) (709851)	Offshore	05/2023 (05/2023)	04/2027 (04/2027)	6183.79 (6183.79)	895.56	28



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
426	2G Ethanol Biorefinery at Bathinda <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (400171)	Punjab	05/2020 (05/2020)	02/2023 (03/2026)	1421.46 (1421.46)	1218.24	95
427	City Gas Distribution Project at Pathankot District <i>(Ministry of Petroleum Natural Gas)</i> (709770)	Punjab	03/2022 (03/2022)	09/2033 (09/2033)	151 (151)	8.81	2
428	CBR 9 MMTA Project <i>(Chennai Petroleum Corporation Limited [CPCL])</i> (604795)	Tamil Nadu	09/2021 (09/2021)	06/2025 (10/2028)	31580 (36354)	1404.61	10
429	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore <i>(Chennai Petroleum Corporation Limited [CPCL])</i> (709750)	Tamil Nadu	01/2024 (01/2024)	09/2025 (12/2026)	205 (205)	76.2	53
430	City Gas Distribution Projects at the Nilgiris and Erode districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709796)	Tamil Nadu	12/2022 (12/2022)	03/2030 (03/2030)	3685 (3685)	261.81	22
431	ATF Pipeline from BPCLs Malkapur POL Installation to Hyderabad International airport <i>(Ministry of Petroleum Natural Gas)</i> (617822)	Telangana	03/2025 (03/2025)	09/2027 (-)	215 (215)	38.16	17
432	Creation of Gas Dehydration Facilities, Tripura Asset <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709837)	Tripura	03/2022 (03/2022)	05/2024 (05/2026)	209.33 (131.51)	71.95	66
433	PP Project, Pata <i>(Gas Authority of India Limited [GAIL])</i> (400161)	Uttar Pradesh	03/2019 (03/2019)	01/2024 (12/2026)	910.56 (1299.02)	1066	99
434	Revamping / Augmentation of Facilities at Mathura Bitumen Plant <i>(Ministry of Petroleum Natural Gas)</i> (709781)	Uttar Pradesh	04/2022 (04/2022)	06/2027 (12/2026)	260.12 (260.12)	10.51	36
435	City Gas Distribution Projects at Lakhimpur Kheri, Sitapur, Bahraich, Shravasti, Balrampur, Siddharth Nagar & Maharajanagar districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709795)	Uttar Pradesh	12/2022 (12/2022)	06/2030 (06/2030)	16654 (16654)	642.18	13
436	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] <i>(Ministry of Petroleum & Natural Gas)</i> (617302)	West Bengal	03/2017 (03/2017)	12/2020 (03/2026)	1740 (2493.15)	2314.2	93
437	Siliguri-Jhapa Pipeline Project <i>(Indian Oil Corporation Limited [IOCL])</i> (617828)	West Bengal	09/2024 (09/2024)	03/2029 (03/2029)	267 (267)	1.37	8
438	Siliguri Marketing Terminal [SMT] Capacity Augmentation Project <i>(Ministry of Petroleum & Natural Gas)</i> (617837)	West Bengal	11/2021 (11/2021)	12/2025 (09/2026)	484 (484)	293.69	82
439	Haldia Panagarh Pipeline Project <i>(Hindustan Petroleum Corporation Limited)</i> (709753)	West Bengal	11/2022 (11/2022)	11/2025 (05/2026)	1010 (1107)	718.12	89
440	CGD Project in Malda, Birbhum, Murshidabad, Dakshin Dinajpur GA ID 11A.03 <i>(Hindustan Petroleum Corporation Limited)</i> (709758)	West Bengal	06/2022 (06/2022)	06/2030 (06/2030)	2628 (2628)	355.85	31
441	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts <i>(Ministry of Petroleum Natural Gas)</i> (709772)	West Bengal	03/2022 (03/2022)	06/2031 (06/2031)	609 (609)	59.3	2
442	City Gas Distribution Projects at Alipurduar and Cooch Behar <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709791)	West Bengal	12/2022 (12/2022)	03/2030 (03/2030)	1017 (1017)	211.59	40
Total (93)					353462.93	191900.78	
Ministry of Health & Family Welfare							
Healthcare							
443	AIIMS Darbhanga <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701172)	Bihar	NA (09/2020)	09/2024 (-)	1264 (1264)	0	0
444	Setting up IT Infrastructure including Network Security and Hosting at AIIMS, New Delhi <i>(PMSSY AND Institute of NATIONAL Importance)</i> (617882)	Delhi	09/2025 (09/2025)	09/2026 (-)	358.19 (358.19)	0	0
445	Redevelopment of Residential colonies at Ayur Vigyan Nagar and West Ansari Nagar campuses of AIIMS, New Delhi <i>(PMSSY AND Institute of NATIONAL Importance)</i> (617883)	Delhi	10/2016 (06/2022)	06/2027 (-)	4441 (4441)	24.68	61
446	AIIMS Rajkot <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701170)	Gujarat	01/2019 (01/2019)	03/2026 (03/2026)	1195 (1195)	774.6	93
447	AIIMS Majra Rewari Haryana <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701173)	Haryana	02/2019 (02/2019)	12/2026 (12/2026)	1299 (1646.43)	479.98	45
448	AIIMS Kashmir at Awantipora Jammu & Kashmir <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701167)	Jammu and Kashmir	01/2019 (03/2019)	12/2025 (06/2026)	1828 (2160.84)	1491.97	72
449	ALL India Institute of Medical Sciences-AIIMS Madurai <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701168)	Tamil Nadu	12/2018 (12/2018)	08/2022 (10/2026)	1264 (2021.51)	366.59	43
450	AIIMS Bibinagar <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701171)	Telangana	12/2018 (07/2022)	06/2026 (06/2026)	1028 (1365.95)	939.72	86
Total (8)					12677.19	4077.54	
Ministry of Labour and Employment							
Healthcare							
451	Construction of 350 beds + 50 Super Specialty beds ESIC Hospital Sheelanagar, Visakhapatnam, Andhra Pradesh <i>(Employee's State Insurance Company [ESIC])</i> (612167)	Andhra Pradesh	02/2021 (04/2023)	10/2025 (03/2026)	384.27 (384.27)	167.37	70



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
452	Construction of 200 bedded ESIC Hospital with 62 Nos Staff quarters , Beltola (Employee's State Insurance Company [ESIC]) (612201)	Assam	12/2017 (10/2021)	04/2025 (02/2026)	143.23 (154.75)	116.08	96
453	C/o Construction of 200 bedded [Up-gradable to 300 bedded] ESI Hospital at Surat Gujarat. (Employee's State Insurance Company [ESIC]) (612185)	Gujarat	06/2019 (03/2021)	06/2025 (01/2026)	209.36 (209.36)	202.62	99
454	350 Bedded [Upgradable to 500 beds] ESI Hospital at Sanand (Employee's State Insurance Company [ESIC]) (612186)	Gujarat	06/2022 (04/2023)	03/2026 (05/2027)	558.12 (558.12)	63.62	15
455	Demolition, Construction and upgradation of ESI Hospital, Kalol, Gujarat from 50 beds to 150 beds. (Employee's State Insurance Company [ESIC]) (612211)	Gujarat	08/2022 (10/2023)	10/2025 (06/2026)	205.87 (205.87)	24.06	20
456	Construction of 200 bed ESI Hospital at Bommasandra, Karnataka (Employee's State Insurance Company [ESIC]) (612745)	Karnataka	02/2015 (10/2024)	01/2027 (05/2027)	278 (278)	228.61	19
457	Construction of 100 bed ESI Hospital and Staff Quarters [32 Nos.] at Harohalli, Karnataka (Employee's State Insurance Company [ESIC]) (612748)	Karnataka	07/2019 (03/2025)	02/2027 (-)	150.92 (150.92)	6.76	10
458	Construction of 200 Bedded [Upgradable to 500 Bedded including 50 beds of SST] ESIC Hospital at Bibewadi, Pune (Employee's State Insurance Company [ESIC]) (612188)	Maharashtra	05/2018 (03/2023)	09/2025 (02/2026)	429.25 (429.25)	282.09	70
459	Construction of 200 Bedded ESIC Hospital at Butibori, Nagpur, Maharashtra. (Employee's State Insurance Company [ESIC]) (612213)	Maharashtra	10/2013 (08/2022)	08/2025 (09/2026)	194.93 (196.7)	114.39	62
460	Upgradation & Extension of ESIC Hospital and Construction of PG Hostel / Staff Housing for ESIC Hospital at Andheri, Mumbai (Employee's State Insurance Company [ESIC]) (616691)	Maharashtra	12/2008 (06/2009)	08/2025 (09/2026)	260.13 (260.13)	210.12	89
461	Construction of 100 Bedded ESI Hospital at Duburi, Odisha. (Employee's State Insurance Company [ESIC]) (612513)	Odisha	12/2010 (02/2025)	06/2027 (-)	164.6 (164.6)	16.4	7
462	Construction of 100 Bedded ESIC Hospital building and 32 Nos Residential Quarters at Vallam Vadangal, SIPCOT, Sriperumbudur (Employee's State Insurance Company [ESIC]) (612178)	Tamil Nadu	02/2015 (03/2023)	06/2025 (01/2026)	152.95 (177.01)	107.83	99
463	CONSTRUCTION OF 300 BEDDED HOSPITAL AT HARIDWAR (Employee's State Insurance Company [ESIC]) (612259)	Uttarakhand	02/2021 (12/2021)	10/2024 (03/2026)	102.4 (297.63)	322.55	81
Total (13)					3234.03	1862.5	
Ministry of Ports, Shipping and Waterways							
Healthcare							
464	Establishment of 600 bed super specialty hospital with optional development of Medical college and further expansion on PPP basis. (Mumbai Port Trust [MPT]) (708662)	Maharashtra	08/2019 (01/2022)	06/2026 (12/2027)	693 (693)	58	11
Total (1)					693	58	
Inland Waterways							
465	Jal Marg Vikas Project (Inland Waterways Authority of India [IWAI]) (701565)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	01/2018 (02/2018)	12/2023 (12/2025)	5369.18 (5061.15)	3717.08	75
466	Fairway Development in West Bengal Farakka - Kahelgaon (Inland Waterways Authority of India [IWAI]) (611142)	Offshore	01/2018 (08/2018)	07/2023 (04/2024)	177 (197)	383.41	100
Total (2)					5546.18	4100.49	
Shipping							
467	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust) (609424)	Gujarat	10/2022 (03/2024)	03/2027 (-)	4243.64 (4243.64)	963.03	37
468	Construction of oil jetty No.8 at old kandla through internal resources (Deendayal Port Trust [DPT]) (701568)	Gujarat	02/2018 (02/2021)	02/2023 (07/2024)	100 (225.85)	186.47	90
469	Replacement and revamping of pipeline projects in oil jetty area, Kandla (Deendayal Port Trust [DPT]) (701570)	Gujarat	09/2021 (09/2021)	09/2023 (03/2025)	171 (211.61)	137.51	71
470	Mechanization of Berth No.14 for handling Containers and other cargo on DBFOT basis - Phase II (New Mangalore Port Authority) (617804)	Karnataka	12/2023 (06/2024)	03/2027 (-)	153.23 (153.23)	24	33
471	Rewas Port Project (Reliance Industries Ltd) (400382)	Maharashtra	12/2019 (01/2020)	03/2023 (-)	6000 (6000)	5999.89	88
472	Setting up of a Floating Storage and Regasification Unit [FSRU] - Mumbai (Mumbai Port Trust [MPT]) (701586)	Maharashtra	11/2020 (04/2021)	11/2026 (11/2026)	900 (900)	65	0
473	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574)	Odisha	05/2022 (01/2023)	12/2027 (10/2028)	3004.63 (3004.63)	1277.52	50
474	Berth No. 2 [previously Berth 3] of HDC Mechanization Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701576)	West Bengal	11/2022 (03/2023)	09/2025 (01/2026)	298.26 (298.26)	468.23	99
475	Shalukkhali Liquid Cargo Handling Facility Development Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701577)	West Bengal	01/2022 (08/2022)	08/2025 (-)	253.65 (253.65)	9.28	0
Total (9)					15124.41	9130.93	



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Tourism, Hospitality & Wellness							
476	National Maritime Heritage Complex [NMHC] Phase-I (<i>Indian Port Rail & Ropeway Corporation Ltd. [IPRCL]</i>) (707215)	Gujarat	02/2019 (01/2022)	03/2024 (03/2026)	573 (1238.05)	545.51	73
Total (1)					573	545.51	
Ministry of Steel							
Metals & Mining							
477	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul (<i>National Mineral Development Corporation Limited [NMDC]</i>) (615202)	Chhattisgarh	08/2021 (07/2022)	12/2028 (03/2028)	1700 (1756.2)	155.07	10
Total (1)					1700	155.07	
Steel							
478	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617243)	Chhattisgarh	07/2024 (08/2024)	07/2026 (-)	198.62 (198.62)	34.96	35
479	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617255)	Chhattisgarh	10/2023 (12/2023)	06/2026 (-)	471.83 (471.83)	193.97	55
480	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617256)	Chhattisgarh	11/2023 (01/2024)	10/2025 (03/2026)	884.1 (884.1)	551.1	83
481	NMDC Slurry Pipeline Project Phase-1 (<i>National Mineral Development Corporation Limited [NMDC]</i>) (706811)	Chhattisgarh	11/2015 (09/2020)	06/2023 (03/2026)	2907 (5427)	3336.05	90
482	SCREENING PLANT-III AT KIRANDUL (<i>National Mineral Development Corporation Limited [NMDC]</i>) (709826)	Chhattisgarh	NA (10/2021)	01/2026 (-)	2718.84 (2718.84)	1409.87	79
483	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (<i>National Mineral Development Corporation Limited [NMDC]</i>) (709827)	Chhattisgarh	NA (10/2022)	12/2025 (-)	349.75 (349.75)	304.58	96
484	New Sinter Plant at BSL, SAIL (<i>Steel Authority of India Limited [SAIL]</i>) (400174)	Jharkhand	03/2015 (10/2015)	10/2017 (06/2027)	1034.01 (1752.3)	928.97	53
485	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617249)	Jharkhand	01/2025 (02/2025)	01/2027 (-)	211.94 (211.94)	21.95	16
486	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617250)	Jharkhand	01/2025 (02/2025)	10/2026 (-)	207.13 (207.13)	21.54	12
487	Revamping of old sub-systems of Blast Furnace 3 at Bokaro Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617253)	Jharkhand	08/2023 (03/2023)	07/2025 (11/2025)	513.82 (513.82)	338.22	76
488	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617254)	Jharkhand	03/2024 (04/2024)	06/2026 (-)	260.37 (260.37)	58.19	27
489	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617257)	Jharkhand	11/2023 (12/2023)	11/2026 (-)	627.31 (627.31)	190.32	49
490	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. (<i>National Mineral Development Corporation Limited [NMDC]</i>) (400121)	Karnataka	11/2014 (06/2024)	08/2026 (-)	1043.63 (1043.63)	375.39	45
491	Rebuilding of COB 4 at Durgapur Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (612781)	West Bengal	09/2023 (09/2023)	12/2026 (-)	916.78 (916.78)	156.82	26
492	Installation of New Bar Mill at Durgapur Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617242)	West Bengal	07/2024 (08/2024)	06/2027 (-)	2115.44 (2115.44)	276.1	41
493	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617246)	West Bengal	09/2024 (08/2024)	06/2026 (-)	758.09 (758.09)	129.95	10
494	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617248)	West Bengal	11/2024 (12/2024)	07/2026 (-)	227.96 (227.96)	45.76	39
495	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617251)	West Bengal	07/2024 (12/2024)	05/2026 (-)	196.4 (196.4)	14.55	8
496	Stamp Charge Battery No.12 Battery Proper at IISCO Steel Plant (<i>Steel Authority of India Limited [SAIL]</i>) (617338)	West Bengal	01/2025 (02/2025)	07/2028 (-)	2518.39 (2518.39)	229.27	10
Total (19)					18161.41	8617.56	
Ministry of Railways							
Railways							
497	Nadikudi - Srikalahasti New Line (<i>South Central Railway [SCR] - II</i>) (400298)	Andhra Pradesh	03/2012 (12/2016)	05/2027 (03/2028)	2312 (5932)	2421.35	54
498	GOOTY-PENDEKALLU DOUBLING 29.225 Km (<i>South Central Railway [SCR] - II</i>) (611752)	Andhra Pradesh	03/2023 (06/2023)	03/2027 (03/2027)	351.83 (351.83)	18	25
499	GUNTAKAL WEST-MALLAPPA GATE RAIL OVER RAIL - ROR TRACK (<i>South Central Railway [SCR] - II</i>) (611754)	Andhra Pradesh	07/2023 (07/2023)	07/2026 (-)	293.3 (293.3)	0	0
500	Kurnool - Setting up facilities for coach midlife rehabilitation workshop (<i>WPO/Patna</i>) (611927)	Andhra Pradesh	01/2014 (10/2017)	12/2023 (-)	560.72 (560.72)	276.66	65



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
501	Flyover between Pendurthi and Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB 73 of 2023 24 NR (East Coast Railway [ECOR] - II) (612827)	Andhra Pradesh	04/2023 (05/2024)	04/2027 (-)	183.65 (183.65)	9.51	11
502	3rd & 4th line between Vadlapudi -Gate Jn. cabin and Tie line between Gate Junction to Gangavaram port (East Coast Railway [ECOR] - II) (616697)	Andhra Pradesh	04/2023 (03/2024)	06/2026 (-)	154.28 (154.28)	27.07	38
503	Tiupati Katpadi 104.39 kms (South Central Railway [SCR] - II) (617210)	Andhra Pradesh	04/2025 (04/2025)	03/2029 (-)	1215.56 (1215.56)	0.12	0
504	3rd Line between Gudur Renigunta 83.17 Km (South Central Railway [SCR] - II) (617216)	Andhra Pradesh	10/2024 (10/2024)	03/2027 (-)	877.34 (877.34)	45.13	0
505	Kurnool Coach Midlife Rehabilitation Project (WPO/Patna) (705253)	Andhra Pradesh	05/2016 (07/2014)	12/2020 (-)	563 (563)	120	0
506	Kotapalli - Narasapur New Line (South Central Railway [SCR] - II) (705436)	Andhra Pradesh	03/2009 (09/2013)	03/2028 (03/2028)	2501 (2501)	1349.09	29
507	Guntur-Guntakal Doubling Project (South Central Railway [SCR] - II) (705633)	Andhra Pradesh	03/2017 (11/2017)	12/2025 (12/2026)	3733 (4295)	4753.38	93
508	Vijaywada-Gudur 3rd Line (RVNL - II) (705648)	Andhra Pradesh	08/2016 (04/2018)	11/2024 (03/2026)	6654 (6654)	6087.52	94
509	Penukonda - Dharmavaram Doubling Project [41.5 Km] (South Western Railway [SWR] - II) (705789)	Andhra Pradesh	06/2018 (12/2018)	03/2026 (03/2026)	307.66 (307.66)	294.61	87
510	Furkating-New Tinsukia[194 Km] (Northeast Frontier Railway [NFR]) (618986)	Assam	09/2025 (09/2025)	06/2029 (-)	3633.58 (3633.58)	0	0
511	Doubling of New Bonggaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3739.15	93
512	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
513	Mariani-Jorhat, Tinsukia-Dangri and Makum - TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
514	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
515	Sakri -Hasanpur [via Harnagar - Kusheshwar Asthan] New Railway line (East Central Railway [ECR] - I) (400254)	Bihar	12/2023 (08/1997)	12/2024 (03/2027)	735.2 (735.2)	588.68	84
516	Construction of Bulb line at Nabinagar Ankorah of East Central Railway (East Central Railway [ECR] - I) (617231)	Bihar	06/2024 (06/2024)	06/2028 (-)	611.74 (611.74)	0	0
517	Khagaria-Kusheshwar Asthan [42Km] new line project (East Central Railway [ECR] - I) (705364)	Bihar	04/2019 (12/1998)	12/2024 (03/2027)	614 (1384.16)	490.08	55
518	Hajipur-Sagauli New line (East Central Railway [ECR] - I) (705366)	Bihar	10/2007 (10/2004)	03/2020 (12/2026)	2067 (2087)	2015.07	74
519	Araria Supaul New BG Line (East Central Railway [ECR] - I) (705368)	Bihar	06/2018 (03/2009)	03/2024 (01/2027)	1605 (2514)	1611.07	42
520	Fatua-Islampur incl. MM for extn.of NL from Neora to Daniawan , Daniawan to Biharsharif, Biharsharif to Barbiga , Barbiga to Shekhpura (East Central Railway [ECR] - I) (705373)	Bihar	08/2002 (03/2002)	03/2023 (08/2025)	1473 (2882)	2540.71	95
521	Jogbani-Biratnagar New Rail Line project (Indian Railway Construction International Limited [IRCON]) (705450)	Bihar	06/2010 (01/2011)	03/2022 (12/2026)	402 (486)	368.42	86
522	Samastipur-Darbhanga Doubling Railway Project (East Central Railway [ECR] - I) (705526)	Bihar	11/2015 (12/2015)	03/2025 (10/2025)	519 (519)	53629.73	92
523	Sagauli-Valmiknagar (East Central Railway [ECR] - I) (705527)	Bihar	03/2018 (03/2017)	12/2025 (12/2025)	1216 (2222)	2083.03	92
524	Muzaffarpur-Sugauli (East Central Railway [ECR] - I) (705528)	Bihar	03/2018 (03/2017)	06/2024 (02/2026)	1586 (1586)	1476.13	99
525	Rampur Dumra-Tal-Rajendrapur Additional Bridge and Railway Line Doubling (Indian Railway Construction International Limited [IRCON]) (706759)	Bihar	03/2016 (05/2017)	12/2024 (12/2025)	2373.64 (1700.24)	1450.99	98
526	Barauni-Bachwara [16 km] - 3rd & 4th line incl. Barauni yard remodelling [32 km] (East Central Railway [ECR] - I) (706860)	Bihar	10/2022 (08/2025)	08/2025 (10/2026)	645 (645)	34.45	55
527	JHAJHA - BATIA (East Central Railway [ECR] - I) (900874)	Bihar	03/2023 (03/2023)	03/2028 (01/2030)	588.18 (588.18)	1.19	0
528	Kharsia-Dharamjaygarh with Spur line [East Corridor-Phase 1] (Indian Railway Construction International Limited [IRCON]) (400220)	Chhattisgarh	03/2016 (01/2014)	09/2018 (03/2026)	3055 (3407.09)	2609.75	94
529	Doubling of Kirandul-Jagdalpur Line [150 km] (East Coast Railway [ECOR] - II) (400291)	Chhattisgarh	02/2013 (03/2013)	03/2020 (12/2025)	1589 (1798)	1592.19	95
530	Gauge Conversion of Kendri-Dhamtari including Abhanpur - Rajim Branch line 67.20 Kms - 2nd Material Modification to Raipur Titlagarh doubling. (SECR) (602792)	Chhattisgarh	07/2011 (05/2021)	02/2025 (03/2026)	1171 (1171)	379.64	100



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
531	4th line between Nipania Bhatapara 14.4 Km (South East Central Railway [SECR] - II) (612815)	Chhattisgarh	12/2022 (05/2024)	03/2027 (-)	170.49 (170.49)	2.11	6
532	Dharamjaigarh-Korba 63 km (CERL) (613003)	Chhattisgarh	08/2023 (07/2022)	08/2026 (-)	1686.26 (1686.26)	288.83	18.5
533	KHARSIA- NAYA RAIPUR-PARMALKASA 5th and 6th Line [278KM] (CAO/C/SECR) (617200)	Chhattisgarh	04/2025 (04/2025)	03/2031 (-)	7853.84 (7853.84)	0	0
534	Dallirajhara - Rowghat New Rail Line Project, Phase-I (Rail Vikas Nigam Limited) (617374)	Chhattisgarh	NA (11/2009)	03/2025 (02/2026)	1516.45 (1881.26)	2063.12	95
535	Dallirajhara- Rowghat New Railway Line - Phase I [95 km] (Rail Vikas Nigam Limited) (705433)	Chhattisgarh	07/2009 (12/2009)	09/2025 (12/2025)	1628 (1628)	1440.85	82
536	Gevra Road-Pendra Road New Railway Line [135 km] (Indian Railway Construction International Limited [IRCON]) (705444)	Chhattisgarh	04/2014 (04/2014)	03/2022 (12/2025)	4970 (7448.52)	4797.72	76
537	Boridand - Ambikapur Doubling Line Project (South East Central Railway [SECR] - II) (706854)	Chhattisgarh	06/2022 (04/2022)	06/2030 (06/2030)	1376 (1576.72)	155.09	22
538	4TH LINE - BHATAPARA-HATHBAND [8.8 KM] [PB-72/NR/2022-23] (SECR) (709815)	Chhattisgarh	09/2022 (05/2024)	01/2027 (12/2027)	177.03 (177.03)	0	4
539	4TH LINE - BHILAI-BHILAI NAGAR [8.8 KM] [PB-72/NR/2022-23] (SECR) (709816)	Chhattisgarh	09/2022 (05/2024)	02/2027 (02/2027)	177.34 (177.34)	1.66	6
540	4TH LINE - DADHAPARA-BELHA [9.2 KM] [PB-72/NR/2022-23] (SECR) (709817)	Chhattisgarh	09/2022 (05/2024)	11/2026 (11/2026)	169.06 (169.06)	20.17	62
541	4TH LINE RAJNANDGAON-DONGARHGARH [31.2 KM] [PB-72/NR/2022-23] (SECR) (709818)	Chhattisgarh	09/2022 (05/2024)	01/2027 (01/2027)	328.34 (328.34)	61.96	28
542	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (709819)	Chhattisgarh	09/2022 (05/2025)	12/2026 (12/2026)	167.64 (167.64)	0.11	5
543	Redevelopment of New Delhi Railway Station and construction of associated infrastructure (Rail Land Development Authority) (613785)	Delhi	01/2023 (06/2024)	12/2028 (-)	4744 (4744)	151.37	2
544	Development of New Bijwasan Railway Terminal (Northern Railways) (617379)	Delhi	02/2008 (03/2013)	03/2020 (12/2026)	446.21 (446.21)	521.74	80
545	Anand Vihar-Tilak Bridge 3rd & 4th line (CAO/C/NR) (705583)	Delhi	03/2013 (03/2013)	03/2023 (12/2027)	667 (667)	289.26	63
546	Kosamba Umarpada 70 Km (PCE/WR) (611918)	Gujarat	07/2023 (07/2022)	03/2027 (-)	468 (468)	20.28	8
547	New Broad Gauge line between Naliya to Jakhau Port (Western Railway (WR) - II) (611943)	Gujarat	02/2023 (02/2023)	01/2028 (01/2028)	410.26 (410.26)	9.27	5
548	Quadrupling between Gandhidham Adipur with Y connection at Adipur for providing direct entry towards Mundra Port and Bhuj and high level platform at Gopalpur 11Kms (Western Railway (WR) - II) (611944)	Gujarat	02/2023 (02/2023)	03/2026 (01/2026)	152.44 (152.44)	104.58	85
549	Petlad Bhadran 23 Kms (Western Railway) (611945)	Gujarat	05/2022 (05/2022)	05/2030 (05/2030)	307.11 (307.11)	13.59	17
550	Samlaya Timba Road 54 km (PCE/WR) (611970)	Gujarat	02/2023 (02/2023)	03/2030 (03/2030)	670.17 (670.17)	45.21	12
551	Samni Jambusar 24 km (PCE/WR) (611971)	Gujarat	05/2022 (05/2022)	03/2030 (03/2030)	350 (349.93)	67.73	31
552	Western Railway Samakhiali Gandhidham Quadrupiling 53 Kms (Western Railway (WR) - II) (611974)	Gujarat	08/2023 (08/2023)	12/2026 (06/2027)	1430 (1430)	271.82	25
553	Dahod Creation of Infrastructure facilities for 9000 HP Electric locomotives Manufacturing at (PCE/WR) (611977)	Gujarat	05/2022 (02/2023)	02/2025 (-)	487 (487)	222.88	53
554	Dahod Rolling Stock Workshop Provision of Infrastructure for CBS at (PCE/WR) (611978)	Gujarat	11/2022 (03/2023)	03/2025 (-)	158 (158)	51.87	10
555	Sabarmati Setting up of Maintenance Facilities for Train Sets Phase ii (Western Railway (WR) - II) (611979)	Gujarat	01/2023 (04/2023)	06/2025 (03/2026)	250 (250)	110.15	70
556	4th LINE BETWEEN BAREJADI NANDEJ-SANAND-AHMEDABAD BYPASS (Western Railway WR - II) (612072)	Gujarat	02/2023 (02/2023)	03/2027 (07/2028)	961.67 (961.67)	359.61	18
557	Redevelopment of Ahmedabad railway station and associated infrastructure on engineering, procurement and construction mode (Rail Land Development Authority) (613786)	Gujarat	01/2023 (11/2023)	03/2028 (-)	2379 (2379)	790.14	23
558	Devbhumi Dwarka [Okha] - Kanalus Doubling (Western Railway (WR) - II) (618972)	Gujarat	12/2025 (12/2025)	12/2028 (-)	1456.77 (1456.77)	0	0
559	Miyagam-Karjan-Dabhoi-Samlaya [GC] (Western Railway [WR] - II) (705458)	Gujarat	01/2017 (01/2017)	03/2021 (12/2026)	483.88 (1039.13)	621.62	41
560	Modasa-Shamlaji Road Railway Line Project (Western Railway WR - II) (706757)	Gujarat	09/2012 (04/2008)	03/2025 (03/2026)	262 (262)	341.47	63



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
561	Rajkot - Kanalus Doubling Project [111.2 Kms] (Western Railway WR - II) (706763)	Gujarat	10/2021 (12/2021)	10/2026 (10/2026)	1080.58 (1080.58)	829.85	78
562	NADIAD-PETLAD [37.26 KM] (Railway) (709812)	Gujarat	05/2022 (10/2023)	06/2030 (06/2030)	461.91 (461.91)	178.31	8
563	NEW BG LINE INTERSECTION [5 NOS] BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD [16.51 KM] (Western Railway (WR) - II) (709813)	Gujarat	10/2022 (07/2025)	06/2028 (10/2027)	437.21 (437.21)	95.09	19
564	Bhiwani - Dobh Bahali Doubling Project [42.30 Km] (North Western Railway [NWR]) (611884)	Haryana	02/2023 (02/2023)	02/2028 (02/2028)	471 (471)	227.35	66
565	Doubling between Pradhankunta-Patherih-Bhjudih of East Central Railway (East Central Railway [ECR] - I) (617372)	Jharkhand	11/2022 (11/2022)	12/2025 (-)	349.22 (349.22)	115.09	70
566	Koderma-Arigada Doubling 133.38 Km of East Central Railway (East Central Railway [ECR] - I) (617832)	Jharkhand	06/2025 (06/2025)	12/2029 (-)	2887.11 (2887.11)	0	0
567	Gomoh - Flyover for DN trains (East Central Railway [ECR] - I) (705765)	Jharkhand	01/2018 (01/2018)	03/2026 (03/2026)	686 (686)	600.25	65
568	Lodhma - Piska - Link Line bypassing Hatia/Ranchi with Y connection (South Eastern Railway [SER] - I) (705785)	Jharkhand	08/2021 (03/2019)	06/2026 (05/2027)	473 (473)	288.75	5
569	Pradhan Kuntha Jn Line Doubling Project (East Central Railway [ECR] - I) (706837)	Jharkhand	11/2022 (11/2022)	11/2027 (11/2027)	349.22 (349.22)	115.09	62
570	Construction of New BG line between Hassan to Belur [27 Km] (South Western Railway [SWR] - II) (400023)	Karnataka	03/2019 (12/2025)	04/2028 (04/2027)	749 (749)	0	0
571	Yeshvanthpur - Channasandra Doubling Project [21.70 Km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703585)	Karnataka	04/2019 (10/2019)	03/2024 (03/2026)	314.1 (683.57)	158.53	55
572	New Railway Line between Ginigera and Raichur [165.57 km] (South Western Railway [SWR] - II) (705434)	Karnataka	03/2008 (05/2009)	03/2019 (03/2027)	2565 (3034.98)	2124.53	66
573	Gadag-Wadi New Railway Line [257 km] (South Western Railway [SWR] - II) (705490)	Karnataka	04/2013 (08/2017)	03/2027 (12/2027)	2842 (6700)	1439.46	30
574	Kadur - Chickamagalur - Sakleshpur [93km] (South Western Railway [SWR] - II) (705492)	Karnataka	01/2014 (11/2016)	06/2025 (12/2025)	825 (825)	725.47	83
575	Bagalkot-Kudachi New Railway Line [142 km] (South Western Railway [SWR] - II) (705495)	Karnataka	10/2013 (11/2012)	03/2027 (01/2027)	1378 (1649)	735.2	35
576	Tumkur-Chitradurga-Davangere New Rail Line Project [191 km] (South Western Railway [SWR] - II) (705496)	Karnataka	10/2013 (01/2017)	03/2019 (12/2027)	1876 (1876)	498.97	14
577	Bangalore-Whitefield-Bangalore City-Krishnarajapuram [23.08 km] - Quadrupling (South Western Railway [SWR] - II) (705663)	Karnataka	02/2018 (06/2022)	02/2026 (02/2026)	493 (493)	279.82	84
578	SHIMOGA - SHIKARIPURA - RANEBENNUR [96 Km] (South Western Railway [SWR] - II) (705761)	Karnataka	09/2019 (02/2023)	12/2027 (06/2028)	1454 (1454)	73.08	11
579	Bangalore Suburban Railway Project (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (705941)	Karnataka	10/2020 (10/2020)	12/2026 (03/2030)	15767 (15767)	2320.86	19
580	Belgaum-Dharwad via Kittur [73.10Km] (South Western Railway [SWR] - II) (706835)	Karnataka	09/2020 (03/2025)	12/2027 (03/2029)	1591 (1591)	0.38	0
581	Kumbalam-Turavur doubling project [15.59 Km] (Ministry of Railways) (705638)	Kerala	04/2023 (04/2023)	03/2027 (03/2027)	813 (802.8)	81.31	20
582	Ernakulam-Kumbalam doubling project [7.71 Km] (SR-ERS) (705639)	Kerala	04/2023 (04/2023)	03/2028 (02/2027)	601 (595.39)	294.57	21
583	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho (North Central Railway) (705480)	Madhya Pradesh	01/2007 (03/1998)	03/2027 (12/2027)	8914 (8914)	6546.4	73
584	Katni - Bina Third Railway Line [279 km] (West Central Railway WCR I) (705651)	Madhya Pradesh	06/2016 (01/2017)	03/2022 (12/2025)	2478.23 (4127.23)	3344.51	98
585	Satna-Rewa Railway Line Doubling Project (West Central Railway [WCR] - II) (705659)	Madhya Pradesh	11/2015 (08/2017)	03/2026 (03/2026)	500 (584)	545.71	85
586	Doubling of Katni - Singrauli Railway Line [261 km] (Indian Railway Construction International Limited [IRCON]) (705660)	Madhya Pradesh	03/2016 (03/2017)	12/2025 (12/2025)	2445 (4377)	3253.53	100
587	Katni Grade Separator/Bye Pass (Indian Railway Construction International Limited [IRCON]) (705661)	Madhya Pradesh	03/2016 (09/2017)	09/2024 (03/2026)	1248 (1248)	1718.76	95
588	Indore - Budni New Railway Line [198 kms] (RVNL - II) (705763)	Madhya Pradesh	08/2019 (10/2020)	09/2030 (09/2030)	7474 (7474)	1939.51	27
589	Nimach-Ratlam Doubling [133 Km] (Western Railway [WR] - II) (705933)	Madhya Pradesh	10/2021 (10/2021)	10/2027 (10/2027)	1095.88 (1095.88)	1067.49	89
590	DHULE [BORVIHIR] - NARDANA NEW LINE [50.60 KMS] (Central Railway) (400019)	Maharashtra	01/2019 (04/2023)	12/2026 (09/2027)	492.76 (1170.83)	415.47	25
591	Wardha-Nanded Via Yavatmal New BG Line (Central Railway [CR] - II) (400271)	Maharashtra	12/2017 (04/2008)	03/2025 (12/2026)	3445 (3445)	3002.93	50



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
592	AURANGABAD-ANKAI - DOUBLING PROJECT 98.25 Km (South Central Railway [SCR] - II) (611751)	Maharashtra	05/2023 (05/2023)	03/2027 (-)	960.64 (960.64)	732.32	1
593	Redevelopment of Chhatrapati Shivaji Maharaj Terminus [CSMT] and construction of associated infrastructure (Rail Land Development Authority) (613015)	Maharashtra	04/2023 (07/2023)	03/2027 (-)	1813 (1813)	635.74	17
594	Gondia-Balharshah [Chanda Fort] Doubling [240 Km] (South East Central Railway) (617201)	Maharashtra	04/2025 (04/2025)	03/2031 (-)	4373.04 (4373.04)	0.29	0
595	Doubling between Parbhani Parli Vaijanath stations 64.71 Km (South Central Railway [SCR] - II) (617215)	Maharashtra	12/2023 (12/2023)	03/2028 (-)	769.93 (769.93)	43.91	0
596	Babupeth - Sasti New Rail Line [13.114 KMs] (Central Railway) (617361)	Maharashtra	10/2024 (10/2024)	03/2028 (-)	362.81 (362.81)	0.47	0
597	Double Chord line Between Nilaje-Kopar (Central Railway) (617364)	Maharashtra	01/2025 (01/2025)	07/2028 (-)	338.33 (205)	7.8	0
598	Ahmednagar - Beed - Parli - Vaijnath New Broad Gauge Line Railway Project [261.3 km] (Central Railway [CR] - II) (705356)	Maharashtra	01/1999 (10/2002)	03/2026 (03/2026)	2538.67 (4957.27)	5183.23	98
599	Baramati Lonand New Line Project (Central Railway) (705357)	Maharashtra	03/2016 (03/1999)	03/2027 (03/2027)	138.48 (1843.9)	877.37	51
600	Wadsa-Gadchiroli (South East Central Railway) (705479)	Maharashtra	05/2017 (03/2012)	03/2027 (03/2027)	1886 (1886)	730.33	53
601	3rd Line Kalyan - Kasara [67.35 Kilometres] (Central Railway) (705498)	Maharashtra	09/2015 (09/2015)	12/2026 (12/2026)	792.89 (1395.79)	996.09	68
602	3rd Line Wardha - Sewagram - Nagpur (Central Railway [CR] - II) (705500)	Maharashtra	09/2015 (05/2016)	12/2025 (10/2026)	540.02 (916.53)	798.01	84
603	3rd Line Wardha - Ballarshah [132 Kilometres] (Central Railway [CR] - II) (705502)	Maharashtra	03/2016 (12/2016)	12/2025 (02/2026)	1384.72 (2033.59)	1727.83	86
604	Pune - Miraj-Londa [467 Kilometres] (Central Railway) (705503)	Maharashtra	06/2016 (06/2016)	02/2025 (08/2025)	4027.53 (4872.52)	5113.51	100
605	Doubling of Daund Manmad Line [247.6 km] (Central Railway) (705504)	Maharashtra	10/2017 (03/2017)	12/2025 (03/2026)	2081.27 (3267.06)	2956.98	92
606	4th Line Wardha - Nagpur [78.7 Kilometres] (Central Railway [CR] - II) (705505)	Maharashtra	04/2017 (05/2018)	12/2025 (10/2026)	637.95 (1214.69)	1035.92	88
607	3rd Line Manmad - Jalgaon [160 Kilometres] (Central Railway [CR] - II) (705506)	Maharashtra	05/2017 (04/2018)	12/2024 (08/2025)	1035.16 (1558.75)	1726.94	95
608	Solapur-tuljapur-Osmanabad (Central Railway) (705735)	Maharashtra	08/2018 (12/2023)	03/2027 (03/2028)	904.92 (3295.74)	1177.85	12
609	Nagpur- Nagbhir Railway Line Gauge Conversion Project (MRIDC) (705799)	Maharashtra	10/2019 (04/2020)	12/2025 (12/2025)	1400 (1400)	1472	80
610	Mumbai Urban Transport Project [MUTP] - PHASE II (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706779)	Maharashtra	05/2008 (04/2008)	03/2014 (12/2027)	8087 (8087)	7428.59	87
611	Mumbai Urban Transport Project [MUTP] Phase-III (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706780)	Maharashtra	04/2019 (04/2019)	12/2027 (12/2027)	33690 (33690)	2922.12	20
612	Mumbai Urban Transport Project Phase-III (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706781)	Maharashtra	11/2016 (12/2016)	03/2022 (12/2026)	10947 (10947)	5760.81	70
613	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15824.48	72
614	Marikuppam - Kuppam New Line Project [23.70 Km] (South Western Railway [SWR] - II) (705491)	Multi-States (Andhra Pradesh, Karnataka)	04/2012 (10/2018)	06/2026 (06/2026)	297 (297)	137.3	20
615	Rayadurg-Tumkur via Kalyandurg New Line [207 km] (South Western Railway [SWR] - II) (705494)	Multi-States (Andhra Pradesh, Karnataka)	03/2008 (07/2010)	09/2015 (02/2028)	2496 (2496)	1807.86	70
616	Renigunta, Wadi & Gooty Bypass Railway Project (South Central Railway [SCR] - II) (705610)	Multi-States (Andhra Pradesh, Karnataka)	04/2016 (04/2016)	12/2025 (12/2025)	302 (543)	381	50
617	Doubling between Mudkhed Medchal & Mahubnagar Dhone section 417.88 Km (South Central Railway [SCR] - II) (617212)	Multi-States (Andhra Pradesh, Maharashtra, Telangana)	08/2023 (08/2023)	03/2029 (-)	4686.09 (4686.09)	1048.12	2
618	Vizianagaram - Titlagarh 3rd line [272 Km including By - pass line of 7.68 KM] (RVNL - II) (400253)	Multi-States (Andhra Pradesh, Odisha)	06/2016 (11/2016)	12/2025 (12/2025)	4803 (6669.91)	6016.71	94
619	Doubling of Kottavalasa-Koraput Rail Line [189 KM] (East Coast Railway [ECoR] - II) (705512)	Multi-States (Andhra Pradesh, Odisha)	12/2015 (01/2016)	03/2022 (03/2028)	2500 (2500)	2091.69	71
620	Tindivanam-Nagari New Line Project [184.5 km] (Ministry of Railways) (400275)	Multi-States (Andhra Pradesh, Tamil Nadu)	07/2008 (10/2008)	09/2025 (03/2028)	3631 (3631)	1176.55	19
621	Doubling between Motumari Vishnupuram - 88.81 Km and Rail over Rail - RoR at Motumari - 10.877 Km (South Central Railway [SCR] - II) (616857)	Multi-States (Andhra Pradesh, Telangana)	02/2024 (03/2025)	03/2029 (-)	1595.55 (1595.55)	46.01	2



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
622	Doubling of Guntur Bibinagar 239 Km (South Central Railway [SCR] - II) (617211)	Multi-States (Andhra Pradesh, Telangana)	08/2023 (08/2023)	03/2029 (-)	2853.23 (2853.23)	107.06	2
623	Rail Connectivity to Errupalem Amravati Namburu 57 Km (South Central Railway [SCR] - II) (617214)	Multi-States (Andhra Pradesh, Telangana)	11/2024 (11/2024)	03/2027 (-)	2047.4 (2047.4)	28.44	0
624	Kazipet-Vijayawada 3rd line with electrification [220 km] (South Central Railway [SCR] - II) (705612)	Multi-States (Andhra Pradesh, Telangana)	03/2013 (08/2014)	02/2025 (12/2025)	1953 (3363)	4037.29	94
625	Vijayawada - Kazipet Bypass line (South Central Railway [SCR] - II) (705632)	Multi-States (Andhra Pradesh, Telangana)	04/2016 (04/2016)	01/2025 (12/2025)	647 (904)	1048.58	93
626	Murkongselek-Pasighat (Northeast Frontier Railway [NFR] - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (03/2023)	03/2025 (05/2026)	435 (1250)	805.31	65
627	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
628	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR] - II) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5828.35	81
629	New Delhi- Howrah Speed Booster[160Kmph] Project (PCE/NCR) (705794)	Multi-States (Bihar, Delhi, Jharkhand, Uttar Pradesh, West Bengal)	09/2019 (09/2019)	03/2024 (-)	6684.81 (6684.81)	127.03	0
630	Third Railway Line between Patratu-Sonnagar [291 kms] (RVNL - II) (400234)	Multi-States (Bihar, Jharkhand)	11/2016 (08/2018)	03/2026 (12/2028)	8975 (8975)	4798.96	90
631	Multi tracking of Son Nagar-Andal 374.53 rkm & 814.38 tkm (East Central Railway [ECR] - I) (616699)	Multi-States (Bihar, Jharkhand)	08/2023 (08/2023)	03/2028 (-)	12333.57 (12333.6)	507.61	14
632	Koderma-Tilaiya New Line (East Central Railway [ECR] - I) (705375)	Multi-States (Bihar, Jharkhand)	11/2004 (03/2002)	02/2025 (02/2026)	1626 (2486.62)	2142.8	94
633	Pirpainti - Jasidih [100.52 Km] New BG line (Eastern Railway [ER] - I) (705385)	Multi-States (Bihar, Jharkhand)	03/2014 (03/2022)	03/2028 (03/2028)	2555 (2555)	795.18	49
634	NER Provision of Automatic Block Signalling on Gorakhpur Cantt[Excl] Chhapra Gramin & Burhwal Jn [Excl] Sitapur Jn section of high density routes (North Eastern Railway [NER]) (611669)	Multi-States (Bihar, Uttar Pradesh)	NA (06/2023)	03/2027 (03/2028)	380.47 (380.47)	238.47	20
635	Gorakhpur-Valmikinagar Doubling project (NER) (617224)	Multi-States (Bihar, Uttar Pradesh)	08/2023 (03/2024)	12/2027 (-)	1120 (1120)	287.73	26
636	Chhapra-Ballia Patch Doubling (North Eastern Railway [NER]) (705562)	Multi-States (Bihar, Uttar Pradesh)	03/2013 (12/2015)	02/2025 (03/2026)	963 (1046)	912.43	95
637	Katihar Kumedpur & Katihar Mukuria BG Doubling Project (Northeast Frontier Railway [NFR]) (617245)	Multi-States (Bihar, West Bengal)	08/2022 (08/2022)	08/2026 (02/2027)	942.64 (942.64)	461.36	60
638	Gondia - Dongargarh 4th line [84 Km] (South Eastern Central Railway) (618978)	Multi-States (Chhattisgarh, Maharashtra)	10/2025 (10/2025)	10/2030 (-)	2222.53 (2222.53)	0	0
639	Rajnandgaon - Nagpur [Kalumna] Third Railway Line [228.30 km] (South East Central Railway [SECR] - II) (705617)	Multi-States (Chhattisgarh, Maharashtra)	09/2016 (12/2016)	12/2024 (06/2026)	3545 (3545)	3555.14	96
640	Sardega -Bhalumuda New Double line [37.24 Km] (SECR) (617390)	Multi-States (Chhattisgarh, Odisha)	09/2024 (09/2024)	03/2028 (-)	1281.81 (1281.81)	128.01	2
641	Jagdarpur-Koraput (East Coast Railway [ECoR] - II) (705511)	Multi-States (Chhattisgarh, Odisha)	12/2015 (03/2016)	03/2024 (12/2026)	1547 (1547)	1348.59	92
642	Jharsuguda-Bilaspur Fourth Railway Line [206 km] (SECR) (705616)	Multi-States (Chhattisgarh, Odisha)	09/2016 (09/2016)	10/2024 (03/2026)	2140 (2979)	2198.05	93
643	Mumbai-Ahmedabad High Speed Rail Project- 508 km (National High Speed Rail Corporation [NHSRC]) (705728)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	03/2015 (09/2017)	08/2027 (12/2029)	108000 (108000)	85337.89	56
644	New Delhi- Mumbai Speed Booster[160Kmph] Project (PCE/WR) (705793)	Multi-States (Delhi, Gujarat, Madhya Pradesh, Maharashtra, Rajasthan)	09/2019 (09/2019)	03/2024 (-)	6806.44 (6806.44)	135.65	0
645	Hospet - Tinaighat - Vasco Rail Doubling Project (RVNL - II) (705650)	Multi-States (Goa, Karnataka)	03/2010 (07/2012)	03/2027 (12/2027)	5060 (5060)	5271.61	86
646	Hospet-Hubli-Vasco da Gama Line Electrification Project (RVNL) (706950)	Multi-States (Goa, Karnataka)	07/2015 (05/2018)	03/2023 (06/2026)	744.49 (1122.62)	1149.24	99
647	Western Dedicated Freight Corridor (DFCCIL) (705237)	Multi-States (Gujarat, Haryana, Maharashtra, Rajasthan, Uttar Pradesh)	02/2008 (01/2012)	03/2022 (12/2025)	51101 (124005)	124623	96
648	New line Dahod-Indore via Sardarpur, Jabuwa and Dhar (Western Railway [WR] - II) (705453)	Multi-States (Gujarat, Madhya Pradesh)	06/2012 (06/2012)	02/2027 (02/2027)	456.07 (3516.77)	3945.04	52
649	Chhota Udaipur - Dhar New Line Project [157 km] (Western Railway [WR] - II) (705454)	Multi-States (Gujarat, Madhya Pradesh)	11/2008 (01/2014)	12/2025 (12/2025)	1794 (1794)	1815.94	80



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
650	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (Western Railway) (611452)	Multi-States (Gujarat, Maharashtra)	09/2019 (03/2023)	12/2025 (12/2026)	311 (311)	263.42	93
651	Taranga Hill-Abu Road via Ambaji (North Western Railway [NWR]) (400022)	Multi-States (Gujarat, Rajasthan)	07/2022 (07/2022)	07/2030 (07/2030)	2798 (2798)	2098.09	17
652	LUNI- SAMDARI- BHILDI DOUBLING (North Western Railway [NWR]) (616842)	Multi-States (Gujarat, Rajasthan)	02/2024 (02/2024)	07/2027 (-)	3085.59 (3085.59)	468.4	13
653	Chandigarh-Baddi New Rail Line- 36 km (Northern Railway [NR]) (705424)	Multi-States (Haryana, Himachal Pradesh)	02/2018 (02/2018)	12/2026 (12/2026)	1540 (1540.13)	554.36	37
654	Rewari - Kathuwas Doubling Project [27.72 Km] (North Western Railway [NWR]) (611861)	Multi-States (Haryana, Rajasthan)	02/2023 (12/2022)	06/2027 (06/2027)	352 (352)	283.12	73
655	Nangal Dam-Talwara New Broad Gauge Line [84 KM] and Taking Over Siding Mukerian-Talwara [29 KM] (Northern Railway [NR]) (705410)	Multi-States (Himachal Pradesh, Punjab)	03/1983 (05/1985)	12/2025 (12/2027)	2018 (2018)	89486.62	83
656	Bhanupalli-Bilaspur-Beri New Railway Line Project (RVNL - II) (705428)	Multi-States (Himachal Pradesh, Punjab)	03/2009 (04/2015)	12/2026 (12/2027)	13447 (13447)	7213.23	61
657	Doubling of Hatia [Ranchi]-Bondamunda Rail Line - 159 km (South Eastern Railway - JH) (705628)	Multi-States (Jharkhand, Odisha)	03/2016 (02/2017)	06/2025 (06/2026)	3029 (3029.04)	2533	87
658	Buramara-Chakulia new line [59.96 km] (South Eastern Railway [SER] - I) (616588)	Multi-States (Jharkhand, Odisha, West Bengal)	08/2024 (12/2024)	12/2029 (-)	1459.13 (1459.13)	4.68	0
659	Chandil - Anara - Damodar - 3rd line [121.26 km] (CAO/C/SER) (616227)	Multi-States (Jharkhand, West Bengal)	09/2024 (07/2025)	09/2029 (-)	1932.01 (1932.01)	0.49	0
660	KHARAGPUR-ADITYAPUR THIRD RAIL LINE- 132 KM (RVNL - I) (705668)	Multi-States (Jharkhand, West Bengal)	09/2016 (01/2018)	03/2025 (06/2026)	3250 (3250)	3247.89	97
661	Hotgi-Kudgi-Gadag Doubling Project (South Western Railway [SWR] - II) (705662)	Multi-States (Karnataka, Maharashtra)	04/2014 (01/2016)	12/2024 (03/2026)	1878 (2459)	2698.29	92
662	Baiyyappanahalli - Hosur Doubling Project [48 km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703586)	Multi-States (Karnataka, Tamil Nadu)	04/2019 (02/2019)	03/2024 (01/2026)	498.7 (748.7)	658.4	86
663	Trivandrum- Kanyakumari (Southern Railway [SR] - I) (705635)	Multi-States (Kerala, Tamil Nadu)	08/2017 (03/2016)	03/2025 (12/2026)	1432 (3785.45)	2554.26	51
664	Rattlam-Mhow-Khandwa-Akola Gauge Conversion (Western Railway [WR] - II) (705457)	Multi-States (Madhya Pradesh, Maharashtra)	04/2008 (03/2010)	03/2027 (09/2028)	1656.25 (6499.86)	4570.33	82
665	Itarsi - Nagpur Third Railway Line [280 km] (Central Railway [CR] - II) (705507)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016 (09/2016)	03/2027 (12/2027)	2449.91 (2506.68)	1985.94	55
666	RATLAM- DUNGARPUR VIA BANSWARA NEW LINE PROJECT (North Western Railway [NWR]) (617406)	Multi-States (Madhya Pradesh, Rajasthan)	10/2015 (05/2023)	03/2028 (-)	2417.24 (2417.24)	6.79	8
667	Gwalior - Seopurkala with extension to Kota [Gauge Conversion] (North Central Railway) (705419)	Multi-States (Madhya Pradesh, Rajasthan)	03/2011 (07/2018)	03/2025 (02/2026)	2913 (2913)	2124.16	86
668	Ramganjmandi-Bhopal New Line Project [262 km] (West Central Railway [WCR] - II) (705481)	Multi-States (Madhya Pradesh, Rajasthan)	03/2001 (10/2004)	12/2025 (12/2027)	3032 (5073)	3817.81	78
669	Nimach-Badi Sadri New Rail Line Project (Western Railway [WR] - II) (705764)	Multi-States (Madhya Pradesh, Rajasthan)	04/2017 (09/2021)	03/2026 (06/2026)	495 (825)	151.77	58
670	Mathura-Jhansi Third Railway Line [274 Km] (RVNL - II) (705667)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	12/2015 (03/2018)	12/2024 (12/2026)	5961 (5961)	5050.26	94
671	Jhansi - Bina Third Railway Line [153 Km] (CAO/C/NCR) (705598)	Multi-States (Madhya Pradesh, Uttar Pradesh)	09/2016 (03/2018)	03/2022 (03/2026)	2002 (2002)	1843.19	93
672	Jhansi-Khairar-Manikpur & Khirar-Bhimsen (North Central Railway) (705608)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2018 (04/2019)	03/2026 (03/2026)	4330 (4330)	2388.71	62
673	Third Line [new] between Kazipet - Balharshah with electrification [201.04 Km] (South Central Railway [SCR] - II) (705613)	Multi-States (Maharashtra, Telangana)	09/2016 (10/2016)	01/2025 (11/2025)	2595 (3071)	3580.19	94
674	Narayangarh-Bhadrak 3rd line (South Eastern Railway [SER] - I) (705629)	Multi-States (Odisha, West Bengal)	03/2019 (03/2017)	12/2025 (06/2026)	2400 (3425.32)	2404.72	66
675	Nagapattinam-Tiruturaipundi and Karaikal-Peralam New Line (Ministry of Railways) (400223)	Multi-States (Puducherry, Tamil Nadu)	07/2008 (01/2019)	03/2027 (03/2028)	713 (981)	633.24	80
676	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Multi-States (Sikkim, West Bengal)	10/2009 (05/2010)	05/2015 (12/2027)	7877 (11775)	9861.45	90
677	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass Line Project (Eastern Railway [ER] - I) (602797)	Multi-States (Uttar Pradesh, West Bengal)	08/2017 (12/2017)	03/2027 (03/2027)	461.64 (461.64)	197.33	9
678	Jharsuguda-Barpali-Sardega Ph II Works- Rail Connectivity for Coal Loading Bulb at Barpali. (South Eastern Railway [SER] - I) (400006)	Odisha	10/2021 (10/2021)	10/2025 (12/2025)	808.99 (808.99)	505.01	31



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
679	Proposed 6 nos Road Over Bridge [ROB] at different locations under MCL Talcher Under Deposit Scheme. (East Coast Railway [ECoR] - II) (400045)	Odisha	08/2022 (07/2022)	03/2025 (01/2025)	168.32 (168.32)	69.85	82
680	Doubling of Lingaraj SILO connectivity of NTPC line and augmentation of NTPC exchange yard and NTPC Block Cabin. (East Coast Railway [ECoR] - II) (400047)	Odisha	08/2022 (06/2022)	12/2024 (07/2024)	210 (210)	13.17	40
681	Doubling of lines connecting the loading spurs in Talcher Yard. (East Coast Railway [ECoR] - II) (400048)	Odisha	09/2022 (06/2022)	12/2024 (09/2024)	186.21 (186.21)	45	80
682	Brundamal-Jharsuguda- flyover connection for joining downline (East Coast Railway [ECoR] - II) (400232)	Odisha	01/2014 (01/2014)	12/2026 (12/2026)	297 (297)	215.87	46
683	3rd & 4th line between Sarla - Sason [8 km] [PB 73/2023-24/NR] (East Coast Railway [ECoR] - II) (612834)	Odisha	04/2023 (04/2023)	12/2025 (-)	252 (252)	97.64	68
684	Bangripoti-Gorumahisani new line [85.60 km] (CAO/C/SER) (616586)	Odisha	08/2024 (09/2025)	12/2029 (-)	2269.49 (2269.49)	4.12	0
685	Badampahar-Kendujhargarh new line [82.06 km] (CAO/C/SER) (616587)	Odisha	08/2024 (09/2025)	12/2029 (-)	1875.72 (1875.72)	1.13	0
686	Flyover between Siju and Paradeep coaching Yard to avoid Surface crossing of trains (East Coast Railway [ECoR] - II) (616694)	Odisha	04/2023 (10/2025)	07/2028 (-)	200.77 (200.77)	30	2
687	Paradeep - Badabandha 3rd & 4th Line / 18.51kms (East Coast Railway [ECoR] - II) (616695)	Odisha	08/2023 (04/2025)	11/2028 (-)	300.15 (300.15)	0.1	5
688	New Line between Junagarh - Nabarangpur [116.21 Km] (Indian Railway) (618995)	Odisha	08/2024 (08/2025)	08/2030 (-)	2864.51 (2864.51)	0	0
689	Khurda-Bolangir New Broad Gauge Rail Link [301km] (East Coast Railway [ECoR] - II) (705358)	Odisha	03/1994 (03/2001)	12/2026 (12/2026)	3792 (5089)	5315.25	90
690	Talcher-Bimlagarh New Railway Line (East Coast Railway [ECoR] - II) (705359)	Odisha	03/2004 (12/2004)	03/2025 (03/2027)	1928 (1928)	1995.82	50
691	Bhadrak-Nergundi Third Line (East Coast Railway [ECoR] - II) (705510)	Odisha	10/2015 (04/2015)	11/2024 (01/2026)	1284 (1284)	1323.62	91
692	Koraput - Singapur Railway Doubling (East Coast Railway [ECoR] - II) (705513)	Odisha	12/2015 (12/2015)	12/2027 (03/2028)	2362 (2362)	1856.42	71
693	Jarapada- Budhapank with flyover at Talcher road 3rd and 4th Line (East Coast Railway [ECoR] - II) (705514)	Odisha	11/2015 (12/2015)	11/2018 (03/2026)	1000 (810.02)	428.84	58
694	3rd & 4th Railway Line Project from Salegaon to Budhapank via Rajathgarh. (East Coast Railway [ECoR] - II) (705515)	Odisha	07/2013 (12/2015)	03/2026 (03/2026)	1173 (2092)	2063.93	85
695	Jeypore-Navarangpur New Rail Line Project (East Coast Railway [ECoR] - II) (705741)	Odisha	07/2017 (04/2023)	07/2028 (12/2029)	748 (748)	13.16	1
696	Jeypore-Malkanagiri New Railway Line Project (East Coast Railway [ECoR] - II) (705742)	Odisha	02/2018 (12/2023)	07/2033 (07/2033)	2344 (2344)	491.99	20
697	Khurda Road - Balangir Electrification of Railway Track Project (Ministry of Railways) (706898)	Odisha	09/2018 (09/2019)	03/2021 (-)	267.61 (267.61)	0	0
698	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION/12.76kms (East Coast Railway [ECoR] - II) (709811)	Odisha	09/2022 (05/2025)	09/2027 (09/2027)	190 (189.93)	0	0
699	Jaynagar-Bijalpura, incl. extn. Bet, Bijalpura-Bardibas [Nepal] (East Central Railway [ECR] - I) (705362)	Offshore	08/2015 (03/2011)	03/2022 (03/2026)	819 (819)	580.51	75
700	North Region Video Surveillance Project (RCIL) (705298)	PAN India	06/2020 (04/2023)	03/2024 (-)	274.39 (274.39)	0	48
701	Ludhiana- Killa Raipur Railway Doubling Project (Railway) (705783)	Punjab	03/2019 (12/2022)	03/2025 (03/2026)	237.64 (238)	135.92	56
702	Devgarh Madariya - Nathdwara Gauge Conversion [82.54 Km] part of Marwar - Mavli Gauge Conversion [152 Km] (North Western Railway [NWR]) (611849)	Rajasthan	01/2023 (01/2023)	06/2028 (06/2028)	968.92 (968.92)	192.98	57
703	Maintenance cum workshop depot for Vande Bharat Sleeper Trains as per conditions under WTA 527 (WPO/Patna) (611929)	Rajasthan	09/2022 (06/2023)	12/2024 (-)	166.86 (166.86)	0	0
704	PUSHKAR- MERTA CITY NEW LINE (North Western Railway [NWR]) (616841)	Rajasthan	02/2024 (02/2024)	12/2026 (-)	799.64 (799.64)	75.45	6
705	AJMER- CHANDERIYA DOUBLING (North Western Railway [NWR]) (616843)	Rajasthan	02/2024 (02/2024)	06/2027 (-)	1634.79 (1634.79)	203.52	9
706	SADULPUR - CHURU DOUBLING PROJECT (North Western Railway [NWR]) (617403)	Rajasthan	01/2024 (01/2024)	06/2026 (-)	468.64 (468.64)	136.58	55
707	POKHRAN - RAMDEVRA New Line (North Western Railway [NWR]) (617404)	Rajasthan	04/2025 (04/2025)	03/2028 (-)	189.21 (189.21)	0	0
708	NATHDWARA- NATHDWARA TOWN NL (North Western Railway [NWR]) (617408)	Rajasthan	03/2019 (04/2024)	03/2027 (-)	166.33 (166.33)	89.62	5



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
709	Dholpur - Sirmuttra Gauge Conversion (North Central Railway) (705482)	Rajasthan	03/2022 (04/2020)	02/2019 (02/2027)	747 (747)	436.56	45
710	Gudha-Thatha Mithri Construction of Railway Track Project (North Western Railway [NWR]) (705752)	Rajasthan	04/2019 (04/2019)	11/2026 (11/2026)	819.48 (967.06)	393.8	99
711	Sawai Madhopur-Jaipur Railway Line Project (North Western Railway [NWR]) (705912)	Rajasthan	02/2024 (04/2023)	03/2027 (-)	1203.89 (1203.89)	137.81	13
712	Agra Fort-Bandikui Doubling Line Project (CAO/C/NCR) (705919)	Rajasthan	06/2022 (02/2021)	06/2027 (06/2027)	1390 (1390)	362.92	57
713	Sawaimadhopur Bye Pass Line Project (North Western Railway [NWR]) (706866)	Rajasthan	12/2022 (01/2023)	03/2026 (05/2027)	304 (304)	60.48	65
714	Phase II extension of MRTS from Velachery to St Thomas Mount (Ministry of Railways) (400280)	Tamil Nadu	11/2007 (11/2008)	07/2025 (09/2025)	734 (734.01)	479.19	99
715	Redevelopment of Chennai Egmore Station (Ministry of Railways) (613002)	Tamil Nadu	05/2022 (10/2022)	03/2026 (-)	842 (842)	340	0
716	Coach Production Factory Upgradation Project (CPM/ICF) (705244)	Tamil Nadu	12/2017 (07/2018)	12/2021 (-)	520 (520)	192.25	0
717	Doubling between Bhadrachalam Road and Dornakal (South Central Railway [SCR] - II) (616856)	Telangana	08/2023 (04/2025)	04/2029 (-)	770.12 (770.12)	48.35	0
718	Railway Manufacturing Unit (RVNL - II) (617409)	Telangana	07/2016 (02/2023)	12/2026 (03/2026)	521.36 (521.36)	439.95	80
719	Kazipet Wagon Overhauling Project (RVNL) (705252)	Telangana	09/2017 (07/2017)	12/2023 (-)	385 (385)	0	0
720	Manoharabad-Kothapalli New Rail Line [151 km] (South Central Railway [SCR] - II) (705437)	Telangana	07/2016 (01/2017)	03/2027 (12/2027)	1160 (2781)	2332.39	71
721	Bahraich-Shravasti-Balrampur-Siddharthnagar -Santkabar nagar (North Eastern Railway [NER]) (400204)	Uttar Pradesh	10/2018 (03/2017)	10/2030 (10/2030)	4939.78 (4939.78)	1263.98	8
722	Sahjanwa-Dohrighat (North Eastern Railway [NER]) (400205)	Uttar Pradesh	08/2019 (03/2017)	03/2029 (03/2029)	1319.75 (1319.75)	511.08	3
723	Varanasi-Pt. Deen Dayal Upadhyaya multitracking 15km including construction of new Rail-cum-Road Bridge across Ganga River. (Northern Railways) (617213)	Uttar Pradesh	10/2024 (10/2025)	10/2029 (-)	2464.46 (2464.46)	0	0
724	Anandnagar - Ghugli via Maharajganj New line 52.7 km (Construction NER) (617252)	Uttar Pradesh	10/2023 (11/2023)	03/2028 (-)	958.27 (958.27)	455.29	23
725	Chunar-Chopan doubling project (North Central Railway) (617284)	Uttar Pradesh	08/2023 (01/2025)	03/2028 (-)	1423.96 (1423.96)	64.45	8
726	Surface triangle line bet. Bhadura stn and new crossing stn Karma (East Central Railway [ECR] - I) (617333)	Uttar Pradesh	10/2022 (05/2024)	02/2027 (-)	199.96 (199.96)	1.05	0
727	Doubling between Jaunpur Jn - Zaffarabad 6.28 km (M/S SRC company Infra Private Limited) (617370)	Uttar Pradesh	03/2023 (02/2025)	01/2027 (-)	180.66 (180.66)	4	13
728	Burhwal Gonda 3rd line (North Eastern Railway [NER]) (705567)	Uttar Pradesh	11/2017 (07/2019)	03/2025 (01/2026)	1016 (1118)	1461.48	88
729	Janghai-Pratapgarh- Amethi (CAO/C/II/NR) (705588)	Uttar Pradesh	11/2017 (03/2017)	03/2025 (03/2026)	722 (1194)	1601	70
730	Lalitpur-Birari with flyover at Lalitpur- 16 Km (North Central Railway) (705766)	Uttar Pradesh	03/2017 (11/2017)	12/2024 (01/2026)	304.44 (356)	241.27	80
731	Allahabad-Bamhrauli Flyover Construction & 4th Railway Line Project (North Central Railway) (705771)	Uttar Pradesh	04/2019 (10/2020)	03/2026 (03/2026)	494 (494)	371.2	67
732	Mughalsarai-Allahabad, 3rd line (North Central Railway) (705772)	Uttar Pradesh	12/2015 (03/2016)	12/2026 (03/2027)	2649 (2649.44)	1728.5	66
733	Aligarh -Daud Khan Flyover Construction & 3rd Railway Line Project (CAO/C/NCR) (705774)	Uttar Pradesh	04/2019 (09/2020)	01/2025 (03/2027)	758 (779.49)	421.6	73
734	Bhandai - Flyover for Etawah bound down train- 10 Km (North Central Railway (NCR) - II) (705777)	Uttar Pradesh	07/2020 (04/2021)	02/2026 (02/2027)	250.18 (250.18)	115.69	8
735	Bhatni-Aurnihar with electrification excluding Indara-Mau (RVNL - I) (705780)	Uttar Pradesh	03/2018 (03/2017)	12/2024 (03/2026)	2529 (2529.46)	2080.41	94
736	Barabanki-Malhour 3rd & 4th Railway Line Project (Ministry of Railways) (705782)	Uttar Pradesh	01/2019 (04/2017)	03/2025 (03/2026)	407 (407)	317	75
737	Rishikesh-Karnaprayag New Rail Line- 125 km (RVNL - II) (705429)	Uttarakhand	11/2016 (08/2018)	12/2025 (12/2028)	38953 (38953)	26840.95	72
738	Kalinarayanpur-Krishnanagar Doubling Alongwith Krishnanagar - Chapra New Line And Naihati-Ranaghat 3rd Line. (Eastern Railway [ER] - I) (400247)	West Bengal	07/2015 (11/2005)	02/2027 (02/2027)	1000 (1000)	1054.94	69



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
739	Tarakeshwar-Bishnupur New Line [82.47 km] (Eastern Railway [ER] - I) (400273)	West Bengal	03/2001 (02/2008)	03/2019 (02/2026)	1189 (1542)	1338.36	92
740	Dum Dum Airport-New Garia via Rajarhat-Construction of Metro Railway (RVNL - II) (400277)	West Bengal	03/2010 (10/2011)	12/2025 (03/2026)	8964 (8964)	8428.89	85
741	Construction of Balurghat-Hilli new BG Line (Northeast Frontier Railway [NFR]) (612096)	West Bengal	12/2010 (12/2010)	03/2027 (03/2027)	1209 (1181.57)	428.37	12
742	SER Upgradation of maintenance infrastructure at Shalimar into Vande Bharat Chair Car maintenance cum workshop depot. (South Eastern Railway - JH) (617345)	West Bengal	03/2024 (12/2024)	10/2026 (-)	226.87 (226.87)	33.7	36
743	Joka-BBD Bag new metro project (RVNL - II) (705730)	West Bengal	03/2010 (04/2010)	12/2026 (12/2029)	4835 (10362)	4740.17	51
744	Noapara-Barasat via Bimanbandar - Construction of Metro railway [18 km] (Metro Railway, Kolkata) (706776)	West Bengal	11/2010 (03/2010)	08/2026 (03/2029)	4830 (4830)	2764.13	32
745	Baranagar-Barrackpore and Dakshineswar- Construction of Metro Railway (RVNL - II) (706777)	West Bengal	03/2010 (03/2010)	12/2026 (12/2030)	2298 (2734)	393.01	17
Total (249)					702266.73	686201.12	
Department for Promotion of Industry & Internal Trade							
Real Estate							
746	Krishnapatnam Node - Phase 1 - Roads and Services Development (National Industrial Corridor Development Corporation) (701658)	Andhra Pradesh	12/2020 (02/2024)	02/2028 (-)	2139.44 (2139.44)	568.22	27
747	Tumakuru Node - Phase 1 - Roads and Services Development (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (701657)	Karnataka	12/2020 (02/2023)	09/2026 (-)	1701.81 (1701.81)	184.16	17
Total (2)					3841.25	752.38	
Ministry of Road Transport & Highways							
Roads & Highways							
748	Rehabilitation and Up-gradation from Km 170700 Bhadrachalam to Km 234567 Konta on NH-30 to Two lane with Paved Shoulder in the State of Andhra Pradesh on EPC mode. (MoRTH) (617907)	Andhra Pradesh	12/2021 (09/2022)	09/2024 (-)	436.09 (436.09)	207.05	89
749	Tadipatri Bypass Km 0000 to Km 6285 of 4-Lane on NH-67 in Anantapuramu district of AP state under NHO on EPC Mode under Annual Plan 2022-23 (MoRTH) (617949)	Andhra Pradesh	03/2023 (03/2024)	03/2026 (-)	159.66 (159.66)	32.57	69
750	Gudivada Town 2 RoB, and Road improvement NH-165 (MoRTH) (617984)	Andhra Pradesh	03/2022 (05/2023)	05/2025 (-)	317.22 (317.22)	0	67
751	Widening to two lane with paved shoulders from Km 0/0 to 64/020 Pamarru to Akiveedu (MoRTH) (617985)	Andhra Pradesh	03/2020 (11/2021)	11/2023 (02/2024)	529.54 (588.65)	0	0
752	Kurnool/Kadapa Border-Jammalamadugu section of NH-167K i.e. Design Ch. Km 248010 to km 269900 to 2 (MoRTH) (617986)	Andhra Pradesh	03/2023 (12/2024)	12/2026 (-)	292.63 (292.63)	0	40
753	Construction of bypass road to Adoni town connecting NH-167 Hagari - Jadcharla road from km.62/700 to 71/400 in Kurnool District in the State of Andhra Pradesh. (MoRTH) (617990)	Andhra Pradesh	03/2023 (02/2024)	11/2025 (-)	242 (242)	78.49	95
754	Rehabilitation and up-gradation of NH-167 from Km 14/900 to Km70/000 Design Ch. 14/900 to 69/700 Chintakunta to Adoni section to two lane with paved shoulders in the State of Andhra Pradesh under Corridor Approach through Engineering, Procurement (MoRTH) (617991)	Andhra Pradesh	11/2016 (05/2017)	05/2019 (11/2020)	290.15 (290.15)	0	0
755	Rehabilitation and Up-gradation of existin of road from 2-lane to 2-lane with paved shoulders from km. 0.00 to km 53.590 total length-53.590 km of Raychoti to Vempalli section of NH-440 in the State of Andhra Pradesh on EPC mode. (MoRTH) (618037)	Andhra Pradesh	12/2021 (05/2022)	05/2024 (-)	439.82 (359.52)	121.22	0
756	Dornala to Kunta Junction from Design Chainage Km 244000 to 267990 section of NH-765 Package-2 (MoRTH) (618062)	Andhra Pradesh	12/2022 (03/2024)	09/2025 (-)	244.83 (244.83)	0	83
757	Widening to two lane with paved shoulder of Rampachodavaram - Koyyuru section of NH 516E from Km 43700 to Km 113820 in the State of Andhra Pradesh on EPC mode Job No. 737 (MoRTH) (618145)	Andhra Pradesh	03/2022 (01/2023)	01/2025 (-)	568.12 (568.12)	289.47	92
758	Widening and Reconstruction of existing road to four lane from Km.56400 to Km 120300 i.e. from B.Kothapalli Junction to Gorantla excluding Kadiri Bypass from Km 70200 to Km 77105 of NH 716G in the State of Andhra Pradesh on EPC mode Job no. 742 (MoRTH) (618161)	Andhra Pradesh	03/2022 (09/2023)	12/2025 (-)	839.98 (839.98)	360.45	99
759	Rehabilitation and upgradation of NH-167AD from Macherla to Dacheppalli via Paluvai Junction, Rentachinthala, Gurazala from Km.0.000 to 43.659 to two lane with paved shoulders in the state of Andhra Pradesh job-729 (MoRTH) (618191)	Andhra Pradesh	01/2022 (01/2023)	01/2025 (-)	403.22 (403.22)	220.99	97
760	Duttalur at NH-565 Junction to Kavali Joining on NH-16 Chainage Km. 36/400 to Km. 107/224 excluding the stretch from Km 101.880 to 105.300 67.404 Km of NH-167BG from in the State of Andhra Pradesh on EPC mode (MoRTH) (618192)	Andhra Pradesh	03/2021 (07/2022)	07/2024 (-)	423.67 (423.67)	0	81



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
761	Rehabilitation and upgradation of New NH 544DD from design Chainage Km. 56/000 to 102/20 of Kalyandrg - Molakalmuru Section (MoRTH) (618194)	Andhra Pradesh	03/2018 (08/2018)	02/2020 (11/2021)	294.13 (285.29)	287.94	98
762	Rehabilitation and Up-gradation of Pasarlapudi to Dhindi section from Km 105/170 to Km 126/510 of NH -214 New NH -216 to two lane with paved shoulder in the state of Andhra Pradesh under NHDP-IV (MoRTH) (618237)	Andhra Pradesh	03/2017 (09/2017)	09/2019 (05/2024)	263.45 (263.45)	151.56	98
763	Rehabilitation and Up-gradation of Thimmapuram to Gurajanapalli section from Km 26/150 to Km 41/161 of NH - 214 New NH - 216 to two lane with paved shoulder in the state of Andhra Pradesh under NHDP-IV (MoRTH) (618238)	Andhra Pradesh	08/2016 (01/2017)	07/2018 (12/2021)	350.61 (432.91)	0	0
764	Construction of Paderu bypass Km 0000 to Km 13000 of 2- lane with paved shoulder on NH-516E (MoRTH) (618254)	Andhra Pradesh	03/2023 (01/2025)	07/2026 (-)	244.43 (244.43)	2.14	3
765	Two laning with paved shoulders of Lambasingi to Paderusection of NH 516E (MoRTH) (618255)	Andhra Pradesh	04/2020 (11/2023)	11/2025 (-)	361.24 (358.05)	77.68	23
766	Rehabilitation and Upgradation to 2-lane with paved should ders Sir, configuration of Chaprathipalem to Lambasingi section Km 165500 to Km 205000 of NH-516E in the State of Andhra Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode (MoRTH) (618256)	Andhra Pradesh	08/2020 (10/2022)	10/2024 (-)	311.22 (311.22)	172.01	76
767	Rehabilitation and Upgradation to 2-lane with paved shoulders configuration of Koyyuru to Chaprathipalem section Km 120000 to Km 165500 of NH-516E in the State of Andhra Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode (MoRTH) (618257)	Andhra Pradesh	08/2020 (07/2022)	07/2024 (06/2025)	349.29 (349.29)	221.52	86
768	Two laning with paved shoulders of Gondiguda to Araku uptoBhallaguda section of NH 516E (MoRTH) (618258)	Andhra Pradesh	08/2020 (09/2021)	09/2023 (09/2024)	296.66 (289.11)	237.52	91
769	Two laning with paved shoulders of Paderu to GundigudaSection of NH 516E (MoRTH) (618259)	Andhra Pradesh	08/2020 (03/2021)	03/2023 (03/2024)	222.61 (222.61)	122.52	100
770	Construction of i Connecting Road from Z-Morh Tunnel to Zojila Tunnel Road Length 18.475km and ii 14.150 Km long 2-L Bi-directional single tube Zoji-la Tunnel across Zojila Pass on Sonamarg - Kargil section from Km 82 to Km 118 of NH-01 under PMDP (NHIDCL) (618412)	Andhra Pradesh	01/2018 (10/2020)	09/2026 (12/2027)	6808.69 (6808.69)	0	0
771	Bangalore Chennai Expressway Phase-II Pkg-II from km.96.000 to Km 127.000 Baireddypalle to Bangarupalem section (National Highways Authority of India [NHAI]) (618475)	Andhra Pradesh	02/2021 (06/2023)	06/2025 (06/2026)	2548.04 (2548.04)	1058.1	81
772	Bangalore Chennai Expressway Phase-II Pkg-III from km.127.000 to Km 156.000 Bangarupalem to Gudipala section (National Highways Authority of India [NHAI]) (618476)	Andhra Pradesh	11/2020 (10/2022)	10/2024 (-)	1407.33 (1407.33)	675.5	99
773	Six Laning of Vijayawada Bypass from Gollapudi to Chinnakani in Vijayawada - Gundugolanu Section from km. 30.00 to km. 47.881 Pkg-IV (National Highways Authority of India [NHAI]) (618527)	Andhra Pradesh	01/2020 (07/2021)	01/2024 (-)	1194.57 (1757.82)	683.06	97
774	Renigunta - Poyya - Naidupeta km 124.60 to km 183.4 of NH 71 (National Highways Authority of India [NHAI]) (618700)	Andhra Pradesh	03/2020 (01/2022)	01/2024 (10/2024)	1863.09 (2510.14)	1231.42	98
775	6L Access Controlled Greenfield Highway from Kodur Ch. 0000 to Vanavolu Ch. 24300 of [NH-544G] Package-1 (National Highways Authority of India [NHAI]) (618712)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (-)	912.94 (798.25)	300.35	79
776	6L Access Controlled Greenfield Highway from Yerragudipadu Ch. 129000 to Audireddipalle Ch. 160000 of [NH 544G] Package-6 (National Highways Authority of India [NHAI]) (618713)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (-)	1200.42 (1019.69)	178.26	24
777	6L Access Controlled Greenfield Highway from Nallacheruvu palli Ch. 96300 to Yerragudipadu Ch. 129000 of [NH-544G] Package-5 (National Highways Authority of India [NHAI]) (618714)	Andhra Pradesh	02/2022 (02/2024)	02/2026 (-)	1253.26 (1095.78)	253.91	41
778	6L Access Controlled Greenfield Highway from Odulapalle Ch. 72000 to Nallacheruvu-palli Ch. 96300 of [NH-544G]Package-4 (National Highways Authority of India [NHAI]) (618715)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (-)	1058.9 (946.1)	328.59	63
779	6L Access Controlled Greenfield Highway from Vankarakunta Ch. 45700 to Odulapalle Ch. 72000 of [NH-544G]Package-3 (National Highways Authority of India [NHAI]) (618716)	Andhra Pradesh	12/2022 (03/2024)	03/2026 (-)	992.91 (888.07)	279.55	65
780	6L Access Controlled Greenfield Highway from Vanavolu Ch. 24300 to Vankarakunta Ch. 45700 of [NH-544G] Package-2 (National Highways Authority of India [NHAI]) (618717)	Andhra Pradesh	01/2023 (03/2024)	03/2026 (-)	750.81 (626.91)	203.13	72
781	6L Access Controlled Greenfield Highway from Mallapalle Ch. 176000 to Kavulakuntla Ch. 196000 Package-08 (National Highways Authority of India [NHAI]) (618719)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (-)	909.02 (751.81)	225.97	40
782	6L Access Controlled Greenfield Highway from Audireddipalle Ch. 160000 to Mallapalle Ch. 176000Package-07 (National Highways Authority of India [NHAI]) (618720)	Andhra Pradesh	02/2023 (03/2024)	03/2026 (-)	987.1 (848.06)	254.31	54
783	6L Access Controlled Greenfield Highway from Chandrasekharapuram Ch. 228000 to Polavaram Ch. 260000of [NH-544G] Package-11 (National Highways Authority of India [NHAI]) (618721)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (07/2026)	1292.65 (1110.33)	255.71	43



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
784	Khammam-Devarapalle Pkg IV [4L Access Controlled Greenfield from Recherla village to Gurvaygudem village Design Chainage 105236 to 132664] (National Highways Authority of India [NHAI]) (618748)	Andhra Pradesh	11/2020 (09/2022)	09/2024 (05/2025)	569.37 (752.02)	322.19	94
785	Khammam-Devarapalle Pkg V [4L Access Controlled Greenfield from Gurvaygudem village to Devarapalle village Design Chainage 132664 to 162126] (National Highways Authority of India [NHAI]) (618749)	Andhra Pradesh	12/2020 (09/2022)	09/2024 (06/2025)	711.94 (926.48)	376.11	88
786	4L of Pileru to Kalur Section from Km 55.900 to Km 92.800 & Km 94.500 to Km 95.717 of NH-71Package-II (National Highways Authority of India [NHAI]) (618777)	Andhra Pradesh	03/2022 (10/2023)	11/2025 (-)	1877.47 (592.85)	245.55	98
787	4L of Madanapalle to Pileru Section from Km 0.000 to Km 55.900 of NH-71Package-I (National Highways Authority of India [NHAI]) (618778)	Andhra Pradesh	02/2022 (01/2023)	01/2025 (06/2025)	1877.47 (1994.1)	1024.27	94
788	Development of 4L Road from Samarlakota to Achampeta Junction as part of Kakinada Port Connectivity to NH-16 Rajanagaram Junction in East Godavari District (National Highways Authority of India [NHAI]) (618803)	Andhra Pradesh	09/2022 (08/2023)	08/2025 (-)	645.63 (750.2)	543.32	74
789	Dedicated Port road to Krishnapatnam Port Package-I from Km. 0.000 to Km. 18.000 (National Highways Authority of India [NHAI]) (618804)	Andhra Pradesh	03/2018 (12/2018)	12/2020 (-)	348.72 (341.36)	59.91	75
790	4L Greenfield Road connecting North and South industrial cluster of Khandaleru Creek near Krishnapatnam port at Thaminapatnam to Mollur from Km 0.0 to Km 16.046, Part I & 6L extension of dedicated port road of NH-67 Km 18.0 to Km 19.3, Part II (National Highways Authority of India [NHAI]) (618807)	Andhra Pradesh	08/2022 (09/2023)	09/2025 (-)	609.43 (559.98)	403.36	73
791	4 Laning of NH-544D from Km 0.000 to km 37.000 of Anantapur- Muchukota section Pkg-1 (National Highways Authority of India [NHAI]) (618826)	Andhra Pradesh	10/2022 (07/2023)	07/2025 (-)	907.76 (905.98)	410.28	91
792	4 Laning of NH-544D from Km 37.000 to km 69.000 of Muchukota- Bugga section Pkg-2 (National Highways Authority of India [NHAI]) (618827)	Andhra Pradesh	10/2022 (08/2023)	08/2025 (-)	1097.57 (1055.23)	320.15	70
793	4L PS from Mandlem Existing Km. 38.000/Design Km.30.600 to Atmakur Existing Km.73.000/Design Km 66.115 of NH340C Package2 (National Highways Authority of India [NHAI]) (618919)	Andhra Pradesh	03/2023 (11/2023)	11/2025 (-)	887.28 (913.03)	374.34	99
794	Construction of 2-lane road of Potin to Pangin section of NH-13 from Km 163.59 to Km 206.66 Package-5 on EPC Mode in the State of Arunachal Pradesh under Arunachal Pradesh Package of Roads and Highways of SARDP-NE [Job No SARDP-NE/P-P/Pkg-A/NH-13/Ar.Pr./PWD/2018-19/116] (MoRTH) (617892)	Arunachal Pradesh	03/2019 (11/2020)	11/2023 (07/2024)	450.65 (450.65)	303.39	96
795	4-Laning of Itanagar to Bandardewa section of NH-415from km 40430 to km 51735 Package-Bon EPC Mode in the state of Arunachal Pradesh Job NO. 415/Ar. P/2020-21/031 (MoRTH) (618033)	Arunachal Pradesh	06/2020 (12/2021)	12/2024 (-)	496.47 (496.47)	153.63	48
796	Construction of 2-Laning with hard shoulders of Hayuliang Hawaii bypass Road on EPC basis from design Km. 51.825 to Km. 63.131 Existing Km 45.050 of HayuliangHawaii road to Hawaii Town under SARDP-NE -Balance work Pkg - IV (NHIDCL) (618424)	Arunachal Pradesh	01/2017 (05/2021)	05/2023 (07/2026)	256.66 (216.76)	0	93
797	Construction of Balance work of 2-Lane with PS of Joram-Koloriang Road NH-713 on EPC basis from Design Km 44.989 to Km 61.547 Existing Km 50.050 to Km 70.000 in the state of Arunachal Pradesh under SARDP-NE Pkg-3 (NHIDCL) (618432)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (07/2023)	228.72 (228.72)	0	99
798	Construction of Balance work of 2-Lane with PS of Joram Koloriang Road from existing Km122.600 to km138.00 [Design Km108.724 to Km123.714] in Arunachal Pradesh on EPC Mode under SARDP-NE Pkg-7 (NHIDCL) (618433)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (07/2023)	184.89 (184.89)	0	98
799	Roing-Hunli Road Greenfield Alignment Project (NHIDCL) (618434)	Arunachal Pradesh	02/2017 (03/2018)	03/2022 (04/2025)	1718.59 (1718.59)	0	77
800	Construction of Mangaldoi Bypass NH-15 starting at Ch 26400 and terminating at Ch 41505 under Rangia NH Division L 15.105 Km in the State of Assam. Job No. 15/AS/2021-22/234 (MoRTH) (617895)	Assam	03/2022 (04/2023)	04/2025 (-)	535.03 (535.03)	104.57	55
801	4-L Bilasipara-Guwahati Package-10 (NHIDCL) (618282)	Assam	03/2023 (12/2023)	06/2026 (-)	1264.9 (1264.9)	0	39
802	4-L Bilasipara-Guwahati Package-9 (NHIDCL) (618283)	Assam	03/2023 (12/2023)	06/2026 (-)	1000.27 (1000.27)	0	40
803	Widening/Improvement to 4-Lane with paved shoulder from Km 99930 to Km 143680 Design Chainage 96000 to 139750 of Paikan to Dhupdhara Sahar of Bilasipara-Guwahati Road on NH-17 in the state of Assam on EPC mode under Bharatmala Pariyojana in Economic Corridors Project Length 43.750km under NHO-NE Package-8 (NHIDCL) (618284)	Assam	03/2023 (12/2023)	12/2026 (-)	1457.59 (1457.59)	0	56
804	Widening/Improvement to 4 -Lane with Paved Shoulder from Ch. 88.000km to Ch.99.930 km Design Ch.84.100km to Ch.96.000 km of Sagunbashi forest near Nichinta to starting of Krishnai Bypass Section of Bilasipara Guwahati road NH 17 on EPC Package-7 (NHIDCL) (618285)	Assam	03/2021 (10/2023)	10/2025 (-)	286.72 (286.72)	0	100
805	Construction of New 2-Lane Bridge with its approaches from km 0000 to Km 4385 across River Brahmaputra on NH-17 at Jogighopa in Assam on EPC mode (NHIDCL) (618286)	Assam	09/2021 (11/2021)	11/2024 (06/2026)	746.76 (746.76)	0	0



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
806	Construction and up gradation to 4-Lane of existing two lane with paved shoulder from Hapachara to Tulungia road of NH-117 of existing Km 0.00 to km 14.050 and Design Km 0.000 to km 14.660 under BMP on EPC mode (NHIDCL) (618289)	Assam	03/2020 (06/2020)	12/2022 (06/2024)	224.85 (224.85)	204.19	0
807	Construction of 4-Lane Panchgram Bypass from Design Chainage km 15500 on NH-37 Old NH-53 at Kalinagar Pt.-I Village to Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Package-2 (NHIDCL) (618308)	Assam	03/2023 (08/2024)	02/2027 (-)	676.18 (728.97)	0	46
808	4-Laning of Dhanehari Lailapur / Vairengte section from Existing Chainage km 12920 to km 43000 of NH 306 Design Chainage km 20000 to km 49360 on Silchar - Vairengte Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode. Project Length 29.360 km under NHO-NE Package-2 (NHIDCL) (618314)	Assam	03/2023 (02/2024)	08/2026 (-)	1716.21 (1716.21)	848.23	64
809	4-Laning of Silchar - Dhanehari section from Existing Chainage km 263800 of NH 37 to km 12920 of NH 306 Design Chainage km 0000 to km 20000 on Silchar - Vairengte - Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode Package-1 (NHIDCL) (618315)	Assam	02/2023 (01/2024)	07/2026 (-)	1256.9 (1256.9)	0	0
810	Dillai to Lahorijan Package-7 (NHIDCL) (618325)	Assam	11/2021 (01/2023)	07/2024 (12/2025)	204.1 (204.1)	0	0
811	Widening/Improvement to 4-Lane with Paved Shoulder from KM 38500 to Km 51246 Design Chainage 38500 to 50959 with proposed Daboka Bypass of Daboka-Parokhaowa of NH 29 on EPC under NHO-NE Package-1 (NHIDCL) (618326)	Assam	01/2023 (11/2023)	11/2025 (-)	516.88 (516.88)	0	0
812	Widening/Improvement to 4-Lane with Paved Shoulder from KM 113300 to Km 146230 Design Chainage 113830 to 145712 of Kwaram Taro Village - Dillai Section in Assam on EPC Package-6 (NHIDCL) (618327)	Assam	09/2021 (07/2022)	07/2024 (03/2025)	625.64 (625.64)	0	0
813	Construction of 4/6 Laning from existing Km 159.400 of NH-36 to existing Km 102.500 of NH-39 and upto end point of Assam portion [Design Km 118.050 to design Km 132.375] Total New Alignment length of 14.325 Km of Daboka -Dimapur Section Dimapur Bypass in the state of Assam under SARDP-NE 'Phase-A' on EPC mode Assam Portion (NHIDCL) (618330)	Assam	03/2018 (11/2019)	11/2022 (08/2024)	511.02 (511.02)	0	0
814	Widening/Improvement to 2-Lane Lane with Paved Shoulder from km 16900 Bogapani to km 27150 Golai Goan on existing Dibrugarh to Ledo section with proposed Digboi Bypass Green Field and Brownfield 2-LanePS of NH-315 OLD NH-38 in Tinsukia District under NHO- NE Package-4 (NHIDCL) (618339)	Assam	01/2023 (12/2023)	12/2026 (-)	356.65 (356.65)	0	20
815	Widening/Improvement to 4-Lane with Paved Shoulder from km 626030 Nalani hulla Gaon to km 650450 Chotahapjan on existing Tinsukhia -Makum Bypass of NH-15 OLD NH-37 and Strengthening of existing NH-315 OLD NH-38 from Km 0000 Chotahapjan to Km 16900 Bogapani section 2-Lane PS in Assam on EPCMode under NHO-NE Package-3 (NHIDCL) (618340)	Assam	01/2023 (05/2023)	09/2025 (-)	458.59 (458.59)	0	68
816	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 156.489 near P. Leikul to km 176.410 near Borowapu on EPC mode under NHO-NE Assam portion Package-10 (NHIDCL) (618351)	Assam	03/2023 (08/2023)	08/2025 (-)	890.33 (693.15)	0	0
817	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 136.500 near Hejaichak to km 156.489 near P. Leikul Package-9 on EPC mode under NHO-NE Package-9 (NHIDCL) (618352)	Assam	03/2023 (08/2023)	08/2025 (-)	860.37 (614.43)	0	0
818	Widening & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 116.480 near Hangrum to km 136.500 near Hejaichak Package-8 on EPC mode under NHO-NE Package 8 (NHIDCL) (618353)	Assam	03/2023 (08/2023)	08/2025 (-)	904.04 (904.04)	0	0
819	Wideinig & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 96.870 near Jiri River to km 116.550 near Hangrum Package-7 on EPC mode Package7 (NHIDCL) (618354)	Assam	12/2023 (03/2024)	03/2026 (-)	846.82 (846.82)	0	71
820	Widening/Improvement to 4-Lane with Paved Shoulder from km 55000 Nagabang Gamsuk to km 82514 Oyan in the State of Assam and Arunachal Pradesh on EPC mode under Bharatmala Pariyojna of Length 27.514 Km Package-3 (NHIDCL) (618359)	Assam	03/2023 (09/2024)	08/2025 (-)	665.47 (665.47)	0	54
821	Widening/Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Srirampur near Bhairiguri Village to Kachukhana Harichara Paglagaunj Package-I of Srirampur - Dhubri Section of NH-127B from existing Km 0.000 to Km 28.050 Design Km 0.000 to Km 27.650, Design Length27.650 Km under JICA ODA Loan assistance Phase-V -Balance work (NHIDCL) (618371)	Assam	03/2022 (11/2024)	11/2026 (-)	613.89 (613.89)	0	43
822	Widening / Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Kachukhana Harichara Paglagaunj to Dhubri - Phulbari Bridge approach Package-II of Srirampur - Dhubri Section of NH-127B from existing Km 28.050 to Km 55.060 Design Km 27.650 to Km 54.154, Design Length26.504 Km under JICA ODA Loan assistance Phase-V [Srirampur - Dhubri Pkg-2] (NHIDCL) (618372)	Assam	03/2022 (01/2023)	06/2025 (-)	909.02 (909.02)	0	100



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
823	Construction of 4-Lane Bridge including approaches over River Brahmaputra between Dhubri on North Bank, Assam and Phulbari on south Bank, Meghalaya on NH-127B under JICA ODA Loan assistance Phase-III (NHIDCL) (618373)	Assam	05/2019 (12/2020)	09/2028 (12/2028)	4997.04 (4997.04)	0	67
824	4-Laning from Rangagara to Kaliabor Tiniali from km 297.00 to km 315.315 of NH-37 on EPC basis under SARDP-NE in state of Assam (NHIDCL) (618435)	Assam	01/2016 (10/2017)	04/2020 (03/2025)	386.51 (386.51)	0	0
825	4-Laning of Jamugurihat to end of Biswanath Chariali By-Pass from Km 182.000 to Km 208.000 of NH-52 on EPC mode in state of Assam under SARDP-NE (NHIDCL) (618436)	Assam	03/2015 (12/2016)	06/2019 (03/2025)	599 (599)	0	0
826	Construction of Balance Work of 4-Laning of NH-37 Section between End of Moran Bypass to Bogibeel junction near Lapetketa Km. 561.700-Km. 580.875 under SARDP-NE, Phase 'A' in the State of Assam on EPC mode Pkg-I Road works & Toll Plaza (NHIDCL) (618437)	Assam	01/2016 (09/2024)	08/2025 (-)	274.34 (274.34)	0	100
827	4-Laning of NH-37 Section between Demow to End of Moran Bypass From Km. 534.800 to Km. 561.700 including Emergency Landing Facility ELF under SARDP-NE, Phase 'A' in the State of Assam on EPC mode (NHIDCL) (618438)	Assam	01/2016 (01/2023)	08/2025 (01/2025)	385.57 (385.57)	0	0
828	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 501.800 11.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618441)	Assam	01/2016 (10/2024)	09/2025 (-)	467.79 (476.5)	72.13	0
829	Development of External Trunk Connectivity and Internal Infrastructure Works at Multi Model Logistics ParkMMLP at Jogihopa in the State of Assam on EPC Mode Package-I Road and Utility Works (NHIDCL) (618455)	Assam	02/2020 (09/2020)	09/2024 (10/2024)	693.97 (693.97)	0	0
830	6L Standalone Flyovers at Bongaigaon, Chapaguri, Pathsala, Simlaguri chowk and Baihata Bypass Junctions on stretches of NH-31 and NH-27 (National Highways Authority of India [NHAI]) (618575)	Assam	03/2022 (01/2023)	07/2024 (-)	457.72 (412.15)	371.63	100
831	6L Standalone Flyovers at Raha, Demow, Borghat, Kathiatiali junctions and ROB at Jagiroad on stretches of NH 36 and NH 27 (National Highways Authority of India [NHAI]) (618576)	Assam	03/2022 (12/2022)	06/2024 (-)	280.75 (255.53)	211.79	99
832	Construction of proposed 4Lane Revelgunj bypass NH-19 in the State of Bihar on EPC mode connecting NH 19 to 85 origin (MoRTH) (617897)	Bihar	03/2022 (07/2023)	07/2025 (-)	295.24 (295.24)	33.07	73
833	Widening & Strengthening from km132.895 to km 190.15 NH-80 (MoRTH) (617958)	Bihar	03/2021 (11/2022)	11/2024 (-)	566.1 (566.1)	221.6	37
834	Rehabilitation & Widening work for 2 Lane with Paved Shoulder of Existing NH-80 from km 70.15 to Km 121.025 of Munger-Suttanganj -BhagatpurMirzachowki section on EPC Mode in the State of Bihar. (MoRTH) (617959)	Bihar	03/2021 (02/2023)	01/2025 (-)	477.54 (477.54)	311.39	95
835	Gaya-Hisua-Rajgir-Nalanda-Biharsharif section km0.00 to 92.935 NH-82 (MoRTH) (617961)	Bihar	01/2014 (11/2016)	11/2019 (07/2022)	1408.85 (2138.16)	0	0
836	Rehabilitation and Upgrading to 2 lanes/2-lane with paved shoulders configuration and strengthening of of Birpur and Bihpur Section from km 0.0 to Km 106 of NH 106 under phase I of National Highways Interconnectivity Improvement Projects NHIP ICB No. NHIP-BR-106-7 [NHIP-BR-106-7] (MoRTH) (617966)	Bihar	01/2014 (10/2016)	10/2019 (06/2022)	780.77 (961.33)	0	0
837	Construction of 4 Lane ROB and its approaches at the level crossing LC No 29 B of Km 29 Ekangarsarai at NH 110 New NH 33 & Railway Km 32.63 at Fatwa FUT Islampur IPR section in the state of Bihar on EPC mode. (MoRTH) (617969)	Bihar	03/2023 (07/2024)	07/2026 (-)	201.08 (201.08)	0.01	32
838	Construction of Bhabhua Bypass from Ch. 10800Design Ch. 10800 to Ch. 19860 Design Ch. 18150 and Chand Bypass from Ch. 38060 Design Ch. 36250 to Ch. 40460 Design Ch. 38650 and widening of existing road to 2 - lane with Paved shoulder from Ch. 40460 Design Ch. 38650 to Ch. 46860 Design Ch. 45050 of NH-219 Total length-16.150 Km under EPC mode in the state of Bihar (MoRTH) (618004)	Bihar	02/2022 (01/2025)	07/2026 (-)	179.86 (179.86)	0	0
839	Sheohar-Sitamarhi Section km 40.000 to 79.400 km Lot-I (MoRTH) (618005)	Bihar	02/2016 (05/2016)	05/2018 (06/2021)	178.85 (278.53)	0	98
840	Sitamarhi-Jaynagar Section km 79.400 to km 156.500 Lot-II (MoRTH) (618006)	Bihar	02/2016 (06/2016)	12/2018 (06/2021)	369.77 (503.28)	0	98
841	Jaynagar-Narahia Section km 156.500 to km 219.945 Lot-III (MoRTH) (618007)	Bihar	02/2016 (05/2016)	11/2018 (03/2021)	553.3 (706.39)	0	99
842	Improvement to Two lane with Paved Shoulder from Junction of NH22 near Hajipur to Junction of NH -122 at Bachhwara via Mahnar and Mohiuddin Nagar from Km 0.00 to Km 29.730 of NH 122 B in the State of Bihar. (MoRTH) (618073)	Bihar	02/2024 (08/2024)	11/2025 (-)	226.16 (226.16)	0	0
843	Pre construction activity of NH 122B from km 0 to 72.348 and Improvement to two lane with paved shoulders of NH 122B from km 29.730 to km 72.348 in state of Bihar under EPC mode (MoRTH) (618074)	Bihar	02/2022 (05/2023)	11/2024 (-)	624.43 (624.43)	153.21	90



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
844	Improvement to two lane with paved shoulders of BH WB Border Amdabad Manihari section from design Km 0.000 to Km 23.945 of NH 131 A Total length 23.945 Km under EPC mode in the state of Bihar (MoRTH) (618080)	Bihar	01/2022 (09/2024)	03/2026 (-)	353.27 (353.27)	0	2
845	Improvement to two lane with paved shoulders of NH-319A from km 0 to km 45 in state of Bihar under EPC mode (MoRTH) (618121)	Bihar	02/2022 (06/2023)	12/2024 (-)	427.29 (427.29)	176.32	0
846	Estimate for Improvement to two lane with paved shoulder from Ramnagar to Roseda from km 3.500 to 43.000 of NH 527 E on EPC mode in State of Bihar (MoRTH) (618146)	Bihar	01/2022 (10/2024)	04/2026 (-)	495.16 (495.16)	0	0
847	construction of a new 4 lane Parallel to existing MG Setu with its approaches from km 0.00 to km 14.500 across river Ganga on NH-19 at Patna in the state of Bihar. (MoRTH) (618228)	Bihar	02/2019 (03/2021)	09/2024 (01/2025)	2926.42 (2926.42)	0	66
848	Construction of a new 4-lane major bridge across river Kosi at Phulaut including Rehabilitation and upgradation of existing Birpur and Bihpur section of NH-106 from km 106.000 to km 136.000 to 2-lane with paved shoulders in the State of Bihar on EPC mode (MoRTH) (618234)	Bihar	09/2018 (06/2021)	06/2024 (03/2026)	1478.4 (1478.4)	753.21	86
849	Construction of New 4-Lane Bridge Parallel to existing Vikramashila Setu from km 8920 to Km 13375 including approach road 35m Naugachhia side & 53 m Bhagalpur side across River Ganga on newly declared NH-131B at Bhagalpur in the State of Bihar (MoRTH) (618246)	Bihar	07/2020 (05/2023)	05/2027 (-)	1110.23 (1110.23)	0	44
850	Construction of 6-Lane Elevated / Extra Dose Cable Bridge on River Ganga parallel to & Western side of Digha-Sonepur Rail cum-Road Bridge of NH 139W in the State of Bihar (MoRTH) (618250)	Bihar	01/2024 (05/2024)	11/2027 (-)	3064.45 (3064.45)	0	8
851	Balance work - WB-10 Gandak Bridge Km 402.00 to Km 440.00 Devanpur - Kotwa (National Highways Authority of India [NHAI]) (618569)	Bihar	11/2021 (07/2022)	01/2024 (-)	210.05 (358.3)	99.85	63
852	4L Elevated Highway and at grade improvements at Gopalganj Town from Km. 384.000 to Km. 386.750 on NH-27 (National Highways Authority of India [NHAI]) (618570)	Bihar	10/2021 (03/2022)	08/2024 (-)	325.57 (248.92)	227.89	96
853	Permanent rectification of 3 nos. of black spots in project Highway NH-27 of U.P border - Dewapur - Kotwa section from Km.360.915 to km.440.000 Total Length of 79.085 Km of NH-27 & Permanent rectification of 5 nos. of black spots of project Highway NH-27 of Kotwa - Mehsi - Muzaffarpur Section from km.440.000 to km.520.000 Total length 80.00Km (National Highways Authority of India [NHAI]) (618571)	Bihar	04/2022 (12/2023)	12/2025 (-)	227.25 (321.23)	193.52	68
854	6L Bridge and its approaches across River Ganga as Part of Patna Ring Road NH-131G starting from Km 8.480 near Sherpur to Km 23.000 near Dighwara (National Highways Authority of India [NHAI]) (618738)	Bihar	09/2022 (09/2023)	09/2027 (-)	6291.69 (3351.62)	421.4	13
855	4L Greenfield Alignment of Amas to Shivrampur from 0.000 Km. to 55.002 Km. of NH 119 D Pkg-I (National Highways Authority of India [NHAI]) (618739)	Bihar	02/2022 (03/2023)	11/2024 (12/2025)	1390.92 (1427.43)	282.35	33
856	4L Greenfield Alignment of Shivrampur to Ramnagar from Km. 55.002 to Km. 109.300 of NH 119 D Pkg-II (National Highways Authority of India [NHAI]) (618740)	Bihar	02/2022 (07/2023)	07/2025 (12/2025)	1494.31 (1546.07)	243.51	34
857	4L Greenfield Alignment from Kalyanapur to Tal Dashraha of NH-119D Pkg-III (NHAI) (618741)	Bihar	03/2022 (02/2023)	02/2025 (-)	1857.58 (1969.3)	345.49	23
858	Ara - Mohania Pkg-II (National Highways Authority of India [NHAI]) (618774)	Bihar	08/2020 (01/2021)	07/2023 (11/2025)	984.63 (827.51)	798.12	100
859	4L of Aurangabad-Paithan (NHAI) (618779)	Bihar	09/2022 (01/2023)	07/2024 (-)	1505 (349.96)	304.99	78
860	Aunta - Simaria including Ganga Bridge (National Highways Authority of India [NHAI]) (618839)	Bihar	NA (08/2018)	02/2022 (05/2025)	1309.47 (2107.68)	796.99	100
861	Simaria Km. 206.050 to Khagaria Km. 266.282 (National Highways Authority of India [NHAI]) (618840)	Bihar	NA (10/2016)	04/2019 (03/2025)	664.02 (891.64)	337.23	97
862	4L Elevated Section and at-grade improvements at Begusarai town Simaria - Khagaria section from Km. 221.047 to Km. 225.302 of NH-31 (National Highways Authority of India [NHAI]) (618841)	Bihar	10/2021 (06/2022)	12/2024 (12/2025)	491.04 (348.38)	316.67	92
863	Bakhtiyarpur-Rajauli Pkg-II from km. 54.405 to km.101.630 (National Highways Authority of India [NHAI]) (618861)	Bihar	09/2020 (04/2021)	07/2023 (-)	897.45 (1397.47)	697.4	91
864	Maheshkunt-Saharsa-Purnea Pkg I km 0.00 to km. 90.00 of NH-107 (National Highways Authority of India [NHAI]) (618902)	Bihar	02/2017 (12/2019)	12/2021 (08/2025)	662.44 (1311.22)	867.61	85
865	Maheshkunt-Saharsa-Purnea Pkg II (National Highways Authority of India [NHAI]) (618903)	Bihar	NA (12/2018)	12/2020 (11/2025)	1028.28 (1244.09)	805.43	89
866	Chhapra - Hajipur from km. 143.200 to km. 209.200 (National Highways Authority of India [NHAI]) (618904)	Bihar	NA (01/2011)	07/2013 (-)	2127.86 (2171.6)	3.78	57
867	4L of Bal. works of Patna - Gaya -Dobhi Pkg-II from km. 39.00 to km. 83.00 of Old NH-83 (National Highways Authority of India [NHAI]) (618915)	Bihar	09/2019 (11/2020)	11/2022 (05/2025)	1637.29 (777.2)	728.91	89



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
868	4L of Bal. works of Patna - Gaya -Dobhi Pkg-III from km. 83.00 to km. 127.217 of Old NH-83 (National Highways Authority of India [NHAI]) (618916)	Bihar	09/2019 (11/2020)	11/2022 (05/2025)	1077.46 (799.7)	774.78	92
869	Umagaon-Saharsa Package-IV Koshi Bridge & approach Road - Bheja-Bakaur (NHAI) (618953)	Bihar	02/2019 (02/2020)	08/2023 (-)	1199.58 (1223.94)	837.89	81
870	2L PS of Majhauri to Charout section from km. 0.00 to km. 63.655 (NHAI) (618955)	Bihar	01/2018 (11/2019)	11/2021 (-)	638.29 (1067.51)	125.16	95
871	Construction of 4 Nos Grade separator between km. 281.000 to km. 307.600 km. 286.400 kumhari km. 299.000 Transport Nagar km. 302.000 Power House km. 304.000 Chandra Moura Chowk to km. 305.000 supeia of NH-53 old NH-06 Raipur - Durg 4 Lane on EPC mode in the state of chhattisgarh job NO. NH-53old NH-06 CG-2017-18-56 (MoRTH) (617919)	Chhattisgarh	03/2018 (01/2019)	01/2021 (01/2021)	349.03 (349.03)	0	97
872	Strengthening and widening of existing 2 lane road to two lane paved shoulder from km 7.750 to 26.542 & km. 32.093 to 45.786 of NH-130 on EPC mode in the state of chhattisgarh.job No. 130-CG-2017-18-348 (MoRTH) (617973)	Chhattisgarh	11/2017 (05/2019)	11/2020 (-)	188.8 (188.8)	1.06	97
873	Up-gradation of NH-930 Sherpar to Kohka from Km.67880 to Km.114860 to 2LPS in Chhattisgarh under EPC mode (MoRTH) (618064)	Chhattisgarh	03/2020 (05/2022)	05/2024 (-)	278.97 (278.97)	201.05	0
874	Up-gradation of NH-130C Abhanpur to Paund from NH Km. 0000 to KM 40380 to two lane with paved shoulders in the State of Chhattisgarh on EPC mode. (MoRTH) (618078)	Chhattisgarh	12/2020 (03/2022)	09/2023 (-)	193.16 (193.16)	56.27	0
875	Durg-Raipur Bypass Section Package - 1 from km. 0.00 to km. 44.50 near Tendesara to near Khatti Village (National Highways Authority of India [NHAI]) (618589)	Chhattisgarh	06/2022 (07/2023)	07/2025 (-)	1072.99 (1656.73)	537	60
876	Durg-Raipur-Arang Package - 2 from km. 44.50 to km. 92.23 near Khatti Village to near Aurang (National Highways Authority of India [NHAI]) (618590)	Chhattisgarh	06/2022 (06/2023)	05/2025 (-)	1216.23 (1561.97)	406.66	40
877	Development of 6L of Jhanki Sargi Section Road from km 0.000 to km 42.800 of NH-130CD Pkg-CG-1 (National Highways Authority of India [NHAI]) (618673)	Chhattisgarh	11/2021 (09/2022)	09/2024 (-)	1368.19 (1129.14)	613.02	77
878	Development of 6L Sargi Basanwahi Section from km 42.800 to km 99.500 of NH-130CD Pkg-CG-2 (National Highways Authority of India [NHAI]) (618674)	Chhattisgarh	12/2021 (01/2023)	01/2025 (09/2025)	1470.73 (1461.81)	694.31	92
879	Development of 6L of Basanwahi Marangpuri Section from km 99.500 to km 124.661 of NH-130-CD (National Highways Authority of India [NHAI]) (618675)	Chhattisgarh	03/2022 (10/2023)	10/2025 (07/2026)	1307.16 (1303.63)	373.53	53
880	Conversion of Partially Excavated Escape Tunnel to Uni-Directional 2L Tunnel including construction of cross passages and approach roads on either side of the tunnel from Km 12.732 to Km 14.568 of Kiratpur to Nerchowk Section of NH-21 (National Highways Authority of India [NHAI]) (618849)	Chhattisgarh	05/2022 (09/2022)	03/2024 (08/2025)	444.21 (412.88)	394.5	100
881	Development of 6L UER II [Package - I] NH-1 Near Bakoli till Karala Kanjhawala Road from km. 0.70 to km.15.00 (National Highways Authority of India [NHAI]) (618509)	Delhi	07/2020 (10/2021)	10/2023 (02/2025)	2089.94 (2203.45)	1794.18	99
882	6L Access Controlled Highway from DND Maharani Bagh - Jn. with Jaitpur - Pushta Road of NH-148NA from km. 0.00 to km. 9.00 in NCR (National Highways Authority of India [NHAI]) (618578)	Delhi	07/2020 (01/2022)	07/2024 (09/2025)	1467.44 (2510.34)	1349.78	95
883	Construction of Six lane Elevated Corridor from Km. 508.000 to Km. 513.150 including approaches on NH-66 (MoRTH) (617942)	Goa	04/2023 (04/2024)	04/2026 (02/2026)	641.46 (641.46)	0	62
884	Widening 2 lane to 4-lane from KM 92/320 to Km 115/320 Vav Chokdi-Satlasana to to Vrundavan Chokdi, Kheralu on NH-58 in the State of Gujarat. (MoRTH) (617928)	Gujarat	03/2022 (03/2024)	03/2026 (-)	151.13 (171.27)	0	78
885	Work of development and construction of elevated corridor from km 38/660 to km 42/690 Iscon junction to start point of approach of sanand flyover of NH-147 in the sate of Gujarat (MoRTH) (617976)	Gujarat	03/2023 (06/2024)	06/2026 (-)	530.2 (530.2)	28.67	55
886	Up-gradation and strengthening to 2lanePS from Km 95/500 to km 129/775 of Nh 168G Idar-Bhiloda-Samlaji in the state of Gujarat Length 34.275 km (MoRTH) (618108)	Gujarat	09/2022 (12/2023)	12/2025 (-)	237.28 (237.28)	0	47
887	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-26 Ch.696890 to Ch.726390 (National Highways Authority of India [NHAI]) (618459)	Gujarat	09/2020 (12/2022)	08/2024 (-)	1555.2 (1556.4)	941.64	72
888	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-28 Ch.756052 to Ch.781282 (National Highways Authority of India [NHAI]) (618460)	Gujarat	09/2020 (11/2021)	11/2023 (05/2025)	1263.38 (1266.98)	860.42	96
889	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-30 Ch 803420 to Ch.824920 [Baletiya Village - Junction near Pratap Nagar Village] (National Highways Authority of India [NHAI]) (618461)	Gujarat	11/2019 (09/2021)	09/2023 (06/2024)	1800.73 (1800.73)	1090.06	99
890	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-31 Ch.824920 to Ch.844382 [Junction near Pratap nagar Village - Junction near Dodka Village] (National Highways Authority of India [NHAI]) (618462)	Gujarat	11/2019 (05/2021)	05/2023 (-)	1644.85 (1651.14)	926.73	95



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
891	Vadodara Mumbai Expressway Kim to Ankleshwar Phase IA - Pkg V (National Highways Authority of India [NHAI]) (618463)	Gujarat	02/2018 (11/2019)	10/2021 (04/2025)	1324.84 (2807.48)	1232.22	61
892	Vadodara Mumbai Expressway Gandeva to Ena Phase IB - Pkg VII [Km 190.00 to Km 217.500] (National Highways Authority of India [NHAI]) (618465)	Gujarat	07/2020 (11/2021)	11/2023 (03/2025)	1710.3 (3392.21)	2152.35	52
893	Ahmedabad - Dholera Pkg I from km. 0.00 to km. 22.00 [Sardar Patel Ring Road - Sindhrej Village] (National Highways Authority of India [NHAI]) (618501)	Gujarat	05/2020 (01/2022)	01/2024 (10/2024)	1298 (1421.05)	994.98	99
894	Ahmedabad - Dholera Pkg II from km. 22.00 to km. 48.52 [Sindhrej Village - Vejalika Village] (National Highways Authority of India [NHAI]) (618502)	Gujarat	05/2020 (01/2022)	01/2024 (-)	1415.34 (1729.69)	982.57	99
895	Ahmedabad - Dholera Pkg III from km. 48.52 to km. 71.06 [Vejalika Village - Start of DSIR zone] (National Highways Authority of India [NHAI]) (618503)	Gujarat	05/2020 (07/2021)	07/2023 (05/2024)	1034.04 (1155.41)	942.31	99
896	Ahmedabad - Dholera Pkg IV from km. 71.06 to km. 109.019 [Start of DSIR zone - Adhelai Village] (National Highways Authority of India [NHAI]) (618504)	Gujarat	05/2020 (12/2021)	12/2023 (10/2024)	1181.76 (1358.73)	1202.2	97
897	Sanchole - Santalpur from km 67.000 - km 99.000 of NH-754K AJ-RGBS-Package-3 (National Highways Authority of India [NHAI]) (618614)	Gujarat	02/2020 (08/2021)	08/2023 (01/2024)	752.3 (765.25)	560.81	99
898	Sanchole - Santalpur from km 99.000 - km 130.073 of NH-754K AJ-RGBS-Package-4 (National Highways Authority of India [NHAI]) (618615)	Gujarat	02/2020 (03/2021)	03/2023 (12/2024)	778.15 (835.55)	663.18	73
899	Upgradation to 4L PS from Bhimasar, Junction of NH-41 to Anjar- Bhuj upto Airport Junction from Km 0.000 to Km 65.478 of NH-341 (National Highways Authority of India [NHAI]) (618787)	Gujarat	03/2022 (01/2023)	06/2025 (-)	1373.06 (1687.25)	728.15	90
900	Kodinar - Veraval Package VI from km. 221.610 to km. 263.00 of NH-8E & km. 120.900 to km. 121.150 of NH-8D (National Highways Authority of India [NHAI]) (618833)	Gujarat	NA (02/2018)	07/2020 (10/2024)	894.01 (1127.42)	439.5	98
901	4L Kodinar - Veraval Package VI from km. 222.400 to km. 230.00 Kodinar Bypass of NH-8E NH 51 new (National Highways Authority of India [NHAI]) (618834)	Gujarat	03/2022 (04/2022)	09/2023 (-)	162.73 (192.01)	162	100
902	4L of Bal Works of Talaja - Mahuva from 54.990 km. to 100.450 km. of Old NH-8E Package-II (National Highways Authority of India [NHAI]) (618835)	Gujarat	08/2020 (03/2021)	09/2022 (-)	698.4 (735.51)	418.26	100
903	Delhi-Amritsar-Katra Expressway Phase-I Pkg-III from Junction with Jind-Panipat road NH-352A near Gangana village to Junction with Jind-Karnal road NH-709A near Alewa village Km 60800 to Km 91400 (National Highways Authority of India [NHAI]) (618484)	Haryana	12/2020 (12/2021)	12/2023 (05/2024)	1606.27 (1813.91)	631.62	79
904	Delhi-Amritsar-Katra Expressway Phase-I Pkg-IV from Junction with Jind-Karnal road NH-709A near Alewa village to Junction with Ambala-Kaithal-Hissar road NH-152 near Kharak Pandwa village Km 91400 to Km 120250 (National Highways Authority of India [NHAI]) (618485)	Haryana	01/2021 (12/2021)	12/2023 (03/2024)	1306.95 (1578.66)	563.2	76
905	Gohana - Sonipat PKG-2 (National Highways Authority of India [NHAI]) (618580)	Haryana	01/2019 (07/2020)	07/2022 (-)	1275.31 (1957.44)	457.89	80
906	Jagadhari - Tajewala from Km -0.175 to 32.337 km of NH-344 (National Highways Authority of India [NHAI]) (618936)	Haryana	03/2022 (02/2023)	02/2025 (03/2026)	1269.5 (919.43)	610.57	53
907	Rehabilitation and Upgradation to 2-lane/Intermediate lane configuration of Ashyari-Shri Kyari Section km 50.000 to km 75.000 of NH-707 in the state of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode. (MoRTH) (618050)	Himachal Pradesh	08/2020 (09/2021)	09/2023 (11/2024)	345.89 (359.56)	146.64	0
908	Rehabilitation and Upgrading of NH-707 OLD 72-B Package - 2 Hewna to Ashyari (MoRTH) (618051)	Himachal Pradesh	04/2020 (03/2021)	03/2023 (03/2023)	242.8 (220.95)	74.87	98
909	Improvement/construction of existing CL-5 Road to NH Intermediate lane specification with hard shoulder from Km 133.000 to 166.000 net Length 33.000 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh on EPC mode under project Deepak, BRO (MoRTH) (618216)	Himachal Pradesh	03/2021 (07/2023)	06/2026 (-)	230.55 (203.15)	42.4	0
910	Improvement/construction of existing Class-5 Road to NH Intermediate lane specification with hard shoulder from existing Km 76/340 to 134/940 Design chainage from Km 76/300 to 133/000 net Length 56.700 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh Package I (MoRTH) (618217)	Himachal Pradesh	03/2021 (05/2023)	05/2026 (-)	314.67 (244.15)	76.97	0
911	Rehabilitation and Upgradation to 2-lane configuration of Kalwahn-Mandi Section km 208.950 to 250.592 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-3 (MoRTH) (618230)	Himachal Pradesh	08/2020 (10/2022)	04/2025 (-)	314.32 (314.32)	0	0
912	Rehabilitation and Upgradation to 2-lane configuration of Hamirpur-Karnohal Section km 141.00 to 181.00 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-1 (MoRTH) (618231)	Himachal Pradesh	08/2020 (06/2022)	12/2024 (-)	371.93 (371.93)	185.24	0
913	Nerchowk km 190.000 to Pandoh including Pandoh bypass km221.305 (National Highways Authority of India [NHAI]) (618850)	Himachal Pradesh	03/2016 (01/2018)	07/2020 (07/2025)	1464.12 (1651.67)	837.27	99



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
914	4L Sundar Nagar Bypass from Km.173.900 to Km.179.600 of NH-21 (National Highways Authority of India [NHAI]) (618852)	Himachal Pradesh	02/2022 (06/2022)	06/2024 (-)	191.11 (192.11)	181.27	100
915	Rehabilitation and Upgradation to 4L configuration & Strengthening of Sihuni to Rajol from Km 51.000 to Km 72.000 of NH-154 Package-IIA (National Highways Authority of India [NHAI]) (618878)	Himachal Pradesh	03/2022 (09/2023)	09/2025 (-)	696.65 (776.59)	288.14	82
916	Rehabilitation and Up-gradation of existing road to 2L PS from End of Hamirpur Bypass near Chilbahal to Bhangbar section from Km. 138.295 to Km.175.270 of NH-88 Pkg-IV (National Highways Authority of India [NHAI]) (618888)	Himachal Pradesh	03/2022 (04/2023)	04/2025 (-)	1146.19 (1358.62)	270.47	84
917	4L of Bhangbar Near Ranital to Kangra Bypass Section of Old NH-88 New NH-303,503 up to Intersection with NH-154 from Km 175.270 to Km 193.400 Pkg-VB (National Highways Authority of India [NHAI]) (618889)	Himachal Pradesh	03/2021 (12/2022)	12/2024 (-)	1322.95 (1829.49)	739.17	96
918	2L PS of Hamirpur Bypass from Km 121.175 to Km.138.295 of NH-103&3 (National Highways Authority of India [NHAI]) (618890)	Himachal Pradesh	08/2022 (10/2023)	10/2025 (-)	739.39 (754.82)	231.02	91
919	4L of Kathlighat to Shakral Village from Km 128.835 to Km 146.300 of NH- 5 Shimla Bypass - Pkg I (National Highways Authority of India [NHAI]) (618921)	Himachal Pradesh	03/2022 (04/2023)	04/2026 (-)	1703.48 (2648.8)	752.37	49
920	Up-gradation to 2-lane with Paved Shoulder from Km 12.850 to Km20.300 of 7.450Km length on Goha-Khellani section and a link road to Goha village of 2.016 km on NH-244 in UT of Jammu and Kashmir on EPC Mode Pkg-1 (NHIDCL) (618394)	Jammu and Kashmir	07/2020 (10/2020)	04/2022 (06/2025)	228.39 (225.37)	159.56	90
921	Construction & Upgradation to 2-lane with paved shoulder from Design Ch. Km 51700 at Premnagar km 66315 to Km 66535 New Thatri at Start of Km 83rd, Tunnel Km 82665 of 14.835 Km design length on Chenani-Sudhmahadev-Goha Khellani-Kishtwar-Vailoo Donipawa-Ashajipora section of NH-244 in the UT of J&K on EPC Mode under NHO-Gen Pkg - 2 (NHIDCL) (618395)	Jammu and Kashmir	03/2021 (08/2021)	03/2023 (07/2025)	512.43 (512.43)	0	0
922	Construction & Upgradation to 2 lane with paved shoulder from Design Km. 31.449 Khellani Ex. Km 44.946 to Km 51.700 Prem Nagar Ex. Km 68617 of 20.251 Km length on Khellani - Kishtwar - Chattroo section of NH-244 in the UT of J&K on EPC Mode under NHO-Gen PKG- 1 (NHIDCL) (618396)	Jammu and Kashmir	02/2021 (03/2021)	09/2021 (10/2024)	486.45 (486.45)	0	0
923	Up-gradation to 2-lane with Paved Shoulder from Km 20.300 to Km 29.030 of 8.730 Km length on Goha-Khellani section on NH-244 in UT of Jammu and Kashmir on EPC Mode Package II (NHIDCL) (618398)	Jammu and Kashmir	07/2020 (10/2020)	04/2022 (06/2025)	210.79 (210.79)	172.27	94
924	Construction of Kishtwar bypass with 2 lane with paved shoulder from Design Km. 80.675 Dulhasti to km 95.550 Bandarkoot of 14.88 km & a link road to Kishtwar town from 0000 to 1.871 of length 1.871 Km on Khellani - Kishtwar - Chattroo section in UT of Jammu and Kashmir on EPC Mode Pkg-4 (NHIDCL) (618399)	Jammu and Kashmir	03/2021 (08/2021)	08/2023 (11/2024)	859.67 (859.67)	0	0
925	Construction & Upgradation to 2-lane with paved shoulder from Design Km 67.805 at the end of Km 83rd Tunnel near Dhrabshalla Ex. Km 83905 to Km 80.675 start of Kishtwar Bypass - Dulhasti Ex. Km 970751 of 12.870 Km length on chenani-Sudhmahadev-Goha Khellani-Kishtwar-vailoo-Donipawa-Ashajipora seition of NH-244 in the UT of J&K on EPC Mode under NHO-Gen Pkg-3 (NHIDCL) (618400)	Jammu and Kashmir	03/2021 (07/2021)	12/2022 (10/2024)	398.51 (398.51)	0	0
926	Up-gradation to 4-lane with Paved Shoulder of Jammu-Akhnor road section of NH-144A from Ganesh Vihar Km 6.000 to Khati Chowk Km 26.350 in UT of Jammu and Kashmir on EPC basis Pkg-3A (NHIDCL) (618406)	Jammu and Kashmir	03/2018 (07/2019)	07/2021 (05/2022)	322.49 (322.49)	0	0
927	Jammu-Akhnor Road Pkg-I (NHIDCL) (618407)	Jammu and Kashmir	03/2018 (01/2023)	01/2025 (-)	245.3 (245.3)	0	0
928	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XV [Junction with Hiranagar Road near village Gurha Baildaran to Junction with Jammu Ring Road NH-244A near Jakh village from Km 468100 to Km 503250] (National Highways Authority of India [NHAI]) (618494)	Jammu and Kashmir	10/2021 (09/2022)	09/2024 (02/2026)	2714.95 (3716.56)	1602.61	88
929	4/6L Access Control Expressway from Design Chainage Km 515.000 to 528.300 Kunjwani to Sidhra Section of NH-44 and from Design Chainage Km 550.900 to Km 566.520 Domel to Katra Section Phase II-Package XVII (National Highways Authority of India [NHAI]) (618495)	Jammu and Kashmir	06/2022 (06/2023)	06/2025 (02/2026)	2894.74 (2894.74)	682.85	53
930	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XVI Existing Jakh Vijaypur-Kunjwani section of NH-44 including spur Connectivity to Jammu Airport NH-144A [Km 503500 to km 514500] (National Highways Authority of India [NHAI]) (618496)	Jammu and Kashmir	09/2021 (09/2022)	09/2024 (03/2026)	1821.72 (2522.56)	1120.3	92
931	Delhi Amritsar Katra Expressway Phase-II Pkg XVIII Development and Upgradation of Four lane Access Control Expressway from Design Chainage KM 530.00 to KM 545.300 Sidhra to Domel Section of NH-44 (National Highways Authority of India [NHAI]) (618497)	Jammu and Kashmir	12/2022 (11/2023)	11/2025 (-)	975.38 (975.38)	433.72	51
932	4L Ring road/bypass around Srinagar city from km 0.000 to km 42.100 Phase-I (National Highways Authority of India [NHAI]) (618541)	Jammu and Kashmir	03/2021 (08/2021)	02/2024 (10/2025)	2919.96 (2604.76)	1662.84	83
933	4L of twin tube tunnel configuration including approaches from Marog to Digidol from Km.154.210 to Km.158.650 North Bound and from Km.155.940 to Km.160.260 South Bound of Ramban to Banihal Pkg-I of Old NH-1A New NH-44 (National Highways Authority of India [NHAI]) (618543)	Jammu and Kashmir	07/2021 (08/2022)	08/2025 (06/2026)	1912.17 (1034.3)	272.7	21



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
934	4L twin tube tunnel including approaches from Digdol to Khuni Nallah North Bound connecting with existing major bridge on NB and South Bound connecting with Tunnel T4 ,Single tube tunnel of Ramban to Banihal Pkg-II of Old NH-1A New NH-44 (National Highways Authority of India [NHAI]) (618544)	Jammu and Kashmir	07/2021 (02/2022)	06/2024 (05/2025)	1401.87 (1020.99)	898.96	84
935	4L of Km.165.092 to Km.171.855 North Bound and from Km.166.895 to Km.173.638 South Bound, excl. certain reaches of North Bound and South Bound of Ramban to Banihal Pkg-III of Old NH-1A New NH-44 (National Highways Authority of India [NHAI]) (618545)	Jammu and Kashmir	07/2021 (02/2022)	08/2024 (-)	614.48 (444.76)	231.2	35
936	Construction of Tunnels/Viaducts at identified sliding/slip zones at Km 130.550 to Km.130.750 Km. 131.170 to Km. 131.763 Km. 132.560 to Km. 133.168 Km. 133.590 to Km. 133.743 and Km. 147.877 to Km. 148.715 of Udampur-Ramban section of NH-44 (National Highways Authority of India [NHAI]) (618546)	Jammu and Kashmir	09/2021 (04/2022)	10/2023 (06/2025)	442.14 (533.11)	324.74	36
937	2L NH-1 from km 8.660 to km 33.775 Sumbal to Wayul to 4L dual carriageway NH standard as part of Srinagar Ring Road PhaseII [Design Ch. 41.907 to Ch. 66.609] (National Highways Authority of India [NHAI]) (618547)	Jammu and Kashmir	11/2022 (12/2023)	06/2026 (-)	961 (643.64)	355.59	41
938	Stand-alone Ring road/bypass around Jammu City from Raya Morh km. -0.687 to Jagti km. 57.568 (National Highways Authority of India [NHAI]) (618548)	Jammu and Kashmir	12/2017 (01/2018)	01/2021 (10/2023)	2023.88 (2117.63)	54.24	99
939	Construction of twin tube tunnels on Jammu Kashmir Ring Road NH-244A Between Design Ch. 50600 to 51700 and design Ch. 53535 to 55700 on EPC mode under residual NHDP component of Bharatmala Pariyojna (National Highways Authority of India [NHAI]) (618549)	Jammu and Kashmir	11/2022 (06/2023)	06/2025 (03/2026)	242.65 (731.59)	637.61	81
940	Corridor Efficiency Improvement including removal of black spots in Lakhanpur - Samba section of NH-44 from Chainage Km. 16.300 to Km. 74.100 (National Highways Authority of India [NHAI]) (618550)	Jammu and Kashmir	06/2022 (12/2022)	06/2024 (05/2025)	855.74 (215.68)	176.32	70
941	Widening and Strengthening of existing paveemnt to two lane with paved shoulders from km 116.00 to km 176.355 of NH-75E in the State of Jharkhand on EPC mode. (MoRTH) (618060)	Jharkhand	01/2022 (01/2023)	07/2024 (-)	315.21 (315.21)	129.49	87
942	Widening to 2-lane with paved shoulder from km 0.00 to 44.00 Kuru-Ghaghra section of NH-143A including re-construction of culverts and bridges. (MoRTH) (618084)	Jharkhand	02/2020 (08/2021)	08/2023 (11/2023)	153.01 (133.67)	77	0
943	Widening and Strengthening/Reconstruction to Two Lane with Paved Shoulder/ Two Lane with paved shoulders with service road from km 0000 to km 42250 excluding design Ch. 03220 to 04200 & 28350 to 29060 of NH-320G in the state of Jharkhand under EPC mode (MoRTH) (618123)	Jharkhand	03/2022 (08/2023)	08/2025 (-)	423.18 (423.18)	4.11	0
944	4L of Palma to Gumla from km. 26.00 to km. 89.170 of NH-23 (National Highways Authority of India [NHAI]) (618642)	Jharkhand	03/2020 (04/2022)	03/2024 (10/2024)	1882.93 (1895.75)	826.77	98
945	4L of Ormanjhi-Gola section from Km 81.450 to Km 53.600 of NH- 320BPKG-II (National Highways Authority of India [NHAI]) (618644)	Jharkhand	02/2022 (06/2023)	06/2025 (-)	1214.93 (1462.19)	763.1	87
946	4L of Gola-BokaroJaina More section from Km 53.600 to Km 21.110 of NH-320PKG-1 (National Highways Authority of India [NHAI]) (618645)	Jharkhand	02/2022 (06/2023)	06/2025 (01/2026)	1007.97 (1030.64)	366.57	72
947	4L from km 196.87 Sankha to km 219.6 Khajuri on NH-75 [Rehla / Garhwa Bypass] (National Highways Authority of India [NHAI]) (618829)	Jharkhand	09/2020 (10/2021)	10/2023 (-)	1129.48 (1129.48)	527.11	93
948	4L from Km 147.450 Bhogu to Km 196.870 Sankha on NH-75 Sec-III (National Highways Authority of India [NHAI]) (618830)	Jharkhand	10/2022 (11/2023)	11/2025 (-)	1517.87 (1652.09)	962.12	76
949	4L of Mehgama - Hansdiha from km. 41.900 to km. 93.000 of NH -133A Pkg-II (National Highways Authority of India [NHAI]) (618946)	Jharkhand	03/2022 (05/2023)	05/2025 (03/2026)	1479.72 (1568.18)	849.01	98
950	4L of NH-80 from km 215.00 to km 260.00 Mirza Chauki to Farkka Pkg-I (National Highways Authority of India [NHAI]) (618947)	Jharkhand	03/2018 (12/2021)	07/2023 (06/2025)	1504.8 (1508.21)	643.11	75
951	4L of Basukinath- Deoghar Section of NH-114A (National Highways Authority of India [NHAI]) (618949)	Jharkhand	09/2022 (12/2023)	12/2025 (-)	1444.94 (1553.76)	593.59	76
952	Construction of Elevated corridor from Km. 135.650 to 136.300 on 63, from Km. 249 to Km. 250.050 on old NH-4 and from Km. 192.910 to Km. 193.350 on NH-218 from decongestion of traffic in Ranichennamma circle in Hubli city in the state of Karnataka on EPC basis (MoRTH) (617935)	Karnataka	08/2020 (06/2021)	06/2024 (08/2025)	298 (349.49)	141.25	52
953	Balance work of Rehabilitation and upgrading to 2lane/2lane with paved shoulder configuration and strengthening from from Km 343.80 to 400.33 of Gowribidanur-Chik Ballapur section in the state of Karnataka Under Annual Plan 2021-22 under EPC Mode.-952 (MoRTH) (617954)	Karnataka	03/2022 (02/2023)	02/2025 (-)	398.48 (398.48)	179.01	72
954	Widening to two lane with paved Shoulders from Km 40.00 to Km 75.00 Existing chainages of Mangalore - Tumkur section of NH-73 in the State of Karnataka on EPC Mode under Annual Plan 2021-22 Job No NH-73-KNT-2021-22-945 (MoRTH) (617955)	Karnataka	03/2022 (03/2023)	03/2025 (-)	718.52 (718.52)	260.03	72
955	Construction of Major Bridge at Km.180.865 across river Krishna on NH 167 Hagari Jadcherla section (MoRTH) (617989)	Karnataka	03/2019 (05/2019)	11/2021 (10/2024)	157.32 (187.61)	92.25	68



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
956	Widening to existing 2 lane with paved Shoulder to 4 Lane with paved shoulder from design Km 153.00 to 168.27 Mala Gate to Karkala of NH -169 on Shimoga - Mangalore section in the state of Karnataka on EPC mode under Annula Plan 2021-22 Job No. NH-169-KNT-2021-22-949 (MoRTH) (617998)	Karnataka	03/2022 (02/2023)	02/2025 (-)	177.94 (177.94)	94.59	75
957	Widening to 2-Lane with Paved Shoulders from Km 116.800 to 149.070 Design Changes on Hosadurga - Holalkere Section of NH-173 in the State of Karnataka on EPC mode under Annual Plan 2021-22 Job no. NH-173-KNT-2021-22-946 (MoRTH) (618000)	Karnataka	03/2022 (08/2022)	02/2024 (-)	170.34 (147.39)	60.21	92
958	Widening to 4 lane from Km. 133.00 to 158.04 design Chainage Km. 130.88 to 155.145 Shirur Cross to Gaddankeri of NH-367 in the State of Karnataka on EPC mode. Job No. NH-367-KNT-2021-22-930 (MoRTH) (618029)	Karnataka	01/2022 (01/2023)	01/2025 (-)	350.69 (312.06)	195.06	78
959	Widening to 2 lane with paved shoulder from Km. 103.225 Pattadakal to Km. 133.00 Shirur cross of NH-367 in the state of Karnataka on EPC Mode. Job No. NH-367-KNT-2021-22-934 (MoRTH) (618030)	Karnataka	02/2022 (11/2022)	05/2024 (-)	264.14 (264.14)	3.58	0
960	Balance work of Construction of Two/Four lane with paved shoulder from Km 422.000 to 523.600 Chitradurga to Shivamogga of NH-13 in the state of Kanataka on EPC mode. (MoRTH) (618031)	Karnataka	01/2021 (12/2021)	06/2024 (-)	516.96 (516.96)	333.48	0
961	Widening to intermediate/two lane to 2 lane with paved shoulder from Existing changes Km 112.750 to 142.00 Liingasur to Mudabal cross & from Km. 147.070 to Km. 149.070 Maski city limit of Jewargi Chamrajnagar setion of NH-150A in the state of Karnataka on EPC mode. Job No. NH-150A-KNT-2021-22-951 (MoRTH) (618087)	Karnataka	03/2022 (01/2023)	07/2024 (-)	255.88 (255.88)	175.75	93
962	Widening to 4 lane from Km 51.60 to 76.20 Hebri to Parkala and from Km 85.20 to 88.90 Karavali junction to Malpe of Thirthahalli-Udupi-Malpe Section of NH-169A in the State of Karnataka on EPC Mode under Annual plan 2021-22 Job No. NH-169A-KNT-2021-22-927 (MoRTH) (618109)	Karnataka	01/2022 (12/2022)	12/2024 (-)	355.72 (355.72)	170.76	76
963	Construction of Major Bridge Across Sharavathi Backwaters and approaches between Ambargodu and Kalasavalli Near Sigandhur in Sagar Taluk on NH 369E in the State of Karnataka on EPC mode. Job No. NH-369E-KNT-2018-19-895 dated 06.03.2019. (MoRTH) (618144)	Karnataka	03/2019 (12/2019)	12/2022 (-)	423.15 (423.15)	0	0
964	4/6L of Bangalore - Pune Section of bypass connecting Dharwad - Hubli from km. 403.80 to km. 433.20 (National Highways Authority of India [NHAI]) (618517)	Karnataka	12/2021 (03/2023)	09/2025 (-)	1135.39 (763.36)	659.51	76
965	6L of MH/KN Border Nimal Village to KN/TS Border Singnodi Village from Km. 26.000 to Km. 97.000 in Gulbarga of NH-150C Pkg-II (National Highways Authority of India [NHAI]) (618630)	Karnataka	02/2022 (12/2022)	06/2025 (05/2026)	2355.56 (1923.3)	696.37	55
966	4L of Addahole Near Gundya to Bantwal Cross section Pkg-02 from Design Km 270.270 to Design km 318.55 including flyover at Kalladka Town including approaches from Km. 311.57 to Km. 313.67 of NH-75 Old NH-48 (National Highways Authority of India [NHAI]) (618702)	Karnataka	12/2020 (11/2021)	11/2023 (04/2026)	1660.19 (1318.24)	1235.46	89
967	Belakeri Port to Kumta - Sirsi road from km 0.00 - km 4.265 of Belekeri Port Road Link Rd. and km 4.965 - km 60.00 of SH-69 (National Highways Authority of India [NHAI]) (618799)	Karnataka	03/2018 (12/2020)	12/2022 (12/2025)	456.32 (456.79)	381.34	79
968	4L of Bettadahalli- Shivamogga section from Km.170.415 to km. 226.750 of NH-206 Tumkur- Shivamogga Pkg-IV (National Highways Authority of India [NHAI]) (618887)	Karnataka	01/2019 (10/2021)	10/2023 (10/2024)	2082.98 (2545.11)	859.62	80
969	4L of Sannur to Bikarnakatte section from Km 691.350 to Km 736.362 of NH-169 Karkala - Mangalore Package-III (National Highways Authority of India [NHAI]) (618896)	Karnataka	03/2021 (10/2022)	10/2024 (06/2026)	1386.41 (2038.71)	900.61	60
970	Widening to 2 Lanes with paved shoulders from Km.87/000 to 133/720 Nattukal to Thanau Jn. in Palakkad of NH-966 Old NH-213 on EPC mode Basis under NHO Annual Plan 2016-17 in the state of Kerala (MoRTH) (618070)	Kerala	02/2017 (08/2017)	08/2019 (06/2025)	294.28 (315.63)	0	98
971	6L of Chengala - Neeleshwaram from km. 56.200 to km. 93.468 (National Highways Authority of India [NHAI]) (618595)	Kerala	06/2020 (10/2021)	04/2024 (-)	1746.45 (2538.06)	775.85	79
972	6L of Taliparamba to Muzhappilangad from Km 134.650 to Km 170.6 of NH-66 (National Highways Authority of India [NHAI]) (618596)	Kerala	08/2020 (11/2021)	05/2024 (08/2025)	2714.6 (3557.65)	1006.75	80
973	6L of Azhiyur-Vengalam from km. 189.200 to km. 230.400 of NH-66 (National Highways Authority of India [NHAI]) (618597)	Kerala	10/2020 (10/2021)	07/2024 (-)	3205.77 (3898.46)	771.21	57
974	6L Minor Bridge Paloli Palam at km. 203.160 & Major Bridge Morad at km. 204.895 and allied works (National Highways Authority of India [NHAI]) (618598)	Kerala	03/2020 (12/2020)	06/2022 (02/2024)	210 (216.94)	70.89	93
975	6L of Ramanatukkara Junction to start of Valanchery bypass section of NH-66 (National Highways Authority of India [NHAI]) (618599)	Kerala	01/2021 (01/2022)	07/2024 (03/2025)	4924.11 (4919.46)	1668.84	99
976	6L of Valanchery bypass to Kappirikkad of NH 66 from km. 298500 to km 335850 (National Highways Authority of India [NHAI]) (618600)	Kerala	02/2021 (01/2022)	07/2024 (03/2025)	4023.94 (4023.94)	1348.96	98
977	6L of Kappirikkad to Thalikulam section from km 335.85 to km 369.015 of NH - 66 old NH-17 (National Highways Authority of India [NHAI]) (618601)	Kerala	06/2021 (09/2022)	01/2025 (10/2025)	4225.59 (4225.59)	646.6	85



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
978	6L of Thalikulam to Kodugallur section from km 369.015 to km 397.850 of NH - 66 old NH-17 (National Highways Authority of India [NHAI]) (618602)	Kerala	06/2021 (09/2022)	02/2025 (11/2025)	4302.06 (4302.06)	618.13	80
979	6L of Kodugallur to Edappally section from km 397.750 to km 423.780 of NH - 66 old NH-17 (National Highways Authority of India [NHAI]) (618603)	Kerala	11/2021 (10/2022)	04/2025 (-)	3465.82 (3606.2)	767.36	64
980	Aroor-Thuravoor Thekku (National Highways Authority of India [NHAI]) (618604)	Kerala	08/2022 (02/2023)	01/2026 (-)	2429.52 (2382.83)	1567.88	81
981	Thuravoor Thekku-Paravoor (National Highways Authority of India [NHAI]) (618605)	Kerala	09/2021 (03/2022)	09/2024 (03/2026)	2878.97 (2638.67)	1880.96	65
982	Paravoor-Kottankulangara (National Highways Authority of India [NHAI]) (618606)	Kerala	12/2021 (08/2022)	02/2025 (-)	3273.61 (3200.24)	1131.86	61
983	Kottankulangara- Start of Kollam Bypass (National Highways Authority of India [NHAI]) (618607)	Kerala	06/2021 (04/2022)	10/2024 (-)	2842.14 (3680.49)	684.52	73
984	Widening/Development of Existing NH-85 from Km 0.000 to Km 124.636 section to 2L/LPS section in the state of Kerala on EPC Mode under Bharatmala Pariyojana (National Highways Authority of India [NHAI]) (618708)	Kerala	09/2022 (06/2023)	06/2025 (-)	1187.47 (1265.47)	545.52	50
985	Kargil Zanskar Road (NHIDCL) (618408)	Ladakh	03/2021 (07/2021)	01/2023 (03/2025)	398.37 (398.37)	0	0
986	Widening & Up-gradation to 2 lane with Paved shoulder of NH-301 Kargil- Zanskar Road from Design km 57.000 Ex. Km. 57.905 to Km 87.000 Ex. Km. 88.2491 of 30.000 Km length Pkg-III (NHIDCL) (618409)	Ladakh	03/2021 (07/2021)	01/2023 (02/2025)	381.01 (381.01)	0	0
987	Widening & Up-gradation to 2 lane with paved shoulder of NH-301 Kargil- Zanskar Road from Design Km .30.040 Ex. Km. 30.000 to Design Km 57.000 Ex. Km. 57.905 of 26.960 Km length Pkg-II (NHIDCL) (618410)	Ladakh	03/2021 (07/2021)	01/2023 (12/2026)	404.89 (404.89)	0	0
988	Rehabilitation and upgradation Umaria to Shahdol section of NH-78 from Existing Km. 68/4 to Km. 142/2 to 2LPS including construction of Birshinghpur and Shahdol Bypass on EPC mode under NHDP-IVA (MoRTH) (617911)	Madhya Pradesh	03/2015 (08/2015)	07/2017 (07/2023)	511.83 (613.16)	0	0
989	Upgradation of Dindori-Sagartola-kabichabutra MP-CG border section of NH -45 from km 000Design to km 77.00 Design to Two lane with paved shoulder configuration along with one time improvement in 04 nos. of bypaased built-up areas in a total length of 9.1 km in the state of Madhya Pradesh on EPC mode. (MoRTH) (617915)	Madhya Pradesh	01/2022 (09/2023)	09/2025 (-)	329.14 (319.09)	0	0
990	Upgradation & widening of Jharkheda- Berasia - Dholkhedi from design km 0000 to km 87900 Design length 87.90km of NH-346 including 3 nos. bypasses of 13.10 Km in the State of Madhya Pradesh under EPC mode. (MoRTH) (618019)	Madhya Pradesh	03/2022 (05/2023)	05/2025 (-)	365.21 (365.21)	0	0
991	Rehabilitation & Upgradation of KurwaiMungaoliChanderi Road section of NH-346, from Design Chainge 0.000 to 81.300 Km Total length 83.1 km to Two lane with paved shoulder configuration along with One time improvement in 07 nos of bypassed built-up areas in a total length of 22.615 km in the state of Madhya Pradesh on EPC mode. (MoRTH) (618020)	Madhya Pradesh	03/2022 (02/2023)	02/2025 (07/2025)	386.49 (386.49)	160.38	0
992	Construction of Mihona bypass, Lahar bypass, Daboh bypass & Bhander Bypass total length 20.60 km to 2-lane with paved shoulder from on Mihona-Bhander-MP/UP border section of NH 552E in the State of Madhya Pradesh on EPC mode (MoRTH) (618045)	Madhya Pradesh	03/2022 (06/2023)	12/2024 (-)	179.18 (179.18)	71.77	67
993	Construction of Kaithi-Padaria Kala bypass, Patna-Tamoli bypass, Jaso bypass and Nagod bypass total length 15.44 Km to 2-lane with paved shoulders flexible pavement on NH-943 in the State of Madhya Pradesh on EPC Mode. (MoRTH) (618068)	Madhya Pradesh	03/2022 (10/2023)	10/2025 (-)	158.36 (158.36)	0	0
994	Upgradation of Nasrullagani-Rehti-Budhni Scction to 2-lane with paved shoulder from Km 0150 to Km 50500 of NH-146B in the state of Madhya Pradesh on EPC mode. (MoRTH) (618085)	Madhya Pradesh	12/2021 (04/2023)	10/2024 (02/2025)	305.12 (293.74)	0	0
995	Indore - Edlabad Pkg-II [Tejainagar to Balwara] (National Highways Authority of India [NHAI]) (618621)	Madhya Pradesh	03/2022 (01/2023)	01/2025 (-)	1162.8 (1530.82)	484.47	79
996	4L of Indore - Boregaon Pkg-III [Balwara to Dhangaon] from km. 42.260 to km. 82.660 of NH347BG & 753L (National Highways Authority of India [NHAI]) (618622)	Madhya Pradesh	01/2021 (04/2022)	04/2024 (05/2025)	1001.69 (888.81)	679.16	87
997	4L Greenfield Rudhi to Deshgaon Pkg V of Betul-Khandwa/Deshgaon (National Highways Authority of India [NHAI]) (618654)	Madhya Pradesh	11/2022 (10/2023)	10/2025 (03/2026)	521.21 (469.68)	162.85	59
998	i 4L Vidisha to Hinotiya from km 0.000 to Km 27.000 Vidisha Mehulwa-Talbehat Pkg-I Section of NH- 346 and ii 4L Vidisha to Morikori from Km 39.000 to 59.476 section of NH-146 (National Highways Authority of India [NHAI]) (618663)	Madhya Pradesh	09/2022 (12/2023)	12/2025 (05/2026)	1003.87 (941.12)	305.39	70
999	Berkhedi to Godpehra on NH-44 Sagar link road (National Highways Authority of India [NHAI]) (618664)	Madhya Pradesh	02/2022 (11/2022)	11/2024 (08/2025)	524.84 (471.31)	292.9	0
1000	4L of Sagar - Mohari from Km.8 to Km.50 Pkg-I (National Highways Authority of India [NHAI]) (618665)	Madhya Pradesh	03/2021 (04/2022)	04/2024 (-)	790.78 (660.38)	411.38	75



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1001	Indore - Harda Pkg-I [Indore to Raghav Garh from km. 0.25 to km. 26.903] (National Highways Authority of India [NHAI]) (618694)	Madhya Pradesh	01/2022 (11/2022)	10/2024 (07/2025)	1011.29 (813.03)	326.05	73
1002	Indore - Harda Pkg-III [Nanasa to Pidgaon Section from km 95.000 to km 142.445] (National Highways Authority of India [NHAI]) (618695)	Madhya Pradesh	01/2020 (10/2021)	10/2023 (-)	1146.22 (1240.64)	386.74	78
1003	Balance work of 4L of Nauradehi Sanctuary de-scoped stretch of Hiran River to Sindoor River from Km. 66.00 to 130.00 NH-12 New NH-45 (National Highways Authority of India [NHAI]) (618701)	Madhya Pradesh	01/2021 (07/2021)	07/2023 (04/2024)	178.18 (153.15)	142.2	57
1004	4L of Chandesara to Khedakhajuriya from Km. 0.000 to - 750 & Km 0.000 to km 41.400 of NH-148NG Pkg-I (National Highways Authority of India [NHAI]) (618735)	Madhya Pradesh	12/2021 (09/2022)	05/2024 (12/2024)	909.84 (976.55)	399.02	99
1005	2L PS of Hinotiya-Mehulwa section of NH-346 from Km. 27.000 to Km 75.700 Vidisha Mehulwa-Talbehat Pkg-II Section of NH- 346 (National Highways Authority of India [NHAI]) (618751)	Madhya Pradesh	10/2022 (09/2023)	09/2025 (04/2026)	581.65 (592.71)	182.7	55
1006	Construction of 4 Lane Flyover at Nagpur RTO Chowk To Nagpur University Campus from Ch 2/250 to 5/100 and 4 lane flyover at wadi/midc junction from km 8/360 to km, 10/300 on NH 53 in state of Maharashtra. (MoRTH) (617917)	Maharashtra	03/2021 (03/2022)	03/2024 (04/2025)	478.83 (490.52)	0	95
1007	Construction of New Four Lane Bypass to Parbhani City Parwa to Asola Km 463/265 to Km 481/180 Design Ch. 19220 to Ch. 34434 Length-15.214 Km section of NH-61 on EPC mode in the State of Maharashtra. (MoRTH) (617932)	Maharashtra	03/2022 (07/2023)	10/2024 (05/2025)	496.64 (496.64)	0	60
1008	Up-gradation to four lane/ Two lane with paved shoulders configuration of Kalyan - Murbad - Malshej Ghat - Nirmal Road NH- 61 km 15/200 to Km 38/00 and from Km. 58/00 to Km 84/00 Design length 48.58 km of NH-61 on EPC Mode in Thane District in the state of Maharashtra (MoRTH) (617933)	Maharashtra	02/2023 (03/2024)	08/2026 (-)	984.07 (984.07)	0	74
1009	Nasratpur to Barasgaon section of NH-61 2L / 4L PS from Km.514/00 to 558/200 (MoRTH) (617934)	Maharashtra	07/2017 (09/2017)	09/2019 (12/2020)	406.54 (406.54)	0	95
1010	Kashedi ghat tunnel NH-66 [Bhogaon Khurd - Kashedi section] 4 lanes under NHDP on EPC mode (MoRTH) (617944)	Maharashtra	09/2018 (10/2018)	04/2021 (04/2021)	680.43 (701.46)	0	98
1011	Arawali Kante section of NH-17New NH-66 4L PS from Km.241/300 to 281/300 (MoRTH) (617947)	Maharashtra	03/2016 (11/2017)	11/2019 (02/2024)	1006.99 (1443.09)	0	0
1012	Kante - Wakad section of NH-66 4L PS from Km.281/300 to 332/200 (MoRTH) (617948)	Maharashtra	03/2016 (11/2017)	11/2019 (03/2023)	1117.75 (2020.56)	171.12	90
1013	Kopargaon to Savali Vihir section (MoRTH) (617965)	Maharashtra	06/2022 (01/2023)	07/2024 (09/2025)	195.38 (195.38)	0	77
1014	Rehabilitation/ Upgradation of existing Highway to four lane standards in Kurkheda town from km.413257 to km 410775, Two lane in Shankarpur Gurnuli km 42400 to km 43100 section and Reconstruction of Major Bridge at Ch. 448558 Bhuti Nallah and Ch. 411695 Sati River bridge, Minor Bridge at Ch. 411477 and Ch. 405800 Lendhari Bridge of NH 543 Bhamhapuri-wadsa-kurkheda-korchi-Deori-Amgaon road on EPC mode in the State of Maharashtra (MoRTH) (618042)	Maharashtra	03/2022 (11/2023)	05/2025 (-)	163.86 (163.86)	0	33
1015	Rehabilitation & Up-gradation of Sabalkhed to Ashti Section from Km 37900 to Km 55100 & Chinchpur to Jamkhed Section from km 70000 to km 72922 of NH-561 to Two lane with Paved shoulder/ Four lane configuration in the State of Maharashtra on EPC Mode Length20.122km. (MoRTH) (618046)	Maharashtra	03/2022 (04/2023)	09/2024 (-)	213.33 (213.33)	0	95
1016	Construction of four-lane Concrete Road from Police Headquarter Gondia City to Rawanwadi Village Birsi Airport Junction from design km 0.000 to km 15.781 existing km 39/720 of NH-753 to existing Km 8/400 of NH 543 on sections from Kohmara-Goregaon- Police HeadquarterKaranja - Collector Office Square - Balaghat T Point-Rawanwadi- Rajegaon of NH-753 and NH-543 in Gondia District in the state of Maharashtra. Total Length of the project 15.781 Km. (MoRTH) (618059)	Maharashtra	02/2023 (02/2024)	08/2025 (-)	328.11 (328.11)	0	34
1017	Rehabilitation/Upgradation of existing Highway to 2LPS/4 lane of Dhawali to Rajoli from Design Km.149476 to 163476 existing Km.150000 to 164000, Pandhasala to Mohadongri from design Km.170476 to 181476 existing Km.171000 to 182000, Ambeshivni Fata to Bodli from design Km.183476 to 185476 existing Km.184000 to 186000 and Made Tukum to Gadchiroli from design Km.188476 to 189476 existing Km.188000 to 18900 having length 28 km of NH-930 of Dhawali to Gadchiroli road in the (MoRTH) (618065)	Maharashtra	03/2022 (03/2024)	09/2025 (-)	316.44 (316.44)	0	25
1018	Rehabilitation & Up-gradation of Mudkhed to Nanded section from Km. 372000 to Km 388400 of NH 161A i.e. Nanded-Bhokar-Himayatnagar-Kinwat-Mahur-Arani Road Design chainage from Km 372000 Mudkhed to Km 387650 Nanded of NH 161A Length 15.65 Km to 2/4Lane with paved shoulders configuration in the State of Maharashtra on EPC mode. (MoRTH) (618089)	Maharashtra	03/2022 (04/2023)	04/2025 (04/2025)	206.54 (206.54)	0	63
1019	Sarsam - Kothari of NH-161A - 2L PS from Km.33/00 to 90/00 (MoRTH) (618090)	Maharashtra	02/2017 (06/2017)	06/2019 (10/2022)	545.64 (545.64)	0	97
1020	Pen to Khopoli 2LPS (MoRTH) (618094)	Maharashtra	03/2018 (06/2018)	12/2019 (10/2022)	369.39 (369.39)	143.65	86
1021	Guhagar - Rampur - 2L-PS - km 0/00 Guhagar to 26/230 Rampur and 40/00 Mirjoli to 53/600 Sati on NH-166E (MoRTH) (618097)	Maharashtra	01/2017 (06/2017)	06/2019 (09/2022)	407.2 (407.2)	0	91



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1022	Upgradation of existing 2 lane flexible pavement to 2 lane paved shoulders rigid pavement from design chainage Km 66.00 to Design Km 82.440 Start of Kolhapur Municipal corporation near Phulewadi to kale, design length 16.440 Km section on Talere Gaganbawada-Kolhapur road NH 166G in the state of Maharashtra on EPC mode (MoRTH) (618098)	Maharashtra	03/2021 (11/2022)	05/2024 (05/2025)	167.97 (167.97)	0	83
1023	Strengthening and Widening of road Sakoli- Wadsa-Armori-Gadchiroli-Ashti- Allapalli - Sironcha National highway NH 353C in Km 262/00 to 321/00 including 16 minor Bridges and 2 Major Bridge Total length 59 Km section from repalpalli to sironcha in Gadchiroli Dist in the State of Maharashtra. (MoRTH) (618133)	Maharashtra	03/2021 (06/2022)	05/2024 (07/2025)	280.57 (280.57)	0	0
1024	Upgradation and Rehabilitation of Section of NH 361 F from Parli 00/000 to Gangakhed 30/400 to Two Lanes with paved shoulder / Four lane configurations on EPC mode in the State of Maharashtra. (MoRTH) (618136)	Maharashtra	03/2021 (02/2022)	09/2023 (08/2024)	224.44 (224.44)	0	87
1025	Mhaswad to Tembhurni section of NH-548C - 2L PS (MoRTH) (618152)	Maharashtra	01/2017 (08/2017)	07/2019 (07/2019)	488.6 (488.6)	0	96
1026	Satara to Mhaswad (MoRTH) (618153)	Maharashtra	01/2017 (08/2017)	08/2019 (-)	653.46 (653.46)	0	98
1027	Rehabilitation & upgradation of Jamkhed to Sautada Section of NH548 D from km 195.375 to km 208.774, Length 13.399 Km to 2L PS /4L configuration with rigid pavement in the state of Maharashtra on EPC mode. (MoRTH) (618154)	Maharashtra	03/2022 (01/2023)	07/2024 (-)	157.62 (157.62)	0	62
1028	Paithan - Shirur section 2LPS Km 0.0 to 55.00 (MoRTH) (618172)	Maharashtra	03/2017 (06/2017)	06/2019 (03/2022)	341.8 (341.8)	0	80
1029	Shirur-Kharda section from 55937 km to 114486 km to 2LPS/4L (MoRTH) (618173)	Maharashtra	02/2017 (06/2017)	06/2019 (03/2022)	381.77 (381.77)	0	83
1030	Rehabilitation and Upgradation of Satana to Mangrul Chandwad Section of NH752 G Design Ch Km 64.000 to Ch Km 101.140 two lane with paved shoulder/four lane configuration in the state of Maharashtra on EPC mode. (MoRTH) (618175)	Maharashtra	03/2022 (05/2023)	05/2025 (-)	428.8 (428.8)	0	62
1031	Pal Phata Phulambri - Khultabad 2LPS (MoRTH) (618177)	Maharashtra	03/2018 (06/2018)	12/2019 (06/2021)	227.19 (227.19)	0	99
1032	Pune raigarh District Border To Mangaon Ch 69000 to 103775 NH-753F (MoRTH) (618180)	Maharashtra	03/2018 (06/2018)	12/2019 (-)	223.46 (223.46)	0	89
1033	Rehabilitation / Upgradation to 4 Lane with Paved shoulder of Existing Section in Sillod Town with Design Ch. Km54500 to Km 60679 [Length6.179 km] section of NH 753F Aurangabad-Jalgaon road on EPC Mode in the State of Maharashtra (MoRTH) (618181)	Maharashtra	03/2023 (01/2024)	07/2025 (-)	153.79 (153.79)	0	93
1034	Rehabilitation and Up-gradation to 2 lane with paved shoulder configuration of Mahud Sangola road NH 965 G 159400 to 161900and 162400 to 183960 Design Chainage from km. 32/300 to km. 34/800 and km. 35/800 to km. 56/860 Rigid Pavement on EPC mode in the State of Maharashtra. (MoRTH) (618188)	Maharashtra	02/2023 (11/2023)	05/2025 (-)	253.78 (253.78)	0	99
1035	Balance work of Rehabilitation and Up-gradation to 2-lane road with paved shoulders configuration for NH- 965DD from Pacharal-Mandangad-Mhapral-Rajewadi Upto Junction of NH-66 Ch-22700 to 75100 Km and Ambadave connector Birth place of Dr. Babasaheb Ambedkar Ch-0000 to 7325 Km length Km 59.725 in the state of Maharashtra on EPC mode. Balance Work (MoRTH) (618198)	Maharashtra	03/2018 (01/2022)	01/2024 (-)	388.93 (341.69)	0	81
1036	Rehabilitation, Upgradation & Widening of existing Highway to Rigid Pavement 2 Lane with Paved Shoulder of NH 965DD from Lonand Shirval-Bhor Mandangad-Pchral Section ShindewadiPhata to Varandah Ghat Dist Border from Km 33/550 to 92/550 in the state of Maharashtra on EPC mode. (MoRTH) (618199)	Maharashtra	02/2023 (07/2024)	07/2026 (-)	723.13 (723.13)	0	34
1037	Vadodara Mumbai Expressway Phase II - Pkg XI [Km. 77.000 to Km. 103.400] Ganjad - Talsari (National Highways Authority of India [NHAI]) (618468)	Maharashtra	06/2020 (05/2022)	05/2024 (01/2025)	1524.71 (1913.95)	813.07	99
1038	Vadodara Mumbai Expressway Phase II - Pkg XIII [Km. 26.582 to Km. 50.700] Shirsad - Masvan (National Highways Authority of India [NHAI]) (618469)	Maharashtra	06/2020 (02/2022)	02/2024 (06/2025)	3536.9 (4679.54)	1707.29	87
1039	Vadodara Mumbai Expressway Phase II - Pkg XIV [Km. 3.000 to Km. 20.200 of Spur] Shirsad - Akloli (National Highways Authority of India [NHAI]) (618470)	Maharashtra	05/2021 (11/2022)	05/2024 (06/2025)	2058.79 (2324.72)	541.49	80
1040	Vadodara Mumbai Expressway Phase II - Pkg XV [Km. 20.200 to Km. 43.000 of Spur] Akloli - Amne (National Highways Authority of India [NHAI]) (618471)	Maharashtra	05/2021 (11/2022)	05/2024 (11/2025)	2610.88 (2918.39)	571.76	90
1041	Vadodara Mumbai Expressway Phase II - Pkg XVI [Km. 43.000 to Km. 69.800 of Spur] Amne - Bhoj (National Highways Authority of India [NHAI]) (618472)	Maharashtra	06/2021 (11/2022)	10/2024 (06/2025)	4051.8 (4315.56)	824.37	86
1042	Vadodara Mumbai Expressway Phase II - Pkg XVII [Km. 69.800 to Km. 79.783 of Spur] Bhoj - Morbe (National Highways Authority of India [NHAI]) (618473)	Maharashtra	09/2021 (01/2023)	07/2025 (-)	2208.68 (2463.02)	802.11	84



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1043	Tunnel at Khambataki Ghat Section and its approaches from existing Km. 771.730 to existing Km. 782.000 (National Highways Authority of India [NHAI]) (618512)	Maharashtra	11/2017 (02/2019)	02/2022 (08/2025)	907.03 (816.12)	520.53	85
1044	6L of Kagal-Satara section from Km 592.500 to Km 658.000 of NH-48 Pkg-I (National Highways Authority of India [NHAI]) (618513)	Maharashtra	12/2021 (01/2023)	01/2025 (04/2026)	2111.95 (1435.46)	613.7	49
1045	6L of Kagal-Satara section from Km 658.000 to Km 725.000 of NH-48 Pkg-II (National Highways Authority of India [NHAI]) (618514)	Maharashtra	12/2021 (12/2022)	12/2024 (-)	2330.71 (317.4)	171.02	70
1046	Flyover at Km.544.650 including ROB, Service Roads ,Footpath for RCC drains on urban link to Nagpur -Raipur road Pardi octroi Naka to Itwari (National Highways Authority of India [NHAI]) (618555)	Maharashtra	12/2015 (03/2016)	03/2019 (03/2019)	1097.81 (758.4)	25.94	0
1047	4L of Indora Chowk to Pachpaoli and Agrasen Chowk - Ashoka Chowk (National Highways Authority of India [NHAI]) (618557)	Maharashtra	03/2023 (07/2023)	06/2026 (-)	1038.84 (918.53)	551.23	69
1048	4L Mitigation Measure structures on CH/MH Border to Wainganga Bridge Section of NH-6 New NH-53 (National Highways Authority of India [NHAI]) (618588)	Maharashtra	02/2021 (11/2021)	11/2023 (01/2025)	540.24 (468.92)	464.23	70
1049	Balance work of 4L Panvel to Indapur section of NH-66 Old NH- 17 from km 0.000 Panvel to km 42.300 Kasu (National Highways Authority of India [NHAI]) (618594)	Maharashtra	12/2022 (03/2023)	10/2024 (-)	329.82 (196.87)	183.56	43
1050	Bodhre - Dhule (National Highways Authority of India [NHAI]) (618693)	Maharashtra	02/2021 (01/2022)	07/2024 (-)	1344.78 (1292.7)	712.97	78
1051	4L of Ratnagiri - Kolhapur section from km 67.140 to km 112.340 of NH-166 Pkg II (National Highways Authority of India [NHAI]) (618836)	Maharashtra	02/2022 (05/2023)	05/2025 (-)	1985.38 (1798)	300.57	62
1052	4L of Ratnagiri - Kolhapur section from km 112.340 to km 145.300 of NH-166 PkgIII (National Highways Authority of India [NHAI]) (618837)	Maharashtra	02/2022 (05/2023)	05/2025 (05/2026)	1939.23 (1910.41)	389.93	62
1053	4L of Nagpur-Katol Section from Km. 13.00 to Km. 62.900 of NH-353J (National Highways Authority of India [NHAI]) (618937)	Maharashtra	02/2021 (10/2021)	10/2023 (-)	1166.96 (1432.82)	836.13	56
1054	Widening/Improvement of existing 2-Lane road to 4-Lane Divided Highway from Sekmai to Nilakuthi section of Imphal-Kohima Road Design Chainage from Km 297700 to Km 308729 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5B (NHIDCL) (618298)	Manipur	03/2021 (07/2021)	01/2023 (06/2025)	211.7 (211.7)	209.48	78
1055	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Taphukuki to Daili section of Imphal-Kohima road NH-02 Design Chainage from Km 262175 to Km 274610 in the state of Manipur on EPC mode Pkg-4A (NHIDCL) (618300)	Manipur	09/2020 (10/2020)	04/2022 (07/2025)	379.39 (379.39)	0	78
1056	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 16.900 to Km 30.970 of NH-202 in the state of Manipur on EPC mode Package-2 (NHIDCL) (618302)	Manipur	03/2020 (07/2020)	06/2022 (12/2025)	256.04 (256.04)	0	35
1057	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 0.000 to Km 16.900 of NH-202 in the state of Manipur on EPC mode Package-1 (NHIDCL) (618303)	Manipur	03/2020 (07/2020)	06/2022 (04/2025)	222.77 (222.77)	0	37
1058	Widening to 2 lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 169570 Near Nungkao village under Tamenglong District to km 205974 near Jiribam Bridge under Jiribam district under NHO-NE PKG-7 (NHIDCL) (618333)	Manipur	01/2023 (12/2023)	12/2025 (-)	760.16 (760.16)	365.34	75
1059	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 131.280 to km 169.570 on EPC mode in Manipur under NHO-TSP PKG-6 (NHIDCL) (618334)	Manipur	12/2021 (02/2023)	02/2025 (05/2025)	504.76 (504.76)	269.89	0
1060	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from Km 101280 Near Khongsang Village to Km 131280 near Pulton Kambiron Village on EPC Mode in Manipur PKG-5 (NHIDCL) (618335)	Manipur	12/2021 (11/2022)	05/2024 (02/2026)	410.68 (410.68)	309.93	80
1061	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 66.110 km to 101.280 Km Existing Chainage km 67.496 to km 103.557 on EPC Mode in Manipur PKG-4 (NHIDCL) (618336)	Manipur	09/2021 (06/2022)	12/2023 (08/2025)	579.63 (579.63)	355.94	79
1062	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 33.000 km to 66.390 Km Existing Chainage from km 33.395 to km 67.496 on EPC Mode in Manipur PKG-3 (NHIDCL) (618337)	Manipur	03/2021 (09/2021)	03/2023 (07/2025)	467 (467)	552.2	82
1063	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from Design Chainage 69.875 Km to 121.769 Km in the State of Manipur on EPC mode Package-3 (NHIDCL) (618344)	Manipur	03/2021 (08/2021)	08/2023 (04/2025)	673.27 (673.27)	480.59	50
1064	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section from Km 48.587 to Km 69.875 in the State of Manipur on EPC mode under NHO Package-2B (NHIDCL) (618345)	Manipur	06/2020 (08/2020)	08/2022 (02/2023)	365.53 (365.53)	168.23	64
1065	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 32.835 to km 48.587 in the State of Manipur on EPC mode under NHO Package-2A (NHIDCL) (618346)	Manipur	04/2020 (07/2020)	06/2022 (02/2023)	232.99 (232.99)	127.15	81



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1066	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 13.747 to km 32.835 in the State of Manipur on EPC mode under NHO Package-1B (NHIDCL) (618347)	Manipur	04/2020 (07/2020)	06/2022 (04/2025)	241.52 (241.52)	0	45
1067	Construction of of 2 -Lane with paved shoulders road from Tamenglong-Tousem-Lisang-Mahur Road NH-137 starting near Dialong Village from km 10.000 at Dialong to km 31.430 near Old Tamenglong , near Barak River on EPC Mode Package-2 (NHIDCL) (618355)	Manipur	07/2021 (09/2021)	03/2023 (12/2025)	483.87 (483.87)	351.99	92
1068	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur in the state of Manipur from km 31.430 at Old Tamenglong to km 43.480 ending near Phelong on EPC Mode Package-3 (NHIDCL) (618356)	Manipur	03/2021 (06/2021)	12/2022 (12/2025)	234.08 (234.08)	0	94
1069	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 in Manipur starting from km 54.180 near Azuram to km 80.630 near Mandeu on EPC Mode Package 5 (NHIDCL) (618357)	Manipur	09/2021 (11/2021)	05/2023 (04/2025)	477.86 (477.86)	330.1	84
1070	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 starting from km 80.630 near Mandeu to km 96.870 near Jiri River on EPC Mode Package-6 (NHIDCL) (618358)	Manipur	09/2021 (11/2021)	05/2023 (07/2027)	311.18 (311.18)	223.12	84
1071	Construction of 2-laning with Hard shoulder of Ukhrul Tolloi - Tadubi section of NH-102A from Design Chainage km 9450 to km 50850 in the State of Manipur on EPC mode under NHO-NE Package-2 (NHIDCL) (618387)	Manipur	03/2023 (03/2024)	03/2026 (-)	578.98 (578.98)	234.11	77
1072	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 50.850 km to 81.870 km in the State of Manipur on EPC mode under NHO-TSP Package -3 (NHIDCL) (618388)	Manipur	09/2021 (07/2023)	01/2025 (03/2025)	315.56 (315.56)	227.97	90
1073	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 81.870 km to 105.825 km in the State of Manipur on EPC mode under NHO-TSP Package -4 (NHIDCL) (618389)	Manipur	09/2021 (08/2022)	02/2024 (10/2025)	310.76 (310.76)	247	96
1074	Improvement of existing road to 2 laning with Hard Shoulders of Maram-Peren section Package-1B, length- 17.660 km from Design Chainage 22.340 km to 40.000 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618415)	Manipur	02/2021 (06/2021)	12/2022 (08/2023)	188.36 (188.36)	0	99
1075	Improvement of existing road to 2 laning with Hard Shoulders of Maram -Peren section Package-1A, length- 22.340Km from Design Chainage 0.000 km to 22.340 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618416)	Manipur	02/2021 (06/2021)	12/2022 (02/2023)	226.32 (226.32)	0	0
1076	Rehabilitation and Up-gradation of Nongstoin Wahkaji section of Project Road Km 0000 to Km 43060 to Intermediate Lane with earthen shoulder under SARDP-NE Phase-A in the State of Meghalaya on EPC mode. Job No- SARDP-NE/Nong-Don-Maw/MG/2020-21/294 (MoRTH) (617885)	Meghalaya	08/2020 (02/2022)	08/2023 (07/2024)	302.88 (302.88)	182.58	98
1077	Improvement/Widening to 2-L with Paved Shoulder/ 4-Laning of NH-40 section from Km 151330 to Km 163400 design Km 63.530 to Km 71.520 including Dawki Bridge of length 368 m between Shillong-Dawki under JICA ODA Loan assistance Phase-II Pkg-5 -Balance work (NHIDCL) (618374)	Meghalaya	07/2020 (05/2024)	11/2026 (11/2027)	284.21 (284.21)	0	32
1078	Improvement/Widening to 2-Lane with Paved Shoulder from design Km 45.760 to Km 63.530 between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance work Pkg-4 (NHIDCL) (618375)	Meghalaya	07/2020 (04/2024)	04/2026 (07/2026)	445.51 (445.51)	0	37
1079	Improvement/Widening to 2-Lane with Paved Shoulder between Shillong-Dawki road up to Bangladesh Border from design Km 10.670 to Km 37.550 under JICA ODA Loan assistance Phase-II -Balance Work-Pkg-2 (NHIDCL) (618376)	Meghalaya	07/2020 (02/2024)	08/2026 (07/2026)	525.67 (525.67)	0	41
1080	Improvement/Widening to 2-L with Paved Shoulder/4-L from Km 81740 to Km 93490 design Km 0000 to Km 10670 of NH-40 New NH-106 & 206 section & 4-L from design Km 0.00 to Km 0.930 of NH-44 section between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance Work Pkg-1 (NHIDCL) (618377)	Meghalaya	07/2020 (10/2023)	10/2025 (-)	351.12 (351.12)	0	78
1081	Rehabilitation and up gradation of Nongstoin-Rambrai-Kyrshai road up to Meghalaya-Assam border from Km 0.335 to km 34.039 to 2-Lane under NHO - NE in the State of Meghalaya Package-1 (NHIDCL) (618418)	Meghalaya	09/2021 (05/2022)	05/2024 (06/2025)	359.86 (359.86)	0	69
1082	Construction of 2-Lane with paved shoulders of Shillong Western Bypass starting from NH-06 near Ladumsaw existing Km 60.900 of old NH40 to NH106 old NH 44E Package-III, from km 24700 to km 38256 under SARDP-NE PHASE A in the state of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618419)	Meghalaya	03/2023 (09/2024)	09/2026 (-)	562.48 (562.48)	0	33
1083	Construction of 2 lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw existing km 60.900 of old NH-40 to NH-106 old NH-44E, Package-II km 12800 to km 24700 under SARDP-NE Phase A in the State of Meghalaya on EPC Mode (NHIDCL) (618420)	Meghalaya	03/2023 (09/2024)	09/2026 (-)	686.03 (686.03)	0	0



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1084	Construction of 2-Lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw Existing km 60.900 of old NH-40 to NH106 old NH-44E, km 0000 to km 12800 Package-I under SARDP-NE PHASE A in the State of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618421)	Meghalaya	03/2023 (09/2024)	09/2026 (-)	620.3 (620.3)	0	46
1085	Up-gradation to 2-lane with paved shoulders of Ngopa - Pawlrang section of NH 102B of Aizawl - Imphal Economic Corridor from Existing Chainage km 32.796 to km 72.030 [Design Chainage km 31.280 to km 68.170] in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-2 Keifang- Tuivai Pkg-2 (NHIDCL) (618341)	Mizoram	09/2021 (09/2023)	02/2025 (06/2026)	523.78 (523.78)	0	64
1086	Rehabilitation and upgradation to 2 Lane with Paved shoulder of Economic corridor of NH-6 from Design chainage Km 0.000 to Km 13.510 Package-1 in the state of Mizoram under Bharatmala Pariyojana on EPC mode (NHIDCL) (618342)	Mizoram	03/2020 (07/2020)	06/2022 (06/2024)	206.9 (206.9)	0	0
1087	Rehabilitation and Up gradation to 2-lane with paved shoulder of Keifang Section Economic Corridor of NH-06 from Existing Chainage Km 30050 Keifang to Km 50360 Keifang, Design Chainage Km 27400 to Km 45040 PkgIII in the State of Mizoram under Bharatmala Pariyojna on EPC Mode Seling-Dulte - III (NHIDCL) (618343)	Mizoram	03/2020 (07/2020)	06/2022 (12/2024)	292.23 (292.23)	0	0
1088	Construction of 2-laning with hard shoulder of Lunglei to Chhumkhum from Design Chainage Km 0.000 to Km 37.420 of NH-302 [Lunglei-Tlabung] Package-A (NHIDCL) (618362)	Mizoram	03/2021 (06/2021)	12/2022 (05/2025)	698.45 (698.45)	0	0
1089	Construction of 2-laning with hard shoulder configuration of Chhumkhum to Tlabung from Design Chainage Km 37.420 to Km 74.950 of NH-302 in Mizoram under Bharatmala Pariyojana on EPC mode [Pkg-B] (NHIDCL) (618363)	Mizoram	06/2021 (07/2021)	01/2023 (05/2025)	740.58 (740.58)	0	0
1090	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 208. 000 to Km 250.000 Package-5 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-5 (NHIDCL) (618379)	Mizoram	09/2019 (10/2019)	04/2023 (-)	752.89 (752.89)	125.62	95
1091	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 125. 000 to Km 166 Package-3 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-3 (NHIDCL) (618380)	Mizoram	09/2019 (10/2019)	04/2023 (11/2024)	867.09 (867.09)	0	0
1092	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 250.00 Lunglei to km 298.00 on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-6 (NHIDCL) (618381)	Mizoram	09/2019 (12/2019)	06/2023 (03/2025)	768.76 (768.76)	168.78	98
1093	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 298.00 to km 339.00 on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-7 (NHIDCL) (618382)	Mizoram	09/2019 (10/2020)	04/2024 (03/2025)	605.76 (750.32)	0.01	100
1094	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 339.00 to km 380.00 Siaha on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-8 (NHIDCL) (618383)	Mizoram	09/2019 (03/2020)	09/2023 (05/2025)	637.06 (637.06)	101.89	99
1095	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 166. 000 to Km 208.000 Package-4 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-4 (NHIDCL) (618384)	Mizoram	09/2019 (10/2019)	04/2023 (09/2024)	899.45 (899.45)	191.59	99
1096	6L Aluru - Jakkuva Section of NH-130CD Road from km 365.033 to km 396.800 Pkg. 1 (National Highways Authority of India [NHAI]) (618681)	Multi-States (Andhra Pradesh, Odisha)	02/2021 (03/2022)	03/2024 (04/2025)	1216.12 (1241.66)	627.48	90
1097	Bangalore Chennai Expressway Phase-III Package I Gudipala to Walajahpet from Km 156.000 to Km 180.000 (National Highways Authority of India [NHAI]) (618477)	Multi-States (Andhra Pradesh, Tamil Nadu)	10/2020 (05/2022)	05/2024 (08/2024)	1481.87 (1481.87)	711.04	91
1098	6L of Veera Kaveri Raja Puram to Pondavakkam from km 61.380 to km 96.040 of NH 716B Pkg-III (National Highways Authority of India [NHAI]) (618634)	Multi-States (Andhra Pradesh, Tamil Nadu)	03/2021 (01/2023)	01/2025 (-)	1439.77 (1439.77)	685.44	98
1099	6L of Varadharajula to Kumarajapet from km 0.000 to km 43.800 of NH-716B Pkg-I (National Highways Authority of India [NHAI]) (618771)	Multi-States (Andhra Pradesh, Tamil Nadu)	02/2021 (12/2022)	12/2024 (08/2025)	1924.75 (1887.38)	922.92	98
1100	6L of Kumarajapet to Veera Kaveri Raja Puram from km 43.800 to km 61.380 of NH-716B Pkg-II (National Highways Authority of India [NHAI]) (618772)	Multi-States (Andhra Pradesh, Tamil Nadu)	02/2021 (10/2023)	10/2025 (-)	702.52 (799.36)	354.34	92
1101	Khammam-Devarapalle Pkg III [4L Access Controlled Greenfield from Chintagudem village to Recherla village Design Chainage 63117 to 105236] (National Highways Authority of India [NHAI]) (618747)	Multi-States (Andhra Pradesh, Telangana)	01/2021 (09/2022)	10/2024 (09/2025)	829.5 (1227.07)	459.37	98
1102	6L of Aurangabad to Bihar-Jharkhand border Chordaha section from km. 180.000 to km. 209.827 of NH-2 PKG-01 (National Highways Authority of India [NHAI]) (618531)	Multi-States (Bihar, Jharkhand)	02/2021 (12/2024)	12/2026 (-)	1054.46 (786.81)	86	16
1103	6L of Aurangabad to Bihar-Jharkhand border Chordaha section from km. 209.827 to Km. 249.525 of NH-19 PKG-02 (National Highways Authority of India [NHAI]) (618532)	Multi-States (Bihar, Jharkhand)	06/2021 (03/2022)	03/2024 (04/2025)	1822.46 (738.11)	565.91	92
1104	Hariharganj to Parwa Mode section from km 23.284 to km 57.049 of NH-98 (National Highways Authority of India [NHAI]) (618951)	Multi-States (Bihar, Jharkhand)	09/2020 (03/2022)	02/2024 (-)	1125.78 (1186.56)	474.19	79



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1105	4L of Sahibganj - Manihari Ganga Bridge including Manihari Bypass (National Highways Authority of India [NHAI]) (618952)	Multi-States (Bihar, Jharkhand)	10/2016 (11/2020)	10/2024 (12/2026)	1954.77 (1978.01)	1679.16	81
1106	Six Laning of Varanasi to Aurangabad from km. 786.00 to km. 978.40 of Old NH-2 (National Highways Authority of India [NHAI]) (618530)	Multi-States (Bihar, Uttar Pradesh)	NA (09/2011)	03/2014 (03/2014)	3241.56 (3241.56)	20.97	94
1107	6L of Dhanara - Hatibena Section from Km 124.611 to km 146.50 of NH-130-CD Package OD-1 (National Highways Authority of India [NHAI]) (618676)	Multi-States (Chhattisgarh, Odisha)	02/2021 (03/2022)	03/2024 (12/2025)	477.76 (638.32)	276.9	99
1108	Balance work of 2L PS from Km 30.800 to Km 70.800 and 2L with Rigid Carriageway from Km 70.800 to km 84.120 of Khanapur- KA/GOA Border section of NH-4A (National Highways Authority of India [NHAI]) (618942)	Multi-States (Goa, Karnataka)	01/2022 (11/2022)	05/2024 (03/2026)	226.76 (149.44)	102.44	77
1109	Bal. Works of Fagne Km. 510.000 to Maharashtra/Gujarat Border Km. 650.794 (National Highways Authority of India [NHAI]) (618637)	Multi-States (Gujarat, Maharashtra)	12/2019 (09/2020)	09/2022 (06/2024)	1654.07 (1672.89)	1293.06	84
1110	4L Greenfield a Malout bypass from ch. Km 44.500 to ch. Km 35.500 on NH-07 and Ch. Km 0.000 to Km 6.984 on NH-09 bMandi Dabwali Bypass from Ch. 38.450 Km to Km 27.910 Pkg-02 (National Highways Authority of India [NHAI]) (618760)	Multi-States (Haryana, Punjab)	11/2021 (12/2022)	07/2024 (12/2024)	646.42 (556.09)	549.18	95
1111	4L Ambala - Kalaamb from Km. -0.800 to Km. 33.015 of old NH-72 (National Highways Authority of India [NHAI]) (618935)	Multi-States (Haryana, Punjab)	10/2022 (06/2023)	06/2025 (-)	1183.7 (1190.34)	450.53	99
1112	Additional Structures on 6LGurgaon-Jaipur Section of NH-48 between KM 42.700 to KM 273.00 (National Highways Authority of India [NHAI]) (618505)	Multi-States (Haryana, Rajasthan)	08/2022 (12/2022)	06/2024 (-)	409.64 (290.64)	185.01	85
1113	6L access Controlled Greenfield Highway from Ranipur Barsi to Adhoya Musalmana section of Shamli -Ambala Package-II Design Ch. Form km 45.500 to km 84.400 (National Highways Authority of India [NHAI]) (618723)	Multi-States (Haryana, Uttar Pradesh)	06/2022 (05/2023)	05/2025 (12/2025)	1554.21 (1241.89)	674.25	70
1114	4L from Km 219.600 Khajuri to Km 260.483 Wyndhamganj on NH-75 Sec-V (National Highways Authority of India [NHAI]) (618828)	Multi-States (Jharkhand, Uttar Pradesh)	03/2022 (09/2023)	09/2025 (-)	1436.49 (1465.55)	826.55	90
1115	Barwa Adda Km. 398.240 to Panagarh Km. 521.120 (National Highways Authority of India [NHAI]) (618533)	Multi-States (Jharkhand, West Bengal)	08/2010 (04/2014)	09/2016 (-)	1560.39 (1568.22)	6.98	100
1116	2L PS of JH / WB Border km. 70.524 - Purulia km.84.400 & Purulia km. 94.30 - Chandil Junction with NH-33 km. 153.705 of Old NH-32 (National Highways Authority of India [NHAI]) (618909)	Multi-States (Jharkhand, West Bengal)	03/2018 (12/2019)	08/2022 (12/2025)	1652.4 (1771.88)	741.05	97
1117	6L from Belgaum to Sankeshwar Bypass from Km. 515.000 to Km. 555.017 of NH-48 Pkg-I (National Highways Authority of India [NHAI]) (618515)	Multi-States (Karnataka, Maharashtra)	11/2021 (10/2022)	04/2025 (12/2025)	1479.3 (1237.04)	1110.53	95
1118	6L from Sankeshwar Bypass to MH-KNT Border from Km. 555.017 to Km. 592.853 of NH-48 Pkg-II (National Highways Authority of India [NHAI]) (618516)	Multi-States (Karnataka, Maharashtra)	01/2022 (10/2022)	04/2025 (10/2026)	1388.7 (1066.86)	989.21	75
1119	Bangalore Ring Road STRR-NH-948A- Package-I of Phase-III from Belagondapalli TN to TN/KNT border from km 144.480 to 179.969 (National Highways Authority of India [NHAI]) (618519)	Multi-States (Karnataka, Tamil Nadu)	03/2022 (05/2023)	05/2025 (-)	1260.74 (1218.47)	496.7	58
1120	Hosur to Dhamrapuri Pkg-1 [Neraluru - Thorapalli Agraharam] (National Highways Authority of India [NHAI]) (618581)	Multi-States (Karnataka, Tamil Nadu)	10/2021 (10/2022)	10/2024 (08/2025)	1757.27 (1828.66)	902.32	55
1121	6L Access Controlled Greenfield Highway of Nandinne village to Julekal village from Km 202.900 to Km 242.200 Pkg-1 (National Highways Authority of India [NHAI]) (618632)	Multi-States (Karnataka, Telangana)	02/2022 (01/2023)	01/2025 (09/2025)	972.06 (1044.06)	404.06	73
1122	4L of Rajura-Korpana-Adilabad Road upto M.S. Border from km 32.910 to km 89.090 of NH-353B (National Highways Authority of India [NHAI]) (618938)	Multi-States (Maharashtra, Telangana)	03/2022 (10/2022)	10/2024 (04/2025)	1013.33 (1274.63)	546.48	89
1123	Puducherry Km.29.000 to Poondiyanuppam Km.67.000 (National Highways Authority of India [NHAI]) (618845)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (11/2021)	11/2023 (03/2024)	1588.4 (1415.9)	277.19	98
1124	Sattanathapuram to Nagapattinam from Km 123.800 to Km 179.555 (National Highways Authority of India [NHAI]) (618847)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (10/2020)	10/2022 (01/2026)	2899.77 (2899.77)	1011.67	75
1125	6L with access control provision Saharanpur bypass to Ganeshpur section from 13.89 Km to 41.820 Km of Delhi- Dehradun Economic Corridor package-2 (National Highways Authority of India [NHAI]) (618711)	Multi-States (Uttar Pradesh, Uttarakhand)	04/2022 (11/2022)	11/2024 (12/2024)	796.65 (560.03)	494.44	98
1126	Improvement & Up-gradation of NH-734 Section of Moradabad-Thakurdwara Kashipur including Moradabad & Kashipur Bypass Package-III Kashipur Bypass Length 14.490 Km., Starts from Ch. 38770 and ends at Ch. 53260 existing Ch. 05560 (National Highways Authority of India [NHAI]) (618928)	Multi-States (Uttar Pradesh, Uttarakhand)	02/2023 (03/2024)	09/2025 (06/2026)	936.12 (717.5)	271.44	30
1127	4/6L of Spur to Haridwar Greenfield from Km. 0.000 to Km. 50.70 (National Highways Authority of India [NHAI]) (618969)	Multi-States (Uttar Pradesh, Uttarakhand)	11/2021 (02/2023)	02/2025 (03/2026)	2155.95 (2612.3)	1375.08	90
1128	Widening of existing Single lane / Intermediate lane road to 2 lane from Km 101 to Km 125 of NH 61 (MoRTH) (617886)	Nagaland	06/2020 (06/2024)	06/2026 (-)	252.2 (252.2)	0	41
1129	Widening of existing single lane to intermediate lane road from Mokokchung to Chare via Dikhu in the state of Nagaland on EPC mode (MoRTH) (618002)	Nagaland	02/2021 (06/2023)	06/2025 (-)	192.93 (192.93)	99.65	0
1130	Widening to Existing single lane /intermediate lane to 2 lane from Km185.00 to Km 220.00 of NH-61 New NH-02 in the state of Nagaland. (MoRTH) (618072)	Nagaland	03/2021 (07/2022)	07/2024 (03/2025)	297.25 (297.25)	128.97	85



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1131	Construction of 2-lane with Paved shoulder of Kohima- Bypass Road Connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29, NH-39New NH-02 from Design Km 32.00 to Design Km 43.454Design Length-11.454 Km in the State of Nagaland under SARDP-NE on EPC Mode Package-IV (NHIDCL) (618290)	Nagaland	07/2020 (10/2020)	04/2022 (02/2025)	202.36 (202.36)	0	0
1132	Construction of 2-lane with Paved shoulder of Kohima-Bypass Road connecting NH-39 New NH-02, NH150New NH-02, NH7-61 New NH-29 and NH-39 New NH-02 from Design km 21.000 to km 32.268 [Design length11.268 km] in the state of Nagaland Under SARDP-NE on EPC Mode Package- 3 (NHIDCL) (618291)	Nagaland	07/2020 (06/2023)	06/2025 (-)	159.85 (342.29)	0	0
1133	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting New NH-02 and New NH-29 from Design Km 10.500 to design Km 21.000 [Design Length-10.500 km] including TUNNEL of 500m at Ch. 11.000 in the state of Nagaland Under SARDP-NE on EPC Mode Package-2 (NHIDCL) (618292)	Nagaland	07/2020 (10/2020)	10/2022 (01/2024)	277.44 (277.44)	0	0
1134	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29 and NH-39New NH-02 from design Km 0.00 to Km 10.500 in the State of Nagaland under SARDP-NE on EPC Mode Package-1 -Balance work (NHIDCL) (618293)	Nagaland	07/2020 (11/2023)	11/2026 (-)	232.29 (350.88)	0	20
1135	Balance work of Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 old NH-150 from existing km 98.380 near Chizami vill. to km120.367 Nagaland/Manipur Border [Design km 95.700 to design km 117.200] [Design Length 21.500 km] in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode Package-V under NHO (NHIDCL) (618296)	Nagaland	03/2020 (11/2023)	11/2025 (-)	330.8 (330.8)	0	91
1136	Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 Old NH-150 from existing Km 30.474 Near Kidwema road Chakahabama to existing Km 53.220 Near Kikuma Village Design Km 29.60 to Km 51.50 Design length-21.90 Km in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode under NHO Package-II -Balance work (NHIDCL) (618297)	Nagaland	03/2020 (01/2024)	01/2026 (-)	355.79 (355.79)	0	29
1137	4-Laning of Balance work of Dimapur-Kohima Road from design km 152.490 to km 166.700 Existing km 156.000 to km 172.900 Excluding Dimapur & Kohima Bypass under SARDP-NE Package-III (NHIDCL) (618328)	Nagaland	03/2016 (09/2023)	09/2025 (-)	562.98 (794.75)	0	0
1138	Construction of 4/6 Laning from Km 132.375 to Km 153.058 Total New Alignment length of 20.683 Km of Daboka-Dimapur Section Dimapur Bypass Nagaland Portion of NH-36 & 39 in the State of Nagaland on EPC basis under PhaseA of SARDP-NE (NHIDCL) (618329)	Nagaland	02/2017 (09/2017)	09/2020 (02/2023)	819.39 (819.39)	0	0
1139	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-I Design Chainage 0000 Km to 34795 Km, in the State of Nagaland on EPC mode under NH O-NE (NHIDCL) (618364)	Nagaland	12/2022 (08/2023)	02/2026 (-)	430.24 (430.24)	0	78
1140	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-III Design Chainage 69875 Km to 106816 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618365)	Nagaland	12/2022 (08/2023)	02/2026 (-)	497.18 (497.18)	0	80
1141	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-II Design Chainage 34795 Km to 69875 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618366)	Nagaland	12/2022 (08/2023)	02/2026 (-)	442.54 (442.54)	0	38
1142	Construction of 2 laning with Hard shoulder of Peren-Dimapur section on NH 129A from Design Km 146.208 to Km 163.592 Length- 17.384 km in the state of Nagaland on EPC mode under NHO-TSP Package-III (NHIDCL) (618413)	Nagaland	02/2021 (06/2023)	06/2025 (11/2025)	177.77 (199.02)	0	76
1143	Construction of Balance work for 2-lane with hard shoulder of Peren- Dimapur section on NH-129A from Design Km 126.775 to Km 146.208 Length 19.433 Km in the state of Nagaland on EPC mode under NHO-TSP Package-II (NHIDCL) (618414)	Nagaland	01/2021 (09/2023)	09/2025 (-)	258.52 (258.52)	0	0
1144	Construction of 2-lane with hard shoulders of Merangkong-Tamlu-Mon road Wakching Twon portion on EPC basis from existing Chainage Km 59000 to Km 73640 [Design Km. 59000 to Km, 72450] Design length - 13.450 Km under SARDP-NE package-V Balance work (NHIDCL) (618422)	Nagaland	03/2021 (09/2023)	09/2025 (-)	161.73 (161.73)	0	0
1145	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon MTM Road from existing Km 20.456 to Km 41.065 Design Km. 20 to Km. 40.0 Design Length-20.000 Km in the State of Nagaland under SARDP-NE Phase-A Pkg-2 Balance work (NHIDCL) (618423)	Nagaland	03/2018 (08/2023)	08/2025 (-)	215.79 (215.79)	0	0
1146	Widening and Strengthening to 4LPS/2LPS from km 0.000 to 35.800 Kuakhia - Mangalpur section of NH 20 in the state of Odisha on Annual Plan 2021-22 (MoRTH) (617899)	Odisha	03/2022 (02/2024)	02/2026 (-)	636.1 (636.1)	47.79	45
1147	Construction of Bypass road to Balangir town from km 72/400 Desing km 0/0 to km 79/800 Design km 11/670 of NH-26 in the State of Odisha. (MoRTH) (617904)	Odisha	02/2022 (04/2023)	10/2025 (-)	238.78 (238.78)	6.09	0
1148	Construction of 4 lane ROB with approaches in lieu of LC No. RV-172 at km 176.00 of NH-201 present NH-26 at Kesinga including land acquisition in the state of Odisha on EPC mode under Annual Plan 2021-22 (MoRTH) (617905)	Odisha	12/2021 (05/2023)	05/2025 (-)	324.09 (324.09)	65.83	70



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1149	Widening and strengthening to 2LPS including LA of Kandarpur-Balikuda from km 277/500 to 318/970 of NH-55 in the State of Odisha under Annual Plan 2021-22. (MoRTH) (617921)	Odisha	03/2022 (06/2023)	06/2025 (-)	499.79 (499.79)	99.63	50
1150	Construction of bypass to Nayagarh town from km 235.469 to 252.482 of NH-57 including land acquisition in the state of Odisha. (MoRTH) (617924)	Odisha	01/2022 (05/2023)	04/2025 (-)	300.33 (300.33)	78.14	68
1151	Construction of Bypass to Khordha town from Km 294/000 to 300/300 on NH-57 including LA in the State of Odisha on EPC mode. (MoRTH) (617925)	Odisha	02/2022 (05/2023)	11/2024 (07/2025)	157.49 (157.49)	33.61	35
1152	Construction of Bypass on NH-59 from Km 336/350 to 349/910 13.56 km near Berhampur town including 4-lane RoB in the state of Odisha. (MoRTH) (617930)	Odisha	03/2021 (03/2022)	03/2024 (-)	196.94 (196.94)	30.46	35
1153	Construction of four lane ROB and its approaches in lieu of existing Level Crossing No. RV-71 at km 435 on NH-217 New NH-353 at Khariar including land acquisition under NHO in Annual Plan 2021-22 for the state of Odisha for F.Y. 2021-22 to F.Y 2033-34 (MoRTH) (618003)	Odisha	11/2021 (06/2023)	12/2024 (-)	154.49 (154.49)	22.32	0
1154	Widening & strengthening to 2LPS from km 0,000 to 40.000 Dhaugaon- Podamari section of NH 326 in the State of Odisha under Annual Plan 2021.22. (MoRTH) (618012)	Odisha	03/2022 (02/2024)	02/2026 (-)	186.52 (186.52)	42.7	60
1155	Bhadrak KM 136.500 to Baleshwar KM 199.141 (National Highways Authority of India [NHAI]) (618523)	Odisha	11/2014 (03/2019)	09/2021 (-)	844.67 (1394.82)	231.14	91
1156	6L Greenfield Kaliagura Baunsagar Section of NH-130-CD Road from km 249000 to km 293000 Package OD-5 (National Highways Authority of India [NHAI]) (618677)	Odisha	09/2021 (05/2022)	05/2024 (10/2025)	1539.75 (1918.49)	881.05	92
1157	6L Greenfield Baunsagar - Baraja Section of NH-130-CD Road from km 293000 to km 338500 Package OD-6 (National Highways Authority of India [NHAI]) (618678)	Odisha	08/2021 (06/2022)	05/2024 (06/2025)	1265.59 (1635.44)	762.26	98
1158	6L Greenfield Kandili - Aluru Section of NH-130-CD Road from km 342500 to km 365033 Package-OD-8 (National Highways Authority of India [NHAI]) (618680)	Odisha	12/2021 (10/2022)	10/2024 (08/2025)	1492.74 (1912.84)	965.07	92
1159	Balance work of Panikoili Rimoli Section of new NH-20 from Km 0.00 to Km. 163.000 (National Highways Authority of India [NHAI]) (618819)	Odisha	09/2020 (03/2021)	03/2022 (07/2022)	183.03 (200.79)	89.36	99
1160	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.39.000 to Km.60.00 Package-3 (National Highways Authority of India [NHAI]) (618820)	Odisha	03/2023 (12/2023)	12/2025 (-)	861.84 (938.55)	344.24	81
1161	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km 18.00 to Km 39.00 in the State of Odisha on HAM mode Package-2 (National Highways Authority of India [NHAI]) (618821)	Odisha	03/2023 (12/2023)	12/2025 (-)	920.47 (950.4)	363.82	83
1162	3L Major Bridge over River Brahmani at Km. 401.250 Duburi - Chandikhole Section of NH-200 New NH -53 (National Highways Authority of India [NHAI]) (618908)	Odisha	04/2022 (08/2022)	01/2025 (-)	153.61 (103.68)	61.82	0
1163	4-L of Rajamunda to Barkote Section of NH-23 from km. 287.200 to km. 337.185 (National Highways Authority of India [NHAI]) (618913)	Odisha	10/2017 (12/2018)	06/2021 (12/2024)	609.63 (630.97)	114.77	96
1164	Work of Widening/upgradation of 2-Lane with paved shoulder of Sri Muktsar Sahib to Malout road from Km 279.400 to Km 307.060 section of NH-354 in the State of Punjab on EPC mode. Job No. NH-354-PB-2021-22-555 (MoRTH) (618023)	Punjab	03/2022 (10/2023)	04/2025 (-)	152.58 (152.58)	0	96
1165	Up-gradation to two lane with paved shoulder configuration of NH-354 Section Arifkes-Ferozepur-Muktsar-Malaut from Km 201.500 to Km 212.500 & Km 229.690 to Km 269.960 and strengthening of existing pavement from Km 212.500 to Km 229.690 excluding Km 218.500 to 223.690 of NH-354 on EPC Mode in the State of Punjab. Job No. NH-354-PB-2020-21-532 (MoRTH) (618024)	Punjab	03/2021 (10/2023)	04/2025 (-)	263.19 (263.19)	0	0
1166	Delhi-Amritsar-Katra Expressway Phase-I Pkg-VII from Junction with Patiala-Bathinda road NH-7 near Bhawanigarh to Junction with Ludhiana-Malerkotla SH-11 near Bhogiwal village Km 188830 to km 225770 (National Highways Authority of India [NHAI]) (618487)	Punjab	12/2020 (07/2022)	07/2024 (-)	1759.82 (1774.32)	1217.21	95
1167	Delhi-Amritsar-Katra Expressway Phase-I Pkg-VIII from Junction with Ludhiana-Malerkotla SH-11 near Bhogiwal village to Junction with Ludhiana-Moga road NH-5 near Mullanpur Dakha Km 225770 to km 260860 (National Highways Authority of India [NHAI]) (618488)	Punjab	12/2020 (03/2023)	03/2025 (-)	1895.74 (2034.94)	751.95	31
1168	Delhi-Amritsar-Katra Expressway Phase-I Pkg-IX from Junction with Ludhiana-Moga road NH-5 near Mullanpur Dakha to Junction with Jalandhar - Moga road NH-703 near Kang Sahibu village Km 260860 to km 303900 (National Highways Authority of India [NHAI]) (618489)	Punjab	12/2020 (07/2022)	07/2024 (09/2025)	1851.47 (2407.14)	1305.41	69
1169	Delhi-Amritsar-Katra Expressway Phase-I Pkg-X from Jn. with Jalandhar - Moga road NH-703 to Jn. with Jalandhar-Kapurthala road NH-703A and to Jn. with Kapurthala - Sultanpur Lodhi road NH-703A km 000 to km 24000 to Amritsar connectivity (National Highways Authority of India [NHAI]) (618490)	Punjab	12/2020 (07/2022)	07/2024 (09/2025)	2177.54 (2062.74)	1004.28	62



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1170	Delhi-Amritsar-Katra Expressway Phase-I Pkg-XI from Junction with Jalandhar - Kapurthala road NH-703A near Khojewal village to Junction with Amritsar-Mehta-SriHargobindpur-Tanda road NH-503A near SriHargobindpur Km 319400 to km 362420 (National Highways Authority of India [NHAI]) (618491)	Punjab	03/2021 (11/2022)	11/2024 (-)	2175.35 (2206.71)	941.19	43
1171	Delhi-Amritsar-Katra Expressway Phase-I Pkg-XII from Junction with Amritsar-Mehta-SriHargobindpur-Tanda road NH-503A near SriHargobindpur to Junction with Pathankot-Gurdaspur road NH-54 near Gurdaspur Km 362420 to km 397700 (National Highways Authority of India [NHAI]) (618492)	Punjab	03/2021 (01/2024)	12/2025 (-)	1734.18 (1538.47)	470.44	25
1172	Delhi-Amritsar-Katra Expressway Phase-I Spur-I from Jn. with Kapurthala - Sultanpur Lodhi Road NH-703A near Isharwal village to Jn. with Kapurthala - Tarn Taran road NH-703AA near Goinwal Sahib [Km 24000 to Km 41000 of Amritsar connectivity] (National Highways Authority of India [NHAI]) (618493)	Punjab	12/2021 (04/2023)	04/2026 (-)	2165.23 (1519.6)	331.17	27
1173	Development of 6L Greenfield Jalandhar Bypass starting from Kahlwan NH-03 ending at Kang Sahbu NH-703 via Sarmastpur NH-44 - Madara NH-03 - Khajurla NH-44 (National Highways Authority of India [NHAI]) (618552)	Punjab	03/2021 (01/2023)	01/2025 (03/2026)	1754.84 (2167.39)	797.22	41
1174	6L of Jodhpur Romana Bathinda - Mandi Dabwali Punjab Haryana Border section of NH-54 from km. 0.000 to km. 27.400 of NH-54 (National Highways Authority of India [NHAI]) (618610)	Punjab	05/2020 (08/2023)	08/2025 (-)	789.26 (1318.91)	507.03	98
1175	6L Amritsar-Bathinda Greenfield section from village Tiba on NE-5A to Jn. with Moga Jalandhar road NH-703 near Dharamkot from km 0.000 to km 39.000 of NH-754A Pkg-1 (National Highways Authority of India [NHAI]) (618617)	Punjab	03/2021 (11/2022)	11/2024 (09/2025)	1229.38 (1549.32)	732.07	64
1176	6L Amritsar-Bathinda Greenfield section from Jn. with Bhagta Bhai Ka-Bhadaur Road near Dyalpura Bhai Ka to Jn. with Mandi Dabwali Bathinda Road on NH-54 near Sangat Kalan from km 93.000 to km 154.866 of NH-754A Pkg-3 (National Highways Authority of India [NHAI]) (618618)	Punjab	03/2021 (06/2024)	06/2026 (-)	2029.17 (2677.23)	504.83	65
1177	6L Access Controlled Ludhiana-Bathinda Greenfield highway from Jn. with Amritsar-Bathinda Greenfield Road NH-754A near Rampura Phul to Jn. with Moga-Barnala Road NH-703 near village Tallewal from Km 0.0 to Km 30.3 of NH-754AD Pkg-1 (National Highways Authority of India [NHAI]) (618647)	Punjab	06/2021 (09/2023)	09/2025 (-)	906.51 (1020.52)	429.44	78
1178	Moga - Bagha Purana - Bajakhana from km. 0.00 to km. 43.32 (National Highways Authority of India [NHAI]) (618764)	Punjab	05/2020 (12/2022)	12/2024 (08/2025)	864.23 (1264.17)	625.94	75
1179	4/6L Greenfield LudhianaRupnagar highway from Jn. with NE-5 village near to ManewalLudhiana to Jn. with NH-205 near Bheora Village Rupnagar from Km 66.0 to Km 91.0 i/c spur to Kharar from Km 0.0 to Km 19.5 with Ludhiana bypass of NH-205K Pkg-3 (National Highways Authority of India [NHAI]) (618785)	Punjab	07/2021 (02/2023)	02/2025 (-)	1501.02 (1815.13)	992.69	76
1180	6L of IT City Chowk to Kurali Chandigarh Road (National Highways Authority of India [NHAI]) (618789)	Punjab	03/2021 (10/2022)	10/2024 (06/2025)	1525.31 (1936.54)	1689.83	98
1181	Amritsarairport Junction - Ramdas from km. 100.835 to km. 139.813 Pkg - IV (National Highways Authority of India [NHAI]) (618794)	Punjab	12/2020 (03/2022)	09/2023 (-)	524.88 (416.58)	345.41	60
1182	Amritsar Bypass Pkg III from km. 71.496 to km. 105.158 (National Highways Authority of India [NHAI]) (618795)	Punjab	02/2021 (08/2022)	08/2024 (-)	1474.77 (1228.42)	863.93	79
1183	4L of Beas-Mehta-Batala-Dera Baba Nanak from intersection with Jalandhar-Amritsar Highway NH-3 near Beas till start of Batala Bypass near Village Acchhal from Km. 0.000 to Km. 31.300 Pkg-1 (National Highways Authority of India [NHAI]) (618809)	Punjab	08/2021 (06/2023)	06/2025 (-)	809.51 (966.99)	467.61	53
1184	4L of existing Beas Baba Bakala - Dera Baba Nanak Section from start of Batala Bypass till intersection with Ajnala Gurdaspur Highway NH 354 near Dera Baba Nanak from Km. 31.300 to Km. 69.100 with Additional batala Bypass Pkg-II (National Highways Authority of India [NHAI]) (618810)	Punjab	10/2021 (06/2023)	06/2025 (-)	1003.38 (993.6)	564.01	74
1185	4L of Amritsar-Ghoman - Tanda - Una Section from Km 8.270 to Km 54.000 of NH-503A Package-I (National Highways Authority of India [NHAI]) (618906)	Punjab	12/2020 (06/2022)	06/2024 (-)	857.91 (1443.47)	466.83	58
1186	Beaver Gomti 4LPS from km 58.245 to km 108.600 Pkg-I (MoRTH) (617887)	Rajasthan	12/2020 (10/2021)	10/2023 (12/2025)	379.23 (379.23)	201.18	0
1187	Construction of Two lane with Paved Shoulder for Fatehpur Bypass Design Km 0.000 to Km 7.400 , Mandawa Bypass Design Km 20.925 to Km 27.300 & Jhunjhunu Bypass Design Km 41.625 to Km 54.689 of NH-11 on EPC Mode in the state of Rajasthan . (MoRTH) (617891)	Rajasthan	03/2022 (02/2023)	08/2024 (06/2025)	186.29 (186.29)	66.7	99
1188	Upgradation to Two Lane Paved Shoulder in km 33/0 to 126/520 of NH-23 Old NH-11B Kothun-Lalsot-Karoli-Dholpur road in the state of Rajasthan under EPC mode Length-93.52 Km. (MoRTH) (617900)	Rajasthan	12/2021 (09/2022)	09/2024 (03/2025)	150.11 (150.11)	12.2	97
1189	Widening of Pachpadra-Bagundi Section to 4 Lane from Km 73/60 to 95/70 of NH-25 on EPC mode in the state of Rajasthan. (MoRTH) (617901)	Rajasthan	01/2022 (12/2022)	12/2024 (07/2025)	194.88 (194.88)	48.47	85
1190	Construction of 2 lane with paved shoulder for the work of Development of remaining sections of NH-325 Balotra to sanderao via Jalore to 2 lane with paved shoulder configuration by Construction of Bypasses for town portions1 Asotra- Brahmddham bypass 2Siwana Bypass 3 Mokalsar Bypass 4 Major realignment at Kathadi 5 Major realignment at Bishangarh 6 Jalore Bypass 7 Ahore Town portion 8 Dujana Bypass in the state of Rajasthan on EPC Mode (MoRTH) (618011)	Rajasthan	12/2021 (05/2022)	05/2024 (06/2025)	411.44 (411.44)	66.63	83



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1191	Up-gradation to 2 lane with Paved shoulder from Charbhujia at Design km 0.00 existing km 150.00 to Neechli Oden Nathdwara at Design ch. Km 88.800 existing km 55.950 of NH-162E on EPC mode. (MoRTH) (618093)	Rajasthan	02/2022 (09/2023)	09/2025 (-)	838.43 (838.43)	55.04	0
1192	Upgradation of two lane paved shoulder from Shahpura existing km. 0.00 Design Ch. 000 to Thanagazi existing Km.37352 Design Ch. 36810 of NH-248A on EPC mode in the State of Rajasthan. (MoRTH) (618118)	Rajasthan	03/2022 (02/2023)	07/2024 (03/2025)	174.34 (174.34)	63.51	90
1193	Construction of 2 lane with Paved Shoulder for Northern Bypass Phase-II of Kota city in the State of Rajasthan. (MoRTH) (618200)	Rajasthan	03/2022 (10/2023)	04/2025 (06/2026)	317.74 (317.74)	5.97	0
1194	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-14 Ch. 388.420 to Ch. 419.000 [Junction with NH- 76 to Junction with NH-12 near village Ummedpura] (National Highways Authority of India [NHAI]) (618456)	Rajasthan	11/2019 (05/2021)	05/2023 (03/2025)	1119.35 (1194.17)	975.7	99
1195	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-10 Ch. 292.950 to Ch. 319.400 [End of Interchange on NH-166 near village Mui to Hardeoganj village near Indergarh] (National Highways Authority of India [NHAI]) (618457)	Rajasthan	11/2019 (05/2021)	05/2023 (07/2024)	1272.97 (1265.16)	1070.22	94
1196	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-15 Ch. 419.000 to Ch.427.300 [Junction with NH-12 near village Ummedpura to Major bridge over Takli river near Nayagaon Jageer village] (National Highways Authority of India [NHAI]) (618458)	Rajasthan	07/2020 (07/2021)	01/2024 (02/2026)	1854.68 (1854.68)	1270.78	85
1197	Deogarh near Dhandhaniya-Rajasthan/Gujarat Border Phase-I AJ/DRGB-Package-6 (National Highways Authority of India [NHAI]) (618612)	Rajasthan	10/2019 (08/2021)	08/2023 (12/2024)	846.59 (740.62)	666.43	100
1198	Deogarh near Dhandhaniya-Rajasthan/Gujarat Border Phase-I AJ/DRGB-Package-7 (National Highways Authority of India [NHAI]) (618613)	Rajasthan	10/2019 (07/2021)	07/2023 (12/2024)	662.08 (597.77)	503.05	100
1199	Tanot -Ramgarh-Bhadasar-Jaisalmer NH-68 and BhadasarMokal-Sarkaritala up to Pakistan Border NH-968 Pkg-BM/5 (National Highways Authority of India [NHAI]) (618796)	Rajasthan	02/2018 (04/2019)	04/2021 (-)	828.58 (830.37)	226.86	100
1200	4L of Karwar Km. 281.980 of NH-62 Nagaur road to Dangiyavas of Jodhpur Ring Road Pkg-II (National Highways Authority of India [NHAI]) (618838)	Rajasthan	11/2021 (08/2022)	08/2024 (-)	736.75 (512.77)	395.34	98
1201	Construction of two lane with paved shoulder Gangtok Bypass Road from Ranipool to Burtuk Ch 0.00 Km to 23.316 L23.316 Km in the State of Sikkim (MoRTH) (618071)	Sikkim	10/2021 (05/2022)	05/2024 (01/2025)	385.15 (342.89)	0	78
1202	Construction & Upgradation of existing road to 2-lane with paved shoulder from New Rolep Bridge at km 37.600 to Chochenpheri at km 52.00 in the section of Rongli to Chochenpheri of NH 717B Pkg-II C (NHIDCL) (618446)	Sikkim	10/2020 (05/2021)	05/2024 (02/2025)	493.42 (478.79)	0	64
1203	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Helipad near Menla at Km 82000 to Menla at Km 94030 of Rhenock-Menla Spur NH-717B Package-IIIB on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618447)	Sikkim	01/2021 (02/2021)	02/2024 (11/2025)	410.6 (379.3)	0	33
1204	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Chochenpheri at Km 52000 to Helipad near Menla at Km 82000 of Rhenock-Menla Spur NH-717B Package-IIIA on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618448)	Sikkim	10/2020 (12/2020)	12/2023 (09/2025)	816.79 (786.6)	0	0
1205	Construction & Upgradation of existing road to 2-lane with paved shoulder from km27.200 End of Rongli bypass to km37.600New Rolep Bridge of Rhenok-Menla spur NH-717B on EPC Mode under SARDP-NE Phase-A in Sikkim Pkg-II B (NHIDCL) (618449)	Sikkim	07/2020 (10/2020)	04/2023 (02/2025)	230.45 (244.91)	0	64
1206	Rehabilitation & Upgradation of existing road to 2-lane with paved shoulder including geometric improvement of section from start of Rabangla km33.600 to km58.840 under SARDP-NE Phase A Pkg- IV (NHIDCL) (618450)	Sikkim	07/2020 (10/2020)	05/2022 (04/2025)	292.8 (292.8)	1.91	18
1207	Construction of Bypass to Madurai Achambathu Viratipathu in between km 6/850 10/382 of NH 49 Extn New NH 85 including Land Acquisition on Engineering, Procurement & Construction EPC basis Contract under NH O Annual Plan 2021-22 in the state of Tamil Nadu job No.NH-49 Extn New NH 85 - TN-2021-22-997 (MoRTH) (617962)	Tamil Nadu	03/2022 (09/2024)	08/2026 (-)	238.97 (260.07)	85.64	72
1208	Bangalore Chennai Expressway Phase-III Package II Walajahpet to Arakkonam from Km 180.000 to Km 204.500 (National Highways Authority of India [NHAI]) (618478)	Tamil Nadu	01/2021 (07/2022)	07/2024 (-)	1106.65 (1106.65)	496.04	90
1209	Bangalore Chennai Expressway Phase-III Package III Arakkonam to Kancheepuram from Km 204.500 to Km 230.000 (National Highways Authority of India [NHAI]) (618479)	Tamil Nadu	12/2020 (08/2022)	07/2024 (03/2025)	1525.1 (1525.1)	353.81	53
1210	4L Bangalore-Chennai Expressway from Km. 230.000 to Km. 261.705 of Kancheepuram to Sriperumbudur Section Phase-III/Package-IV (National Highways Authority of India [NHAI]) (618481)	Tamil Nadu	02/2021 (07/2022)	07/2024 (-)	3605.73 (3605.73)	878.13	62
1211	Karaipettai to Walajapet from Km 71.015 to 107.091 (National Highways Authority of India [NHAI]) (618521)	Tamil Nadu	08/2018 (02/2019)	02/2021 (04/2025)	766.51 (766.51)	426.79	88
1212	4L of Madurai Ring Road Phase 1 [Vadipatti-Thamrapatti] from km 0.00 - km 29.960 (National Highways Authority of India [NHAI]) (618563)	Tamil Nadu	12/2018 (03/2020)	03/2022 (08/2025)	900.05 (900.05)	535.7	90



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1213	4L of left-over works including additional structures from Kerala/Tamil Nadu border to Kanyakumari Section from Km 43.0 to Km 96.174 of NH66 (National Highways Authority of India [NHAI]) (618608)	Tamil Nadu	11/2022 (08/2023)	08/2025 (04/2026)	1564.23 (1263.42)	802.39	70
1214	6L of Pondavakkam to Kannigaipair from km 96.040 to km 116.100 of NH 716B Pkg-IV (National Highways Authority of India [NHAI]) (618635)	Tamil Nadu	02/2021 (01/2023)	01/2025 (11/2025)	1359.81 (1359.81)	301.77	31
1215	4L of Thirumangalam to Vadugapatti section from km 0.000 to km 36.000 of NH-744 (National Highways Authority of India [NHAI]) (618744)	Tamil Nadu	03/2022 (02/2023)	02/2025 (-)	1076.97 (791.6)	651.91	92
1216	4L of Vadugapatti to Theruvengallur Rajapalyam section from km 36.000 to km 71.600 of NH-744 (National Highways Authority of India [NHAI]) (618745)	Tamil Nadu	02/2022 (04/2023)	04/2025 (-)	1317.6 (1137.16)	917.08	99
1217	Melur - Pilayarpatti - Karaikudi from km 99.920 of NH 38 to km 12.9 of NH 383 Ext. (National Highways Authority of India [NHAI]) (618756)	Tamil Nadu	12/2018 (03/2020)	03/2022 (05/2025)	1103.86 (1085.41)	157.65	90
1218	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package II from Km 4.604 to Km 9.700 (National Highways Authority of India [NHAI]) (618800)	Tamil Nadu	03/2023 (11/2023)	05/2026 (-)	1616.97 (1616.97)	99.84	13
1219	Construction of New Double Tier 4-lane Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from Km -0342 to Km 20223 Package 1 from Km -0342 to Km 4604 (National Highways Authority of India [NHAI]) (618801)	Tamil Nadu	03/2023 (11/2023)	05/2026 (-)	1388.59 (1388.59)	120.51	14
1220	4L of Madathukulam - Pollachi from km. 74.38 to km. 116.95 of old NH-209 New NH-83 (National Highways Authority of India [NHAI]) (618894)	Tamil Nadu	01/2019 (12/2020)	12/2022 (-)	1772.13 (1772.13)	211.73	90
1221	Kamalapuram to Oddanchatram from km. 0.00 to km. 35.822 (National Highways Authority of India [NHAI]) (618895)	Tamil Nadu	01/2019 (01/2021)	01/2023 (03/2026)	1319.42 (1319.42)	331.43	88
1222	4L of Sethiyathope -Cholapuram section from Km. 65.960 to Km. 116.440 section of NH45 C Pkg-II (National Highways Authority of India [NHAI]) (618897)	Tamil Nadu	NA (08/2018)	08/2020 (06/2024)	2356.19 (2356.9)	1011.27	100
1223	6-laning of km 9.900 to km 19/948 Aramgarh to Shamshabad Section of Hyderabad-Bangalore section of NH-44 Under NHO EPC basis in the state of Telangana (MoRTH) (617913)	Telangana	01/2018 (05/2018)	05/2020 (07/2021)	283.15 (300.7)	252.28	88
1224	Widening to two/four lane with paved shoulder from Km.180.600 to Km.223.000 of NH-63 on Nizamabad-Jagadapur road on EPC mode under NHO in the state of Telangana. (MoRTH) (617936)	Telangana	10/2016 (03/2017)	03/2019 (-)	253.99 (183.26)	0	0
1225	Rehabilitation and Upgradation of LB-Nagar to Malkapur section to 6-Lane main carriageway with service roads, drains cum footpath, including VUPs and widening of Minor bridge & road safety provisions from Km. 15/00 to Km 40/00 of NH-65 Old NH-9 under NH O for the year 2020-21 in the state of Telangana on EPC Mode. (MoRTH) (617940)	Telangana	03/2021 (07/2022)	07/2024 (09/2025)	545.11 (545.11)	258.75	60
1226	Construction of six lane elevated corridor from km 7.950 Uppal to km 14.200 of NH-163 to De-Congest the urban limits of Hyderabad-Bhoopalapatnam section on EPC mode in the state of Telangana (MoRTH) (617980)	Telangana	03/2018 (07/2018)	07/2020 (04/2026)	626.76 (626.76)	13.91	49
1227	Widening and strengthening of existing 2-lane to 2-lane with paved shoulders from km 159/0 to 165/4 and 186/0 to 215/0 of NH-163 on EPC mode in the state of Telangana (MoRTH) (617982)	Telangana	01/2018 (06/2018)	11/2019 (12/2020)	230.03 (230.03)	0	0
1228	Widening & Strengthening of Existing 2LPS to 4 lane PS from Km 150000 to Km 159000 and Km 165400 to Km 186000 of NH-163 old NH-202 under NH O for the year 2020-21 on EPC Mode in the state of Telangana. (MoRTH) (617983)	Telangana	03/2021 (07/2022)	07/2024 (04/2025)	317.19 (300.56)	168.8	82
1229	Rehabilitation & upgradation of NH - 167 from design km 187.723 to 234.434 Miryalaguda to Kodad section to two lane with paved shoulder on EPC mode in the state of Telangana (MoRTH) (617992)	Telangana	03/2018 (09/2018)	09/2020 (-)	322.81 (322.81)	43.78	0
1230	Rehabilitation and upgradation of NH-167 from design km 113.900 to 154.479 Mallepally Haliya section to two lane with paved shoulders on EPC mode in the state of Telangana (MoRTH) (617994)	Telangana	02/2018 (06/2018)	11/2019 (-)	294.13 (257.61)	3.16	88
1231	Widening to Two Lane with Paved Shoulders from Km 67.000 to Km 114.425 of Kalwakurthy- Mallapally Section of NH 167 Erstwhile section of SH 18 in the State of Telangana on EPC mode under NH O Annual Plan 2016-17 (MoRTH) (617995)	Telangana	01/2017 (05/2017)	05/2019 (07/2021)	300 (300)	2.08	99
1232	Widening to 2/4 Lane with paved shoulders from Km 182.120 to Km 227.600 of NH 167 on Haggari-Jadcherla Road on EPC mode under NHO in the state of Telangana (MoRTH) (617996)	Telangana	10/2016 (02/2017)	02/2019 (07/2023)	298 (298)	228.09	95
1233	Construction of 4-lane flyover at Amberpet-X road, Hyderabad on NH-202 in the State of Telangana (MoRTH) (618001)	Telangana	05/2018 (06/2021)	06/2023 (04/2024)	216.53 (265.88)	154.05	36
1234	Rehabilitation and upgradation from km 121/000 to 154/000 Nakrekal to Mallampally section of NH-365 to 2 lane with paved shoulders in the state of Telangana in the EPC mode (MoRTH) (618025)	Telangana	03/2018 (06/2018)	12/2019 (-)	192.67 (192.67)	0	96



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1235	Rehabilitation and upgradation to two lane with paved shoulders from Km 0/000 to 72/6 of NH-365 Nakrekal to Tanamcherla section under NHDP IV in the state of Telangana under EPC mode (MoRTH) (618026)	Telangana	06/2017 (11/2017)	10/2019 (-)	605.08 (605.08)	0	0
1236	Widening to two lane with paved shoulders from Km 0/000 to Km 79/300 of Kalwakurthy - Kollapur section of NH-167K in the state of Telangana under annual plan 2021-22 on EPC mode under NHO. (MoRTH) (618104)	Telangana	03/2022 (07/2023)	07/2025 (-)	886.69 (886.69)	557.4	78
1237	Widening and strengthening to 4 lane / 2-lane with paved shoulders of Mahabubnagar - Chincholi section from km 60/255 to Km 102/834 of NH-167N in the State of Telangana on EPC mode. (MoRTH) (618105)	Telangana	03/2022 (10/2023)	10/2025 (-)	631.49 (631.49)	71.91	0
1238	Widening and Strengthening to 2/4 lane with paved shoulders of Mahabubnagar Chincholi section from Km 0/0 to Km 60/255 of NH-167N in the state of Telangana under Annual plan 2021-22 on EPC modepackage-I under NHO Job No.167N-TS-2021-22-75 (MoRTH) (618106)	Telangana	01/2022 (01/2023)	01/2025 (-)	703.68 (703.68)	252.3	87
1239	Widening & strengthening of existing carriageway in 2 lane with paved shoulders from km 25/0 to 59/2 design Ch km 25.467 to 59.200 of NH - 353C on EPC mode in the state of Telangana (MoRTH) (618132)	Telangana	02/2018 (06/2018)	06/2020 (-)	206.13 (206.13)	152.77	98
1240	Widening and Improvement of existing carriage way to 2 lane with paved shoulders from Km. 86/160 to 131/730 of Jangaon-Duddeda section of NH-365B in the State of Telangana on EPC Mode (MoRTH) (618141)	Telangana	01/2022 (12/2022)	12/2024 (06/2025)	423.48 (423.48)	159.94	0
1241	Widening to Two lane with Paved shoulders from km.40/410 to 84/037 of Thirumanlagiri-- Suryapet Section of NH-365B eastwhile section of SH-16 (MoRTH) (618142)	Telangana	01/2017 (05/2017)	05/2019 (05/2019)	244.54 (244.54)	0	99
1242	widening to two lane with Paved shoulders from Km.0/970 to Km.40/410 of Jangaon - Thirumal giri of NH- 365B in the state of Telangana on EPC mode under NHO Annual Plan 2016-17 (MoRTH) (618143)	Telangana	03/2017 (11/2017)	10/2019 (10/2019)	197 (197)	0	92
1243	Rehabilitation and Up-gradation of Valigonda to Thorur Section to Two Lane with Paved Shoulders from Km 39.180 to Km 108.300 of NH-930P in the State of Telangana on Engineering, Procurement and Construction EPC Basis (MoRTH) (618186)	Telangana	01/2022 (12/2022)	12/2024 (04/2025)	549.28 (549.28)	280.02	82
1244	Widening to two lane with paved shoulders of 'Bodhan Basar Bhainsa ' section from Km 38/900 to 95/300 of NH-161BB in the state of Telangana under Annual Plan 2021-22 on EPC Mode under NH O. (MoRTH) (618190)	Telangana	03/2022 (03/2023)	03/2025 (-)	644.45 (644.45)	348.93	0
1245	Widening to 2 lane with Paved Shoulders of Siddipet-Elkathurthy section from Km 69/978 to km 133/619 of NH-765DG in the State of Telangana under Annual plan 2021-22 on EPC mode (MoRTH) (618196)	Telangana	01/2022 (12/2022)	12/2024 (01/2025)	578.85 (578.85)	0	76
1246	Widening to 2 lane with Paved Shoulders of Medak - Siddipet section from Km 0/0 to km 69/978 of NH-765DG in the State of Telangana under Annual plan 2021-22 on EPC mode (MoRTH) (618197)	Telangana	01/2022 (01/2023)	01/2025 (07/2025)	882.18 (882.18)	347.42	73
1247	Improvement of Geometrics of Kalkallu to Gundla Pochanpalli from Km 454.00 to Km 471.00 of NH-44 (National Highways Authority of India [NHAI]) (618558)	Telangana	03/2022 (01/2023)	01/2025 (07/2026)	955.49 (903.17)	427.03	35
1248	6L of existing 4L from Gundlapochampally to Bowenpally from km 471.300 to km 481.331 of NH-44 (National Highways Authority of India [NHAI]) (618559)	Telangana	12/2021 (08/2022)	07/2024 (04/2026)	521.53 (528.21)	256.27	50
1249	Improvement of Geometrics of Thondupally to Kothur from Km 22.300 to Km 34.14 of NH-44 (National Highways Authority of India [NHAI]) (618560)	Telangana	03/2022 (03/2023)	09/2024 (-)	541.58 (527.43)	45.13	10
1250	Khammam-Devarapalle Pkg I [4L Access Controlled Greenfield from Thallampadu village to Somavaram village Design Chainage 0000 to 33604] (National Highways Authority of India [NHAI]) (618746)	Telangana	01/2021 (10/2022)	10/2024 (01/2026)	797.36 (1337.18)	570.63	91
1251	4L of Kodad Design Km 0.00/Existing Km 185.00 of NH-65 to Khammam Design Km 31.800/Existing Km 29.400 of NH-365A (National Highways Authority of India [NHAI]) (618945)	Telangana	01/2021 (01/2022)	05/2024 (05/2025)	1149.17 (1606.99)	688.18	99
1252	Rehabilitation and up-gradation of road from km 16.077 to km 43.935 total length 27.858 km of Lalchara-Kanchanpur section via Shivbari on NH-44A to 2 lane with paved shoulder in the state of Tripura on EPC Mode Pkg-2 under BharatMala Pariyojana Manu-Simlung -2 (NHIDCL) (618307)	Tripura	02/2022 (01/2023)	01/2025 (04/2025)	456.88 (456.88)	0	0
1253	Improvement and Widening to 2-lane with paved shoulder of road from design Km 36.000 Rangamati to design Km 72.000 Pati Chhari Total length 36.000 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-3 (NHIDCL) (618368)	Tripura	01/2024 (09/2024)	09/2026 (-)	670.9 (670.9)	0	6



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1254	Improvement and Widening to 2-lane with paved shoulder of road from existing Km 438.170 Khowai Chowmuhani to existing Km 439.410 South Pulipur of NH-08 and from design Km 0.000 South Pulipur to design Km 36.00 near Rangamati of NH 208 on Khowai Teliamura- Harina section Total length 37.24 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-2 (NHIDCL) (618369)	Tripura	01/2024 (09/2024)	09/2026 (-)	657.21 (657.21)	0	42
1255	Improvement and Widening to 2-lane with paved shoulder of road from Km 101.300 to km 127.319 Total Length 26.019 Km i.e. the Khowai Teliamura-Amarpur-Harina-Sabroom section of NH 208 in the state of Tripura on EPC under JICA ODA Loan Phase VI Package-1 (NHIDCL) (618370)	Tripura	01/2024 (07/2024)	07/2026 (-)	431.78 (431.78)	0	0
1256	Rehabilitation and up-gradation of road from design km 25.250 to km 36.460 Total length 11.210 km of Kailashahar-Kurti Bridge section on NH-208A to 2-lane with paved shoulder on EPC basis under NHO Package-III- Balance Work (NHIDCL) (618385)	Tripura	02/2020 (09/2024)	09/2025 (-)	174.43 (174.43)	0	0
1257	Rehabilitation & Upgradation of Road from Km 0.00 to Km 18.600 Total length-18.600 km of Kumarghat-Kailashahar section on NH-208 to 2-lane with Paved shoulder on EPC basis under NHO (NHIDCL) (618386)	Tripura	02/2020 (07/2020)	01/2022 (10/2024)	277.5 (302.03)	0	0
1258	Melaghar-Srimantapur section on NH-08 Spur from Km 23 to Km 34.500 11.5 Km and overlay from Km 20.30 to Km 22.00 1.7 Km Total Length 13.2 Km (NHIDCL) (618411)	Tripura	01/2023 (05/2023)	11/2024 (12/2025)	195.95 (195.95)	0	0
1259	Construction of 4-Lane with paved shoulder Agartala bypass Western side, length 25.402 km connecting NH-8 near Amtali to NH-108B near Lembuchhera in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618417)	Tripura	03/2023 (03/2024)	03/2027 (-)	2026.05 (2026.05)	0	0
1260	Construction of Jasra Bypass with four lane paved shoulder configuration from Km 379.670 on NH-76New NH-35 to Km 18.00 on NH-27New NH-30 on EPC in the State of Uttar Pradesh. (MoRTH) (617957)	Uttar Pradesh	02/2023 (03/2024)	09/2025 (-)	274.06 (274.06)	0	91
1261	Widening to Four Lane rigid pavement configuration from Km 90.00 to Km 100.800 on NH-96 Km 42.0 to Km 53.300 as per new NH-330, design length of 11.300 km under EPC mode in the state of Uttar Pradesh. (MoRTH) (617964)	Uttar Pradesh	12/2022 (11/2024)	11/2026 (-)	309.63 (309.63)	24.81	22
1262	Construction of four-lane elevated viaduct from km.4634 to km.6345 on NH-24A including Retaining wall, service lane, at grade road and improvement of junctions, on EPC mode (MoRTH) (618008)	Uttar Pradesh	03/2021 (03/2022)	09/2023 (03/2024)	185.09 (269.81)	158.8	100
1263	Balance work of Construction of Ring Road for Raebareli City on eastern side of NH-24B Phase-1 on EPC mode. (MoRTH) (618009)	Uttar Pradesh	12/2019 (10/2020)	04/2022 (07/2022)	319.96 (347.8)	0	0
1264	Construction of Balrampur bypass with 2L flexible pavement configuration from km.223.000 of NH-330 to km.328.300 of NH-730 under EPC mode (MoRTH) (618054)	Uttar Pradesh	12/2022 (08/2024)	02/2026 (-)	515.69 (515.69)	80.95	40
1265	Construction of Pratapgarh Bypass Extension connecting NH-31 to NH-330 on EPC mode in the State of Uttar Pradesh. (MoRTH) (618055)	Uttar Pradesh	10/2022 (01/2024)	06/2025 (-)	225.17 (225.17)	0	66
1266	Improvement and Up-gradation to two Lane with Paved Shoulder Configuration from existing km. 420.00 Shohratgarh to km. 454.00 Uska Bazar of NH-730 in the state of Uttar Pradesh EPC basis (MoRTH) (618056)	Uttar Pradesh	01/2022 (03/2024)	09/2025 (04/2026)	509.65 (484.42)	84.14	48
1267	Construction of Shohratgarh Bypass on NH-730 under EPC mode in the State of Uttar Pradesh (MoRTH) (618057)	Uttar Pradesh	10/2022 (11/2023)	05/2025 (-)	189.31 (189.31)	0	0
1268	Widening & Strengthening of section from Bharthana chowk to Kodarkoot km.0.00 to km.40.00 of NH-91-A on EPC mode (MoRTH) (618063)	Uttar Pradesh	03/2020 (03/2023)	09/2024 (08/2025)	262.37 (343.77)	112.46	90
1269	Construction of two lane with paved shoulder from existing Km.0.000 to Km.55.610 design km. 0.000 to km. 54.048 of NH-124D (MoRTH) (618075)	Uttar Pradesh	12/2021 (02/2024)	02/2026 (-)	840.93 (773.58)	134.9	55
1270	Construction of Mariahu Bypass with four lane paved shoulder configuration Km. 53.540 to Km.59.200 of NH-135A on EPC mode in the state of Uttar Pradesh (MoRTH) (618081)	Uttar Pradesh	03/2023 (02/2024)	02/2026 (-)	438.24 (362.39)	0	44
1271	Widening & Upgradation to four lane configuration from Km.34.900 Bhadohi to km.73.134 Jaunpur of NH-135A on EPC mode (MoRTH) (618082)	Uttar Pradesh	03/2021 (11/2022)	05/2024 (-)	395.62 (392.03)	0	84
1272	Improvement and upgradation to two lane with Paved Shoulder configuration from existing km 55.00 to km 90.00 Design length 34.76 of NH-227A near Chhapiya Village to near Sikriganj in the State of UP on EPC Mode. (MoRTH) (618110)	Uttar Pradesh	11/2021 (11/2022)	05/2024 (07/2025)	307.11 (307.11)	125.88	0
1273	Improvement and upgradation to two lane with paved shoulder configuration from existing km 90.00 to 130.00 Design length 39.15 of NH-227A near Sikriganj to Barhalganj in the State of UP on EPC Mode. (MoRTH) (618111)	Uttar Pradesh	08/2021 (12/2023)	06/2025 (-)	403.36 (345.34)	0	84



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1274	Rehabilitation and upgradation from km 51.600 to km 75.700 of NH-321G Nuhkhas to Etah section to two lane with paved shoulder configuration under EPC mode in the State of Uttar Pradesh (MoRTH) (618124)	Uttar Pradesh	01/2022 (02/2024)	08/2025 (-)	343.54 (343.54)	53.25	47
1275	Rehabilitation and Up-gradation from km. 0000 to km.40390 of NH-730S MaharajganjNchloulThuthibari to two lane with paved shoulders in the State of U.P. on Engineering, Procurement & Construction EPC Basis. (MoRTH) (618163)	Uttar Pradesh	03/2023 (06/2024)	12/2025 (-)	809.25 (603.19)	0	52
1276	Construction of four lane highway with paved shoulder from Km.74.700 to Km.112.950 of NH-731A i/c Yamuna Bridge on HAM in the state of Uttar Pradesh. (MoRTH) (618164)	Uttar Pradesh	03/2022 (06/2024)	06/2026 (-)	1141.67 (1157.31)	0	66
1277	Construction of 4-lane highway with paved shoulders from Km 49.155 to Km 74.700 of NH-731A on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) (618165)	Uttar Pradesh	01/2022 (02/2024)	01/2026 (-)	1156.72 (1156.72)	0	90
1278	Construction of 4-lane green field highway from Km. 35.000 to Km. 49.155 of NH-731A with paved shoulders on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) (618166)	Uttar Pradesh	01/2022 (10/2023)	10/2025 (-)	697.66 (697.66)	0.04	98
1279	Rehabilitation & Upgradation of NH-731A from Km.0.00 to Km.35.00 to 2-lane with paved shoulder under EPC mode (MoRTH) (618167)	Uttar Pradesh	03/2021 (08/2022)	08/2023 (-)	264.86 (264.86)	0	50
1280	Widening to four lane with paved shoulder from Design Km.49.200 to Km.89.285 of NH-731B on EPC mode in the state of Uttar Pradesh (MoRTH) (618168)	Uttar Pradesh	03/2022 (01/2024)	01/2026 (-)	917.91 (965.3)	116.91	50
1281	Construction of Two Lane with paved shoulder highway from Design Ch.0.000 to Ch.49.200 of NH-731B on EPC Mode (MoRTH) (618169)	Uttar Pradesh	03/2022 (11/2023)	11/2025 (-)	640.18 (602.76)	227.12	93
1282	Rehabilitation and upgradation to 2-lane with paved sholders configuration of Near Karri village-Etawah section Km30.000 to Km 57.346 Pakage-II of NH-92 in state of Uttar Pradesh undergreen national Highway Corridor ProjectGNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618229)	Uttar Pradesh	04/2020 (08/2022)	02/2024 (02/2025)	211.09 (206.56)	0	100
1283	Construction of 6-lane bridge on Ganga on NH-96 and its approaches in Phaphamau Allahabad on EPC mode (MoRTH) (618233)	Uttar Pradesh	07/2018 (02/2021)	02/2024 (07/2024)	1948.25 (1465.41)	0	60
1284	Rehabilitation and upgradation to 2-lane with paved sholders configuration of Bewar-naer Karri village section Km0.00 to Km30.00 Pakage-I of NH-92 in state of Uttar Pradesh undergreen national Highway Corridor ProjectGNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618240)	Uttar Pradesh	04/2020 (09/2022)	03/2024 (05/2024)	236.47 (236.47)	0	90
1285	Rehabilitation and upgradation to 2-lane with paved sholders configuration of Miranpur Katra to radhaita section of NH-730CKm.114.000 to Km 137.250package-III in state of Uttar Pradesh undergreen national Highway Corridor ProjectGNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618265)	Uttar Pradesh	04/2020 (07/2022)	07/2024 (12/2025)	172.5 (169.56)	0	71
1286	Rehabilitation and upgradation to 2-lane with paved sholders configuration of Bewar-Allahaganj- section of NH-730CKm.0.000 to Km 52.770package-I in state of Uttar Pradesh undergreen national Highway Corridor ProjectGNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618266)	Uttar Pradesh	04/2020 (11/2022)	11/2024 (-)	325.24 (340.16)	0	98
1287	6L Greenfield Kanpur - Lucknow Expressway Pkg II from km. 28.500 to km. 73.744 (National Highways Authority of India [NHAI]) (618498)	Uttar Pradesh	12/2021 (11/2022)	05/2025 (-)	2471.56 (2489)	1162.84	87
1288	6L Elevated Kanpur - Lucknow Exeressway Pkg-1 from Km. 10980 to Km. 28500 (National Highways Authority of India [NHAI]) (618499)	Uttar Pradesh	12/2021 (02/2023)	07/2025 (-)	1972.94 (1943.27)	765.57	75
1289	Construction of 4L Connector from Delhi Meerut Expressway Km 50.000 of Pkg IV to Km 8.520 of NH-235 Pkg-5 (National Highways Authority of India [NHAI]) (618500)	Uttar Pradesh	09/2021 (03/2022)	03/2024 (12/2025)	1081.39 (1116.19)	401.34	76
1290	Varanasi Ring Road Pkg-II connecting Sandaha Village km 11.70 / NH-29 with Revasa Village km 818.80 / NH-2 (National Highways Authority of India [NHAI]) (618529)	Uttar Pradesh	12/2017 (02/2019)	02/2022 (06/2025)	1991.71 (1832.66)	985.18	92
1291	Construction of Ring Road around Kanpur from Km.000 to Km. 23.325 Chachendi Sachendi I to Maharajpur Package-I (National Highways Authority of India [NHAI]) (618537)	Uttar Pradesh	01/2023 (12/2023)	06/2026 (-)	1753.75 (1311.7)	318.17	47
1292	6L of Agra Bypass Northern connecting Km. 174.500 of NH-2 new NH-19 to Km. 141.000 of Yamuna Expressways (National Highways Authority of India [NHAI]) (618553)	Uttar Pradesh	01/2022 (02/2023)	02/2025 (-)	957.62 (1034.42)	757.89	99
1293	Construction of left out portion of Agra Inner Ring Road connecting village Deori to NH-44 village Bad from Km. 0.000 to Km. 7.772 (National Highways Authority of India [NHAI]) (618554)	Uttar Pradesh	07/2022 (03/2023)	09/2024 (-)	879.26 (787.58)	606.99	87
1294	Strengthening of existing 4L Ayodhya Bypass Section from design Km. 121 600 to Km. 144020 of NH 28 New NH 27Pkg-3 (NHAI) (618565)	Uttar Pradesh	03/2023 (09/2023)	03/2025 (08/2025)	526.45 (281.13)	259.66	81
1295	4L Green Field Northern East side Gorakhpur Bypass 26.616 Kms starting from NH-29E Chainage 83.308 and end at NH-28 Chainage 285.100 (National Highways Authority of India [NHAI]) (618566)	Uttar Pradesh	02/2023 (01/2024)	01/2026 (-)	1973.98 (1244.44)	835.5	52



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1296	4L Rampur Bypass from Km. 181.000 to Km. 189.500 (National Highways Authority of India [NHAI]) (618689)	Uttar Pradesh	10/2021 (10/2022)	04/2024 (01/2025)	364.47 (307.95)	271.61	99
1297	DL/UP Border - EPE Crossing Pkg-02 (National Highways Authority of India [NHAI]) (618710)	Uttar Pradesh	09/2020 (05/2021)	11/2023 (08/2024)	2002.79 (1889.78)	1732.01	98
1298	6L access Controlled Greenfield Highway from Gogwan Jalalpur Shamli to Ranipur Barsi Saharanpur of Shamli -Ambala section Package-I Design Ch. Form km 00.600 to km 45.500 (National Highways Authority of India [NHAI]) (618722)	Uttar Pradesh	06/2022 (05/2023)	05/2025 (01/2026)	1843.59 (1247.55)	567.64	56
1299	4L Spur of Meerut-Garh-Mukteshwar section connecting NH-119 and NH-58 bypassing Meerut Town of NH 709 A (National Highways Authority of India [NHAI]) (618761)	Uttar Pradesh	10/2021 (02/2023)	02/2025 (-)	991.89 (977.73)	800.68	52
1300	4L Spur of Panipat - Shamli connecting NH-709AD Panipat Shamli Muzaffarnagar and NH-709A Karnal Meerut bypassing Shamli district UP (National Highways Authority of India [NHAI]) (618770)	Uttar Pradesh	10/2021 (10/2022)	10/2024 (03/2025)	516.16 (273.42)	232.93	74
1301	4L of Sonauli - Gorakhpur (National Highways Authority of India [NHAI]) (618798)	Uttar Pradesh	12/2021 (03/2023)	03/2025 (02/2026)	2555.5 (2275.43)	1238.07	54
1302	2L PS of Raebareli - Jagdishpur with 4L Jagdishpur Bypass Spur (National Highways Authority of India [NHAI]) (618854)	Uttar Pradesh	02/2021 (01/2022)	01/2024 (06/2025)	706.41 (752.52)	515.37	97
1303	Improvement and Up-Gradation of Existing Road to 2/4L PS from Km 40.000 to 88.750, start of Khutar bypass to start of Shahjahanpur bypass of NH 731Pkg-I (National Highways Authority of India [NHAI]) (618855)	Uttar Pradesh	03/2022 (02/2023)	02/2025 (09/2025)	838.68 (838.68)	556.76	99
1304	Improvement and Up-Gradation of Existing Road to 4L PS from Km 123.650 to 175.080, from Start of Shahabad Bypass to End of Hardoi bypass of NH 731 Pkg-2B (National Highways Authority of India [NHAI]) (618856)	Uttar Pradesh	09/2022 (11/2023)	11/2025 (04/2026)	1101.79 (1212.26)	312.56	50
1305	Improvement and Up-Gradation of Existing Road to 4L PS from Km 229.070 to 260.800, End of Hardoi District to Lucknow Ring road of NH 731 Pkg-4 (National Highways Authority of India [NHAI]) (618859)	Uttar Pradesh	09/2021 (10/2022)	10/2024 (05/2025)	575.66 (553.61)	371.12	93
1306	4L from Mathura Bypass Start at Existing Km. 154.20 of NH-44 to Gaju Village at Km 32.982 of NH-530B Pkg-IB (National Highways Authority of India [NHAI]) (618864)	Uttar Pradesh	01/2022 (03/2023)	03/2025 (10/2025)	1722.11 (1820.77)	1000.51	99
1307	4L from Gaju Village at Km. 32.982 to Devinagar Bypass End at Km. 208.000 of NH-530B Pkg-1C. (National Highways Authority of India [NHAI]) (618865)	Uttar Pradesh	12/2021 (01/2023)	01/2025 (-)	1384.79 (1496.44)	823.04	99
1308	Construction of Four Lane Highway form Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package I [from Hridaipur km 0.000 to Shahapur km 42.500] on EPC Mode in the state of Uttar Pradesh. (National Highways Authority of India [NHAI]) (618883)	Uttar Pradesh	10/2022 (07/2023)	07/2025 (12/2025)	1706.47 (1579.59)	723.1	92
1309	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package II [from Shahapur km 42.500 to Pindari km 78.150] on EPC Mode in the state of Uttar Pradesh. (National Highways Authority of India [NHAI]) (618884)	Uttar Pradesh	10/2022 (10/2023)	10/2025 (-)	1493.65 (1311.44)	610.51	80
1310	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package IV [from Buxur Spur of length km 17.270 on EPC Mode in the state of Uttar Pradesh. (National Highways Authority of India [NHAI]) (618885)	Uttar Pradesh	10/2022 (06/2023)	06/2025 (-)	617.88 (549.02)	218.78	74
1311	4L Greenfield Western Side spur of Rampur-Rudrapur Section from Km 0.000 to Km 13.700 connecting NH-24 to NH-87 bypassing rampur town (National Highways Authority of India [NHAI]) (618911)	Uttar Pradesh	12/2021 (05/2023)	11/2024 (03/2026)	646.27 (637.83)	146.09	61
1312	Bijnor-Kotawali (National Highways Authority of India [NHAI]) (618925)	Uttar Pradesh	02/2021 (11/2021)	05/2023 (02/2026)	300.58 (334.48)	247.05	95
1313	4L Prayagraj Greenfield By-pass from design Km 50860 near Nibi Kala Uperhar to design Km 64763 on NH-19 near Khodaypur Kasgaon including Interchange loop at NH-19 (National Highways Authority of India [NHAI]) (618959)	Uttar Pradesh	08/2023 (12/2023)	03/2025 (-)	1017.99 (427.54)	406.1	99
1314	4 Lane Inner Ring Road around Allahabad City Pkg-2 Prayagraj Southern Bypass 43.200 - 50.860 (National Highways Authority of India [NHAI]) (618960)	Uttar Pradesh	08/2023 (12/2023)	06/2026 (-)	1377.51 (1007.62)	292.08	39
1315	6L access control Greenfield highway of Vill-Khyawari to Vill-Latifpur at Saharanpur Bypass from Km. 82.000 to Km. 119.790 Pkg-4 (National Highways Authority of India [NHAI]) (618968)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (-)	1428.19 (1439.35)	1166.56	69
1316	6L access control Greenfield highway of Vill-Lohadda to Vill-Karaunda Mahajan from Km. 27.000 to Km. 56.500 Pkg-2 (National Highways Authority of India [NHAI]) (618970)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (-)	1335.45 (1335.38)	977.98	62
1317	Construction of 2 lane with paved shoulder of Kund Bypass from Design Km 35.130 to Km 47.700 existing Km 33.130 to Km 41.260 of NH-109 in the State of Uttarakhand (MoRTH) (617929)	Uttarakhand	02/2018 (05/2018)	05/2020 (02/2021)	247.41 (247.41)	0	73
1318	Construction & Widening Including Augustmuni Bypass Ch-16.545 to Ch - 19.890 to 2L/PS from Km 16.545-Km 33.130 & 45.980 -57.975 Augustmuni to Kund & Guptkashi to Sitapur on NH 109 in UK (MoRTH) (617968)	Uttarakhand	03/2017 (02/2018)	02/2020 (07/2021)	418.89 (418.89)	178.35	95



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1319	Reconstruction of existing 2 L/IL to 2L with paved shoulder from existing km 52.200 to 92.880 of NH- (MoRTH) (617970)	Uttarakhand	10/2016 (06/2017)	06/2019 (03/2021)	282.08 (282.08)	156.65	100
1320	Rehabilitation and upgradation to 2 lane with paved shoulder configuration from km 122.00 Dharasu Bend to km 147.230 Silkyara Bend of NH-94 in the state of Uttarakhand (MoRTH) (617975)	Uttarakhand	03/2017 (11/2017)	11/2019 (10/2021)	237.79 (237.79)	50.38	100
1321	Construction, Operation & Maintenance of 2-L Bi-directional Silkyara Bend- Barkot Tunnel with escape passage including approaches Tunnel-4.531 & Approach road-0.328 on Dharasu-Yamunotri section b/w Chainage 25.400km and 51.00km falling along NH-134 Old NH-94 on EPC mode (NHIDCL) (618390)	Uttarakhand	03/2018 (07/2018)	07/2022 (06/2026)	1383.78 (1383.78)	0	68
1322	Construction for Mitigation Measures of 5 Nos. Landslides, 05 No. Sinking Zones and 01 No. Bridge from Ch. 450.00 to Ch. 468.00 18 Km. Length on NH-07 Package-III (NHIDCL) (618391)	Uttarakhand	12/2023 (06/2024)	12/2025 (-)	250.33 (250.33)	0	64
1323	Construction for Mitigation Measures of 10 Nos. Landslides, 01 No. Sinking Zones and 1 No. of Minor Bridge in between at Ch. Km 368.00 to Km 433.00 on NH-07 on EPC Mode in Uttarakhand Package-1 (NHIDCL) (618393)	Uttarakhand	12/2023 (06/2024)	12/2025 (-)	216.68 (216.68)	0	87
1324	Construction of new road at the missing link portion of NH-81 along approved alignment between Harishchandrapur and Eastern approach of Kalindri Bridge from Km 46.550 to Km 59.697 in the district of Malda. (MoRTH) (617960)	West Bengal	08/2016 (11/2016)	11/2018 (11/2021)	271.17 (291.2)	7.4	0
1325	Development to 4/6-Lanning of NH-31 New NH-10 with both side service roads from 569.258 km to 581.030 km End of AH-02 on NH- 31 near Shivmandir to Sevoke Army Cantonment in districts of Darjeeling and Jalpaiguri in the state of West Bengal on EPC mode-reg. (MoRTH) (618227)	West Bengal	03/2022 (03/2023)	09/2025 (-)	995.04 (1059.2)	435.36	61
1326	Construction & upgradation of existing road to 2-lane with paved shoulder including geometric improvement of Kafer- Lava More section from km 40.00 to km 61.100 of NH717-A on EPC under SARDP-NE A in state of West Bengal Pkg-VA (NHIDCL) (618427)	West Bengal	06/2020 (10/2020)	04/2023 (10/2025)	311.02 (273.78)	6.11	0
1327	Construction & upgradation of existing road to 2-lane with paved shoulder including geometric improvement of sect. from Pedong bypass to Reshi Border km 79.700 to km 96.254 of NH-717A under SARDP-NE-A on EPC as part of Alternate connectivity to Gangtok Lava More-Reshi Border Pkg-VB (NHIDCL) (618429)	West Bengal	06/2020 (10/2020)	04/2022 (06/2023)	345.38 (395.59)	0	0
1328	Construction of alternative highway to Gangtok in Sikkim via Bagrakot -Chuikhim-Nimbong -Kafer-Bakhim-Algarah-Rhenock in the State of West Bengal and from Rhenok-Rorathang-Pakyong along with spur from Aritar-Rolep-Menla in the State of Sikkim from Km 0.00 to Km 13.00 of Bagrakot -Kafer section of NH 717A on EPC Mode under Phase-A of SARDP-NE in the State of West Bengal PKG- IVA (NHIDCL) (618430)	West Bengal	03/2018 (10/2019)	04/2022 (06/2025)	402.94 (402.94)	0	0
1329	Construction of alternative highway to Gangtok in Sikkim via Bagrakot -Chuikhim-Nimbong -Kafer-Bakhim-Algarah-Rhenock in the State of West Bengal and from Rhenok-Rorathang-Pakyong along with spur from Aritar-Rolep-Menla in the State of Sikkim from Km 13.00 to Km 25.60 of Bagrakot -Kafer section of NH 717A on EPC Mode under Phase-A of SARDP-NE in the State of West Bengal PKG- IVB (NHIDCL) (618431)	West Bengal	03/2018 (10/2020)	04/2023 (03/2025)	295.97 (295.97)	0.39	0
1330	Bridge over Ganga River at d/s of Farraka Barrage including Approaches connecting Farakka-Raiganj (National Highways Authority of India [NHAI]) (618825)	West Bengal	08/2018 (12/2018)	12/2021 (02/2025)	622.04 (646.1)	339.1	95
1331	4L of Purulia Bypass section from Km 84.030 to Km 94.345 of NH-32 (National Highways Authority of India [NHAI]) (618910)	West Bengal	01/2021 (02/2022)	08/2023 (02/2024)	557.55 (562.57)	444.43	65
Total (584)					527441.16	185963.95	
Department of Telecommunications							
Telecommunication							
1332	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance (Erstwhile NICF)) (709859)	Delhi	10/2014 (04/2018)	02/2020 (06/2026)	248.2 (248.2)	236.91	98
1333	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (03/2026)	971.96 (971.96)	215.36	99
1334	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase 1 Upgradation (Department of Telecommunications [DoT]) (617413)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	04/2022 (05/2024)	05/2025 (03/2026)	1884.6 (1884.6)	376.8	93



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1335	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 (Department of Telecommunications [DoT]) (701599)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	NA (09/2021)	03/2023 (03/2026)	1577.57 (1577.57)	660.02	87
1336	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha (Department of Telecommunications [DoT]) (701602)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	11/2021 (05/2022)	11/2023 (05/2026)	3685 (3685)	1332.2	82
1337	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (03/2026)	1255.49 (1255.49)	299.02	99
1338	354 Uncovered Villages Scheme (Department of Telecommunications [DoT]) (701600)	Multi-States (Bihar, Gujarat, Himachal Pradesh, Jammu and Kashmir, Ladakh, Rajasthan, Uttar Pradesh)	12/2019 (04/2020)	10/2021 (08/2025)	336.89 (301.13)	237.19	100
1339	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajasthan and Uttar Pradesh (Department of Telecommunications [DoT]) (704495)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	NA (03/2021)	03/2022 (12/2025)	421.65 (228.94)	143.06	97
1340	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (709749)	Multi-States (Maharashtra, Telangana)	03/2020 (03/2020)	06/2021 (12/2025)	461.42 (461.42)	166.02	81
1341	Saturation 4G mobile coverage of Uncovered Villages through USOF (Department of Telecommunications [DoT]) (400013)	PAN India	07/2022 (07/2022)	06/2024 (03/2026)	26316 (30620)	9791.8	80
1342	4G Services by BSNL (Department of Telecommunications [DoT]) (701593)	PAN India	11/2020 (11/2020)	03/2024 (03/2026)	28466 (19592)	8471.19	97
1343	BharatNet (Department of Telecommunications [DoT]) (706775)	PAN India	07/2017 (10/2011)	08/2023 (03/2027)	61109 (188000)	46431.54	81
1344	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (709856)	PAN India	05/2023 (05/2023)	08/2024 (01/2026)	645.13 (645.13)	377.59	92
1345	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. (BSNL) (709857)	PAN India	05/2023 (06/2023)	06/2025 (03/2026)	24544.55 (24544.5)	8472.04	97
Total (14)					151923.46	77210.74	
Department of Water Resources, River Development & GR							
Waste & Water							
1346	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616600)	Bihar	10/2017 (03/2022)	02/2025 (12/2025)	413.29 (413.29)	126.67	97
1347	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616611)	Bihar	08/2017 (07/2019)	12/2025 (-)	824 (824)	396.71	56
1348	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616612)	Bihar	08/2017 (07/2019)	12/2025 (-)	578.89 (578.89)	171.79	54
1349	Sewer Network, SPS and STP at Begusarai (National Mission for Clean Ganga) (616615)	Bihar	03/2010 (03/2018)	04/2025 (12/2025)	230.06 (230.06)	261.82	97
1350	Sewer Networks, SPS and STP at Hajipur (National Mission for Clean Ganga) (616616)	Bihar	03/2010 (03/2018)	06/2025 (12/2025)	305.19 (305.19)	346.46	95
1351	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme (National Mission for Clean Ganga) (616594)	Uttar Pradesh	05/2020 (04/2023)	04/2025 (12/2025)	842.25 (842.25)	208.64	77
1352	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP (National Mission for Clean Ganga) (616605)	Uttar Pradesh	05/2020 (11/2024)	12/2024 (05/2027)	690.71 (690.71)	34.79	41
1353	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP (National Mission for Clean Ganga) (616604)	West Bengal	05/2018 (12/2021)	03/2025 (12/2025)	154.73 (154.73)	96.17	92
Total (8)					4039.12	1643.05	
Water Resources							
1354	Sardar Gouthu Latchanna Thotapalli Barrage Project (Water Resources-AP) (400100)	Andhra Pradesh	04/2005 (01/2006)	12/2019 (06/2026)	353.05 (1023.24)	869.11	95



All Ongoing Projects

DECEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1355	Gundlakamma project (Water Resources-AP) (400101)	Andhra Pradesh	04/2005 (04/2005)	12/2019 (03/2027)	397.41 (697.39)	619.09	98
1356	Polavaram Irrigation Project (Water Resources-AP) (701415)	Andhra Pradesh	01/2009 (11/2009)	04/2022 (03/2026)	10151.04 (55548.9)	25833.68	84
1357	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55
1358	Punpun Barrage Project (Water Resources-BR) (400104)	Bihar	04/2007 (04/2007)	12/2019 (03/2026)	571.07 (658.12)	447.68	44
1359	Kelo Irrigation Project (Water Resources-CT) (400111)	Chhattisgarh	04/2008 (04/2008)	12/2019 (06/2026)	459.97 (727.04)	616.93	72
1360	Kudali Irrigation Project (Department of Water Resources, River Development & GR) (701399)	Chhattisgarh	04/2009 (12/2009)	12/2025 (-)	382.29 (382.29)	239.03	86
1361	Sardar Sarovar CADWM Project (Narmada and Water Resources, Water Supply and Kalpsar Department-GJ) (400097)	Gujarat	04/2017 (04/2017)	12/2019 (03/2026)	5021.76 (6670.31)	4956.98	90
1362	Sardar Sarovar Project (Narmada and Water Resources, Water Supply and Kalpsar Department-GJ) (701372)	Gujarat	04/1996 (04/1996)	12/2019 (03/2026)	20718.17 (33412.5)	31860.86	93
1363	Subernarekha Multipurpose Project, Jharkhand (Department of Water Resources-JH) (701376)	Jharkhand	04/2011 (01/2012)	12/2019 (03/2026)	3807.77 (9579.58)	5790.29	70
1364	Upper Tunga Irrigation Project (Water Resources-KA) (701377)	Karnataka	04/2014 (04/2014)	12/2019 (03/2026)	770.16 (1606.07)	1515.32	99
1365	Omkareshwar CADWM Project (Water resource-mp) (400096)	Madhya Pradesh	04/2017 (04/2017)	12/2019 (03/2026)	648.09 (648.09)	206.06	49
1366	Bargi Diversion Project Phase - IV [km. 154 to km 197] (Water Resources-MP) (400115)	Madhya Pradesh	04/2008 (01/2009)	12/2019 (03/2026)	751.03 (893.35)	783.1	75
1367	Bargi Diversion Project Phase - III [km. 104 to km 154] (Water Resources-MP) (400116)	Madhya Pradesh	04/2007 (04/2007)	12/2019 (03/2026)	1229.15 (1399.7)	1993.52	80
1368	Gosikhurd CADWM Project (Department of water resources-MH - II) (400095)	Maharashtra	04/2017 (04/2017)	12/2019 (06/2026)	743.73 (743.73)	396.38	52
1369	Urmodi Irrigation Project (Department of water resources-MH - II) (400105)	Maharashtra	04/2017 (04/2018)	06/2022 (12/2026)	580.79 (895.81)	713.46	76
1370	Sulwade-Jamphal-Kanoli Lift Irrigation Scheme (Department of water resources-MH - II) (400107)	Maharashtra	04/2017 (02/2019)	06/2023 (06/2027)	2407.67 (2407.67)	2587.54	80
1371	Purna Barrage-2 [Ner Dhamana] Medium Irrigation Project (Department of water resources-MH - II) (400109)	Maharashtra	04/2017 (04/2018)	06/2020 (06/2026)	848.07 (888.43)	690.49	69
1372	Jigaon Irrigation Project (Department of water resources-MH - II) (400112)	Maharashtra	04/2017 (04/2018)	06/2028 (-)	7222.95 (7222.95)	9348.58	91
1373	Bodwad Parisar Sinchan Yojna (Department of Water Resources-MH) (617422)	Maharashtra	05/2002 (01/2017)	07/2027 (-)	1923.81 (1923.81)	1770.13	49
1374	Waghur Project (Department of water resources-MH - II) (701383)	Maharashtra	04/1996 (04/1996)	12/2019 (03/2026)	1058.99 (1758.51)	1557.67	89
1375	Gosikhurd Project (Department of water resources-MH - II) (701386)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2028)	7196.47 (12770.1)	13898.18	72
1376	Aruna Medium Irrigation Project (Department of water resources-MH - II) (701391)	Maharashtra	04/2009 (01/2010)	12/2019 (12/2025)	210.45 (1472.14)	1705.83	97
1377	Lower Pedhi Project (Department of water resources-MH - II) (701396)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2026)	255.97 (1480.7)	1324.98	65
1378	Nardave Medium Irrigation Project (Department of water resources-MH - II) (701398)	Maharashtra	04/2009 (04/2009)	12/2019 (06/2026)	211.46 (781.85)	623.5	72
1379	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
1380	North Koel Reservoir Project (Department of Water Resources, River Development & GR) (701412)	Multi-States (Bihar, Jharkhand)	08/2017 (01/2021)	03/2021 (03/2026)	1622.27 (2430.76)	167.16	36
1381	Integrated Anandpur Barrage Project (Water Resources-OR) (603945)	Odisha	04/1997 (01/1998)	12/2019 (06/2026)	567.03 (2990.05)	2715.12	62
1382	Kanupur Irrigation Project (Irrigation and CAD-TG) (701404)	Odisha	04/2003 (01/2004)	12/2019 (06/2026)	989.43 (2301.28)	2712.75	79
1383	Relining of Rajasthan feeder and Sirhind Feeder canal (Department of Water Resources-PB) (701410)	Punjab	02/2016 (04/2018)	06/2021 (06/2026)	1441.26 (2462.16)	3012.69	80
1384	Shahpur Kandi Dam Project (Department of Water Resources-PB) (701411)	Punjab	02/2010 (04/2018)	06/2022 (10/2025)	2285.81 (2715.7)	2169.72	88
1385	Sri Ram Sagar Project Stage - II (Irrigation and CAD-TG) (400102)	Telangana	04/2005 (04/2005)	12/2019 (03/2026)	736.13 (949.87)	940.7	96



All Ongoing Projects

DECEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1386	Indiramma Flood Flow Canal Project <i>(Irrigation and CAD-TG)</i> (400103)	Telangana	04/2005 (01/2006)	12/2019 (12/2026)	1331.3 (5940.09)	4491.08	92
1387	J. Chokka Rao Devadula Lift Irrigation Scheme <i>(Irrigation and CAD-TG)</i> (701405)	Telangana	04/2006 (04/2006)	12/2019 (12/2025)	8200.71 (14730)	4664.8	87
1388	Rajiv Bhima Lift Irrigation Scheme <i>(Irrigation and CAD-TG)</i> (701406)	Telangana	04/2007 (01/2008)	12/2019 (03/2026)	1402 (2509.66)	1839.76	100
1389	Saryu Nahar CADWM Project <i>(Irrigation & Water Resources-UP)</i> (400093)	Uttar Pradesh	04/2017 (04/2017)	12/2019 (03/2026)	1672.7 (1672.7)	22.24	1
1390	Morna [Gureghar] Irrigation Project <i>(Department of Water Resources, River Development & GR)</i> (701395)	Uttar Pradesh	04/2007 (12/2007)	12/2025 (-)	219.9 (219.9)	115.2	31
1391	Madhya Ganga canal Phase-II <i>(Irrigation & Water Resources-UP)</i> (701408)	Uttar Pradesh	04/2008 (04/2008)	12/2019 (12/2025)	1060.67 (4417.21)	4552.44	82
1392	Jamrani Dam Multipurpose Project <i>(Irrigation-UK)</i> (613787)	Uttarakhand	10/2023 (11/2023)	06/2029 (-)	2584.1 (2584.1)	987.61	21
Total (39)					93740.23	140622.27	



सत्यमेव जयते

Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.ipm.mospi.gov.in>
