



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation

478th — Flash Report on Central Sector Infrastructure Projects —



(Rs. 150 crore
& above)

AUGUST 2025



Scan the QR code to access
the PAIMANA Portal.

www.mospi.gov.in @GoIStats /GoIStats GoIStats Ministry of Statistics & PI



CONTENTS

I. Overview*	2-4
II. North Eastern Region	5-6
III. As per Harmonized Master List (HML) 2022	7-13
IV. Major Infrastructure Central Ministries & Departments	14-19
V. Appendix : <i>List of Tables</i>	20 onwards
Table 1: Ministry-wise Ongoing Projects	
Table 2: State-wise Ongoing Projects	
Table 3: Ongoing Projects of North Eastern Region	
Table 4: All Ongoing Projects	

**Note: This report is web-generated from the PAIMANA portal (ipm.mospi.gov.in) as of August 2025, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies (excluding Ministry of Road Transport & Highways, may reflect from next month onwards) on the IPM portal (indiainvestmentgrid.gov.in) latest by 12th September 2025.*





Overview





Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above

AUGUST 2025

800 | 14

Ongoing Projects |
Line Ministries & Departments

₹ 23,75,332

Original Cost
(crores)

₹ 29,07,548

Revised Cost
(crores)


₹ 15,37,609

(52.88% of Revised Cost)

Expenditure
(crores)


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

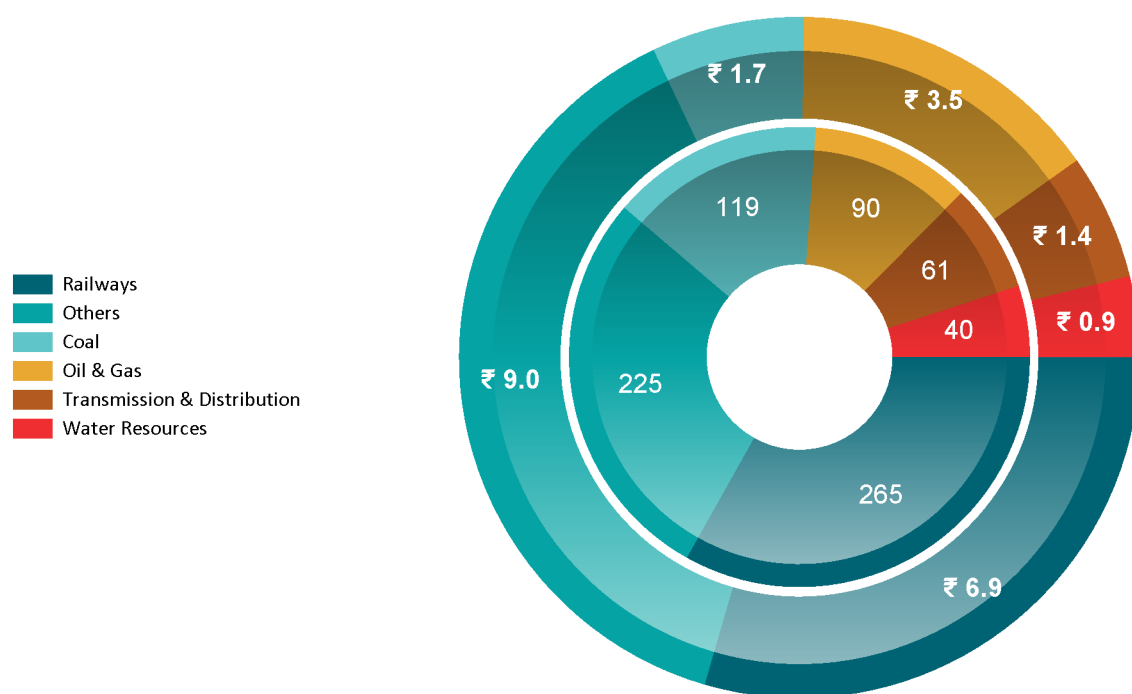


Ministry Comparison : Major Ministries*


[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

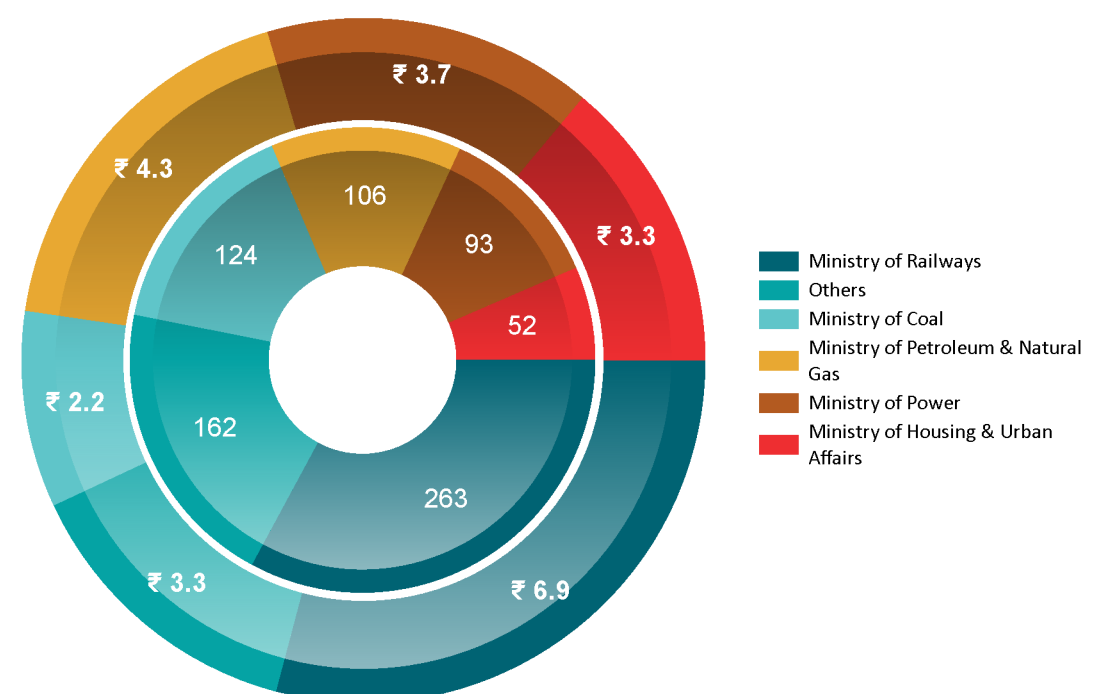

Cost Analytics : Major Sectors*

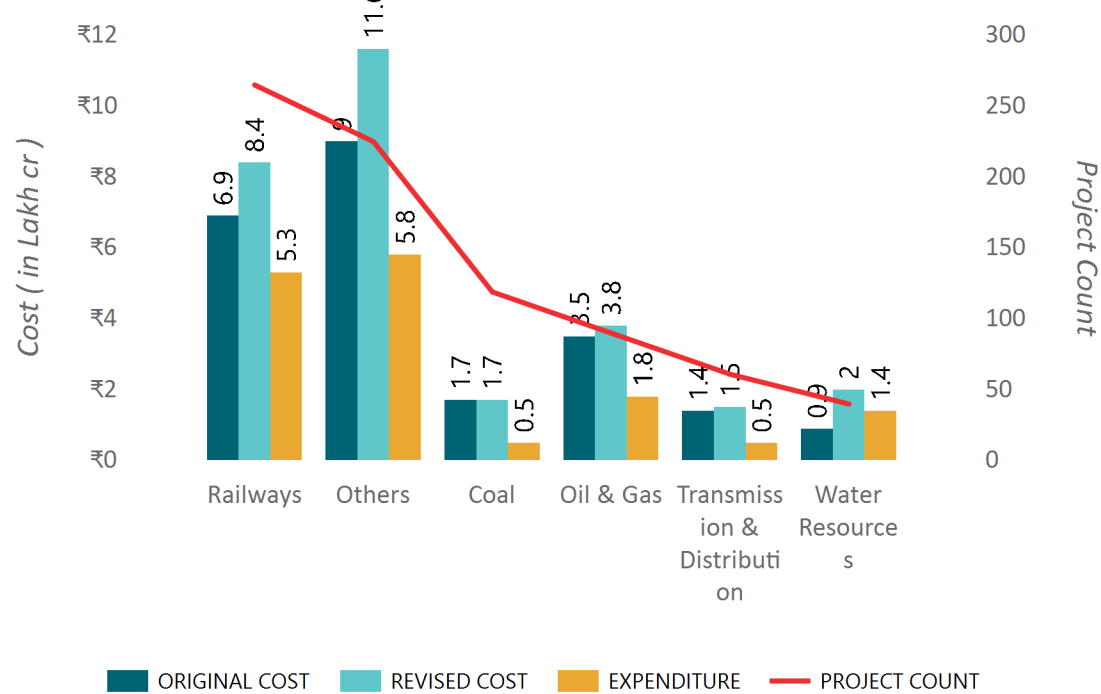


Cost Analytics : Major Ministries*

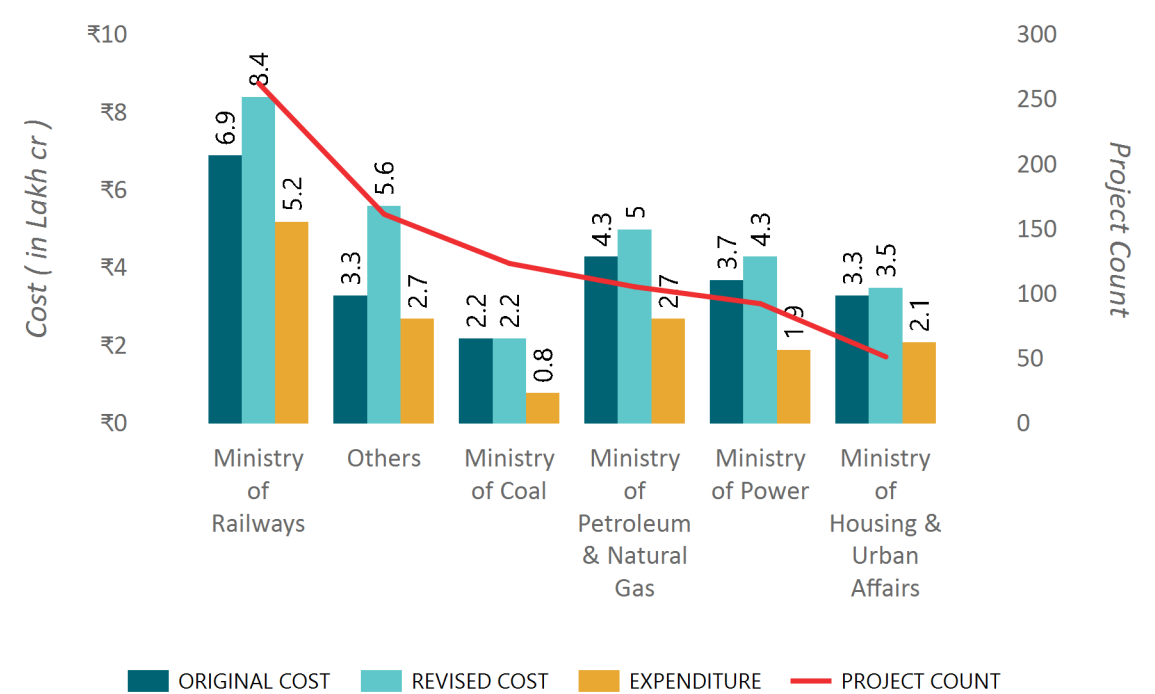


Note: * as per Project Count

Analytics: as per HML

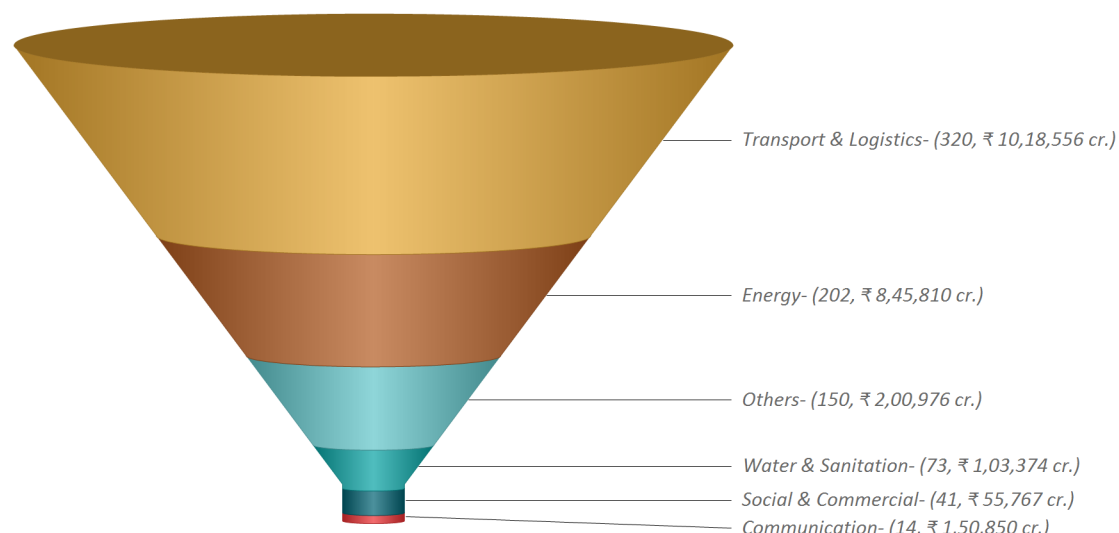


Note: all indicated legends are in format (Project count, Original Cost in crores)

Physical & Financial progress (%) : Project count

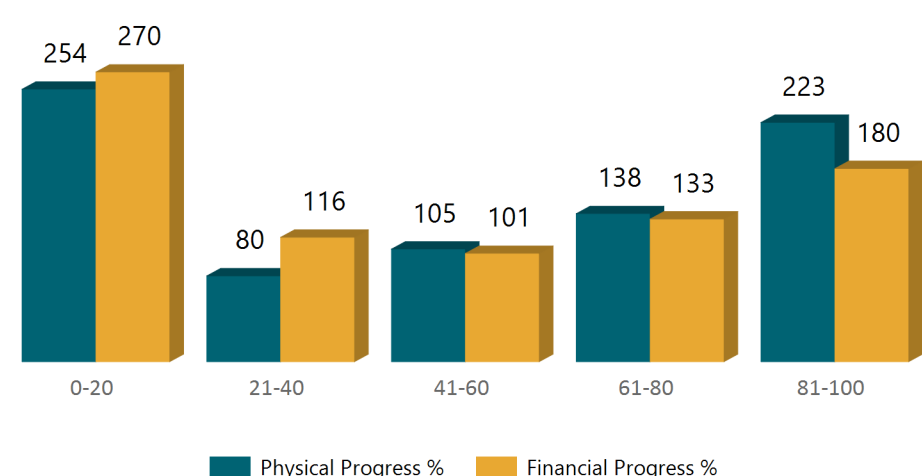




State Comparison : Major States*

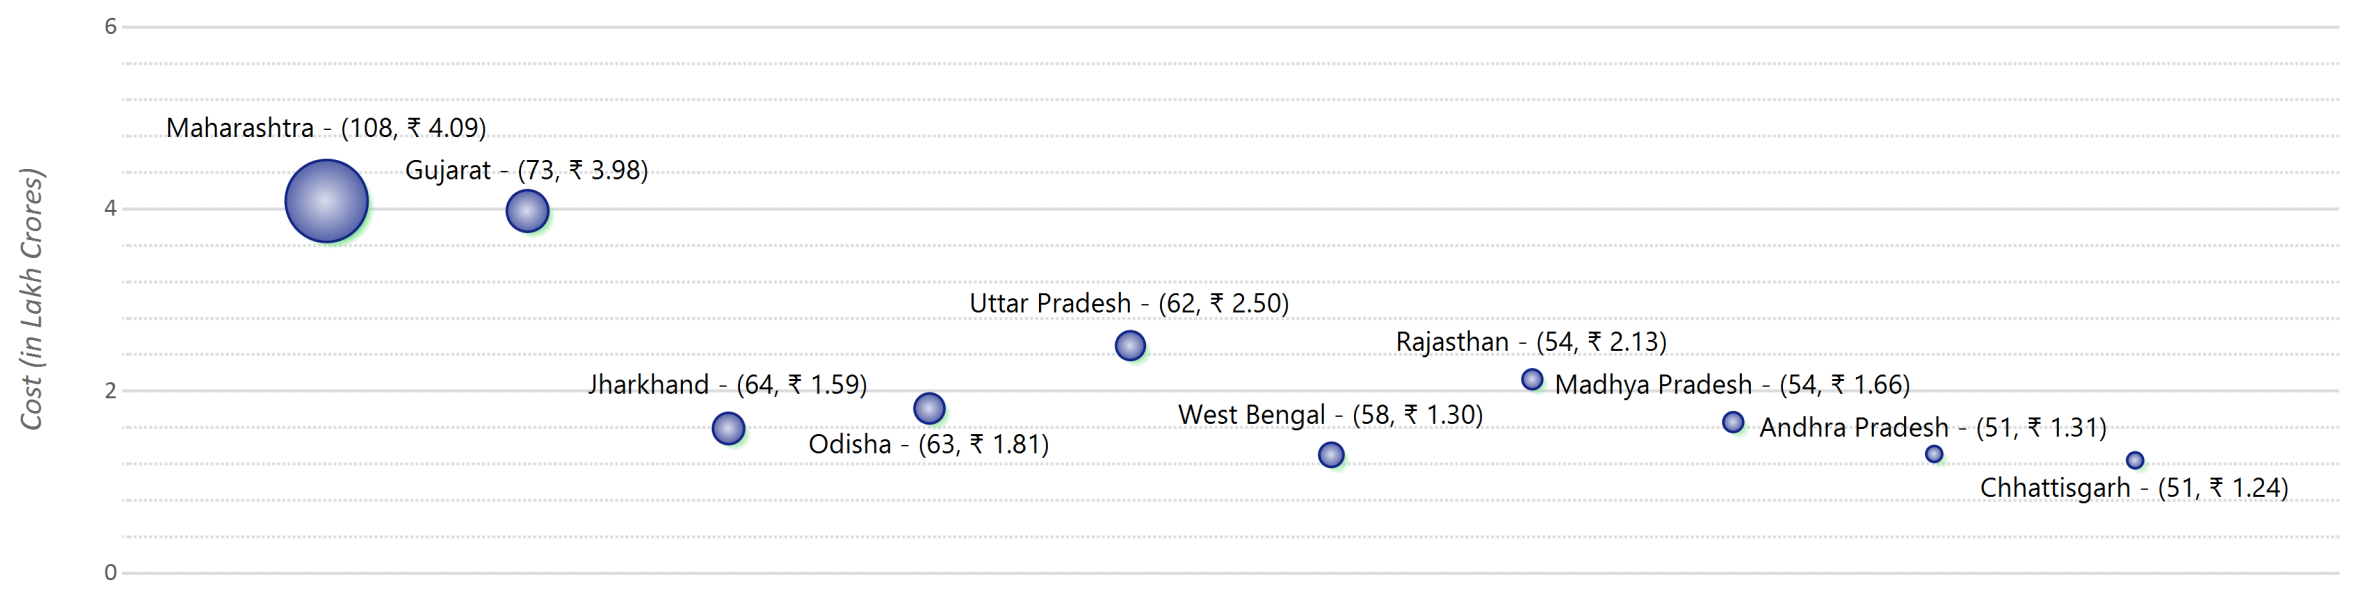


Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count

Ministry-wise Distribution of total 223 projects with reported Physical Progress between 81-100%

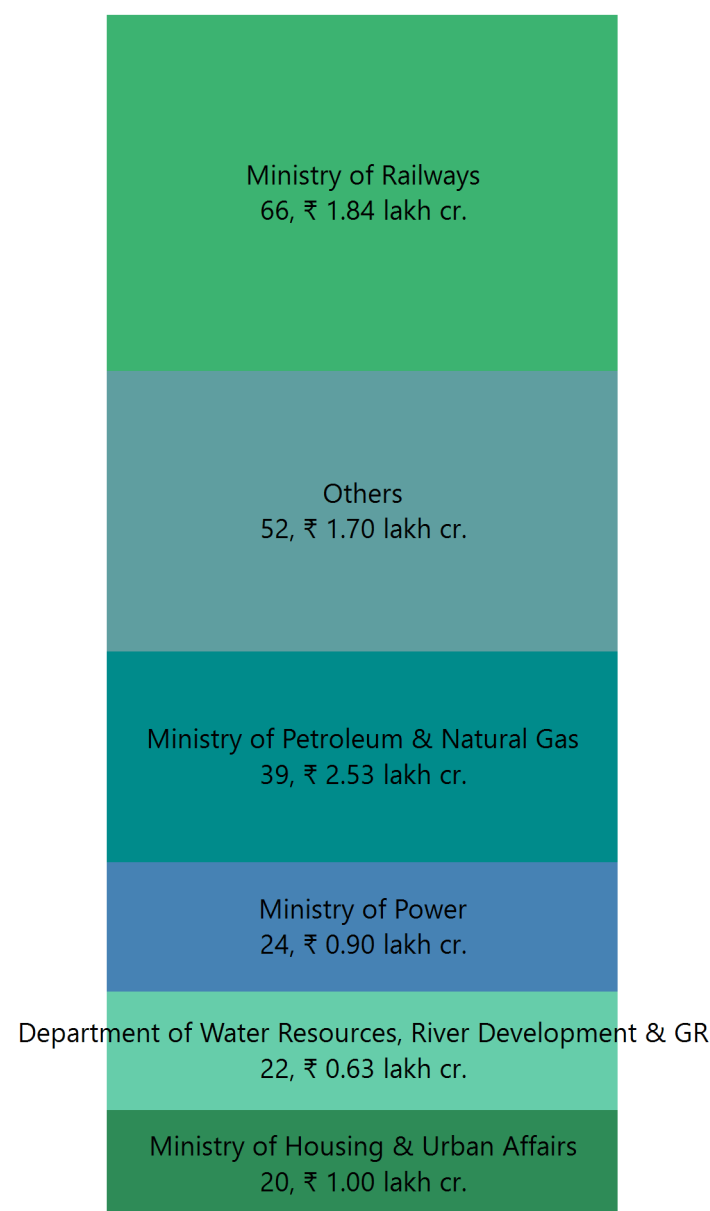

Total Ongoing Projects: Mega & Major

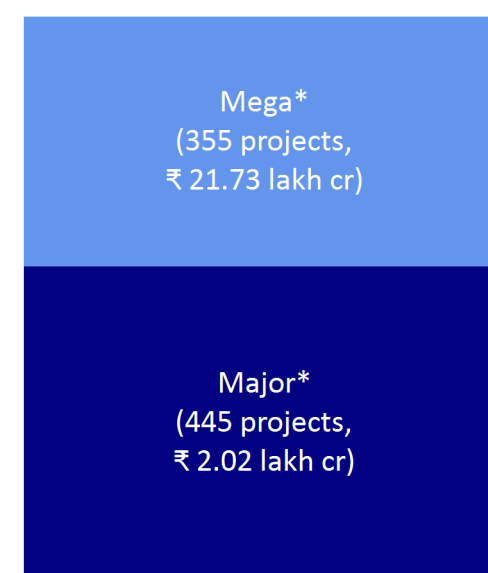


Total North East Region Ongoing Projects: Mega & Major




Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost $\geq$ 1000 crore
* Major project if having original cost $<$ 1000 crore

Project volume (nos.)

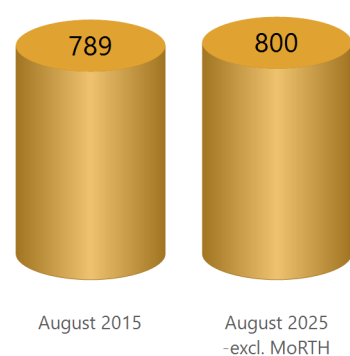


Change in Project Count : +1%

Total Project value (in lakh crore)

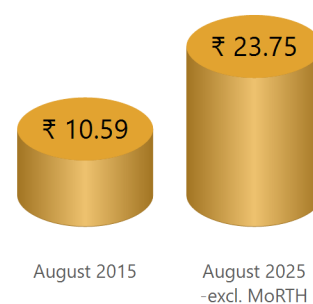

Change in Total Value : +120%

Cumulative Expenditure (in lakh crore)

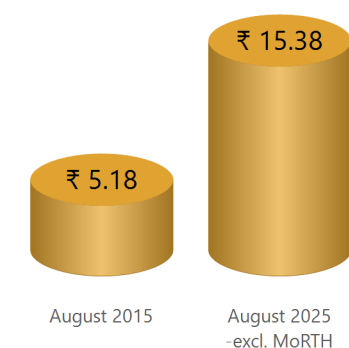

Change in Expenditure : +204%



North Eastern Region





Special Focus : North Eastern Region

AUGUST 2025

54 | 9

Ongoing Projects |
Line Ministries & Departments

₹ 1,88,300

Original Cost
(crores)

₹ 2,79,741

Revised Cost
(crores)


₹ 1,91,944

(68.62% of Revised Cost)


Expenditure
(crores)

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

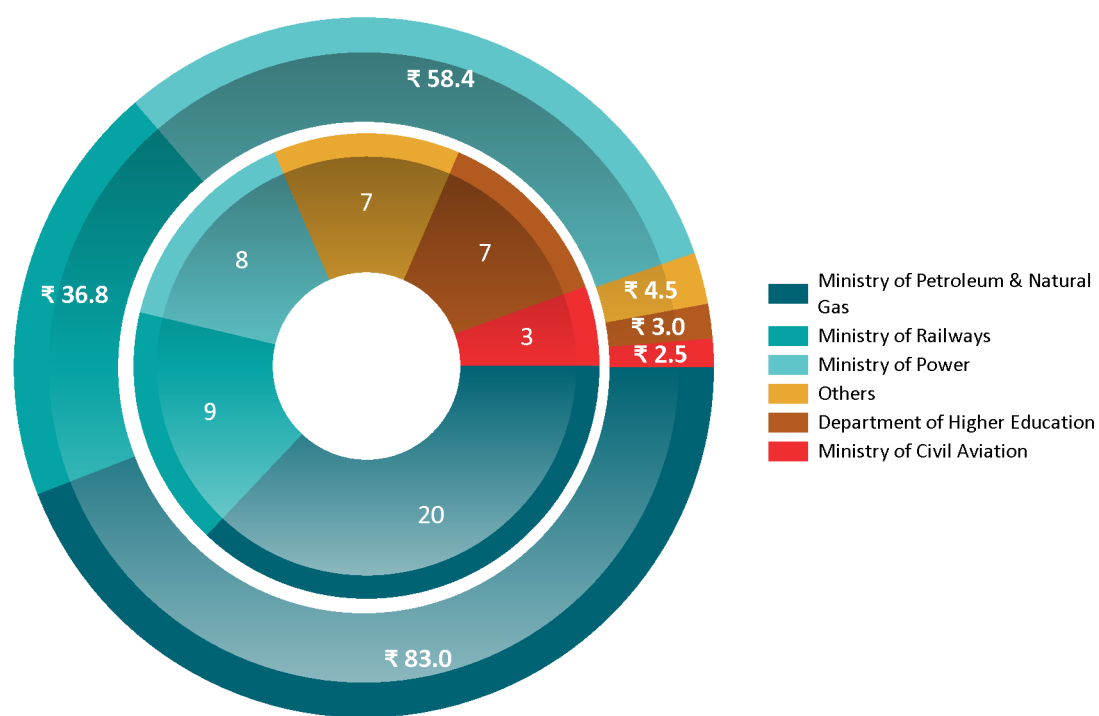


Cost Analytics : Major Ministries*

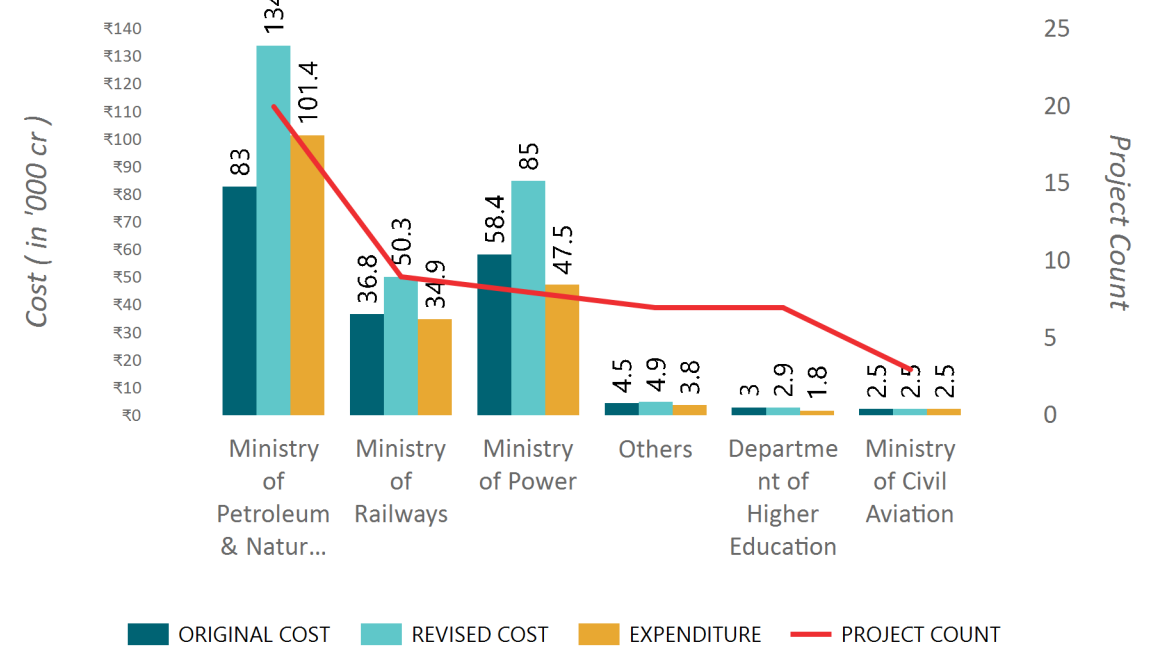


Note: * as per Project Count

Analytics: as per HML

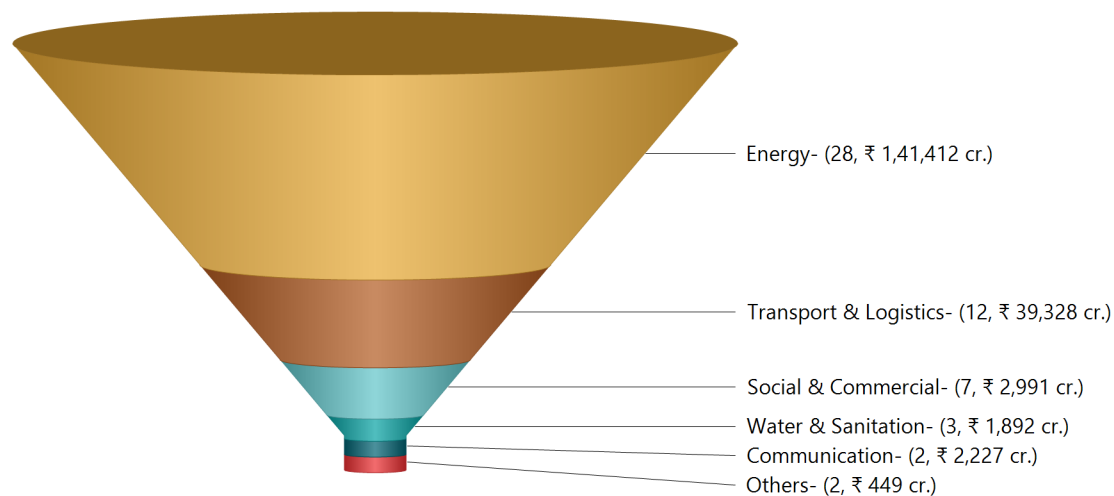


Physical & Financial progress (%) : Project count

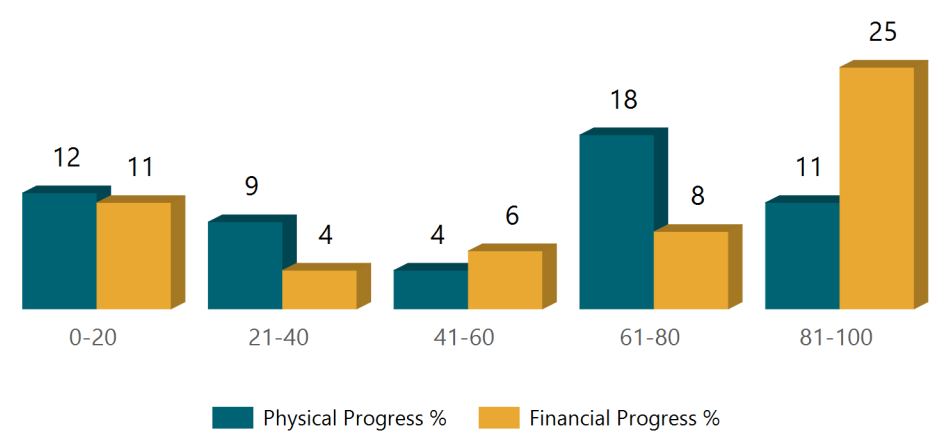

Note: all indicated legends are in format (Project count, Original Cost in crores)

State Comparison : All States

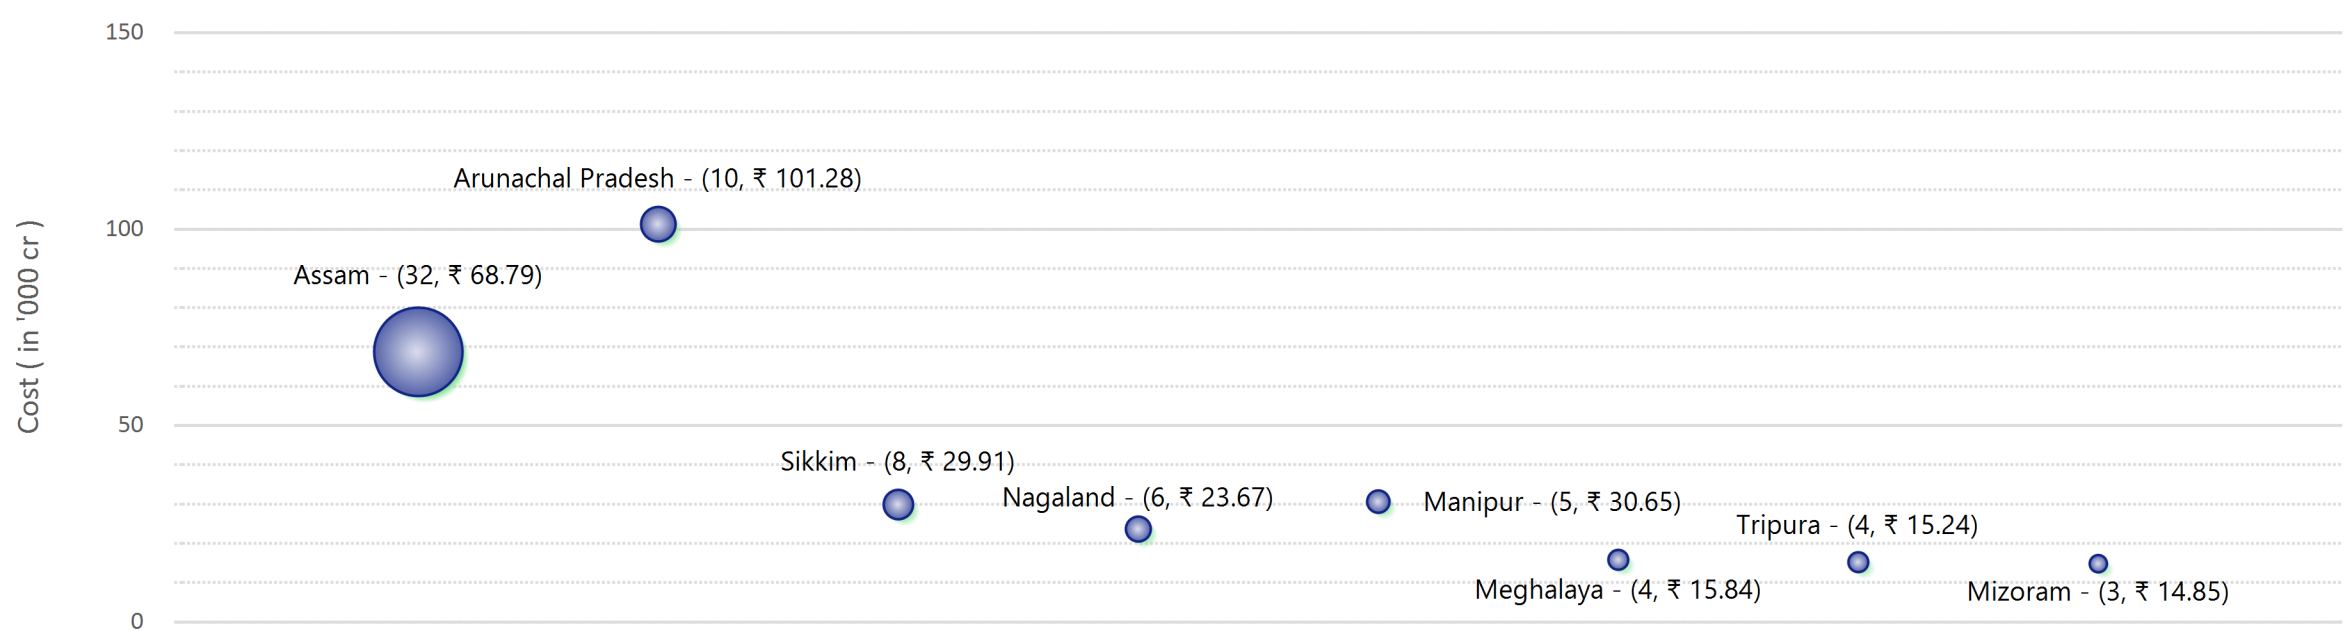

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022



HML Category 1 : Transport & Logistics

AUGUST 2025


320
Ongoing Projects

₹ 10,18,556
Original Cost
(crores)


₹ 11,85,490
Revised Cost
(crores)

₹ 7,42,655
(62.65% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

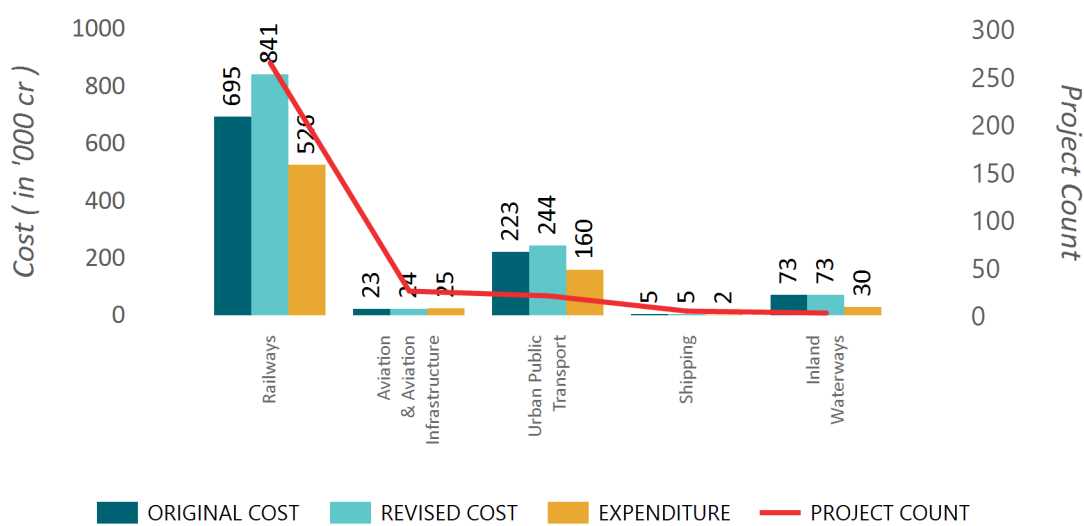

Physical & Financial progress (%) : Project count

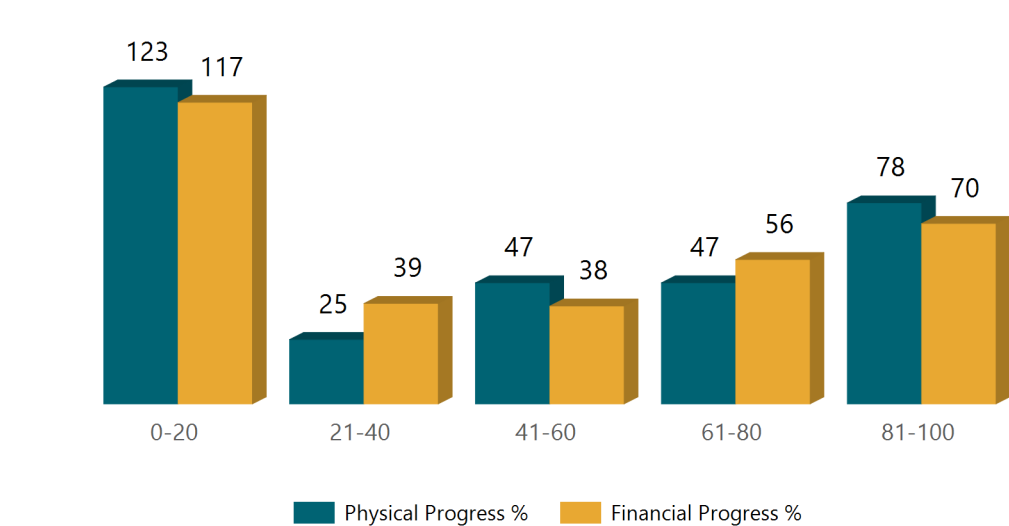

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Railways	265	694,807	841,007	525,898
2	Aviation & Aviation Infrastructure	26	23,050	23,511	24,880
3	Urban Public Transport	21	223,017	243,598	159,570
4	Shipping	5	4,823	4,823	2,021
5	Inland Waterways	3	72,859	72,551	30,287

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	79,919	53
2	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		26,410	45
3	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
4	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
5	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,303	16

HML Category 2 : Energy



AUGUST 2025

202
Ongoing Projects

₹ 8,45,810
Original Cost
(crores)

₹ 9,82,793
Revised Cost
(crores)

₹ 4,82,645
(49.11% of Revised Cost)
Expenditure
(crores)

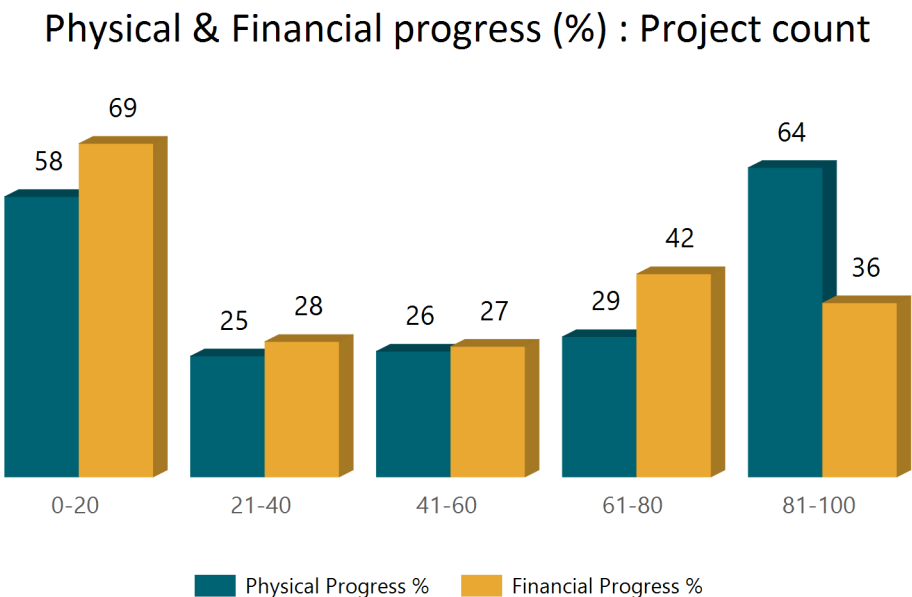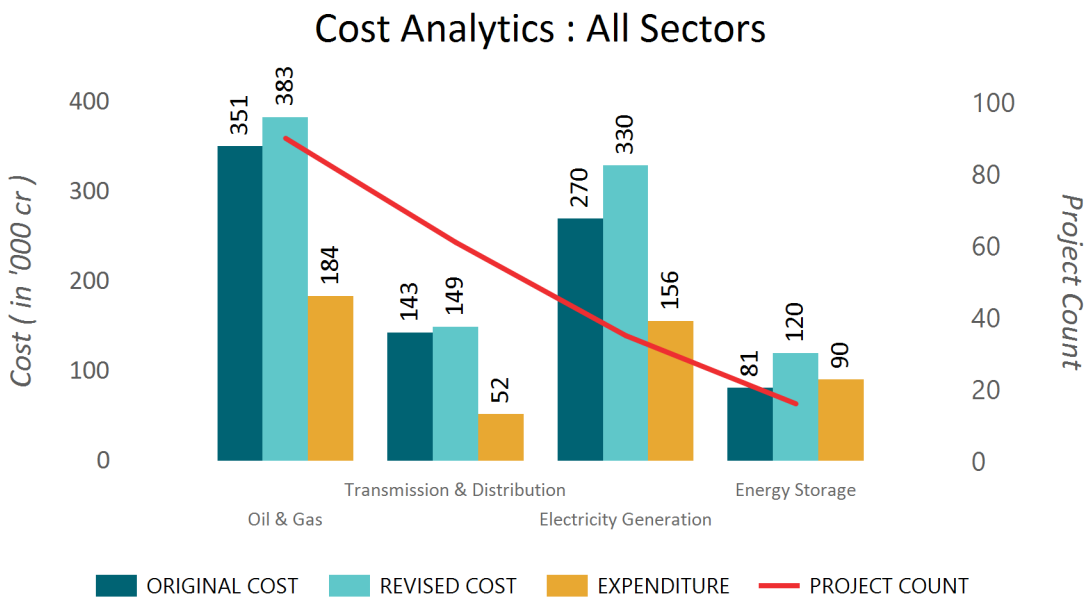

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	90	351,249	383,480	184,032
2	Transmission & Distribution	61	142,977	149,491	52,183
3	Electricity Generation	35	270,284	329,637	155,932
4	Energy Storage	16	81,301	120,185	90,498

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,856	14
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	60,295	88
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	24,355	89
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,238	96
5	602182	DIBANG MULTIPURPOSE PROJECT	31,876		3,554	16



HML Category 3 : Water & Sanitation

AUGUST 2025

73

Ongoing Projects

₹ 1,03,374

Original Cost
(crores)


₹ 2,05,233

Revised Cost
(crores)


₹ 1,59,103

(77.52% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

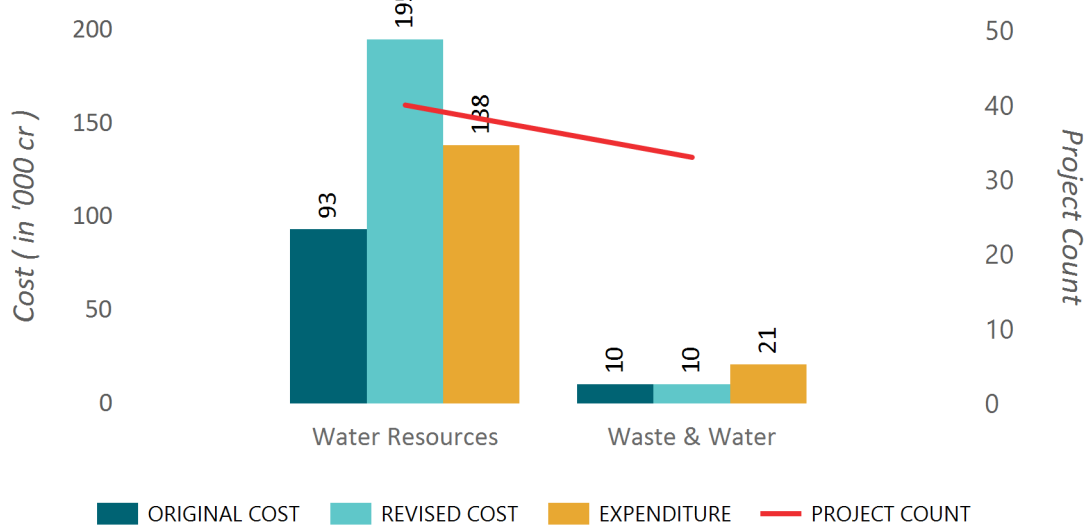

Physical & Financial progress (%) : Project count

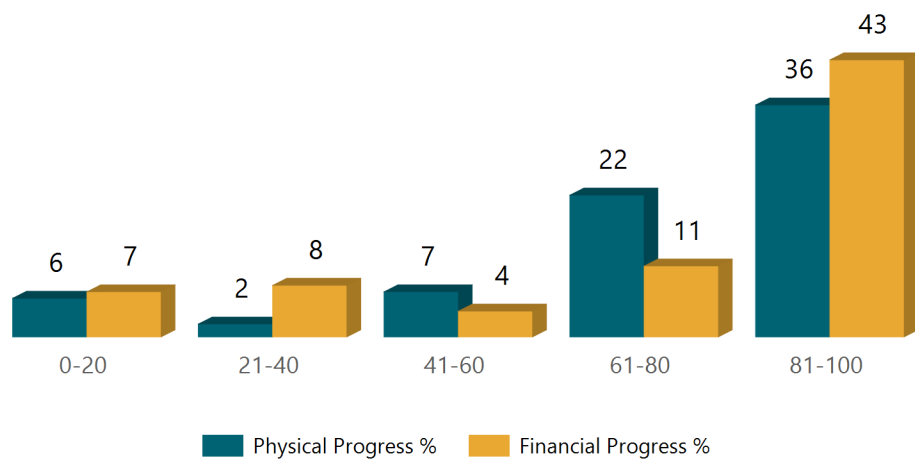

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	40	93,249	195,108	138,397
2	Waste & Water	33	10,125	10,125	20,706

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,768	93
2	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	24,348	83
3	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,559	87
4	400112	JIGAON IRRIGATION PROJECT	7,223		8,501	90
5	701386	GOSIKHURD PROJECT	7,196	12,770	13,533	72



HML Category 4 : Communication

AUGUST 2025

14

Ongoing Projects

₹ 1,50,850

Original Cost
(crores)


₹ 2,72,942

Revised Cost
(crores)


₹ 72,123

(26.42% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

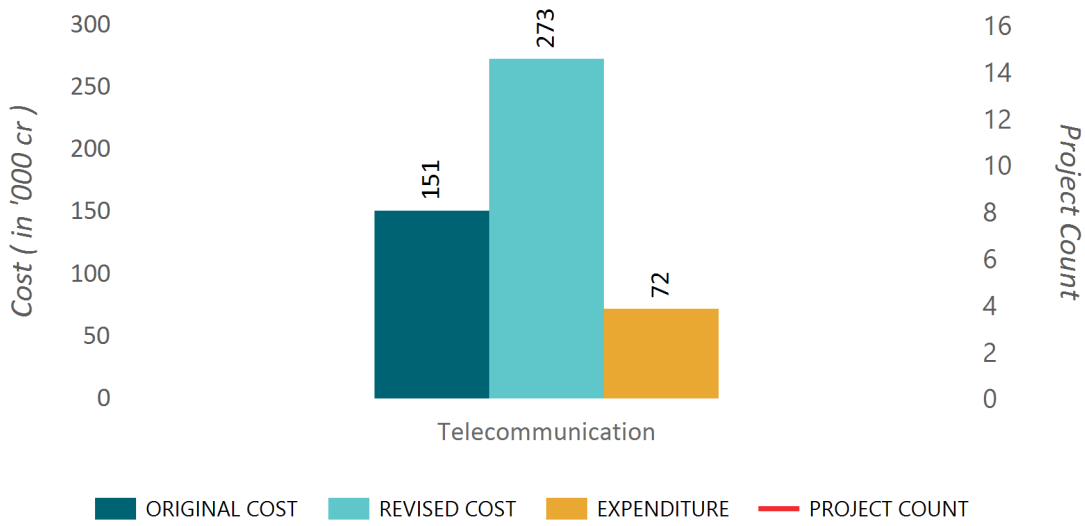

Physical & Financial progress (%) : Project count

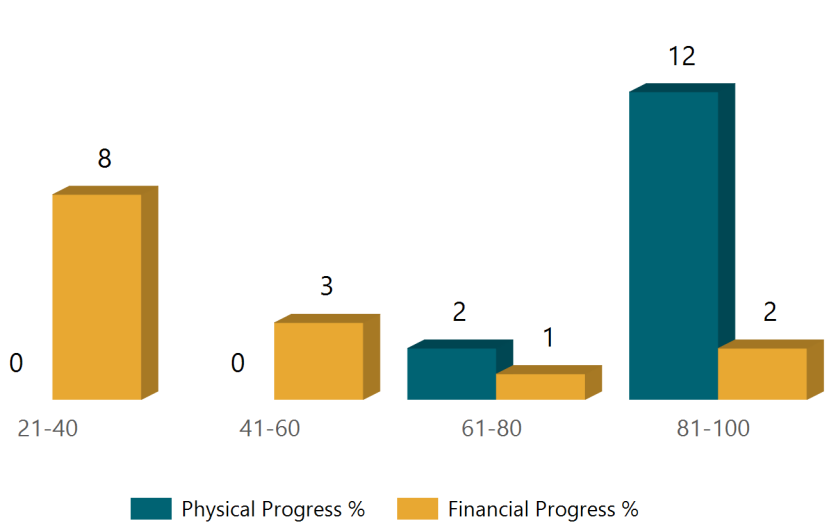

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	14	150,850	272,942	72,123

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	706775	BHARATNET	61,109	188,000	41,486	81
2	701593	4G SERVICES BY BSNL	28,466	19,592	8,390	96
3	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	30,620	9,792	73
4	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		8,391	96
5	701602	PROVISION OF 4G BASED MOBILE SERVICES IN 7,287 UNCOVERED VILLAGES OF 44 ASPIRATIONAL DISTRICT ACROSS 5 STATES OF ANDHRA PRADESH, CHHATTISGARH, JHARKHAND, MAHARASHTRA & ODISHA	3,685		1,101	79

HML Category 5 : Social & Commercial

AUGUST 2025

41

Ongoing Projects

₹ 55,767



Original Cost
(crores)

₹ 56,701

Revised Cost
(crores)

₹ 11,961

(21.1% of Revised Cost)
Expenditure
(crores)

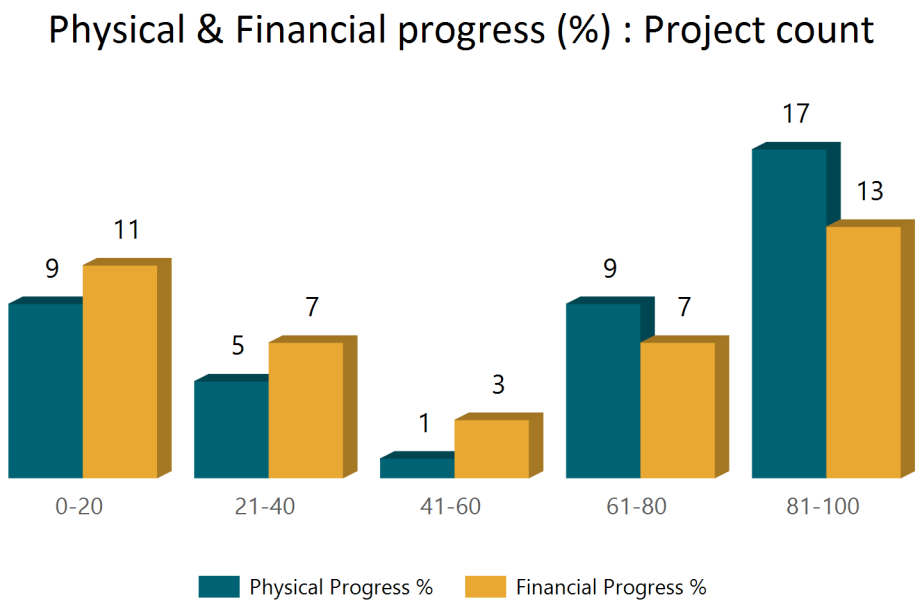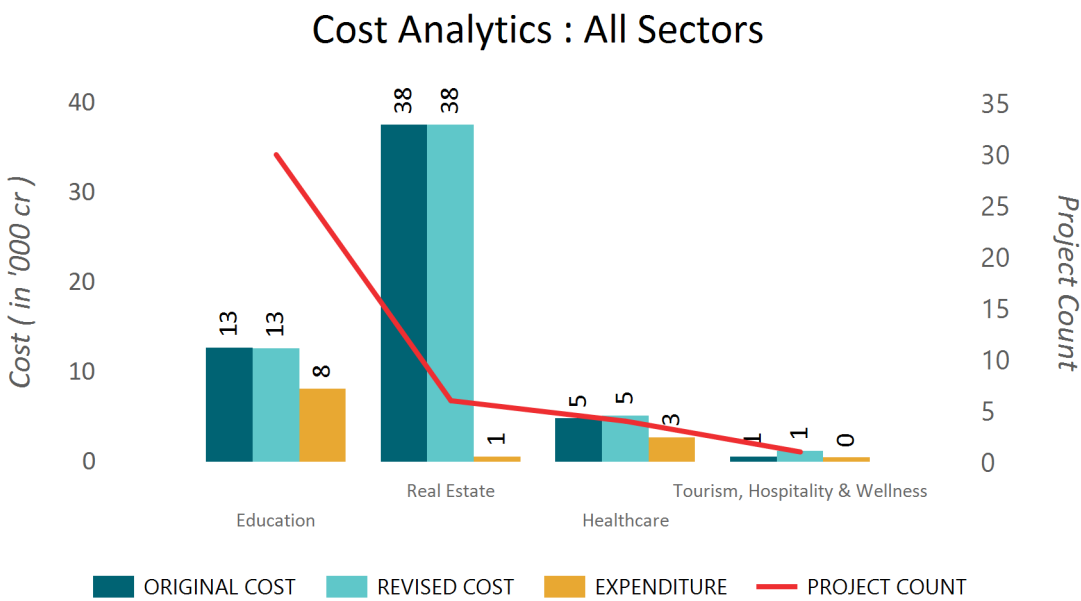

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Education	30	12,754	12,685	8,159
2	Real Estate	6	37,591	37,591	553
3	Healthcare	4	4,848	5,186	2,752
4	Tourism, Hospitality & Wellness	1	573	1,238	497

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850		0	0
2	701658	KRISHNAPATNAM NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	2,139		406	17
3	701167	AIIMS KASHMIR AT AWANTIPORA JAMMU & KASHMIR	1,828	1,828	1,532	66
4	701657	TUMAKURU NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	1,702		88	8
5	701173	AIIMS MAJRA REWARI HARYANA	1,299		349	28



Other Sectors

AUGUST 2025

150

Ongoing Projects

₹ 2,00,976

Original Cost
(crores)


₹ 2,04,389

Revised Cost
(crores)

₹ 69,122

(33.82% of Revised Cost)
Expenditure
(crores)

Physical & Financial progress (%) : Project count

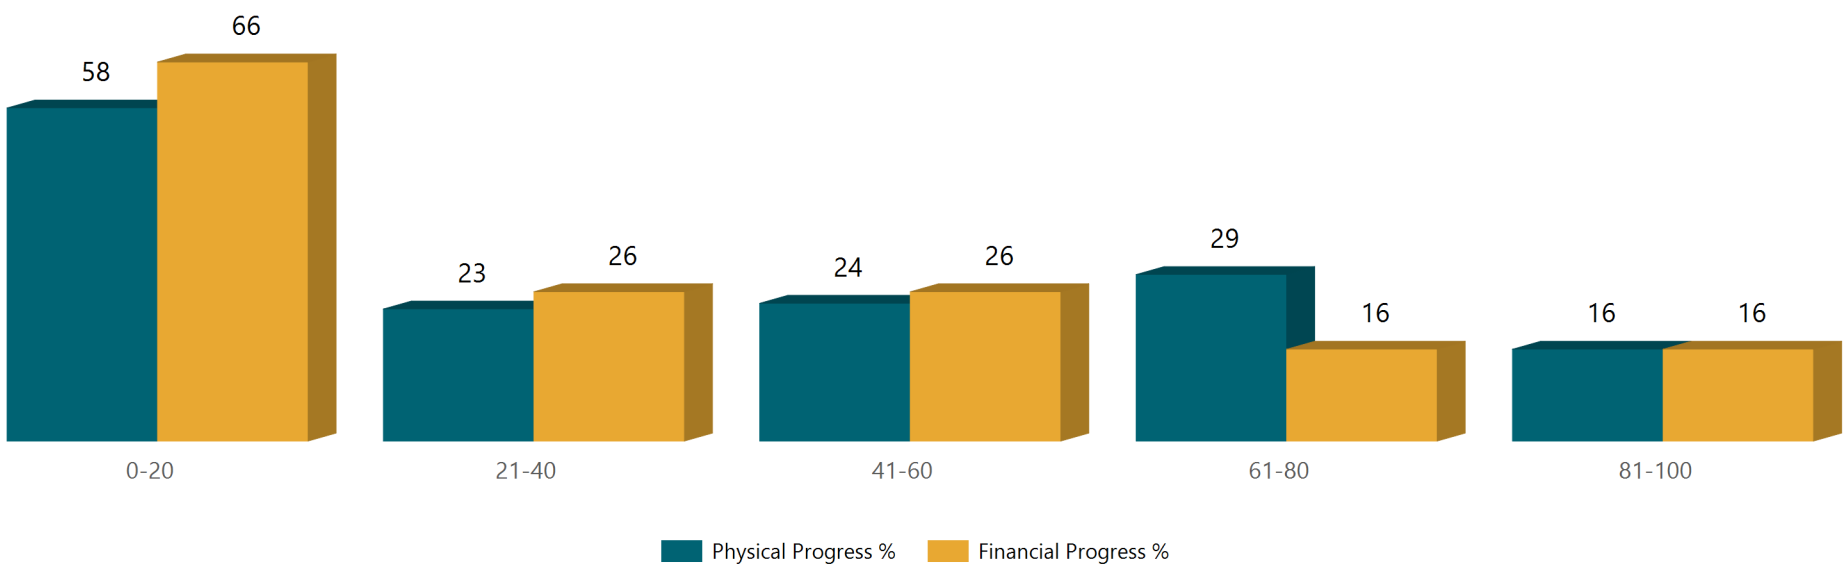

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	119	168,890	166,628	54,350
2	Steel	19	16,748	19,987	7,970
3	Metals & Mining	10	14,436	16,873	6,190
4	Construction	2	902	902	612

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400424	GEVRA OC [70 MTY]	11,816		5,329	77
2	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,709	17
3	400147	KUSMUNDA OC EXPANSION [15 TO 50 MTY]	7,612		4,698	81
4	612838	DIPKA OC	7,580		3,091	65
5	400150	RPR MAGADH EXP OCP	7,254		1,535	38



Major Infrastructure Central Ministries & Departments



Ministry of Railways

AUGUST 2025

263
Ongoing Projects

₹ 6,91,321
Original Cost
(crores)


₹ 8,37,521
Revised Cost
(crores)

₹ 5,24,256
(62.6% of Revised Cost)
Expenditure
(crores)

128 | ₹ 627,817
Mega Projects
Count | Original Cost (crores)

135 | ₹ 63,504
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

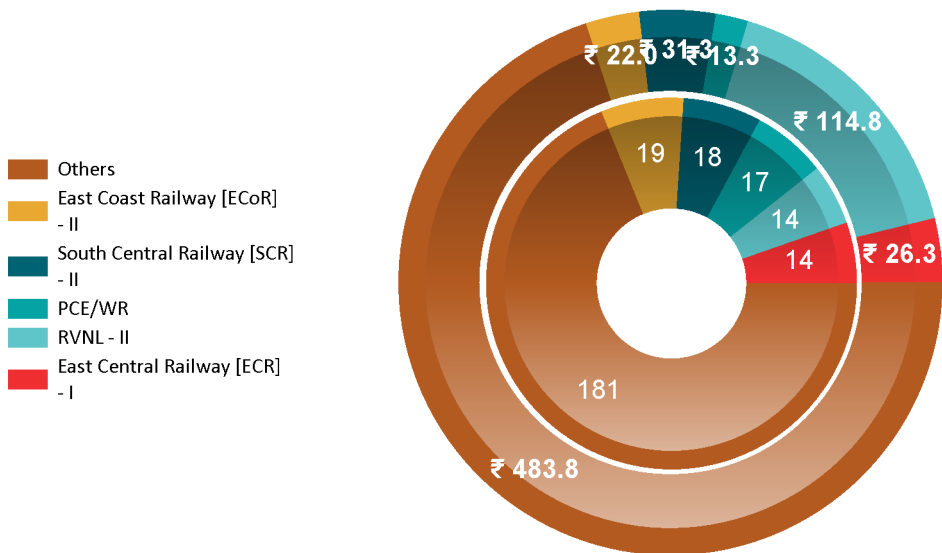


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Physical & Financial progress (%) : Project count

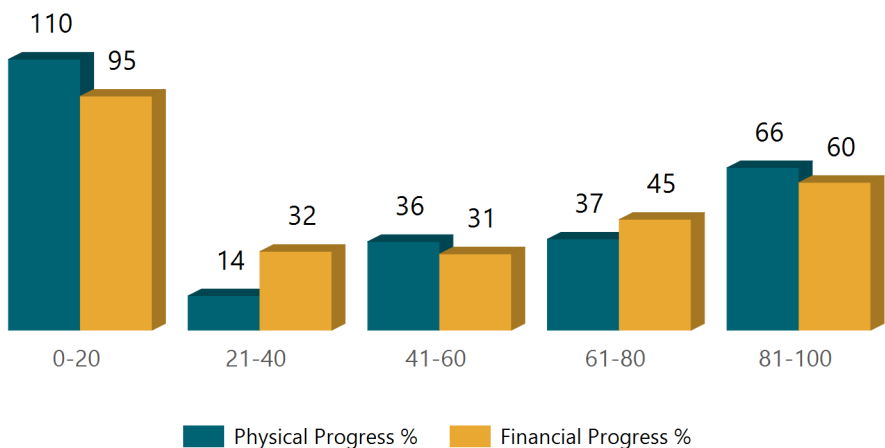

Cost Analytics : Major Sectors*

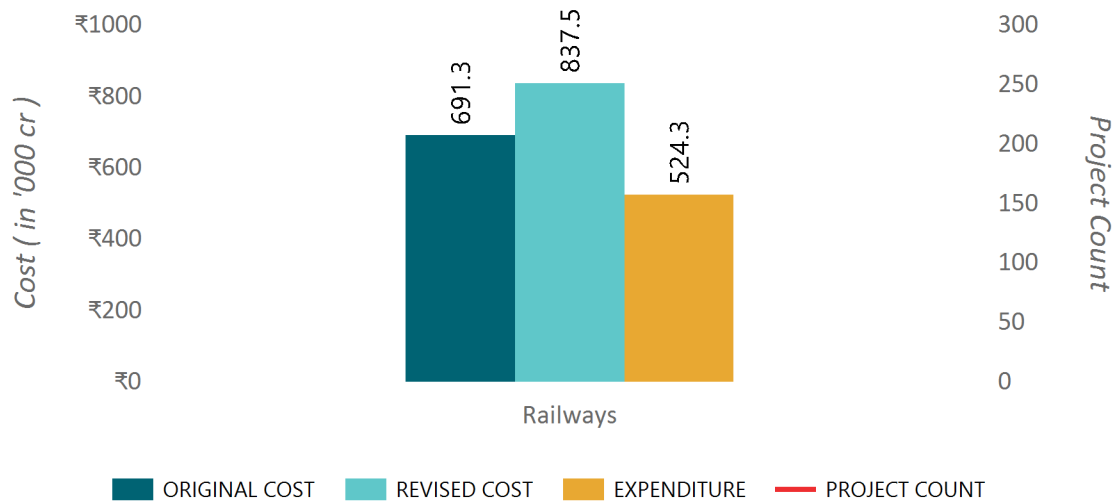

State Comparison : Major States*

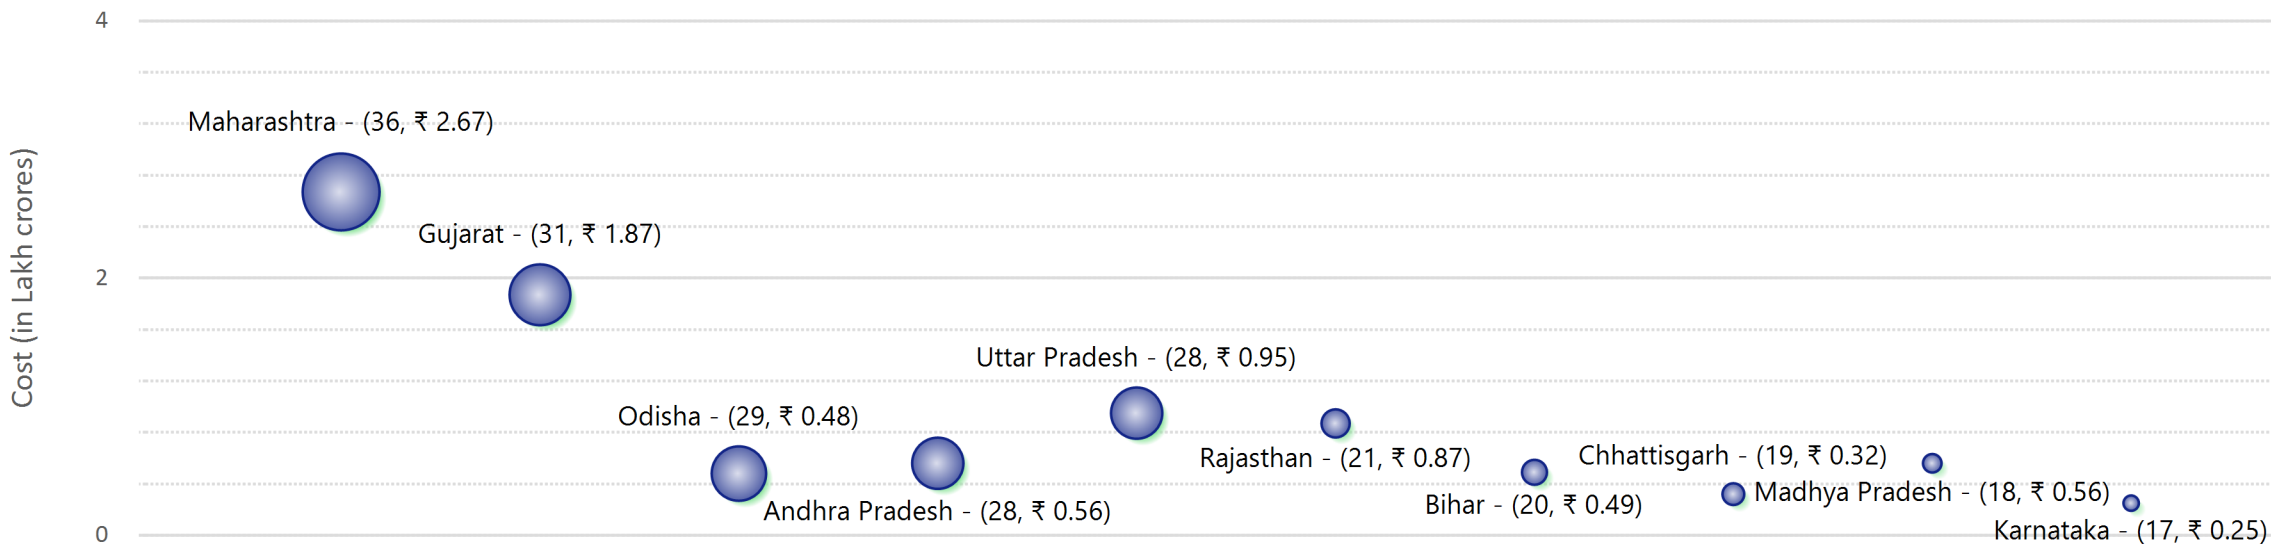

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	79,919	53
2	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
3	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
4	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,303	16
5	705391	JIRIBAM-IMPHAL NEW LINE PROJECT	14,323	21,886	15,598	69

Ministry of Coal

AUGUST 2025

124
Ongoing Projects

₹ 2,17,158
Original Cost
(crores)


₹ 2,19,157
Revised Cost
(crores)

₹ 78,643
(35.88% of Revised Cost)
Expenditure
(crores)


39 | ₹ 175,401
Mega Projects
Count | Original Cost (crores)

85 | ₹ 41,757
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

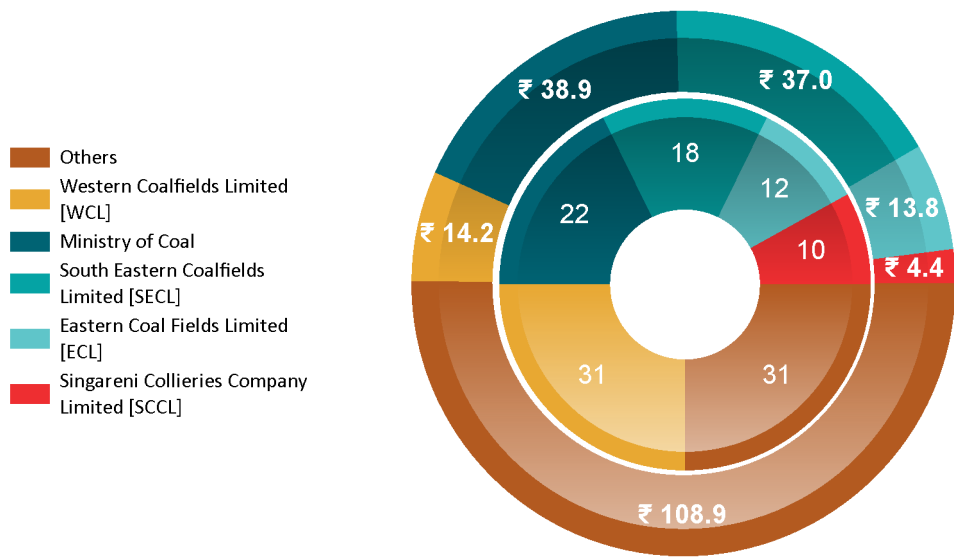


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

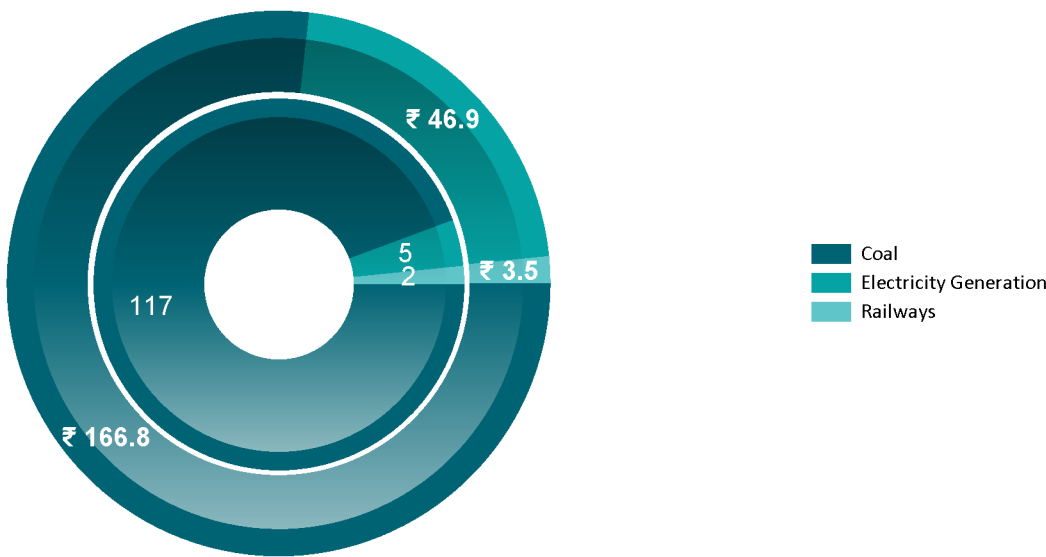


Physical & Financial progress (%) : Project count

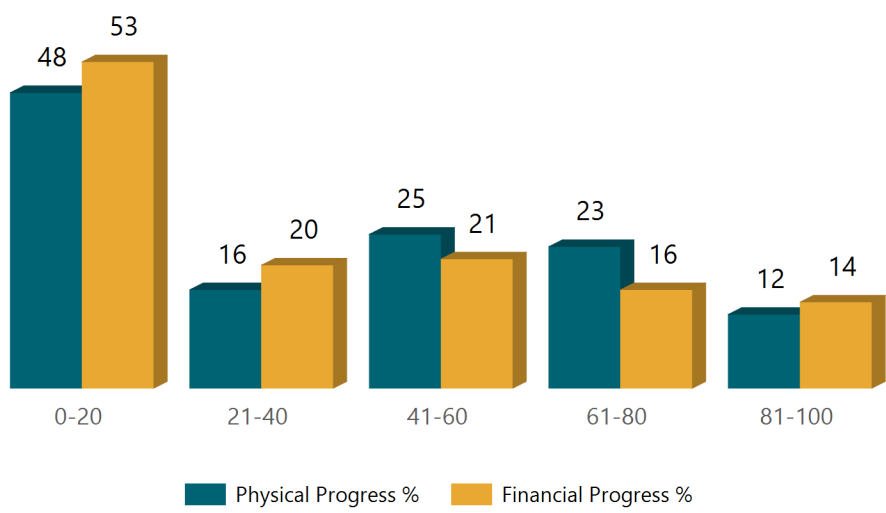

Cost Analytics : Major Sectors*

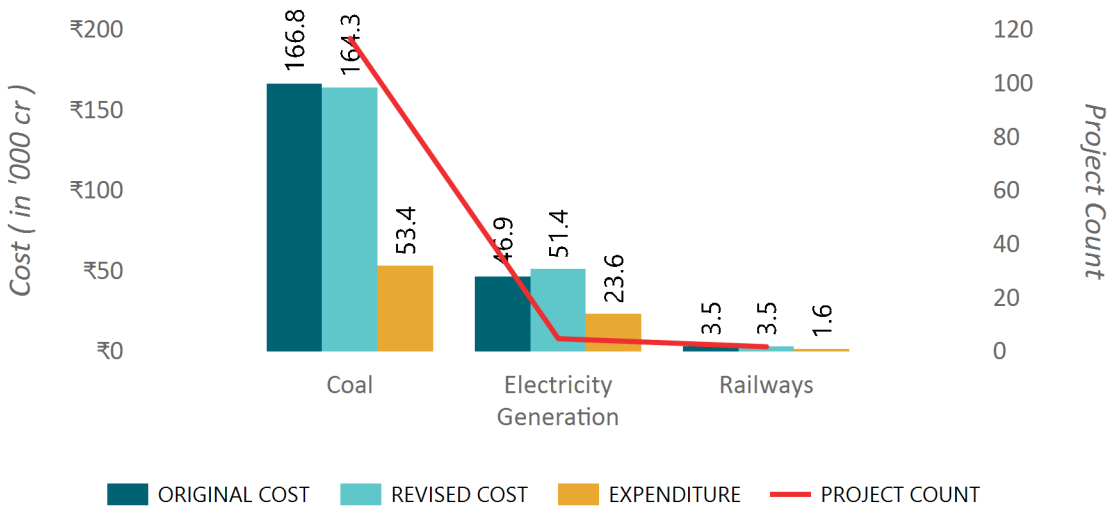

State Comparison : Major States*

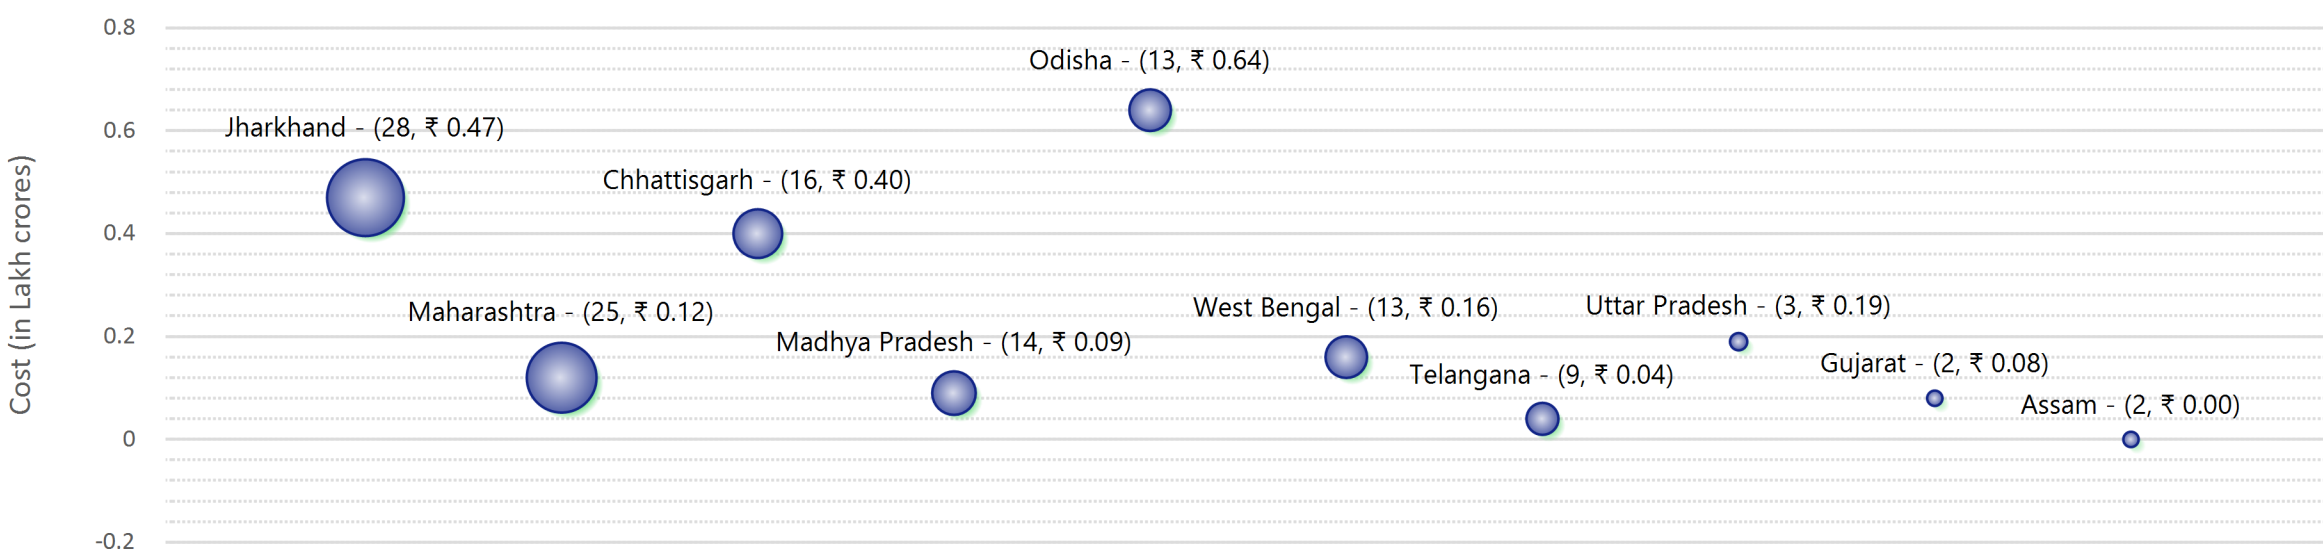

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	1,954	1
2	400259	GHATAMPUR THERMAL POWER PLANT 3 X 660 MW	17,238	21,781	20,270	92
3	400424	GEVRA OC [70 MTY]	11,816	11,816	5,329	77
4	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,709	17
5	400147	KUSMUNDA OC EXPANSION [15 TO 50 MTY]	7,612	7,612	4,698	81



Ministry of Petroleum & Natural Gas

AUGUST 2025

106

Ongoing Projects

₹ 4,32,550

Original Cost
(crores)

₹ 5,03,665

Revised Cost
(crores)

₹ 2,74,530

(54.51% of Revised Cost)

Expenditure
(crores)

49 | ₹ 407,305


Mega Projects
Count | Original Cost (crores)

57 | ₹ 25,245

Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

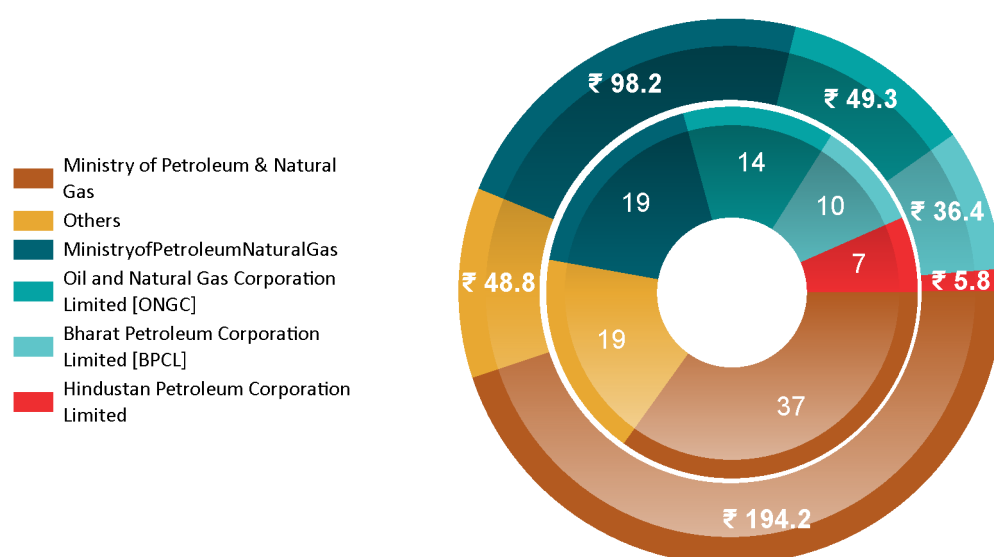


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

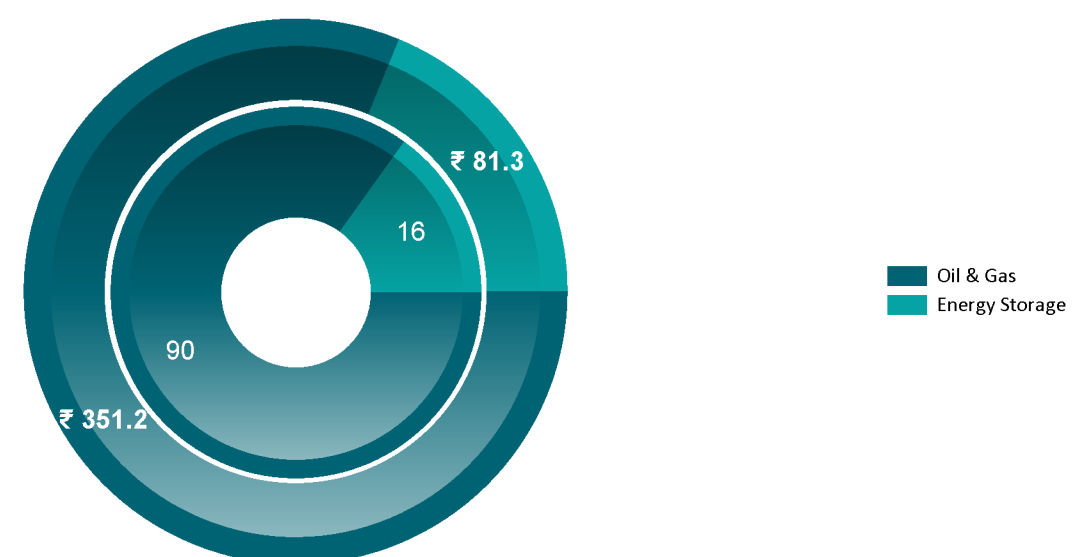


Physical & Financial progress (%) : Project count

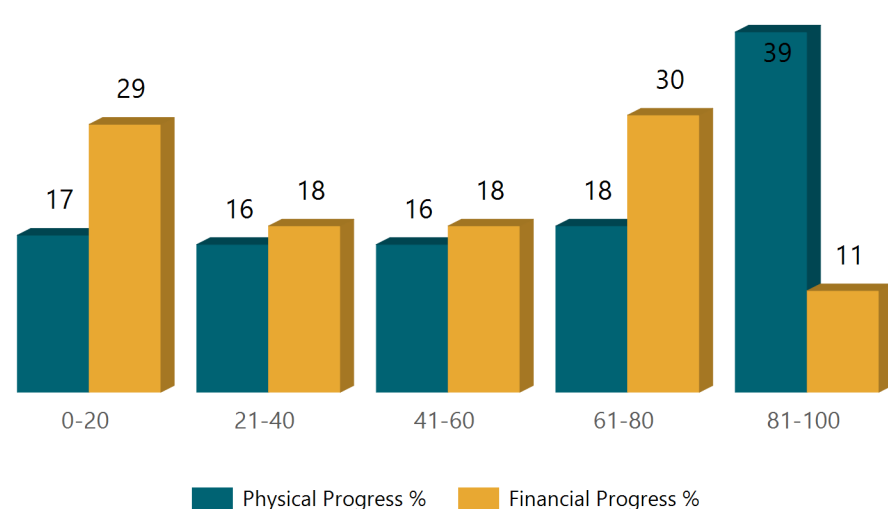

Cost Analytics : Major Sectors*

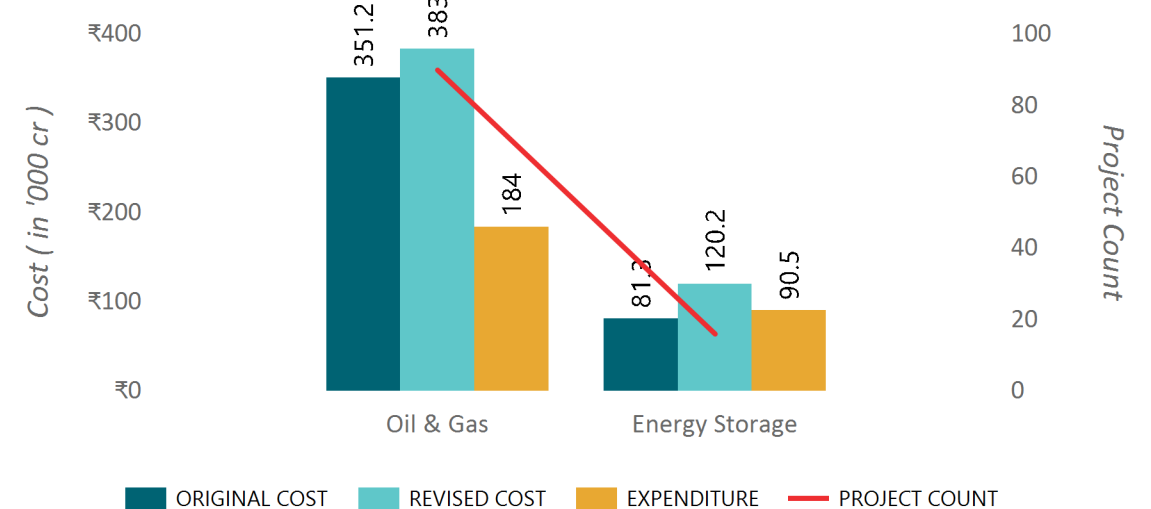

State Comparison : Major States*

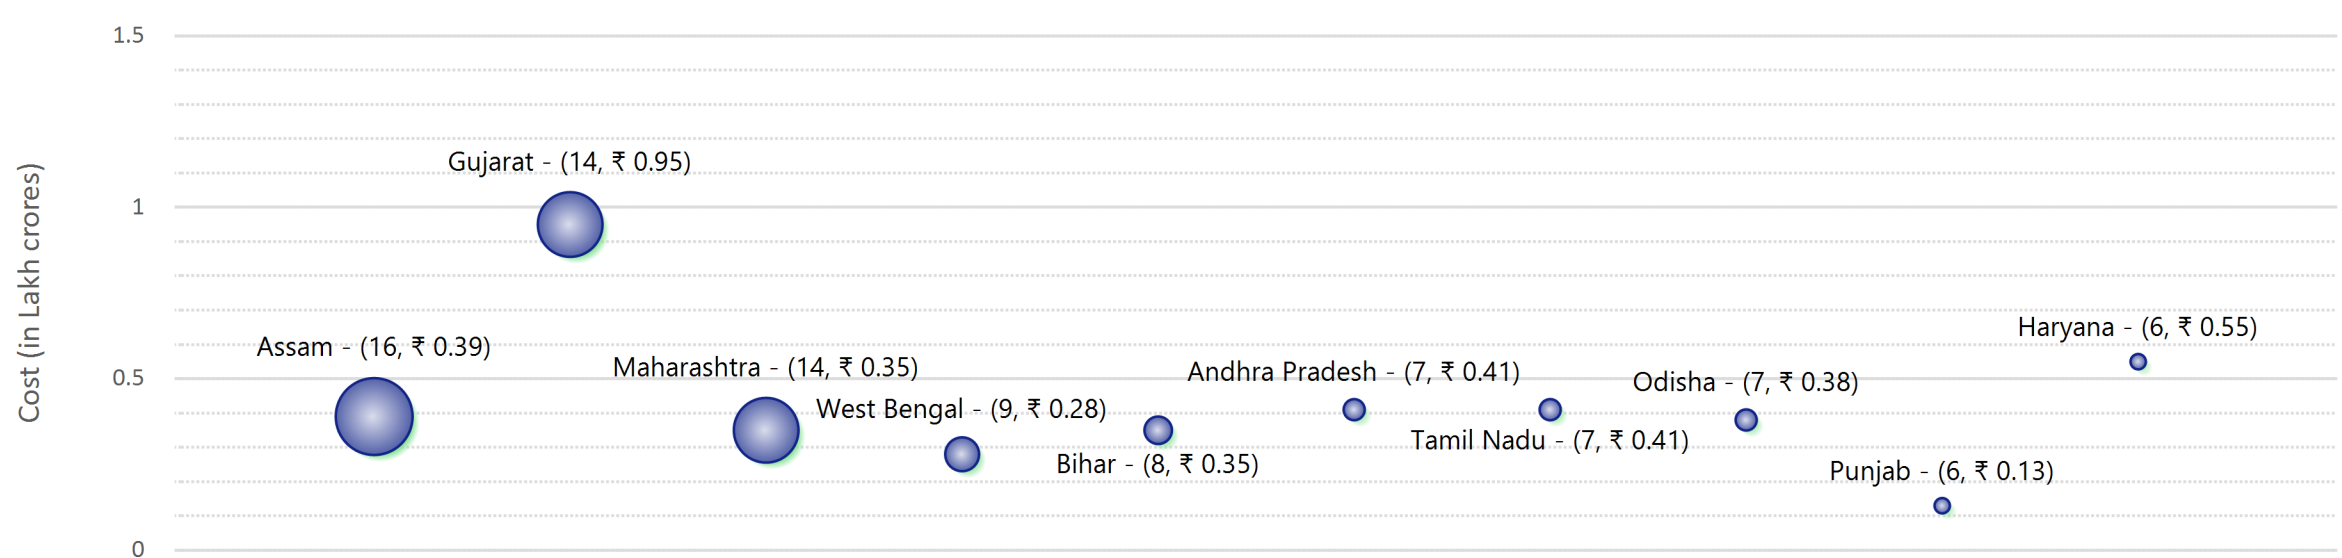

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,856	14
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	60,295	88
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	24,355	89
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,238	96
5	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,342	10

Ministry of Power

AUGUST 2025

93
Ongoing Projects

₹ 3,68,478
Original Cost
(crores)


₹ 4,30,084
Revised Cost
(crores)

₹ 1,85,464
(43.12% of Revised Cost)
Expenditure
(crores)


63 | ₹ 355,654
Mega Projects
Count | Original Cost (crores)

30 | ₹ 12,824
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

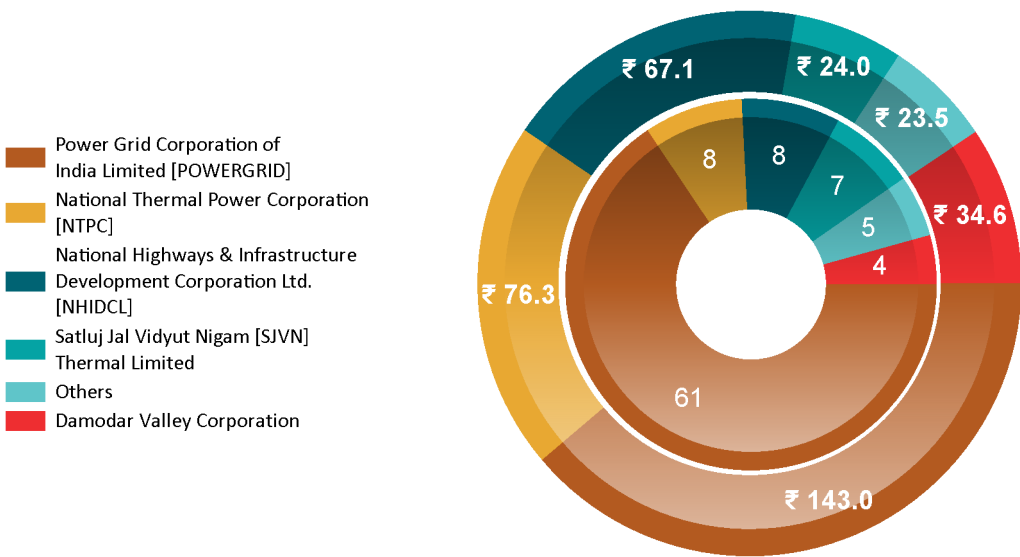


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

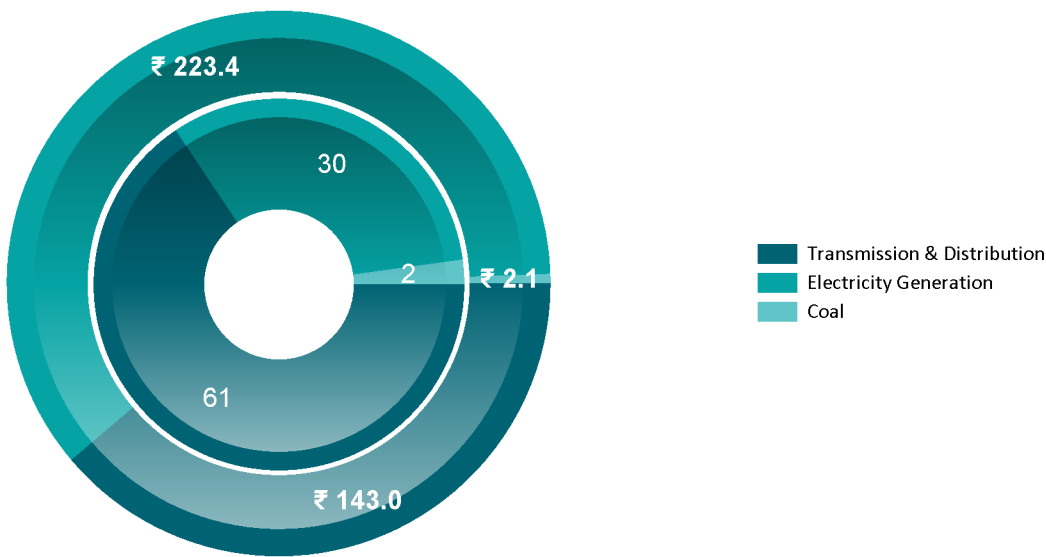


Physical & Financial progress (%) : Project count

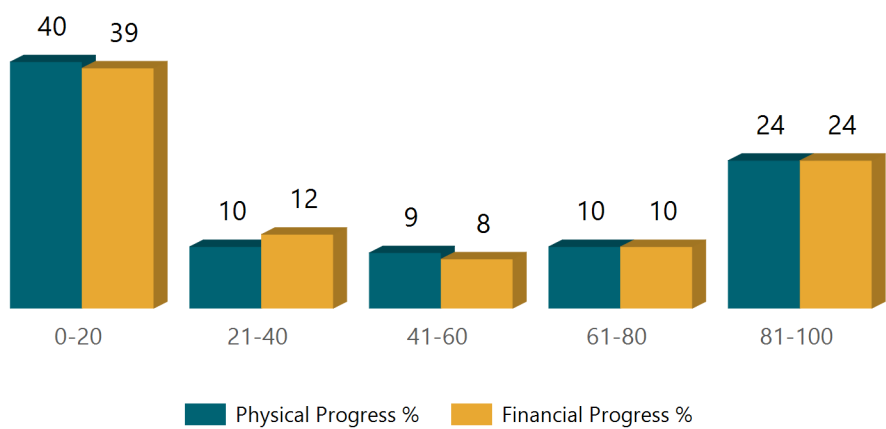

Cost Analytics : Major Sectors*

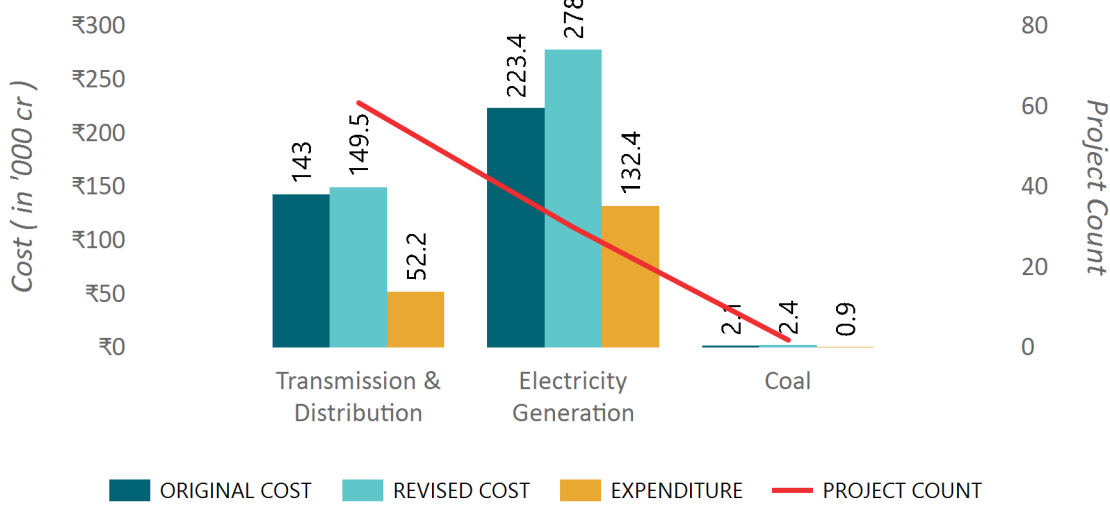

State Comparison : Major States*

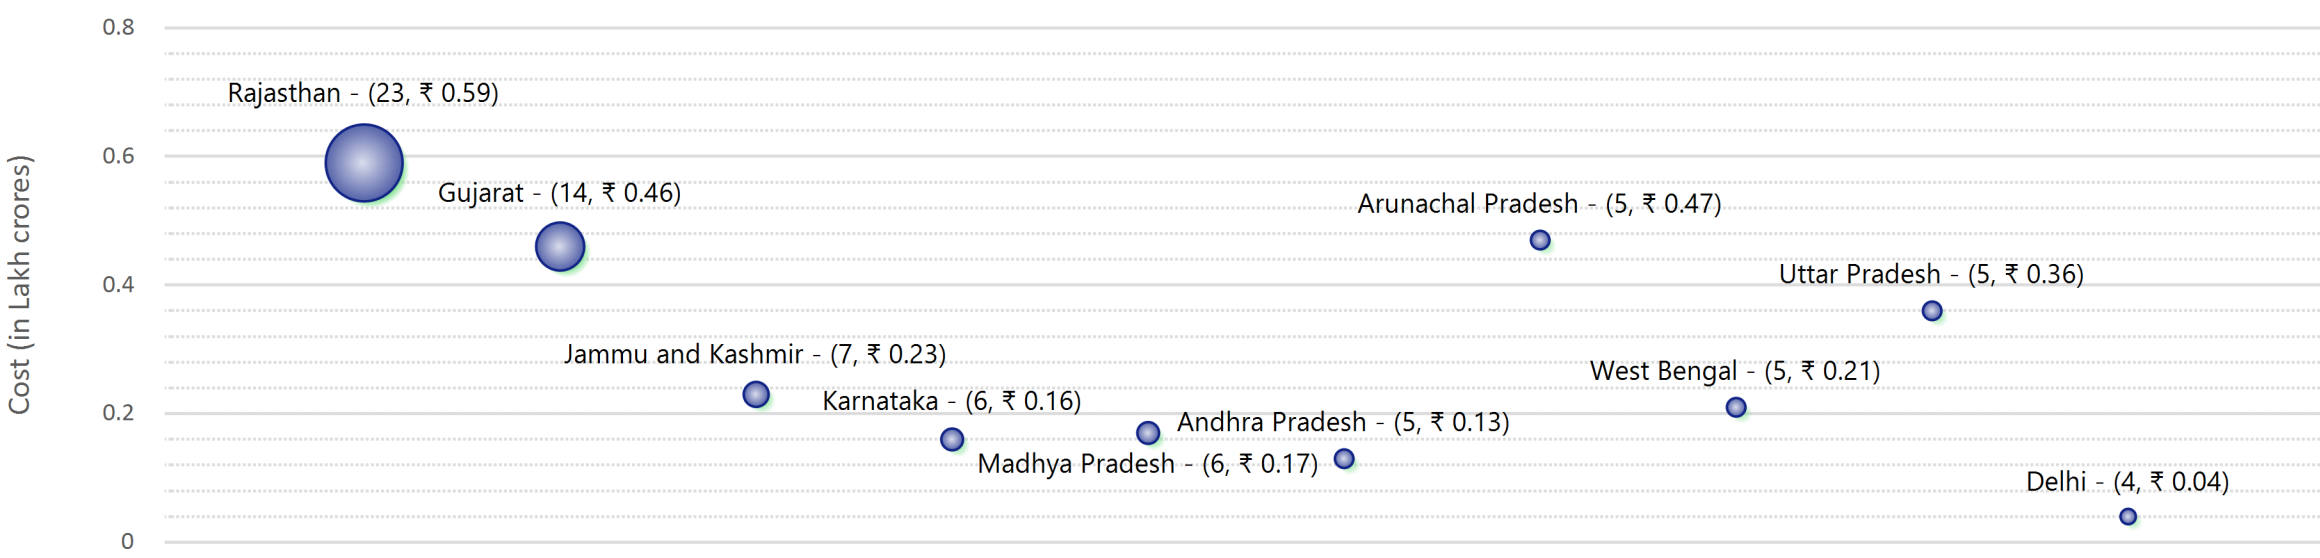

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	3,554	16
2	615347	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV NAME POWERGRID WEST CENTRAL TRANSMISSION LIMITED]	24,819	24,819	1,796	1
3	400062	RAGHUNATHPUR THERMAL POWER STATION PHASE II [2X660 MW] AT RAGHUNATHPUR, PURULIA, WEST BENGAL	17,673	17,673	1,193	1
4	612142	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III [2X800 MW]	17,195	17,195	1,739	9
5	400261	PATRATU THERMAL POWER STATION EXPANSION PROJECT PHASE-I [3X800 MW]	17,112	20,302	17,475	85



Ministry of Housing & Urban Affairs

AUGUST 2025

52
Ongoing Projects

₹ 3,26,745
Original Cost
(crores)

₹ 3,47,326
Revised Cost
(crores)


₹ 2,05,635
(59.21% of Revised Cost)
Expenditure
(crores)

20 | ₹ 317,340
Mega Projects
Count | Original Cost (crores)

32 | ₹ 9,405
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

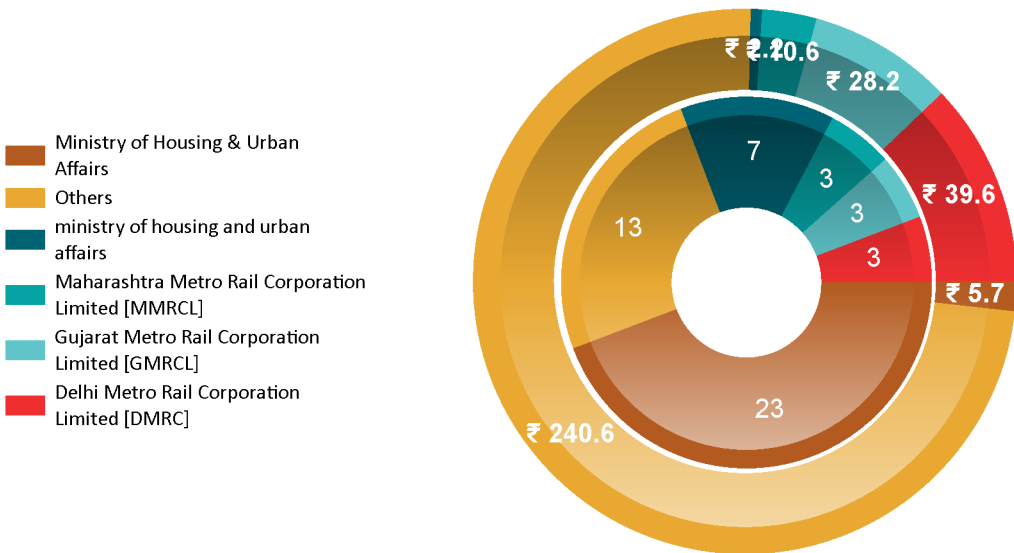


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

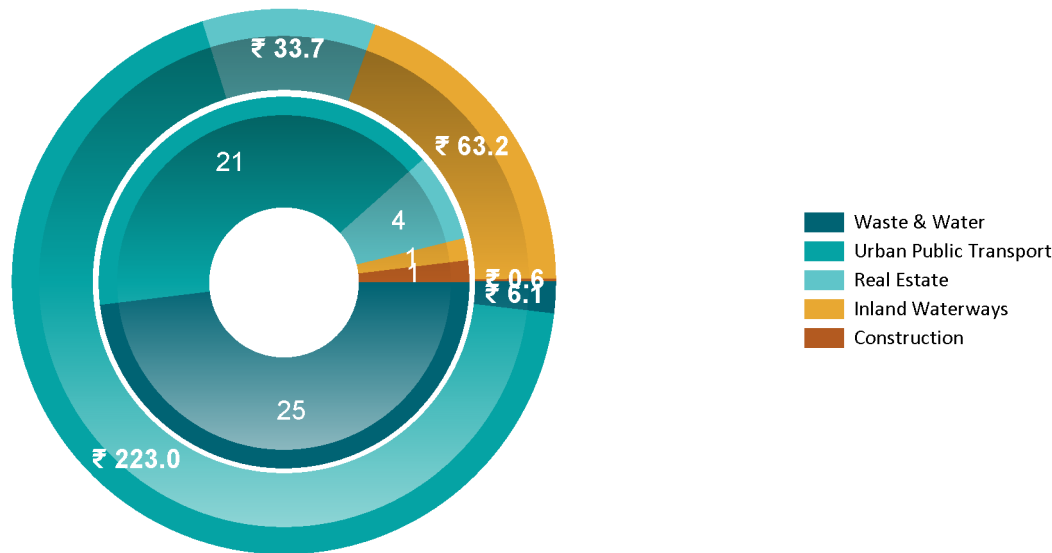


Physical & Financial progress (%) : Project count

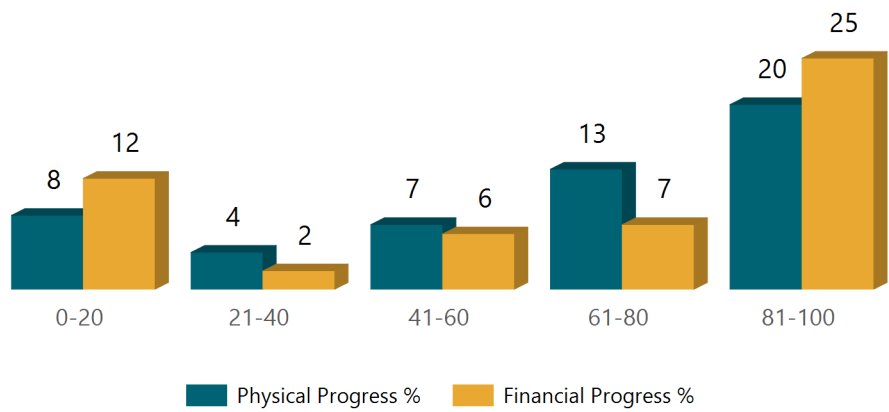

Cost Analytics : Major Sectors*

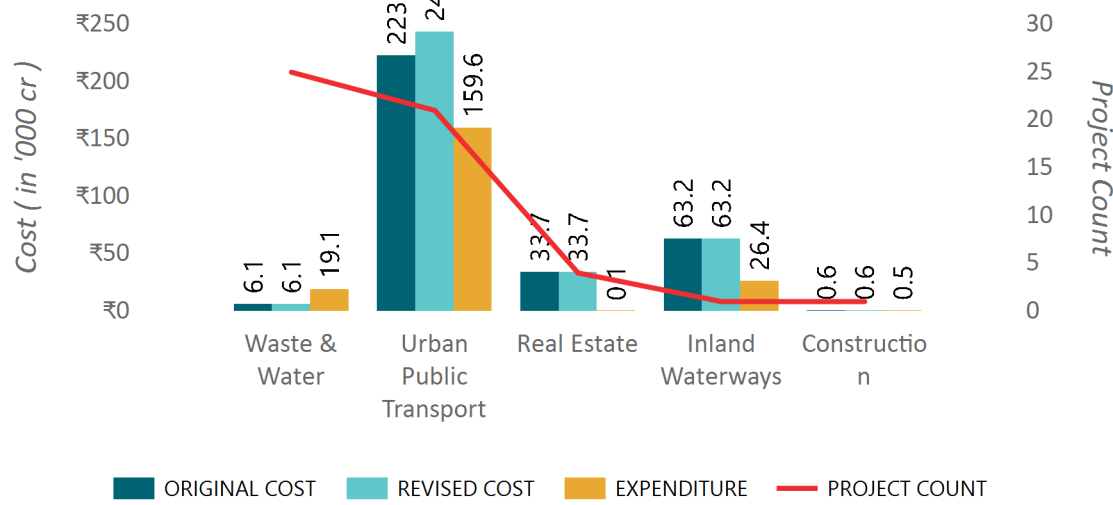

State Comparison : Major States*

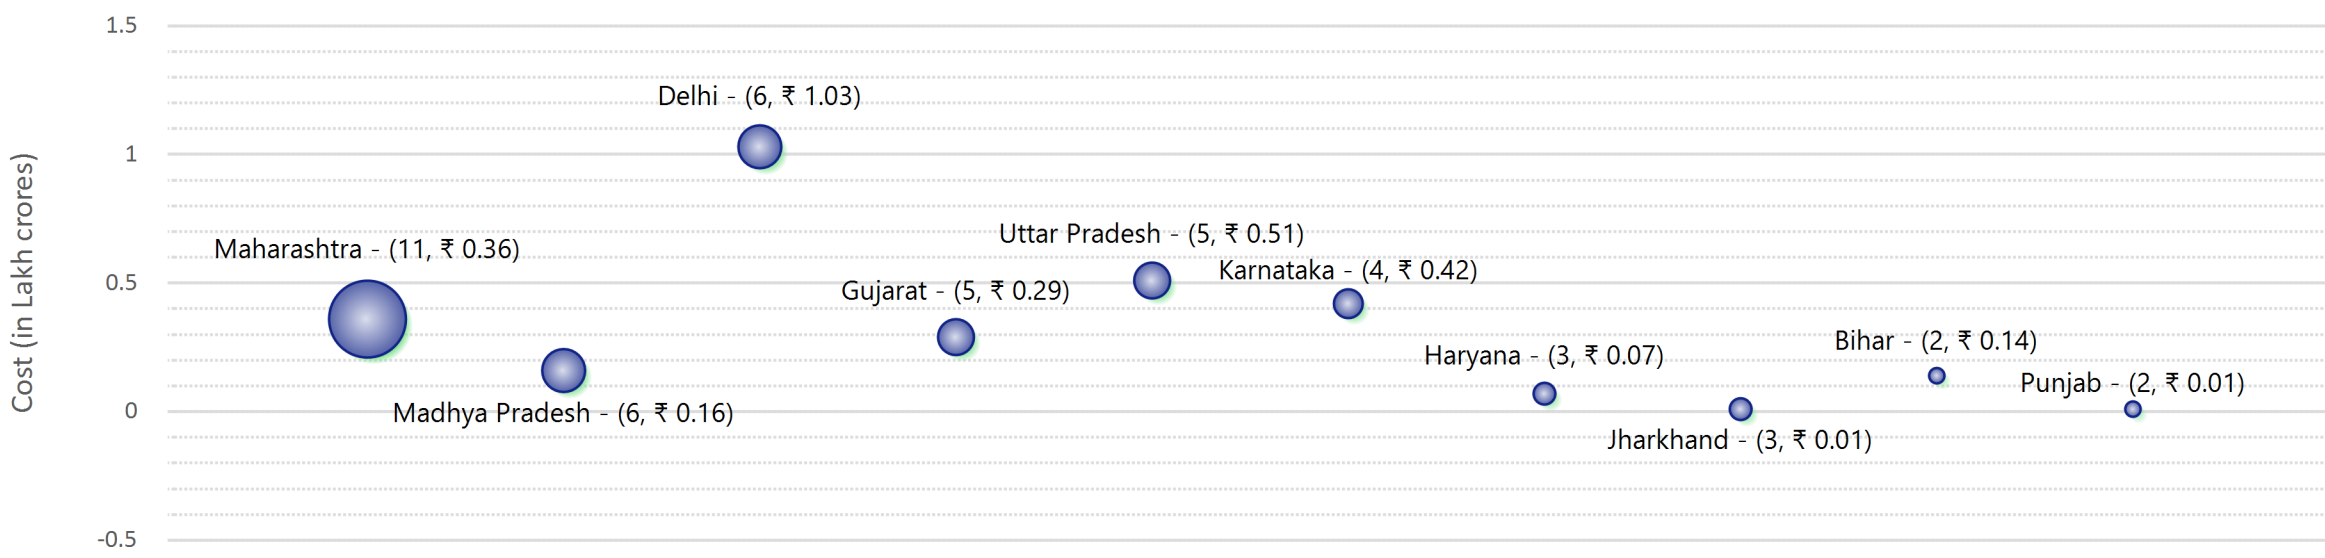

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246	63,246	26,410	45
2	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850	32,850	0	0
3	702633	DELHI-GHAZIABAD-MEERUT REGIONAL RAPID TRANSIT SYSTEM [RRTS] CORRIDOR	30,274	30,274	26,326	95
4	702635	CONSTRUCTION OF BANGALORE METRO RAIL PROJECT PHASE 2.	26,405	30,695	29,478	94
5	702632	DMRTS PHASE - IV [3 PRIORITY CORRIDORS]	24,949	24,949	15,785	69



List of Tables



Table 1: Ministry-wise Ongoing Projects





Ministry-wise Ongoing Projects

AUGUST 2025

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Real Estate	2	3841.25 3841.25	494.3
2	Department of Higher Education	Education	30	12754.41 12685.5	8159.38
3	Department of Telecommunications	Telecommunication	14	150849.85 272942	72122.5
4	Department of Water Resources, River Development & GR	Waste & Water	8	4039.12 4039.12	1643.05
		Water Resources	40	93248.95 195108	138397
5	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	26	23049.84 23511	24879.8
6	Ministry of Coal	Coal	117	166806.82 164263	53439.3
		Electricity Generation	5	46865.63 51408.8	23562.4
		Railways	2	3485.86 3485.86	1641.67
7	Ministry of Health & Family Welfare	Healthcare	3	4155 4492.95	2694.22
8	Ministry of Housing & Urban Affairs	Construction	1	646.53 646.52	533.12
		Inland Waterways	1	63246 63246	26410.2
		Real Estate	4	33749.85 33749.8	58.58
		Urban Public Transport	21	223016.77 243598	159570
		Waste & Water	25	6085.6 6085.6	19062.9
9	Ministry of Mines	Construction	1	255.37 255.37	79.34
		Metals & Mining	9	12736.35 15116.5	6124.59
10	Ministry of Petroleum & Natural Gas	Energy Storage	16	81301.48 120185	90497.5
		Oil & Gas	90	351248.78 383480	184032
11	Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58
		Inland Waterways	2	9612.82 9304.79	3876.92
		Shipping	5	4823.34 4823.34	2020.93
		Tourism, Hospitality & Wellness	1	573 1238.05	496.63
12	Ministry of Power	Coal	2	2083 2365	910.82
		Electricity Generation	30	223418.07 278228	132370
		Transmission & Distribution	61	142976.51 149491	52183.1
13	Ministry of Railways	Railways	263	691320.92 837521	524256
14	Ministry of Steel	Metals & Mining	1	1700 1756.2	65.44
		Steel	19	16748.25 19986.5	7969.76
Total			800	2,375,332.37	1,537,609.45



Table 2: State-wise Ongoing Projects



Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	6	19714.58 22972.8	10210.97
		Ministry of Railways	Railways	2	1311.83 1311.83	583.60
	PAN India	Department of Telecommunications	Telecommunication	6	141891.67 264213	69165.67
	Total			14	162918.08	79960.24
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 209.88	0.00
	Total			1	209.88	0.00
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	2139.44 2139.44	406.05
		Department of Higher Education	Education	1	305 305	83.33
		Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1699.75
		Department of Water Resources, River Development & GR	Water Resources	3	10901.5 57269.5	25827.76
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1224.86 1224.86	613.89
		Ministry of Housing & Urban Affairs	Waste & Water	1	172.22 172.22	622.02
		Ministry of Petroleum & Natural Gas	Energy Storage	2	2898.34 3050	2242.80
			Oil & Gas	5	37997 38057	33498.29
		Ministry of Power	Transmission & Distribution	5	13395.24 13395.2	4512.61
		Ministry of Railways	Railways	28	56255.53 63480.7	32347.60
	Total			51	130551.7	101854.10
4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 592.61	549.96
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Ministry of Petroleum & Natural Gas	Energy Storage	1	43129 79459	60295.14
			Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Electricity Generation	4	41850.64 61640.8	28586.95
			Transmission & Distribution	1	4754.42 9129.32	7462.20
		Ministry of Railways	Railways	1	435 1250	901.00
	Total			10	101282.16	104473.14
5	Assam	Department of Higher Education	Education	1	153.71 153.71	54.05
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 256.16	0.00
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1712 1712	2335.44
		Ministry of Coal	Coal	2	449.23 449.23	186.31
		Ministry of Housing & Urban Affairs	Waste & Water	1	186.8 186.8	1291.55
		Ministry of Petroleum & Natural Gas	Energy Storage	3	10768.4 11947.4	9941.27
			Oil & Gas	13	28019.15 41554	30591.24
		Ministry of Power	Electricity Generation	1	6285.33 26075.5	24880.95
			Transmission & Distribution	1	5111.33 6700	5277.24
	Ministry of Railways	Railways	7	14593.57 16308.6	10302.48	
Total			32	68791.17	85144.57	
6	Bihar	Department of Higher Education	Education	1	499.21 499.21	425.47
		Department of Telecommunications	Telecommunication	3	2336.11 2107.64	960.21
		Department of Water Resources, River Development & GR	Waste & Water	5	2351.43 2351.43	1303.45
			Water Resources	3	2884.49 4060.84	1590.27
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3541.56 3541.56	1256.71
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	13365.77 13365.8	4039.77
			Waste & Water	1	158.78 158.78	48.61
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9766.72
			Oil & Gas	7	24636.5 26501.2	13258.37

Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3510.72
		Ministry of Power	Electricity Generation	1	10439.09 13756.6	12148.46
			Transmission & Distribution	2	751.63 751.63	0.90
		Ministry of Railways	Railways	20	48815.69 52817.3	22483.47
	Total			49	125377.44	70793.13
7	Chhattisgarh	Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1699.75
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 1109.33	616.93
		Ministry of Coal	Coal	15	38654.89 38654.9	15480.40
			Railways	1	1686.22 1686.22	347.96
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	10056.25 10467	6509.05
		Ministry of Power	Electricity Generation	2	25321 25321	2480.00
			Transmission & Distribution	1	385.84 385.84	378.17
		Ministry of Railways	Railways	19	32162 34222.7	18291.67
		Ministry of Steel	Metals & Mining	1	1700 1756.2	65.44
	Steel		6	7530.14 10050.1	5270.32	
Total			51	123601.17	51139.69	
8	Dadra & Nagar Haveli and Daman & Diu	Ministry of Housing & Urban Affairs	Waste & Water	1	210 210	0.00
		Ministry of Power	Transmission & Distribution	1	4546.26 4546.26	4172.96
		Ministry of Railways	Railways	1	108000 108000	79918.89
	Total			3	112756.26	84091.85
9	Delhi	Department of Higher Education	Education	2	706.49 706.49	300.98
		Department of Telecommunications	Telecommunication	1	248.2 248.2	236.91
		Ministry of Housing & Urban Affairs	Construction	1	646.53 646.52	533.12
			Real Estate	1	32850 32850	0.00
			Urban Public Transport	4	69853.45 69853.4	42116.99
		Ministry of Power	Transmission & Distribution	4	4356.47 4908.47	3923.11
		Ministry of Railways	Railways	14	28176.96 28177	5356.29
	Total			27	136838.1	52467.40
10	Goa	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	255.69 255.69	130.00
		Ministry of Railways	Railways	2	5804.49 6182.62	5976.87
	Total			3	6060.18	6106.87
11	Gujarat	Department of Higher Education	Education	1	490.63 490.63	301.44
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Department of Water Resources, River Development & GR	Water Resources	2	25739.93 40082.8	36722.58
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1305 1551	1348.78
		Ministry of Coal	Coal	1	7580 7580	3091.00
			Electricity Generation	1	383.84 383.84	303.50
		Ministry of Housing & Urban Affairs	Real Estate	1	539 539	39.63
			Urban Public Transport	3	28177.49 30329	23950.31
			Waste & Water	1	200 200	100.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	62245 98575	75103.78
			Oil & Gas	11	32704.12 32178.7	22879.89
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	4243.64 4243.64	366.20
			Tourism, Hospitality & Wellness	1	573 1238.05	496.63
			Ministry of Power	Electricity Generation	1	339.35 339.35
	Transmission & Distribution	13		45319.41 45318.9	12842.82	



Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
11	Gujarat	Ministry of Railways	Railways	31	187430.66 262112	216423.66
		Total		73	397607.96	394515.63
12	Haryana	Ministry of Health & Family Welfare	Healthcare	1	1299 1299	349.41
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	6230.99 6230.99	0.29
			Waste & Water	2	491.2 491.2	2617.89
		Ministry of Petroleum & Natural Gas	Energy Storage	1	9028 9028	7136.41
			Oil & Gas	5	45925.07 49596.1	33666.90
		Ministry of Power	Transmission & Distribution	4	13362 13914	2619.30
		Ministry of Railways	Railways	4	53464 126368	125567.23
		Total		18	129800.26	171957.43
13	Himachal Pradesh	Department of Higher Education	Education	3	811.15 921.89	579.09
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Power	Electricity Generation	4	7728.04 12252.1	4137.13
		Ministry of Railways	Railways	3	17005 17005.1	9366.44
		Total		11	25881.08	14310.48
14	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 500.91	484.52
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 861.37	177.69
		Ministry of Health & Family Welfare	Healthcare	1	1828 1828	1531.86
		Ministry of Petroleum & Natural Gas	Energy Storage	1	676.89 676.89	526.10
			Oil & Gas	2	1059.9 1059.9	193.82
		Ministry of Power	Electricity Generation	4	22207.77 27945.1	12525.60
			Transmission & Distribution	3	825.43 825.43	496.12
		Total		14	28221.18	16163.53
15	Jharkhand	Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1699.75
		Department of Water Resources, River Development & GR	Water Resources	2	5430.04 12010.3	5704.07
		Ministry of Coal	Coal	27	45414.48 45178.8	10417.02
			Railways	1	1799.64 1799.64	1293.71
		Ministry of Housing & Urban Affairs	Waste & Water	3	654.14 654.14	2532.48
		Ministry of Mines	Metals & Mining	2	3370.02 3370.02	16.57
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9766.72
			Oil & Gas	3	2010.07 2010.07	595.56
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3510.72
		Ministry of Power	Coal	2	2083 2365	910.82
			Electricity Generation	2	31470 34660	18606.57
		Ministry of Railways	Railways	12	43352.74 43746.7	14874.38
		Ministry of Steel	Steel	6	2854.58 3572.87	1284.99
		Total		64	159298.46	71213.36
16	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1701.81 1701.81	88.25
		Department of Higher Education	Education	1	420.41 420.41	360.72
		Department of Water Resources, River Development & GR	Water Resources	1	770.16 1606.07	1511.22
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1143.4 1143.4	515.77
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	41193.24 45483.2	37902.51
			Waste & Water	2	337.69 337.69	1278.27
		Ministry of Petroleum & Natural Gas	Energy Storage	1	678 1732	713.86
			Oil & Gas	5	9662 12693.6	8749.96

Ongoing Projects State-Wise						AUGUST 2025
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	Karnataka	Ministry of Power	Transmission & Distribution	6	15682.01 15682	2815.76
		Ministry of Railways	Railways	17	25363.59 31532.2	17702.61
		Ministry of Steel	Steel	1	1043.63 1043.63	229.77
		Total		40	97995.94	71868.70
17	Kerala	Department of Higher Education	Education	1	1006.45 1217.4	623.60
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	484.57 484.57	83.95
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1957.05 1957.05	329.94
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	7996.87 10990.9	4912.37
		Ministry of Railways	Railways	3	2846 5199	3026.15
		Total		9	14290.94	8976.01
18	Ladakh	Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480 640	434.79
		Ministry of Power	Transmission & Distribution	1	288.71 288.71	207.80
		Total		3	1105.6	870.41
19	Madhya Pradesh	Department of Higher Education	Education	1	496.28 496.28	143.95
		Department of Telecommunications	Telecommunication	2	1999.22 1806.51	732.39
		Department of Water Resources, River Development & GR	Water Resources	3	2628.27 2941.14	2725.95
		Ministry of Coal	Coal	14	8634.02 8634.02	3368.12
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	14442.2 14442.2	7095.55
			Waste & Water	4	1243.05 1243.05	6956.60
		Ministry of Mines	Metals & Mining	1	1856.36 1856.36	935.32
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10088 10088	7672.23
			Oil & Gas	2	51211.25 51622	8351.10
		Ministry of Power	Transmission & Distribution	6	17446 17446	2930.65
		Ministry of Railways	Railways	18	56050.78 67640.2	42750.83
		Total		54	166095.43	83662.69
20	Maharashtra	Department of Higher Education	Education	2	250.33 446.26	154.70
		Department of Telecommunications	Telecommunication	3	5723.99 5723.99	1865.77
		Department of Water Resources, River Development & GR	Water Resources	10	20736.55 30421.9	31303.79
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	332.26
		Ministry of Coal	Coal	25	12455.88 12455.9	3084.72
		Ministry of Housing & Urban Affairs	Urban Public Transport	6	34571.47 48711.5	28993.92
			Waste & Water	5	1088.72 1088.72	2313.41
		Ministry of Petroleum & Natural Gas	Energy Storage	1	281.35 389.67	230.76
			Oil & Gas	13	34264.24 37660.4	20702.79
		Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58.00
			Shipping	2	1266.8 1266.8	441.86
		Ministry of Power	Transmission & Distribution	3	29589.67 29589.7	5993.74
		Ministry of Railways	Railways	36	267281.11 358733	262133.68
		Total		108	408703.59	357609.40
21	Manipur	Department of Water Resources, River Development & GR	Water Resources	1	1449.44 1822.24	1837.91
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499 499	154.43
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24
		Ministry of Railways	Railways	1	14323 21885.9	15598.11
		Total		5	30647.77	29261.54

Ongoing Projects State-Wise						AUGUST 2025
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
22	Meghalaya	Department of Higher Education	Education	1	494.52 494.52	413.57
		Department of Telecommunications	Telecommunication	1	971.96 971.96	208.25
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24
		Total		4	15842.81	12292.91
23	Mizoram	Department of Higher Education	Education	1	474.23 474.23	167.55
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24
		Total		3	14850.56	11838.64
24	Nagaland	Department of Higher Education	Education	1	275.63 275.63	260.10
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	9492.62 9492.62	6402.97
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24
		Ministry of Railways	Railways	2	8786.7 8786.7	5326.00
		Total		6	23666.28	17266.31
25	Odisha	Department of Higher Education	Education	1	1229.32 773.76	837.04
		Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1699.75
		Department of Water Resources, River Development & GR	Water Resources	2	1556.46 5291.33	5193.30
		Ministry of Coal	Coal	12	36526.28 34218	13335.92
			Electricity Generation	1	27212.96 27213	1953.52
		Ministry of Mines	Metals & Mining	5	7343.97 9724.14	5037.70
		Ministry of Petroleum & Natural Gas	Energy Storage	2	12886.34 14217	11970.70
			Oil & Gas	5	25285.44 23768.5	15778.36
		Ministry of Ports, Shipping and Waterways	Shipping	1	3004.63 3004.63	1149.79
		Ministry of Power	Electricity Generation	1	11843.75 12543	4161.68
			Transmission & Distribution	1	342.69 342.69	0.60
		Ministry of Railways	Railways	28	47401.37 52133.4	31907.65
			Railways	1	267.61 267.61	0.00
		Ministry of Steel	Steel	1	1105.23 1105.23	769.08
		Total		63	181268.62	93795.09
26	Puducherry	Department of Higher Education	Education	1	618.34 544.34	509.55
		Ministry of Railways	Railways	1	713 981	598.38
		Total		2	1331.34	1107.93
27	Punjab	Department of Higher Education	Education	2	559.3 559.3	290.39
		Department of Water Resources, River Development & GR	Water Resources	2	3727.07 5177.86	5072.69
		Ministry of Housing & Urban Affairs	Waste & Water	2	545.53 545.53	612.96
		Ministry of Petroleum & Natural Gas	Oil & Gas	6	13060.36 13090.4	8374.98
		Ministry of Power	Transmission & Distribution	1	5969 5969	218.47
		Ministry of Railways	Railways	3	15702.64 15702.6	8977.71
			Railways	3	15702.64 15702.6	8977.71
		Total		16	39563.9	23547.20
28	Rajasthan	Department of Telecommunications	Telecommunication	2	758.54 530.07	361.90
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1367 1367	634.54
		Ministry of Coal	Electricity Generation	1	1813 1813	874.14
		Ministry of Petroleum & Natural Gas	Energy Storage	3	52618.05 88948.1	67548.03
			Oil & Gas	2	10599 10599	6647.57
		Ministry of Power	Electricity Generation	1	5491.89 5491.89	4805.16
			Transmission & Distribution	22	53646.51 54198.2	16979.78
		Total		33	121118.11	100000.00

Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
28	Rajasthan	Ministry of Railways	Railways	21	86599.15 162169	139520.05
		Total		54	212893.14	237371.17
29	Sikkim	Department of Higher Education	Education	2	999.82 924.82	359.78
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 323.26	29.70
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Electricity Generation	2	6686.33 7576.15	6161.06
			Transmission & Distribution	1	4754.42 9129.32	7462.20
		Ministry of Railways	Railways	1	7877 12133	9039.91
		Total		8	29905.83	29446.50
30	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1207 1207	149.21
		Ministry of Coal	Electricity Generation	1	218.03 218.03	161.73
		Ministry of Housing & Urban Affairs	Inland Waterways	1	63246 63246	26410.15
		Ministry of Mines	Metals & Mining	1	166 166	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	2334 3448.71	1641.58
			Oil & Gas	4	38385 46153	6060.57
		Ministry of Power	Transmission & Distribution	1	548 548	14.68
		Ministry of Railways	Railways	8	8730 11599	5805.89
		Total		20	114834.03	40378.81
31	Telangana	Department of Higher Education	Education	1	262 262	177.09
		Department of Telecommunications	Telecommunication	2	2038.99 2038.99	764.33
		Department of Water Resources, River Development & GR	Water Resources	4	11670.14 24129.6	11830.43
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	332.26
		Ministry of Coal	Coal	9	3890.03 3890.03	2462.36
		Ministry of Health & Family Welfare	Healthcare	1	1028 1365.95	812.95
		Ministry of Power	Transmission & Distribution	2	5694.56 5694.56	4337.14
		Ministry of Railways	Railways	11	22284.15 26048.2	9009.21
		Total		31	47368.35	29725.77
32	Tripura	Ministry of Petroleum & Natural Gas	Energy Storage	1	656 656	478.11
			Oil & Gas	2	9474.33 9396.51	6462.73
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24
		Total		4	15241.66	12218.08
33	Uttar Pradesh	Department of Higher Education	Education	1	246 246	193.38
		Department of Telecommunications	Telecommunication	3	2336.11 2107.64	960.21
		Department of Water Resources, River Development & GR	Waste & Water	2	1532.96 1532.96	243.43
			Water Resources	4	3694.65 8775.49	7633.54
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	5	7268.31 7323.51	16971.73
		Ministry of Coal	Coal	2	1328.09 1328.09	1017.31
			Electricity Generation	1	17237.8 21780.9	20269.54
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	49730.1 49730.1	41466.62
			Waste & Water	2	797.47 797.47	689.15
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11068.45 11068.5	7888.89
			Oil & Gas	3	17824.68 18213.1	1578.44
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3510.72
		Ministry of Power	Electricity Generation	2	28284.42 30471.2	14511.21
			Transmission & Distribution	3	8114.81 8114.81	1650.63

Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
33	Uttar Pradesh	Ministry of Railways	Railways	28	95245.3 169871	148169.27
		Total		62	250078.33	266754.07
34	Uttarakhand	Department of Higher Education	Education	1	650.85 650.85	195.52
		Department of Water Resources, River Development & GR	Water Resources	1	2584.1 2584.1	968.52
		Ministry of Housing & Urban Affairs	Real Estate	1	150.97 150.97	18.95
		Ministry of Power	Electricity Generation	3	11663.95 26070	20361.54
		Ministry of Railways	Railways	1	38953 38953	24645.15
		Total		7	54002.87	46189.68
35	West Bengal	Department of Higher Education	Education	2	787.2 729.2	693.60
		Department of Telecommunications	Telecommunication	1	1577.57 1577.57	598.31
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 154.73	96.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1877.3 1877.3	375.40
		Ministry of Coal	Coal	13	15863.74 15863.7	2802.30
		Ministry of Mines	Construction	1	255.37 255.37	79.34
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9766.72
			Oil & Gas	8	18159.65 19007.2	11294.42
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3510.72
			Shipping	2	551.91 551.91	429.28
		Ministry of Power	Electricity Generation	3	20091.84 20160.8	3566.83
			Transmission & Distribution	2	751.63 751.63	0.90
		Ministry of Railways	Railways	16	49682.05 60254	33496.35
		Ministry of Steel	Steel	5	4214.67 4214.67	415.60
		Total		58	129564.84	67125.94



Table 3: Ongoing Projects North Eastern Region



Ongoing Projects of North-East Region							AUGUST 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (11/2025)	1712 (1712)	2335.44	91
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	154.43	41
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	29.7	12
	Total (3)				2534.26	2519.57	
	Ministry of Coal						
	Coal						
4	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	80.84	0
5	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.47	0
	Total (2)				449.23	186.31	
	Department of Higher Education						
	Education						
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	NA (03/2013)	08/2026 (-)	592.61 (592.61)	549.96	75
7	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (08/2025)	153.71 (153.71)	54.05	95
8	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	03/2020 (09/2014)	03/2022 (07/2025)	494.52 (494.52)	413.57	86
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (Ministry of Education) (612876)	Mizoram	03/2020 (05/2014)	12/2029 (12/2029)	474.23 (474.23)	167.55	4
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	NA (09/2012)	12/2025 (-)	275.63 (275.63)	260.1	95
11	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (Ministry of Education) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	121.56	9
12	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (09/2025)	314.06 (314.06)	238.22	82
	Total (7)				2990.52	1805.01	
	Ministry of Power						
	Electricity Generation						
13	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	49.31	3
14	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	102.79	2
15	Dibang Multipurpose Project (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3553.9	16
16	Subansiri Lower HE Project [2000 MW] (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (09/2003)	09/2010 (05/2026)	6285.33 (26075.5)	24880.95	96
17	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602181)	Sikkim	03/2019 (03/2019)	03/2024 (12/2027)	5748.04 (5748.04)	4576.93	69
18	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (605156)	Sikkim	03/2021 (03/2021)	05/2024 (12/2025)	938.29 (1828.11)	1584.13	91
	Total (6)				48536.97	34748.01	
	Transmission & Distribution						
19	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	03/2021 (01/2016)	12/2018 (03/2027)	4754.42 (9129.32)	7462.2	81
20	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (12/2025)	5111.33 (6700)	5277.24	96

Ongoing Projects of North-East Region							AUGUST 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (2)				9865.75	12739.44	
	Ministry of Petroleum & Natural Gas						
	Energy Storage						
21	Rajasthan Refinery Project (Ministry of Petroleum & Natural Gas) (701263)	Arunachal Pradesh	NA (10/2017)	10/2022 (03/2026)	43129 (79459)	60295.14	88
22	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Assam	NA (01/2019)	07/2024 (09/2025)	10228 (11407)	9766.72	87
23	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	NA (03/2023)	07/2027 (07/2027)	156.36 (156.36)	54.15	46
24	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	NA (03/2023)	07/2027 (07/2027)	384.04 (384.04)	120.4	52
25	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	NA (06/2022)	09/2025 (06/2026)	656 (656)	478.11	86
	Total (5)				54553.4	70714.52	
	Oil & Gas						
26	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	NA (07/2020)	07/2024 (12/2025)	12366 (22494)	16764.09	76
27	Assam Bio Refinery, ABRPL (Ministry of Petroleum & Natural Gas) (604792)	Assam	NA (02/2018)	09/2021 (09/2025)	1750 (4930)	4710	99
28	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	NA (01/2018)	02/2020 (12/2025)	682.9 (726.93)	489.3	94
29	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	NA (05/2021)	10/2023 (05/2026)	412.3 (577)	430.83	85
30	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Assam	NA (06/2021)	12/2024 (10/2025)	860 (860)	584.76	98
31	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	NA (12/2020)	03/2024 (12/2025)	430.76 (430.76)	327.27	85
32	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Ministry of Petroleum & Natural Gas) (709776)	Assam	NA (04/2022)	09/2026 (09/2026)	277 (323.09)	185.18	68
33	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Ministry of Petroleum & Natural Gas) (709779)	Assam	NA (06/2022)	03/2026 (03/2026)	768 (740)	107.72	39
34	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	NA (01/2023)	04/2026 (04/2026)	344.99 (344.99)	211.05	47
35	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	NA (09/2023)	05/2026 (05/2026)	198.7 (198.7)	36.8	30
36	DCU Revamp Project (NRL) (709864)	Assam	NA (08/2021)	07/2024 (10/2025)	370 (370)	253.17	60
37	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	NA (04/2023)	12/2024 (10/2025)	293.5 (293.5)	97.22	94
38	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura)	NA (04/2020)	03/2024 (03/2026)	9265 (9265)	6393.85	85
39	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum & Natural Gas) (709786)	Nagaland	NA (08/2023)	11/2027 (11/2027)	227.62 (227.62)	9.12	22
40	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	NA (03/2022)	05/2024 (12/2025)	209.33 (131.51)	68.88	62
	Total (15)				28456.1	30669.24	
	Ministry of Railways						
	Railways						
41	Doubling of New Bongaigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3683.75	93
42	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
43	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	NA (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
44	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	NA (01/2022)	05/2024 (-)	237.52 (237.52)	0	0

Ongoing Projects of North-East Region

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
45	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15598.11	69
46	Murkongselek-Pasighat (Northeast Frontier Railway (NFR) - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	NA (03/2012)	03/2025 (12/2025)	435 (1250)	901	56
47	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5312.26	80
48	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	NA (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
49	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Sikkim	10/2009 (05/2010)	05/2015 (12/2027)	7877 (12133)	9039.91	84
Total (9)					36793.57	34940.5	
Department of Telecommunications							
Telecommunication							
50	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications [DoT]) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (09/2025)	971.96 (971.96)	208.25	99
51	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications [DoT]) (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (09/2025)	1255.49 (1255.49)	284.04	89
Total (2)					2227.45	492.29	
Ministry of Housing & Urban Affairs							
Waste & Water							
52	Dibrugarh Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702682)	Assam	NA (01/2020)	03/2023 (12/2025)	186.8 (186.8)	1291.55	98
Total (1)					186.8	1291.55	
Department of Water Resources, River Development & GR							
Water Resources							
53	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	NA (12/1996)	12/2022 (03/2026)	256.16 (256.16)	0	55
54	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	01/2022 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
Total (2)					1705.6	1837.91	




Table 4: All Ongoing Projects



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport (Airport Authority of India [AAI]) (612786)	Andhra Pradesh	03/2023 (01/2024)	01/2026 (03/2026)	265.91 (265.91)	50.06	34
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. (Airport Authority of India [AAI]) (701107)	Andhra Pradesh	06/2020 (09/2020)	09/2022 (12/2025)	611.8 (611.8)	473.27	79
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. (Airport Authority of India [AAI]) (701121)	Andhra Pradesh	12/2022 (08/2023)	08/2025 (12/2025)	347.15 (347.15)	90.56	51
4	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (11/2025)	1712 (1712)	2335.44	91
5	Development of New Civil Enclave at Bihta (Airport Authority of India [AAI]) (612183)	Bihar	08/2024 (03/2025)	09/2027 (-)	1413 (1413)	0	1
6	Development of New Civil Enclave and associated works at Darbhanga Airport (Airport Authority of India [AAI]) (612194)	Bihar	07/2024 (07/2024)	01/2026 (-)	911.66 (911.66)	160.2	26
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna (Airport Authority of India [AAI]) (701101)	Bihar	12/2018 (10/2018)	07/2023 (11/2025)	1216.9 (1216.9)	1096.51	94
8	Goa Airport Terminal Building Extension Project (Airport Authority of India [AAI]) (701105)	Goa	11/2017 (12/2019)	12/2021 (09/2025)	255.69 (255.69)	130	90
9	Development of Dholera International Greenfield Airport , Gujarat (Airport Authority of India [AAI]) (701126)	Gujarat	06/2022 (07/2022)	06/2026 (06/2026)	1305 (1551)	1348.78	64
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. (Airport Authority of India [AAI]) (611047)	Jammu and Kashmir	07/2022 (07/2023)	06/2026 (06/2026)	861.37 (861.37)	177.69	35
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport (Airport Authority of India [AAI]) (612787)	Karnataka	06/2023 (01/2024)	01/2026 (03/2026)	320.47 (320.47)	61.79	38
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. (Airport Authority of India [AAI]) (612788)	Karnataka	06/2023 (02/2024)	01/2026 (01/2026)	322.45 (322.45)	121.72	52
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 (Airport Authority of India [AAI]) (612789)	Kerala	06/2023 (02/2024)	09/2025 (03/2026)	484.57 (484.57)	83.95	21
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh (Airport Authority of India [AAI]) (400010)	Ladakh	07/2018 (09/2018)	09/2021 (10/2025)	480 (640)	434.79	71
15	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	154.43	41
16	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, Jewar [earlier MOPA, without ASMGCS], HIAL & BIAL (Airport Authority of India [AAI]) (611570)	Multi-States (Karnataka, Maharashtra, Telangana, Uttar Pradesh)	NA (10/2022)	09/2025 (08/2026)	500.48 (500.48)	332.26	75
17	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. (Airport Authority of India [AAI]) (701127)	Rajasthan	05/2022 (04/2023)	11/2024 (10/2025)	480 (480)	281.72	84
18	Construction of New Integrated Passenger Terminal Building at Udaipur Airport (Airport Authority of India [AAI]) (701128)	Rajasthan	06/2023 (11/2022)	03/2026 (10/2026)	887 (887)	352.82	49
19	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	29.7	12
20	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAI]) (611602)	Tamil Nadu	05/2018 (06/2023)	07/2025 (03/2026)	1207 (1207)	149.21	22
21	Construction of New Terminal Building, Second Link Taxi Track, Apron Expansion, and associated works at Prayagraj Airport- On Design & Build Basis. (Airport Authority of India [AAI]) (612063)	Uttar Pradesh	NA (08/2023)	11/2024 (08/2025)	219.18 (274.38)	215.19	100
22	Lucknow Airport-Terminal 3- Phase 1 & Other Associated Works (Adani Airport Holdings Limited) (701091)	Uttar Pradesh	06/2018 (09/2018)	03/2026 (-)	3100 (3100)	16024.42	100
23	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAI]) (701113)	Uttar Pradesh	07/2024 (07/2024)	07/2027 (07/2027)	2869.65 (2869.65)	322.98	16
24	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAI]) (701122)	Uttar Pradesh	06/2024 (07/2024)	07/2026 (-)	579 (579)	76.88	16
25	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAI]) (611495)	West Bengal	08/2024 (10/2023)	01/2027 (01/2027)	1549 (1549)	274.14	11

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
26	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCB Airport Kolkata. <i>(Airport Authority of India [AAI])</i> (612791)	West Bengal	04/2023 (12/2023)	02/2025 (08/2026)	328.3 (328.3)	101.26	45
	Total (26)				23049.84	24879.77	
	Ministry of Coal						
	Coal						
27	TIKAK EXTENSION OCP <i>(MIS MoCoal Integration Logins)</i> (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	80.84	0
28	TIRAP OCP <i>(MIS MoCoal Integration Logins)</i> (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.47	0
29	PORDA CHINTAPANI OCP [10 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400144)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	2310.12 (2310.12)	83.66	10
30	CHHAL OC SEAM III [6 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400145)	Chhattisgarh	12/2013 (12/2013)	03/2022 (09/2025)	610.63 (610.63)	577.46	85
31	KUSMUNDA OC EXPANSION [15 TO 50 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400147)	Chhattisgarh	08/2013 (08/2013)	03/2023 (03/2030)	7612.33 (7612.33)	4697.95	81
32	BAROUD OC EXPANSION [3.0-10.0M] <i>(South Eastern Coalfields Limited [SECL])</i> (400149)	Chhattisgarh	08/2020 (08/2020)	03/2029 (-)	2309.8 (2309.8)	926.11	48
33	DIPKA EXPANSION OCP [40 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400354)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	5241.4 (5241.4)	2830.01	37
34	GEVRA OC [70 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400424)	Chhattisgarh	03/2016 (03/2016)	03/2023 (03/2026)	11816.4 (11816.4)	5328.96	77
35	JAMPALI OC RCE [2.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613795)	Chhattisgarh	05/2020 (05/2020)	03/2025 (06/2025)	278.64 (278.64)	210.07	82
36	AMERA OC RCE [1.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613798)	Chhattisgarh	02/2015 (02/2015)	03/2026 (-)	335.97 (335.97)	88.21	42
37	AMGAON OC RCE [1.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613799)	Chhattisgarh	07/2015 (07/2015)	03/2026 (-)	316.11 (316.11)	188.6	72
38	JAGANNATHPUR OC RCE PROJECT[3 <i>(South Eastern Coalfields Limited [SECL])</i> (613800)	Chhattisgarh	07/2016 (07/2016)	03/2025 (03/2026)	459.49 (459.49)	274.35	92
39	MAHAMAYA OCP [1.50 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613801)	Chhattisgarh	05/2018 (05/2018)	03/2026 (-)	410.26 (410.26)	181.23	38
40	KATKONA RO UG MINE <i>(South Eastern Coalfields Limited [SECL])</i> (615191)	Chhattisgarh	01/2023 (01/2023)	03/2029 (-)	329.21 (329.21)	60.3	2
41	PELMA OC MDO <i>(South Eastern Coalfields Limited [SECL])</i> (616234)	Chhattisgarh	10/2022 (10/2022)	03/2033 (-)	1725.04 (1725.04)	15.66	17
42	KUSMUNDA OC EXPANSION PROJECT 50-75 MTY <i>(SECL - CIL)</i> (617287)	Chhattisgarh	11/2024 (11/2024)	03/2030 (-)	4516.88 (4516.88)	16.97	3
43	MANIKPUR OC EXPANSION PROJECT 7 MTY <i>(South Eastern Coalfields Limited [SECL])</i> (617288)	Chhattisgarh	01/2025 (01/2025)	03/2029 (-)	382.61 (382.61)	0.86	1
44	DIPKA OC <i>(SECL - CIL)</i> (612838)	Gujarat	NA (01/2017)	03/2025 (-)	7580 (7580)	3091	65
45	HURA C OCP <i>(ECL - CIL)</i> (400018)	Jharkhand	08/2022 (08/2022)	03/2029 (-)	859.41 (859.41)	450.76	62
46	KONAR EXPANSION OCP <i>(Ministry of Coal)</i> (400073)	Jharkhand	01/2022 (01/2022)	03/2032 (-)	799.34 (799.34)	424.01	45
47	KARO EXPANSION OCP <i>(Ministry of Coal)</i> (400074)	Jharkhand	01/2022 (01/2022)	03/2029 (-)	908.47 (908.47)	269.18	22
48	SANGHMITRA OC <i>(Ministry of Coal)</i> (400136)	Jharkhand	03/2024 (03/2027)	03/2032 (-)	2660 (2660)	0	0
49	CHANDRAGUPT OCP <i>(Ministry of Coal)</i> (400138)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	973.5 (973.5)	440.56	25
50	KOTRE BASANTPUR PACHMO OCP <i>(Ministry of Coal)</i> (400139)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	861.06 (625.4)	455.95	42
51	Pachwara South Coal Block <i>(NLC India Limited [NLCIL])</i> (400142)	Jharkhand	NA (12/2019)	09/2028 (-)	2242.9 (2242.9)	1170.75	74
52	RPR MAGADH EXP OCP <i>(Ministry of Coal)</i> (400150)	Jharkhand	08/2020 (08/2020)	03/2028 (-)	7254.37 (7254.37)	1535.31	38
53	NORTH URIMARI EXPANSION OCP <i>(Ministry of Coal)</i> (400151)	Jharkhand	07/2021 (07/2021)	03/2029 (-)	778.8 (778.8)	695.99	67
54	EPR ROHINI - KARKETTA OCP <i>(Central Coalfields Limited [CCL])</i> (400153)	Jharkhand	01/2021 (01/2021)	03/2028 (-)	1020.42 (1020.42)	83.95	20



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
55	EPR PUNDI OCP (Ministry of Coal) (400154)	Jharkhand	11/2020 (11/2020)	03/2027 (-)	713.35 (713.35)	236.58	10
56	EPR ASHOK OC (Ministry of Coal) (400155)	Jharkhand	05/2021 (05/2021)	03/2028 (-)	2898.28 (2898.28)	178.51	22
57	EPR AMRAPALI OCP (Ministry of Coal) (400156)	Jharkhand	02/2020 (02/2020)	03/2028 (-)	5136.15 (5136.15)	1154.6	43
58	RAJRAPPA RCE OCP (Ministry of Coal) (400160)	Jharkhand	12/2009 (12/2009)	03/2016 (03/2027)	510.85 (510.85)	488.67	76
59	CHITRA EAST OC (Eastern Coal Fields Limited [ECL]) (400172)	Jharkhand	08/2018 (08/2018)	03/2026 (-)	513.99 (513.99)	229.01	51
60	JHARKHAND-LAIYO OCP (Ministry of Coal) (400352)	Jharkhand	08/2020 (08/2020)	03/2031 (-)	764.57 (764.57)	145.81	29
61	MOONIDIH XV SEAM UG (Ministry of Coal) (400425)	Jharkhand	08/2011 (08/2011)	03/2019 (05/2026)	1230.27 (1230.27)	626.63	81
62	2.5 MTPA PATHERDIH NLW WASHERY (Ministry of Coal) (611017)	Jharkhand	10/2015 (04/2016)	04/2018 (03/2026)	334.27 (334.27)	140.51	48
63	AMALAGAMATED NTST KUJAMA OCP 8.5MTY (Ministry of Coal) (611864)	Jharkhand	01/2023 (01/2023)	03/2030 (-)	4011.85 (4011.85)	398.5	28
64	MURAIIDH UG PROJECT (Ministry of Coal) (613808)	Jharkhand	02/2011 (02/2011)	04/2014 (12/2026)	339.87 (339.87)	191	70
65	TAPIN SOUTH EXPN (Ministry of Coal) (615349)	Jharkhand	11/2020 (11/2020)	03/2028 (-)	230.41 (230.41)	22.02	20
66	SIRKA OC (Ministry of Coal) (615822)	Jharkhand	05/2020 (05/2020)	03/2028 (-)	222.82 (222.82)	139.31	53
67	TETARIAKHAR OC (Ministry of Coal) (615843)	Jharkhand	11/2019 (11/2019)	03/2025 (03/2027)	243.52 (243.52)	44.64	30
68	CHUPERBHITA SIMLONG OCP MDO 6 MTY (Eastern Coal Fields Limited [ECL]) (616225)	Jharkhand	12/2023 (12/2023)	03/2037 (-)	979.08 (979.08)	0	0
69	JARANGDIH EXPN. OCP 1.5 MTY (CCL - CIL) (616236)	Jharkhand	02/2020 (02/2020)	03/2029 (-)	414.37 (414.37)	85.6	33
70	BLOCK E OCP (Ministry of Coal) (616253)	Jharkhand	03/2024 (03/2024)	03/2029 (-)	5850.83 (5850.83)	20.32	3
71	AMADAND OCP[4.0MTY] (South Eastern Coalfields Limited [SECL]) (400148)	Madhya Pradesh	03/2016 (03/2016)	03/2021 (03/2027)	869.44 (869.44)	273.45	75
72	RAMPUR BATURA OCP [4.0MTY] (South Eastern Coalfields Limited [SECL]) (400152)	Madhya Pradesh	07/2019 (07/2019)	03/2026 (-)	1248.93 (1248.93)	495.4	44
73	BLOCK B EXPANSION [3.5 TO 8.0 (Northern Coalfields Limited [NCL]) (400162)	Madhya Pradesh	07/2019 (07/2019)	03/2023 (03/2027)	998.71 (998.71)	457.2	47
74	NIGAH I EXPANSION [15 TO 25 MTP (Northern Coalfields Limited [NCL]) (400321)	Madhya Pradesh	11/2020 (11/2020)	03/2025 (03/2028)	1729.68 (1729.68)	804.11	48
75	KANCHAN OC EXP (South Eastern Coalfields Limited [SECL]) (613802)	Madhya Pradesh	12/2014 (12/2014)	03/2026 (-)	371.04 (371.04)	144.61	47
76	JHIRIA WEST OCP [1.5 MTY] (South Eastern Coalfields Limited [SECL]) (613803)	Madhya Pradesh	01/2024 (01/2024)	03/2026 (-)	366.94 (366.94)	34.05	41
77	RPR TAWA-III UG 0.84 MTY (Western Coalfields Limited [WCL]) (613804)	Madhya Pradesh	12/2021 (12/2021)	03/2027 (-)	314.09 (314.09)	5.79	17
78	AMALGAMATED DHANKASA & JAMUNIA (Western Coalfields Limited [WCL]) (615185)	Madhya Pradesh	09/2022 (09/2022)	03/2027 (-)	399.2 (399.2)	91.67	66
79	RPR OF VISHNUPURI UG TO OC (Western Coalfields Limited [WCL]) (615187)	Madhya Pradesh	11/2022 (11/2022)	03/2029 (-)	220.62 (220.62)	0	11
80	URDHAN EXPANSION OC COST PLUS (Western Coalfields Limited [WCL]) (615194)	Madhya Pradesh	07/2022 (01/2023)	03/2031 (-)	206.88 (206.88)	27.19	1
81	SHARDA UG MINE (Western Coalfields Limited [WCL]) (615195)	Madhya Pradesh	07/2023 (09/2023)	03/2028 (-)	166.25 (166.25)	3.96	9
82	GANDHIGRAM UG MINE (Western Coalfields Limited [WCL]) (615206)	Madhya Pradesh	08/2019 (08/2019)	03/2026 (-)	414.15 (414.15)	13.38	57
83	BHATADI EXPANSION OC (Western Coalfields Limited [WCL]) (400033)	Maharashtra	02/2020 (05/2022)	03/2028 (-)	580.61 (580.61)	69.73	26
84	AMALGAMATED YEKONA I & YEKONA (Western Coalfields Limited [WCL]) (400177)	Maharashtra	08/2015 (08/2015)	03/2025 (03/2026)	727.28 (727.28)	535.96	80
85	DINESH[MAKARDHOKRA-III] OC (Western Coalfields Limited [WCL]) (400178)	Maharashtra	02/2020 (02/2020)	03/2027 (-)	822.88 (822.88)	621.73	35



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
86	DHUPTALA OC [SASTI UG TO OC] (<i>Western Coalfields Limited [WCL]</i>) (400353)	Maharashtra	10/2021 (10/2021)	03/2028 (-)	711.01 (711.01)	80.61	17
87	SAONER UG MINE -1 EXPANSION 1. (<i>Western Coalfields Limited [WCL]</i>) (615184)	Maharashtra	01/2022 (01/2022)	03/2028 (-)	228.64 (228.64)	141.21	68
88	SASTI EXPANSION OPENCAST (<i>Western Coalfields Limited [WCL]</i>) (615186)	Maharashtra	08/2020 (08/2020)	03/2026 (-)	319.04 (319.04)	90.31	20
89	NEW MAJRI UG TO OC 3 MTY COST (<i>Western Coalfields Limited [WCL]</i>) (615188)	Maharashtra	05/2019 (09/2022)	03/2027 (-)	402.27 (402.27)	55.44	24
90	MAKARDHOKRA EXPN OC 4.9 MTY (<i>Western Coalfields Limited [WCL]</i>) (615189)	Maharashtra	06/2022 (06/2022)	03/2026 (-)	361.87 (361.87)	70.22	12
91	SINGHORI DEEP OC MIN 2.0 MTY (<i>Western Coalfields Limited [WCL]</i>) (615190)	Maharashtra	05/2022 (05/2022)	03/2029 (-)	335.75 (335.75)	26.79	6
92	GOKUL EXTENSION OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615192)	Maharashtra	04/2021 (04/2021)	03/2026 (-)	309.58 (309.58)	40.06	8
93	KOLGAON EXPANSION DEEP OC MINE 0.80 MTY (<i>Western Coalfields Limited [WCL]</i>) (615199)	Maharashtra	09/2023 (09/2023)	03/2027 (-)	198.71 (198.71)	0.71	3
94	BALLARPUR NORTH WEST OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615330)	Maharashtra	12/2022 (12/2022)	03/2029 (-)	360.81 (360.81)	0.02	4
95	GADEGAON OC 3 MTY (<i>Western Coalfields Limited [WCL]</i>) (615331)	Maharashtra	10/2023 (10/2023)	03/2030 (-)	497.41 (497.41)	0.08	0
96	GHONSA EXPANSION DEEP OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615914)	Maharashtra	03/2021 (03/2021)	03/2029 (-)	184.71 (184.71)	11.48	6
97	AMLG GAURI PAUNI EXPANSION OC (<i>Western Coalfields Limited [WCL]</i>) (615916)	Maharashtra	04/2024 (04/2024)	03/2030 (-)	1225.21 (1225.21)	78.87	1
98	GAURIDEEP/GAURI CENTRAL OCP 7. (<i>Western Coalfields Limited [WCL]</i>) (615917)	Maharashtra	06/2024 (06/2024)	03/2030 (-)	973.07 (973.07)	0.24	0
99	RPR OF BHANEGAON OC (<i>Western Coalfields Limited [WCL]</i>) (615918)	Maharashtra	02/2017 (09/2022)	03/2028 (-)	405.2 (405.2)	12.36	8
100	N. EXTN. MUNGOLI NIRGUDA D OCP (<i>Western Coalfields Limited [WCL]</i>) (615919)	Maharashtra	06/2024 (06/2024)	03/2030 (-)	1024.91 (1024.91)	168.59	0
101	NILJAI EXPANSION DEEP OCP (<i>Western Coalfields Limited [WCL]</i>) (615982)	Maharashtra	08/2016 (08/2016)	03/2022 (03/2026)	319.75 (319.75)	367.6	79
102	UKNI DEEP OC MINE -COST PLUS (<i>Western Coalfields Limited [WCL]</i>) (616044)	Maharashtra	01/2019 (01/2019)	03/2021 (03/2026)	237.06 (237.06)	165.57	87
103	AMALGAMATED INDER-KAMPTEE DEEP OC (<i>Western Coalfields Limited [WCL]</i>) (616050)	Maharashtra	09/2018 (09/2018)	03/2024 (03/2026)	235.9 (235.9)	237.12	98
104	ADASA UG TO OC MINE (<i>Western Coalfields Limited [WCL]</i>) (616223)	Maharashtra	11/2018 (11/2018)	03/2024 (03/2026)	316 (316)	308.84	86
105	AMAL GONDEGAON GHATROHANA EXPN (<i>Western Coalfields Limited [WCL]</i>) (616229)	Maharashtra	09/2024 (09/2024)	03/2030 (-)	668.54 (668.54)	1.18	0
106	WAGHODA UG MINE [1.02 MTY] (<i>Western Coalfields Limited [WCL]</i>) (617233)	Maharashtra	01/2024 (01/2025)	03/2030 (-)	379.3 (379.3)	0	0
107	KOLARPIMPRI EXPANSION OC [2.5 MTY] (<i>Western Coalfields Limited [WCL]</i>) (617278)	Maharashtra	06/2024 (02/2025)	03/2030 (-)	630.37 (630.37)	0	0
108	Master Plan for Jharia and Raniganj Coalfields (<i>Bharat Coking Coal Limited [BCCL]</i>) (400313)	Multi-States (Jharkhand, West Bengal)	08/2009 (08/2009)	08/2019 (12/2028)	2661.73 (2661.73)	788.85	43
109	BINA KAKRI AMALGAMATION EXPANS (<i>Northern Coalfields Limited [NCL]</i>) (400369)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020 (08/2020)	03/2024 (03/2027)	836.42 (836.42)	786.99	89
110	KHADIA EXPANSION [10 TO 16 MTP (<i>Northern Coalfields Limited [NCL]</i>) (615183)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021 (06/2021)	03/2025 (03/2027)	491.67 (491.67)	230.32	45
111	SUBHADRA OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400165)	Odisha	05/2021 (05/2021)	04/2032 (-)	1693.81 (1693.81)	1321.15	42
112	SIARMAL OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400166)	Odisha	02/2021 (02/2021)	03/2029 (-)	5194.95 (5194.95)	3456.05	55
113	BALARAM EXPANSION OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400183)	Odisha	06/2020 (08/2020)	03/2029 (-)	3504.21 (3504.21)	1028.92	52
114	GOPALJI KANIHA OCP [10 TO 30 M (<i>MCL - CIL</i>) (400185)	Odisha	04/2022 (04/2022)	03/2030 (-)	8416.19 (6107.87)	1708.88	17
115	INTEGRATED LAKHANPUR-BELPAHAR- (<i>Mahanadi Coalfields Limited [MCL]</i>) (400187)	Odisha	05/2018 (05/2018)	03/2027 (-)	2434.75 (2434.75)	1813.26	69
116	BHARATPUR RE-ORGANIZATION OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400392)	Odisha	11/2018 (11/2018)	03/2029 (-)	2838.86 (2838.86)	1748.41	47

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
117	BASUNDHARA WEST EXTENSION OPEN (MCL - CIL) (615193)	Odisha	05/2014 (05/2014)	03/2019 (03/2029)	479.15 (479.15)	281.01	64
118	Naini Coal Mine (Singareni Collieries Company Limited [SCCL]) (615857)	Odisha	03/2020 (03/2020)	03/2026 (-)	494.3 (494.3)	491.33	80
119	INTEGRATED KULDA GARJANBAHAL O (Mahanadi Coalfields Limited (MCL)) (616226)	Odisha	04/2023 (04/2023)	03/2033 (-)	3563.5 (3563.5)	540.62	4
120	BHUBANESWARI EXPN OCP 50 MTY (MCL - CIL) (616231)	Odisha	03/2024 (03/2024)	03/2033 (-)	5366.27 (5366.27)	465.31	14
121	HINGULA II OC EXPN PH III 15 M (MCL - CIL) (616232)	Odisha	11/2022 (11/2022)	03/2029 (-)	1561.85 (1561.85)	269.61	23
122	BALABHADRA OCP (MCL - CIL) (616233)	Odisha	04/2023 (04/2023)	03/2030 (-)	978.44 (978.44)	211.37	11
123	Jawahar Khani Open Cast Mine (Singareni Collieries Company Limited [SCCL]) (615818)	Telangana	12/2021 (12/2021)	03/2025 (03/2027)	297.88 (297.88)	46.39	20
124	Kalyanikhani Opencast Project (Singareni Collieries Company Limited [SCCL]) (615858)	Telangana	03/2016 (05/2017)	03/2026 (-)	384.32 (384.32)	281.83	75
125	Kakathiya Khani Opencast - III Project Phase - I (Singareni Collieries Company Limited [SCCL]) (615859)	Telangana	03/2017 (05/2017)	03/2026 (-)	413.84 (413.84)	397.55	79
126	Godavarikhani Coal Mine - 5 (Singareni Collieries Company Limited [SCCL]) (615860)	Telangana	07/2019 (05/2019)	03/2025 (03/2026)	607.04 (607.04)	188.15	71
127	Indaram Opencast Project (Singareni Collieries Company Limited [SCCL]) (615861)	Telangana	08/2017 (12/2022)	03/2025 (03/2026)	424.81 (424.81)	402.64	80
128	Goleti Opencast Mine (Singareni Collieries Company Limited [SCCL]) (615862)	Telangana	07/2021 (08/2021)	03/2026 (-)	345.6 (345.6)	74.59	20
129	Venkatesh Khani Coal Mine (Singareni Collieries Company Limited [SCCL]) (615863)	Telangana	10/2020 (06/2020)	03/2026 (-)	484.5 (484.5)	460.67	95
130	Ramagundam OC-II Extension Project (Singareni Collieries Company Limited [SCCL]) (615864)	Telangana	11/2015 (06/2015)	03/2026 (-)	489.62 (489.62)	405.54	77
131	Kakatiyakhani OC - 2 Project (Singareni Collieries Company Limited [SCCL]) (615865)	Telangana	08/2017 (09/2017)	03/2025 (03/2026)	442.42 (442.42)	205	63
132	MOHANPUR EXPANSION OC -PHASE II (Eastern Coal Fields Limited [ECL]) (400173)	West Bengal	11/2020 (11/2020)	03/2026 (-)	888.99 (888.99)	93	30
133	BONJEMEHARI EXPANSION OCP (Eastern Coal Fields Limited [ECL]) (400180)	West Bengal	08/2021 (08/2021)	03/2026 (03/2026)	570.11 (570.11)	81.95	16
134	NAKRAKONDA KUMARDIH- B OCP (Eastern Coal Fields Limited [ECL]) (400181)	West Bengal	08/2018 (08/2018)	03/2029 (-)	502.68 (502.67)	67.61	26
135	SIDULI [OC & UG] (ECL - CIL) (400182)	West Bengal	05/2018 (05/2018)	03/2027 (-)	535.18 (535.17)	5.05	14
136	TILABONI UG (Eastern Coal Fields Limited [ECL]) (400186)	West Bengal	01/2023 (03/2023)	03/2029 (03/2029)	749.08 (749.08)	52.18	10
137	JHANJRA EXPANSION UG (Eastern Coal Fields Limited [ECL]) (400312)	West Bengal	04/2020 (04/2020)	03/2029 (-)	1210.12 (1210.12)	527.67	41
138	SONEPUR BAZARI EXPANSION OCP [12 MTY] (Eastern Coal Fields Limited [ECL]) (400315)	West Bengal	07/2021 (07/2021)	03/2029 (-)	5365.88 (5365.88)	565.26	17
139	2.0 MTPA BHOJUDIH NLW WASHERY (Ministry of Coal) (611016)	West Bengal	12/2015 (03/2019)	09/2020 (10/2025)	384.57 (384.57)	353.21	97
140	ITAPARA OCP (Eastern Coal Fields Limited [ECL]) (612816)	West Bengal	12/2023 (12/2023)	03/2030 (-)	929.1 (929.1)	67.6	7
141	SHYAMSUNDARPUR UG INCLUDING SA (Eastern Coal Fields Limited [ECL]) (613793)	West Bengal	04/2020 (04/2020)	03/2026 (-)	483.65 (483.65)	59.04	12
142	PARASEA-BELBAID UG PROJECT (Eastern Coal Fields Limited [ECL]) (613794)	West Bengal	01/2023 (01/2023)	03/2028 (-)	389.1 (389.1)	131.42	17
143	PARASCOLE JAMBAD OCP (Eastern Coal Fields Limited [ECL]) (616230)	West Bengal	11/2024 (11/2024)	03/2037 (-)	1193.55 (1193.55)	9.46	0
Total (117)					166806.82	53439.3	
Electricity Generation							
144	50 MW Wind Power Project (NLC India Limited [NLCIL]) (617299)	Gujarat	07/2022 (02/2024)	06/2025 (01/2026)	383.84 (383.84)	303.5	41
145	NLC Talabira Thermal Power Project (NLC India Limited [NLCIL]) (400231)	Odisha	NA (01/2024)	03/2030 (-)	27212.96 (27213)	1953.52	1
146	300 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (612819)	Rajasthan	NA (03/2023)	09/2024 (09/2025)	1813 (1813)	874.14	70

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
147	50 MW Solar PP Minedout Area (NLC India Limited [NLCIL]) (615327)	Tamil Nadu	NA (02/2024)	03/2025 (09/2025)	218.03 (218.03)	161.73	50
148	Ghatampur Thermal Power Plant 3 X 660 MW (NLC India Limited [NLCIL]) (400259)	Uttar Pradesh	NA (08/2016)	11/2020 (10/2025)	17237.8 (21780.9)	20269.54	92
Total (5)					46865.63	23562.43	
Railways							
149	Dharamjaigarh-Korba (Railway) (400203)	Chhattisgarh	05/2018 (03/2017)	12/2026 (08/2026)	1686.22 (1686.22)	347.96	41
150	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] (Ministry of Coal) (400416)	Jharkhand	02/2018 (05/2022)	06/2025 (-)	1799.64 (1799.64)	1293.71	60
Total (2)					3485.86	1641.67	
Ministry of Power							
Coal							
151	Tubed Coal Mine (Damodar Valley Corporation) (400192)	Jharkhand	NA (10/2016)	05/2026 (05/2026)	1581 (1581)	596.94	34
152	Badam Coal Mining project of NTPC (National Thermal Power Corporation [NTPC]) (603293)	Jharkhand	02/2019 (09/2019)	12/2056 (04/2027)	502 (784)	313.88	59
Total (2)					2083	910.82	
Electricity Generation							
153	Dibang Multipurpose Project (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3553.9	16
154	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	49.31	3
155	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	102.79	2
156	Buxar Thermal Power Project [1320 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602579)	Bihar	03/2019 (06/2019)	01/2024 (12/2025)	10439.09 (13756.6)	12148.46	92
157	Lara Super Thermal Power Project Stage-II [2 x 800 MW] (National Thermal Power Corporation [NTPC]) (611930)	Chhattisgarh	08/2023 (08/2023)	06/2028 (-)	15530 (15530)	2480	16
158	Sipat Super Thermal Power Project, Stage-III [1x800 MW] (National Thermal Power Corporation [NTPC]) (617188)	Chhattisgarh	09/2024 (09/2024)	09/2029 (-)	9791 (9791)	0	0
159	Bagodara Solar Power Project (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709747)	Gujarat	03/2021 (05/2021)	12/2025 (12/2025)	339.35 (339.35)	317.59	51
160	Dhaulasidh Hydro Electric Project [66 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602582)	Himachal Pradesh	10/2020 (05/2021)	11/2025 (03/2027)	687.97 (1511.87)	927.3	68
161	Luhri Stage-I Hydro Electric Project [210 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602593)	Himachal Pradesh	11/2020 (11/2020)	01/2026 (10/2029)	1810.56 (3584.53)	1751.6	51
162	382 MW Sunni Dam HEP (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602633)	Himachal Pradesh	NA (04/2018)	03/2027 (-)	2615 (2615)	495.57	0.5
163	Sunni Dam Hydro Electric Project [382 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (611586)	Himachal Pradesh	01/2023 (01/2023)	04/2028 (12/2029)	2614.51 (4540.71)	962.66	29
164	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602525)	Jammu and Kashmir	10/2014 (02/2018)	04/2020 (12/2026)	8112.12 (12728)	7238.73	72
165	Kiru HE Project (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602532)	Jammu and Kashmir	03/2019 (03/2019)	09/2023 (12/2026)	4287.59 (5409)	3157.49	68
166	Rattle HE Project - 850 MW, Rattle Hydroelectric Power Corporation Limited. (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602535)	Jammu and Kashmir	02/2021 (02/2021)	02/2026 (08/2029)	5281.94 (5281.94)	1009.79	24
167	Kwar HE Project (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (605155)	Jammu and Kashmir	05/2022 (05/2022)	11/2026 (03/2028)	4526.12 (4526.12)	1119.59	23
168	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] (National Thermal Power Corporation [NTPC]) (400261)	Jharkhand	11/2017 (11/2017)	03/2023 (11/2026)	17112 (20302)	17475	85
169	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand (Damodar Valley Corporation) (611509)	Jharkhand	NA (11/2024)	03/2029 (-)	14358 (14358)	1131.57	3
170	Subansiri Lower HE Project [2000 MW] (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (09/2003)	09/2010 (05/2026)	6285.33 (26075.5)	24880.95	96
171	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion (National Thermal Power Corporation [NTPC]) (602961)	Odisha	08/2022 (09/2022)	05/2027 (03/2028)	11843.75 (12543)	4161.68	32
172	BIKANER SOLAR POWER PROJECT (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709748)	Rajasthan	10/2021 (05/2022)	04/2024 (12/2025)	5491.89 (5491.89)	4805.16	84
173	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602181)	Sikkim	03/2019 (03/2019)	03/2024 (12/2027)	5748.04 (5748.04)	4576.93	69

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
174	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] -A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (605156)	Sikkim	03/2021 (03/2021)	05/2024 (12/2025)	938.29 (1828.11)	1584.13	91
175	Khurja super Thermal Power Plant [2X660 MW] (THDC India Limited) (602194)	Uttar Pradesh	03/2019 (08/2019)	02/2024 (09/2025)	11089.42 (13276.2)	12772.21	97
176	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] (National Thermal Power Corporation [NTPC]) (612142)	Uttar Pradesh	03/2024 (03/2024)	02/2030 (-)	17195 (17195)	1739	9
177	Tapovan-Vishnugad HEP [4x130 MW] (National Thermal Power Corporation [NTPC]) (602185)	Uttarakhand	NA (11/2006)	03/2013 (04/2029)	2978 (10907.3)	7195.58	77
178	Tehri Pumped Storage Plant Project [4x250 MW] (THDC India Limited) (602193)	Uttarakhand	07/2006 (06/2011)	06/2022 (11/2025)	4825.6 (8339)	8064.9	98
179	Vishnugad Pipalkoti Hydro Electric Project [444 MW] (THDC India Limited) (602195)	Uttarakhand	08/2008 (01/2014)	12/2022 (03/2027)	3860.35 (6823.72)	5101.06	72
180	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal (Damodar Valley Corporation) (400062)	West Bengal	NA (02/2025)	06/2029 (-)	17673 (17673)	1192.71	1
181	Rammam-III HEPP [3x40 MW] (National Thermal Power Corporation [NTPC]) (602184)	West Bengal	09/2024 (09/2014)	09/2019 (03/2029)	1381.84 (1381.84)	1281.85	47
182	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 (Damodar Valley Corporation) (602538)	West Bengal	NA (02/2021)	01/2024 (12/2025)	1037 (1106)	1092.27	92
Total (30)					223418.07	132369.78	
Transmission & Distribution							
183	Transmission Scheme for Solar Energy Zone in Ananthpuram 2500MW and Kurnool 1000MW (Power Grid Corporation of India Limited [POWERGRID]) (611967)	Andhra Pradesh	09/2023 (09/2023)	09/2025 (04/2026)	1248.69 (1248.69)	860.97	82
184	Augmentation of 1x1500 MVA 3rd 765/400 kV transformation capacity at Kurnool New Substation (Power Grid Corporation of India Limited [POWERGRID]) (612856)	Andhra Pradesh	05/2023 (12/2023)	09/2025 (11/2025)	163.61 (163.61)	60.53	42
185	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617183)	Andhra Pradesh	03/2025 (03/2025)	12/2027 (-)	2886 (2886)	117.86	0
186	Western Region Expansion Scheme-XXV (Power Grid Corporation of India Limited [POWERGRID]) (611737)	Chhattisgarh	02/2023 (02/2023)	11/2023 (12/2025)	385.84 (385.84)	378.17	97
187	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan 8.1 GW under Phase II- Part- G1 (Power Grid Corporation of India Limited [POWERGRID]) (608301)	Delhi	02/2022 (02/2022)	09/2023 (11/2025)	359.47 (359.47)	330.91	93
188	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part B (Power Grid Corporation of India Limited [POWERGRID]) (611656)	Gujarat	03/2023 (03/2023)	03/2025 (10/2025)	1167.55 (1167)	1050.41	93
189	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part C (Power Grid Corporation of India Limited [POWERGRID]) (611657)	Gujarat	03/2023 (03/2023)	03/2025 (11/2025)	2820.99 (2820.99)	2570.25	84
190	Establishment of Khavda Pooling Station-2 KPS2 in Khavda RE Park KPS2 TRANSMISSION SYSTEM LIMITED (Power Grid Corporation of India Limited [POWERGRID]) (611660)	Gujarat	03/2023 (03/2023)	12/2024 (10/2025)	966.79 (966.79)	904.52	95
191	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (612139)	Gujarat	12/2023 (12/2023)	12/2025 (06/2026)	3751.82 (3751.82)	1575.72	22
192	Transmission System for Evacuation of Power from potential Renewable Energy zone in Khavda Area of Gujarat under Phase IV [7 GW] Part E3 (Power Grid Corporation of India Limited [POWERGRID]) (612151)	Gujarat	07/2023 (07/2023)	07/2025 (12/2025)	334 (334)	73.48	30
193	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (612855)	Gujarat	05/2024 (05/2024)	05/2026 (02/2026)	679 (679)	97.23	19
194	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615342)	Gujarat	10/2024 (10/2024)	07/2026 (-)	329 (329)	10.07	1
195	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] (Power Grid Corporation of India Limited [POWERGRID]) (615343)	Gujarat	11/2024 (11/2024)	11/2026 (-)	501 (501)	6.01	1
196	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345)	Gujarat	10/2024 (10/2024)	10/2026 (-)	4766 (4766)	564.77	7
197	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069)	Gujarat	02/2025 (02/2025)	02/2027 (-)	466 (466)	13.99	1



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
198	Augmentation of Banaskantha [Raghanesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182)	Gujarat	03/2025 (03/2025)	03/2027 (-)	172 (172)	7.27	3
199	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272)	Haryana	06/2024 (06/2024)	12/2026 (-)	370 (370)	3.7	1
200	Transmission system for evacuation of Power from Pakaldul HEP in Chenab Valley HEPs - LTA System (Power Grid Corporation of India Limited [POWERGRID]) (608302)	Jammu and Kashmir	02/2022 (02/2022)	04/2025 (09/2025)	318.12 (318.12)	287.31	99
201	Transmission Scheme for evacuation of Power from Rattle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179)	Jammu and Kashmir	07/2024 (07/2024)	07/2026 (-)	218.6 (218.6)	1.01	0
202	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140)	Karnataka	12/2023 (12/2023)	12/2025 (03/2026)	2889.39 (2889.39)	1332.21	46
203	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672)	Karnataka	01/2025 (01/2025)	06/2027 (-)	1354 (1354)	17.73	0
204	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068)	Karnataka	02/2025 (02/2025)	06/2027 (-)	288 (288)	6.79	0
205	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184)	Karnataka	03/2025 (03/2025)	09/2027 (-)	3453 (3453)	33.14	0
206	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344)	Madhya Pradesh	10/2024 (10/2024)	10/2026 (-)	3674 (3674)	495.18	14
207	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346)	Madhya Pradesh	08/2024 (08/2024)	08/2026 (-)	2708 (2708)	812.4	35
208	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279)	Madhya Pradesh	06/2025 (06/2025)	12/2027 (-)	558 (558)	16.74	0
209	Transmission System for Evacuation of power from Potential RE Zone in Khavda Area of Gujarat under phase IV 7GW-Part E4 (Power Grid Corporation of India Limited [POWERGRID]) (611966)	Maharashtra	11/2023 (11/2023)	07/2025 (12/2025)	224.41 (224.41)	24.64	10
210	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185)	Multi-States (Andhra Pradesh, Karnataka)	03/2025 (03/2025)	03/2027 (-)	5550 (5550)	281	0
211	Transmission System for Kurnool Wind Energy Zone/ Solar Energy Zone Part-A and Part-B (Power Grid Corporation of India Limited [POWERGRID]) (900808)	Multi-States (Andhra Pradesh, Telangana)	11/2022 (03/2023)	11/2024 (12/2025)	3546.94 (3546.94)	3192.25	95
212	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	03/2021 (01/2016)	12/2018 (03/2027)	4754.42 (9129.32)	7462.2	81
213	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (12/2025)	5111.33 (6700)	5277.24	96
214	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271)	Multi-States (Bihar, Odisha, West Bengal)	09/2024 (09/2024)	03/2026 (-)	342.69 (342.69)	0.6	0
215	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270)	Multi-States (Bihar, West Bengal)	11/2024 (11/2024)	05/2026 (-)	408.94 (408.94)	0.3	0
216	Transmission Network Expansion in Gujarat to increase its ATC from ISTS Part B (Power Grid Corporation of India Limited [POWERGRID]) (400005)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	01/2022 (07/2022)	06/2023 (12/2025)	4546.26 (4546.26)	4172.96	93
217	Transmission System Strengthening Scheme for evacuation of power from SEZ in Rajasthan 8.1 GW under Phase II Part G (Power Grid Corporation of India Limited [POWERGRID]) (608922)	Multi-States (Delhi, Haryana, Rajasthan)	05/2022 (05/2022)	11/2023 (11/2025)	1666 (2218)	2129.28	95
218	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735)	Multi-States (Delhi, Rajasthan)	12/2022 (12/2022)	03/2025 (04/2026)	331 (331)	82.72	29
219	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132)	Multi-States (Delhi, Rajasthan)	02/2024 (02/2024)	08/2025 (05/2026)	2000 (2000)	1380.2	62

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
220	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347)	Multi-States (Gujarat, Maharashtra)	11/2024 (11/2024)	05/2029 (-)	24819 (24819)	1796.14	1
221	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024 (11/2024)	11/2026 (-)	5969 (5969)	218.47	5
222	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Siwani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340)	Multi-States (Haryana, Rajasthan)	11/2024 (11/2024)	11/2026 (-)	5357 (5357)	267.85	9
223	Transmission System for Strengthening of Srinagar-Leh Tr. System (Power Grid Corporation of India Limited [POWERGRID]) (606781)	Multi-States (Jammu and Kashmir, Ladakh)	03/2022 (03/2022)	12/2024 (10/2025)	288.71 (288.71)	207.8	75
224	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138)	Multi-States (Karnataka, Telangana)	02/2024 (02/2024)	02/2026 (-)	2147.62 (2147.62)	1144.89	61
225	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (-)	2227 (2227)	622.89	20
226	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (-)	3251 (3251)	780.24	18
227	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [Rajasthan V Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025 (03/2025)	03/2027 (-)	5028 (5028)	203.2	1
228	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023 (12/2023)	12/2025 (06/2026)	2056 (2056)	1356.96	58
229	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024 (12/2024)	12/2026 (-)	5846 (5846)	293.47	4
230	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan[8.1 GW] under phase-II- Part E (Power Grid Corporation of India Limited [POWERGRID]) (611659)	Rajasthan	03/2023 (03/2023)	09/2024 (10/2025)	1433.28 (1433)	1359.63	95
231	Transmission System for Evacuation of Power from REZ in Rajasthan 20GW under Phase III- Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (611947)	Rajasthan	11/2023 (11/2023)	06/2025 (12/2025)	428.3 (428.3)	179.89	51
232	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part H (Power Grid Corporation of India Limited [POWERGRID]) (611948)	Rajasthan	10/2023 (10/2023)	04/2025 (12/2025)	2211.29 (2211.29)	1817.46	80
233	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949)	Rajasthan	10/2023 (10/2023)	04/2025 (10/2025)	1796.02 (1796.02)	1247.87	83
234	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part B1 (Power Grid Corporation of India Limited [POWERGRID]) (611950)	Rajasthan	09/2023 (09/2023)	04/2025 (12/2025)	2190.54 (2190.54)	1870.72	83
235	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part E1 (Power Grid Corporation of India Limited [POWERGRID]) (611951)	Rajasthan	12/2021 (08/2023)	02/2025 (09/2025)	688.74 (688.74)	587.42	96
236	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134)	Rajasthan	12/2023 (12/2023)	12/2025 (03/2026)	2998.34 (2998.34)	1703.11	51
237	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332)	Rajasthan	08/2024 (08/2024)	08/2026 (-)	3279 (3279)	688.59	21
238	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615335)	Rajasthan	08/2024 (08/2024)	08/2026 (-)	1382 (1382)	41.46	4
239	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615337)	Rajasthan	08/2024 (08/2024)	02/2026 (-)	369 (369)	58.26	16
240	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615338)	Rajasthan	11/2024 (11/2024)	11/2026 (-)	2735 (2735)	82.05	8
241	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617181)	Rajasthan	03/2025 (03/2025)	12/2026 (-)	404 (404)	8.04	0

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
242	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Tarnsmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616671)	Tamil Nadu	01/2025 (01/2025)	12/2026 (12/2026)	548 (548)	14.68	6
243	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex (Power Grid Corporation of India Limited [POWERGRID]) (617269)	Uttar Pradesh	12/2024 (12/2024)	06/2026 (-)	212.81 (212.81)	0.2	0
Total (61)					142976.51	52183.05	
Ministry of Housing & Urban Affairs							
Construction							
244	C/o 184 MS Flats for Hon'ble MPs at BKS Marg, New Delhi (Central Public Works Department [CPWD]) (617282)	Delhi	01/2022 (05/2022)	05/2025 (08/2025)	646.53 (646.52)	533.12	99
Total (1)					646.53	533.12	
Inland Waterways							
245	Chennai Metro Rail Phase-II Development Project (Chennai Metro Rail Limited [CMRL]) (702668)	Tamil Nadu	10/2024 (11/2020)	08/2029 (-)	63246 (63246)	26410.15	45
Total (1)					63246	26410.15	
Real Estate							
246	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System (ministry of housing and urban affairs) (707229)	Andaman & Nicobar	07/2021 (11/2021)	05/2023 (-)	209.88 (209.88)	0	70
247	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi (National Buildings Construction Corporation [NBCC]) (400188)	Delhi	07/2016 (05/2018)	12/2025 (12/2025)	32850 (32850)	0	0
248	Rehabilitation in Junavadaj Area Smart City Project (ministry of housing and urban affairs) (701719)	Gujarat	NA (06/2016)	07/2022 (-)	539 (539)	39.63	50
249	Green Building Development Project (ministry of housing and urban affairs) (701766)	Uttarakhand	NA (08/2019)	11/2023 (-)	150.97 (150.97)	18.95	31
Total (4)					33749.85	58.58	
Urban Public Transport							
250	Patna Metro Rail Project (Patna Metro Rail Corporation Ltd. [PMRCL]) (702627)	Bihar	02/2019 (02/2019)	02/2024 (06/2027)	13365.77 (13365.8)	4039.77	40.07
251	Delhi Metro Rail Phase-IV [2 Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (617207)	Delhi	03/2024 (03/2024)	03/2029 (-)	8399.81 (8399.81)	5.58	0
252	DMRTS Phase - IV [3 Priority Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (702632)	Delhi	NA (07/2019)	03/2025 (03/2026)	24948.65 (24948.7)	15785.39	69
253	Surat Metro Rail Project (Gujarat Metro Rail Corporation Limited [GMRCL]) (702630)	Gujarat	03/2019 (04/2019)	03/2024 (06/2026)	12020.32 (12020.3)	7595.47	70
254	Ahmedabad Metro Rail Project, Phase-II (Gujarat Metro Rail Corporation Limited [GMRCL]) (702631)	Gujarat	03/2019 (03/2019)	03/2024 (12/2025)	5384.17 (5384.17)	4180.43	88
255	Ahmedabad Metro Rail Project [Phase-I] (Gujarat Metro Rail Corporation Limited [GMRCL]) (702639)	Gujarat	11/2014 (02/2015)	03/2018 (10/2025)	10773 (12924.5)	12174.41	99
256	Construction of Bangalore Metro Rail Project Phase 2. (Bengaluru Metro Rail) (702635)	Karnataka	02/2014 (02/2016)	03/2021 (09/2026)	26405.14 (30695.1)	29477.97	94
257	Construction Bangalore Metro Rail Project Phase-2A & 2B (Bengaluru Metro Rail) (702665)	Karnataka	06/2021 (01/2019)	06/2026 (06/2026)	14788.1 (14788.1)	8424.54	53
258	Kochi Metro Rail Phase 2 Development Project (CSPCC Projects) (702664)	Kerala	11/2022 (11/2022)	11/2026 (11/2026)	1957.05 (1957.05)	329.94	12
259	Bhopal Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702625)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (06/2028)	6941.4 (6941.4)	3164.15	43
260	Indore Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702626)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (12/2028)	7500.8 (7500.8)	3931.4	55
261	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617225)	Maharashtra	10/2023 (10/2023)	01/2027 (-)	910.18 (910.18)	119.88	22
262	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617226)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	2954.53 (2954.53)	19.61	3
263	New Suburba Station Development Project (ministry of housing and urban affairs) (701745)	Maharashtra	NA (03/2019)	07/2022 (-)	262.76 (262.76)	17.62	6
264	Kalyan Station Precinct Imporvement Project (ministry of housing and urban affairs) (701991)	Maharashtra	NA (07/2020)	07/2023 (-)	600 (600)	272.42	70
265	Mumbai Metro Line 3 (Mumbai Metro Rail Corporation Limited [MMRC]) (702637)	Maharashtra	07/2013 (06/2016)	03/2023 (08/2025)	23136 (37276)	27519.07	91.9
266	Nagpur Metro Rail Phase II Development Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (702658)	Maharashtra	12/2022 (12/2022)	12/2027 (-)	6708 (6708)	1045.32	25

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
267	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] <i>(Delhi Metro Rail Corporation Limited [DMRC])</i> (617206)	Multi-States (Delhi, Haryana)	01/2025 (01/2025)	01/2029 (-)	6230.99 (6230.99)	0.29	0
268	Delhi-Ghaziabad-Meerut Regional Rapid Transit System [RRTS] corridor <i>(National Capital Region Transport Corporation [NCRTC])</i> (702633)	Multi-States (Delhi, Uttar Pradesh)	03/2019 (03/2019)	06/2025 (08/2025)	30274 (30274)	26325.73	95
269	Kanpur Metro Rail Project <i>(Uttar Pradesh metro rail corporation [UPMRC])</i> (702628)	Uttar Pradesh	05/2019 (11/2019)	05/2024 (03/2027)	11076.48 (11076.5)	9083.27	73
270	Agra Metro Rail Project <i>(Uttar Pradesh metro rail corporation [UPMRC])</i> (702629)	Uttar Pradesh	05/2019 (12/2020)	05/2024 (06/2027)	8379.62 (8379.62)	6057.62	62
Total (21)					223016.77	159569.88	
Waste & Water							
271	ESR - 8 nos., distribution system - 216 Km, new house service connections - 38760 nos. upgrading of feeder mains, pumping station etc. - Phase II <i>(Ministry of Housing & Urban Affairs)</i> (702674)	Andhra Pradesh	NA (07/2018)	03/2023 (12/2025)	172.22 (172.22)	622.02	82
272	Dibrugarh Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702682)	Assam	NA (01/2020)	03/2023 (12/2025)	186.8 (186.8)	1291.55	98
273	Muzaffarpur Storm Water Drainage Phase-I Project <i>(Ministry of Housing & Urban Affairs)</i> (702699)	Bihar	NA (02/2019)	10/2023 (03/2024)	158.78 (158.78)	48.61	51
274	Storm water drainag Development Project <i>(ministry of housing and urban affairs)</i> (702355)	Dadra & Nagar Haveli and Daman & Diu	NA (12/2021)	03/2024 (-)	210 (210)	0	20
275	Upgradation of Sewerage system in Gandhinagar City <i>(ministry of housing and urban affairs)</i> (707267)	Gujarat	NA (03/2021)	06/2023 (-)	200 (200)	100	10
276	Sewerage Management Scheme Part-3 Implementation <i>(Ministry of Housing & Urban Affairs)</i> (702734)	Haryana	NA (11/2017)	09/2023 (03/2026)	278.01 (278.01)	1548.15	88
277	Sewerage Management Scheme Part-3 Implementation <i>(Ministry of Housing & Urban Affairs)</i> (702735)	Haryana	NA (10/2018)	03/2023 (12/2025)	213.19 (213.19)	1069.74	91
278	Dhanbad Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702741)	Jharkhand	NA (12/2018)	03/2023 (03/2026)	216.55 (216.55)	696.48	72
279	SAAP-3 Water Supply Infrastructure SAAP-3 Project <i>(Ministry of Housing & Urban Affairs)</i> (702742)	Jharkhand	NA (12/2018)	10/2023 (03/2026)	159.31 (159.31)	612.5	65
280	Augmentation and Strenghthning of Urban Water Supply Phase 1 - SAAP 3 <i>(Ministry of Housing & Urban Affairs)</i> (702746)	Jharkhand	NA (12/2018)	03/2023 (03/2026)	278.28 (278.28)	1223.5	78
281	Belgavi Improvement in Sewerage System Project <i>(Ministry of Housing & Urban Affairs)</i> (702760)	Karnataka	NA (10/2016)	07/2023 (12/2025)	162.73 (162.73)	562.71	80
282	24/7 water supply under AMRUT for Davanagere <i>(Ministry of Housing & Urban Affairs)</i> (702764)	Karnataka	NA (01/2018)	03/2023 (12/2025)	174.96 (174.96)	715.56	65
283	Indore Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702793)	Madhya Pradesh	NA (11/2017)	03/2023 (12/2025)	287.17 (287.17)	1766	99
284	Jabalpur Sewerage Management and Treatment Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702798)	Madhya Pradesh	NA (12/2017)	03/2023 (12/2025)	362.31 (362.31)	2264.18	93
285	Satna Sewerage Management and Treatment Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702808)	Madhya Pradesh	NA (12/2016)	03/2024 (12/2025)	191.56 (191.56)	501.71	86
286	Singrauli Sewerage Management and Treatment Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702810)	Madhya Pradesh	NA (11/2017)	03/2023 (12/2025)	402.01 (402.01)	2424.71	90
287	Kalyan-Dombivali Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702833)	Maharashtra	NA (09/2019)	10/2023 (12/2025)	194.2 (194.2)	375.32	70
288	Mira-Bhayandar Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702840)	Maharashtra	NA (08/2018)	03/2023 (12/2025)	204.55 (204.55)	581.09	99
289	Nagpur Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702842)	Maharashtra	NA (08/2018)	03/2023 (09/2025)	273.78 (273.78)	266.11	99
290	Pune Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702851)	Maharashtra	NA (07/2017)	03/2023 (10/2025)	235.95 (235.95)	614.06	92
291	Solapur Sewerage Management Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702854)	Maharashtra	NA (04/2018)	03/2023 (12/2025)	180.24 (180.24)	476.83	91
292	Jalandhar Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (703021)	Punjab	NA (08/2020)	08/2023 (03/2026)	258.53 (258.53)	161.02	58
293	Patiala Water Supply Infrastructure Part-2 Project <i>(Ministry of Housing & Urban Affairs)</i> (703057)	Punjab	NA (08/2020)	10/2023 (12/2025)	287 (287)	451.94	74
294	Jaunpur Sewerage Management Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702948)	Uttar Pradesh	NA (08/2019)	06/2023 (12/2025)	235.73 (235.73)	166	87
295	Jhansi Water Supply Infrastructure Phase-II Project <i>(Ministry of Housing & Urban Affairs)</i> (702949)	Uttar Pradesh	NA (06/2019)	07/2023 (09/2025)	561.74 (561.74)	523.15	100
Total (25)					6085.6	19062.94	

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Mines							
Construction							
296	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata (Central Public Works Department (CPWD)) (617280)	West Bengal	04/2019 (02/2020)	08/2026 (-)	255.37 (255.37)	79.34	79
Total (1)					255.37	79.34	
Metals & Mining							
297	Rakha Underground Mining Project (Hindustan Copper Limited [HCL]) (611798)	Jharkhand	12/2022 (03/2024)	03/2033 (-)	2705 (2705)	0	0
298	Surda Underground Copper Mining Project (Hindustan Copper Limited [HCL]) (611800)	Jharkhand	02/2022 (03/2024)	03/2028 (-)	665.02 (665.02)	16.57	1
299	Expansion of Malanjhand Copper Project (Hindustan Copper Limited [HCL]) (400426)	Madhya Pradesh	09/2011 (04/2015)	04/2020 (04/2026)	1856.36 (1856.36)	935.32	80
300	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonne Per Annum (National Aluminium Company Limited [NALCO]) (400141)	Odisha	04/2017 (04/2017)	12/2022 (09/2025)	4103 (5677.4)	3984.99	76
301	Pottangi Bauxite Mines Project (National Aluminium Company Limited [NALCO]) (400299)	Odisha	05/2018 (05/2018)	03/2025 (05/2026)	1381 (1960.77)	650.04	51
302	UTKAL D AND E COAL BLOCK (National Aluminium Company Limited [NALCO]) (709829)	Odisha	NA (02/2016)	03/2025 (-)	1021.97 (1021.97)	0	0
303	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (Ministry of Mines) (709830)	Odisha	NA (04/2017)	11/2026 (-)	355 (581)	0	0
304	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (National Aluminium Company Limited [NALCO]) (709831)	Odisha	11/2017 (11/2019)	05/2025 (06/2026)	483 (483)	402.67	90
305	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (National Aluminium Company Limited [NALCO]) (709832)	Tamil Nadu	09/2017 (12/2017)	03/2025 (03/2026)	166 (166)	135	65
Total (9)					12736.35	6124.59	
Department of Higher Education							
Education							
306	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008)	Andhra Pradesh	NA (12/2023)	06/2027 (-)	305 (305)	83.33	24
307	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	NA (03/2013)	08/2026 (-)	592.61 (592.61)	549.96	75
308	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (08/2025)	153.71 (153.71)	54.05	95
309	Additional Campus of NITPatna (NIT Patna) (606013)	Bihar	07/2022 (08/2022)	07/2024 (01/2026)	499.21 (499.21)	425.47	91
310	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis (Ministry of Education) (612851)	Delhi	NA (11/2022)	09/2025 (-)	333.49 (333.49)	277.75	91
311	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886)	Delhi	NA (01/2025)	10/2026 (-)	373 (373)	23.23	15
312	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Gujarat) (612916)	Gujarat	NA (02/2021)	03/2025 (03/2026)	490.63 (490.63)	301.44	76
313	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099)	Himachal Pradesh	09/2018 (08/2020)	10/2023 (02/2026)	392.51 (454.78)	323.64	92
314	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128)	Himachal Pradesh	NA (03/2024)	03/2026 (03/2026)	166.66 (166.66)	72.09	65
315	Construction of Permanent Campus of Central University of Himachal Pradesh at Dehra, District - Kangra, [H.P.] on Engineering. Procurement and Construction [EPC Mode 1] Basis. (Central University, Himachal Pradesh) (612894)	Himachal Pradesh	03/2021 (08/2022)	11/2024 (11/2025)	251.98 (300.45)	183.36	78
316	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098)	Jammu and Kashmir	03/2019 (10/2020)	06/2023 (09/2025)	424.93 (500.91)	484.52	96
317	Additional Infrastructure at IISc Bangalore-RCC Monolithic for Men Hostel S14, Women Hostel S11, Postdoctoral Hostel S12 2 Block, International Hostel S 12, D&E Block S 12 2 Block FR. (IISc Bangalore) (610940)	Karnataka	08/2021 (08/2021)	03/2024 (09/2025)	420.41 (420.41)	360.72	99
318	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431)	Kerala	07/2017 (03/2020)	06/2022 (11/2026)	1006.45 (1217.4)	623.6	71



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
319	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] (Indian Institute of Technology, Indore) (611957)	Madhya Pradesh	NA (11/2023)	12/2026 (-)	496.28 (496.28)	143.95	35
320	Hostel 4 -Earlier Known as Hostel 20 (Indian Institute of Technology, Bombay) (612135)	Maharashtra	NA (05/2022)	09/2025 (-)	182.33 (182.33)	132.44	95
321	Academic Block 1 & 2 (Indian Institute of Technology, Bombay) (612203)	Maharashtra	NA (01/2023)	07/2026 (03/2027)	68 (263.93)	22.26	18
322	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	03/2020 (09/2014)	03/2022 (07/2025)	494.52 (494.52)	413.57	86
323	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (Ministry of Education) (612876)	Mizoram	03/2020 (05/2014)	12/2029 (12/2029)	474.23 (474.23)	167.55	4
324	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	NA (09/2012)	12/2025 (-)	275.63 (275.63)	260.1	95
325	IISER BERHAMPUR (Indian Institutes of Science Education and Research, Behrampur) (610315)	Odisha	10/2018 (09/2019)	03/2021 (12/2025)	1229.32 (773.76)	837.04	97
326	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] (National Institute of Technology, Puducherry) (612877)	Puducherry	03/2020 (07/2013)	12/2024 (08/2025)	618.34 (544.34)	509.55	94
327	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I (Indian intitue of Management, Amritsar) (605292)	Punjab	10/2019 (07/2020)	06/2023 (12/2025)	348.31 (348.31)	290.39	91
328	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment (Central University of Punjab) (617221)	Punjab	08/2024 (04/2025)	10/2027 (-)	210.99 (210.99)	0	0
329	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (09/2025)	314.06 (314.06)	238.22	82
330	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (Ministry of Education) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	121.56	9
331	Construction of Precast housing and hostels at IIT Hyderabad (Indian Institute of Technology, Hyderabad) (609996)	Telangana	NA (11/2022)	10/2024 (01/2026)	262 (262)	177.09	73
332	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] (Banaras Hindu University) (606479)	Uttar Pradesh	NA (06/2020)	09/2022 (03/2026)	246 (246)	193.38	95
333	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal (National Institute of Technology Uttarakhand) (611963)	Uttarakhand	06/2020 (04/2024)	09/2027 (-)	650.85 (650.85)	195.52	24
334	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur (Indian Institute of Technology, Kharagpur) (609019)	West Bengal	06/2018 (04/2019)	03/2023 (03/2026)	500 (442)	383.6	87
335	IoE Projects [Civil Works], IIT Kharagpur (Indian Institute of Technology, Kharagpur) (609041)	West Bengal	NA (04/2019)	03/2023 (12/2026)	287.2 (287.2)	310	86
Total (30)					12754.41	8159.38	
Ministry of Petroleum & Natural Gas							
Energy Storage							
336	Construction of Aviation Fuel farm Facilities at Bhogapuram Airport (Ministry of Petroleum & Natural Gas) (616235)	Andhra Pradesh	NA (08/2024)	03/2026 (03/2026)	240 (240)	38.82	59
337	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	NA (03/2023)	07/2027 (07/2027)	156.36 (156.36)	54.15	46
338	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	NA (03/2023)	07/2027 (07/2027)	384.04 (384.04)	120.4	52
339	Setting up a common user Petroleum Terminal at Jammu, J&K for resitement of existing PSU OMC's Depots from Jammu City (Bharat Petroleum Corporation Limited [BPCL]) (400235)	Jammu and Kashmir	NA (04/2023)	03/2025 (01/2026)	676.89 (676.89)	526.1	79
340	Andheri Residential Towers, Mumbai (Ministry of Petroleum & Natural Gas) (604833)	Maharashtra	NA (06/2017)	05/2025 (06/2026)	281.35 (389.67)	230.76	50
341	Srikakulam Angul Gas Pipeline Project (Ministry of Petroleum & Natural Gas) (701343)	Multi-States (Andhra Pradesh, Odisha)	NA (09/2019)	07/2022 (12/2025)	2658.34 (2810)	2203.98	95
342	Rajasthan Refinery Project (MinistryofPetroleumNaturalGas) (701263)	Multi-States (Arunachal Pradesh, Gujarat, Rajasthan)	NA (10/2017)	10/2022 (03/2026)	43129 (79459)	60295.14	88
343	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Multi-States (Assam, Bihar, Jharkhand, Odisha, West Bengal)	NA (01/2019)	07/2024 (09/2025)	10228 (11407)	9766.72	87
344	New Mundra Panipat Crude Oil Pipeline (Ministry of Petroleum & Natural Gas) (400078)	Multi-States (Gujarat, Haryana, Rajasthan)	NA (12/2021)	12/2024 (12/2025)	9028 (9028)	7136.41	85

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
345	Kandla Gorakhpur LPG Pipeline (Ministry of Petroleum & Natural Gas) (400012)	Multi-States (Gujarat, Madhya Pradesh, Uttar Pradesh)	NA (12/2018)	12/2021 (12/2025)	10088 (10088)	7672.23	92
346	Multi Product Pipeline from Irugur to Devangonchi (Department of Water Resources, River Development & GR) (400301)	Multi-States (Karnataka, Tamil Nadu)	NA (11/2012)	02/2017 (10/2025)	678 (1732)	713.86	69
347	Petrochemical evacuation marketing terminal at Barmer, Rajasthan (Hindustan Petroleum Corporation Limited [HPCL]) (709759)	Rajasthan	NA (12/2023)	12/2026 (12/2026)	461.05 (461.05)	116.48	54
348	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] (Ministry of Petroleum & Natural Gas) (400043)	Tamil Nadu	NA (01/2022)	05/2026 (05/2026)	829 (829)	301.71	63
349	Grass root POL Terminal at Vallur, Chennai (Indian Oil Corporation Limited [IOCL]) (400077)	Tamil Nadu	NA (01/2022)	12/2024 (03/2026)	827 (887.71)	626.01	88
350	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	NA (06/2022)	09/2025 (06/2026)	656 (656)	478.11	86
351	Grass-root Terminal at Mirzapur, Uttar Pradesh (Ministry of Petroleum & Natural Gas) (604852)	Uttar Pradesh	NA (09/2022)	11/2026 (11/2026)	980.45 (980.45)	216.66	52
Total (16)					81301.48	90497.54	
Oil & Gas							
352	KG-DWN-98/2 Cluster - II Development Project - NELP Block (Oil and Natural Gas Corporation Limited [ONGC]) (400120)	Andhra Pradesh	NA (03/2016)	06/2020 (06/2026)	34012 (34012)	33238.47	96
353	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery (Hindustan Petroleum Corporation Limited) (709752)	Andhra Pradesh	NA (09/2021)	06/2024 (03/2026)	160 (220)	80.29	69
354	HP Trijet Unit in Visakh Refinery (Hindustan Petroleum Corporation Limited) (709761)	Andhra Pradesh	NA (07/2024)	07/2027 (07/2027)	193 (193)	0.43	23
355	City Gas Distribution Project at Kurnool, Guntur & Prakasam Districts (Ministry of Petroleum & Natural Gas) (709766)	Andhra Pradesh	NA (03/2022)	03/2030 (03/2030)	1420 (1420)	165.65	6
356	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	NA (07/2020)	07/2024 (12/2025)	12366 (22494)	16764.09	76
357	Assam Bio Refinery, ABRPL (Ministry of Petroleum & Natural Gas) (604792)	Assam	NA (02/2018)	09/2021 (09/2025)	1750 (4930)	4710	99
358	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	NA (01/2018)	02/2020 (12/2025)	682.9 (726.93)	489.3	94
359	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	NA (05/2021)	10/2023 (05/2026)	412.3 (577)	430.83	85
360	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	NA (12/2020)	03/2024 (12/2025)	430.76 (430.76)	327.27	85
361	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Ministry of Petroleum & Natural Gas) (709776)	Assam	NA (04/2022)	09/2026 (09/2026)	277 (323.09)	185.18	68
362	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Ministry of Petroleum & Natural Gas) (709779)	Assam	NA (06/2022)	03/2026 (03/2026)	768 (740)	107.72	39
363	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	NA (01/2023)	04/2026 (04/2026)	344.99 (344.99)	211.05	47
364	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	NA (09/2023)	05/2026 (05/2026)	198.7 (198.7)	36.8	30
365	DCU Revamp Project (NRL) (709864)	Assam	NA (08/2021)	07/2024 (10/2025)	370 (370)	253.17	60
366	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	NA (04/2023)	12/2024 (10/2025)	293.5 (293.5)	97.22	94
367	City Gas Distribution Project at Khagaria, Saharsa and Madhepura (Ministry of Petroleum & Natural Gas) (617303)	Bihar	NA (03/2019)	03/2030 (03/2030)	163 (163)	96.07	40
368	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar (Ministry of Petroleum & Natural Gas) (617304)	Bihar	NA (10/2023)	03/2027 (03/2027)	340.15 (340.15)	91.32	26
369	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA (Ministry of Petroleum & Natural Gas) (701324)	Bihar	NA (01/2020)	04/2023 (08/2026)	14810 (16724)	11880.66	87
370	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery (Ministry of Petroleum & Natural Gas) (709777)	Bihar	NA (01/2022)	04/2025 (10/2026)	389.35 (340)	50.48	40
371	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts (Bharat Petroleum Corporation Limited [BPCL]) (709792)	Bihar	NA (12/2022)	03/2030 (03/2030)	3638 (3638)	407.18	29

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
372	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts (Bharat Petroleum Corporation Limited [BPCL]) (709793)	Bihar	NA (12/2022)	06/2030 (06/2030)	3919 (3919)	400.92	18
373	Redevelopment of Sobhasan Complex (Oil and Natural Gas Corporation Limited [ONGC]) (400087)	Gujarat	NA (08/2021)	02/2026 (02/2026)	885.63 (1286.67)	789.49	78
374	Redevelopment of Santhal Field [Onshore-Mehsana Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (400167)	Gujarat	NA (02/2017)	03/2026 (03/2026)	1162.56 (1162.56)	1157	94
375	Redevelopment of Linch Field (Oil and Natural Gas Corporation Limited [ONGC]) (400169)	Gujarat	NA (04/2021)	03/2025 (10/2025)	631.03 (860.04)	505.15	79
376	Petrochemical and Lube Integration Project at Gujarat Refinery (Ministry of Petroleum & Natural Gas) (701329)	Gujarat	NA (09/2020)	08/2024 (12/2025)	18936 (17825)	12327.91	83
377	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery (Ministry of Petroleum & Natural Gas) (709778)	Gujarat	NA (01/2022)	08/2025 (09/2026)	328.29 (287)	151.53	58
378	Commercial Polymer Flooding Project in Bechraji field (Oil and Natural Gas Corporation Limited [ONGC]) (709838)	Gujarat	NA (01/2022)	11/2024 (11/2025)	621.4 (621.4)	137.71	21
379	Restoration of Gas Terminal, Phase-I [Part-A], Hazira (Oil and Natural Gas Corporation Limited [ONGC]) (709840)	Gujarat	NA (05/2022)	02/2025 (12/2025)	249.43 (249.43)	209.45	94
380	Old Pipe Line Replacement [OPRP] Group-A (Oil and Natural Gas Corporation Limited [ONGC]) (709841)	Gujarat	NA (07/2021)	07/2025 (03/2026)	173.03 (169.84)	147.02	87
381	Kalol Redevelopment Project, Ahmedabad Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709842)	Gujarat	NA (08/2022)	03/2027 (03/2027)	1487.41 (1487.41)	927.5	62
382	Revamping of SV Stations, Gas Terminal & Kribhco Terminal (Oil and Natural Gas Corporation Limited [ONGC]) (709845)	Gujarat	NA (11/2022)	08/2026 (08/2026)	837.34 (837.34)	219.13	52
383	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad (Ministry of Petroleum & Natural Gas) (604853)	Haryana	NA (06/2019)	12/2022 (03/2026)	2281.94 (3200)	1800.61	63
384	Poly Butadiene Rubber plant at Panipat (Indian Oil Corporation Limited [IOCL]) (611917)	Haryana	NA (03/2022)	03/2025 (06/2026)	1459 (2531.44)	1072.59	70
385	Capacity Expansion of Panipat Refinery from 15 to 25 MMTPA (Ministry of Petroleum & Natural Gas) (701289)	Haryana	NA (02/2021)	09/2024 (12/2025)	34627 (36225)	24355.1	89
386	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. (Ministry of Petroleum & Natural Gas) (709783)	Haryana	NA (12/2020)	06/2023 (06/2026)	165.13 (247.69)	130.6	72
387	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts (Ministry of Petroleum & Natural Gas) (709773)	Jammu and Kashmir	NA (03/2022)	03/2032 (03/2032)	538 (538)	3.72	0
388	Development of Jharia CBM Block [Phase-1] (Oil and Natural Gas Corporation Limited [ONGC]) (610984)	Jharkhand	NA (11/2019)	01/2024 (11/2025)	431 (431)	211.4	59
389	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] (Ministry of Petroleum & Natural Gas) (709785)	Jharkhand	NA (02/2023)	02/2026 (02/2026)	202.07 (202.07)	52.42	45
390	Power System Upgradation Project (Mangalore Refinery and Petrochemicals Limited) (612790)	Karnataka	NA (10/2023)	11/2025 (05/2026)	385 (385)	137	64
391	Demo Bio-ATF Project (Ministry of Petroleum & Natural Gas) (616879)	Karnataka	NA (03/2024)	01/2027 (01/2027)	364 (364)	27.02	12
392	Revamping/ Augmentation of facilities at existing port terminal at Mangalore (Ministry of Petroleum & Natural Gas) (709774)	Karnataka	NA (01/2022)	12/2025 (12/2025)	463 (500.62)	271.16	82
393	Replacement and Extension of Jetty Pipelines [REJP] at KR (Bharat Petroleum Corporation Limited [BPCL]) (709790)	Kerala	NA (03/2023)	03/2026 (03/2026)	621.87 (621.87)	193.19	85
394	Setting up Polypropylene Unit at Kochi Refinery (Ministry of Petroleum & Natural Gas) (709799)	Kerala	NA (12/2023)	10/2027 (10/2027)	4460 (4460)	265.89	13
395	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery (Ministry of Petroleum & Natural Gas) (709798)	Madhya Pradesh	NA (05/2023)	05/2028 (05/2028)	43367 (43367)	1855.5	14
396	Debottlenecking and Augmentation of Cryogenic facilities at Uran LPG Import Terminal (Department of Water Resources, River Development & GR) (400158)	Maharashtra	NA (04/2021)	02/2024 (12/2025)	1164.69 (1629.86)	932.25	86
397	500 KTA PDHPP Project, Usar (Ministry of Petroleum & Natural Gas) (400168)	Maharashtra	NA (04/2021)	04/2025 (10/2025)	8797 (11256)	6877.59	85
398	Construction of lube oil blending plant at Rasayani (Ministry of Petroleum & Natural Gas) (610985)	Maharashtra	NA (05/2022)	12/2023 (12/2025)	423.39 (526.26)	301.01	80
399	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery (Ministry of Petroleum & Natural Gas) (616933)	Maharashtra	NA (12/2024)	03/2028 (03/2028)	4679 (4679)	194.44	5
400	HP TDAE Unit in Mumbai Refinery (Hindustan Petroleum Corporation Limited) (709760)	Maharashtra	NA (06/2024)	04/2026 (04/2026)	240 (240)	34.42	40

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
401	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts (Ministry of Petroleum & Natural Gas) (709771)	Maharashtra	NA (03/2022)	09/2031 (09/2031)	865 (865)	69.15	2
402	Construction of Additional Tankages and Allied Facilities at JNPT Terminal (Ministry of Petroleum & Natural Gas) (709780)	Maharashtra	NA (04/2022)	08/2026 (08/2026)	341.43 (436.14)	282.95	51
403	ATF Pipeline from Jawaharlal Nehru Port Trust to Navi Mumbai International Airport (Indian Oil Corporation Limited [IOCL]) (709782)	Maharashtra	NA (08/2022)	08/2025 (03/2026)	165 (165)	90.75	74
404	Installation of Independent De- Aromatized Solvents [DAS] production facilities at MR (Bharat Petroleum Corporation Limited [BPCL]) (709789)	Maharashtra	NA (03/2023)	07/2025 (12/2025)	405 (343)	205.63	86
405	POL & LOBS Installations with Receipt Pipelines at Rasayani (Bharat Petroleum Corporation Limited [BPCL]) (709797)	Maharashtra	NA (05/2023)	05/2026 (05/2026)	2585 (2585)	612.7	61
406	Part Replacement Pipeline Project [PRPP] (Oil and Natural Gas Corporation Limited [ONGC]) (709846)	Maharashtra	NA (11/2022)	05/2024 (11/2025)	1219.48 (1145.1)	744.81	90
407	Visakh Raipur Pipeline Project (Ministry of Petroleum & Natural Gas) (616254)	Multi-States (Andhra Pradesh, Chhattisgarh, Odisha)	NA (09/2024)	09/2027 (09/2027)	2212 (2212)	13.45	8
408	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura, West Bengal)	NA (04/2020)	03/2024 (03/2026)	9265 (9265)	6393.85	85
409	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Multi-States (Assam, West Bengal)	NA (06/2021)	12/2024 (10/2025)	860 (860)	584.76	98
410	CGD Project in Banka, Dumka, Godda, Jamtara, Pakur, Sahibganj GA ID 11A.02 (Hindustan Petroleum Corporation Limited) (709757)	Multi-States (Bihar, Jharkhand)	NA (06/2022)	06/2030 (06/2030)	1377 (1377)	331.74	27
411	Mumbai Nagpur Jharsuguda Pipeline Project (Ministry of Petroleum & Natural Gas) (701354)	Multi-States (Chhattisgarh, Madhya Pradesh, Maharashtra, Odisha)	NA (06/2020)	05/2023 (09/2025)	7844.25 (8255)	6495.6	96
412	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (Ministry of Petroleum & Natural Gas) (701330)	Multi-States (Gujarat, Haryana, Punjab, Rajasthan)	NA (07/2011)	06/2024 (12/2025)	7392 (7392)	6308	90
413	Gurdaspur Jammu Pipeline (Gas Authority of India Limited [GAIL]) (612853)	Multi-States (Jammu and Kashmir, Punjab)	NA (07/2023)	07/2026 (07/2026)	521.9 (521.9)	190.1	36
414	Kochi - Kootanad - Bangalore - Mangalore Pipeline Phase-II (Ministry of Petroleum & Natural Gas) (701228)	Multi-States (Karnataka, Kerala, Tamil Nadu)	NA (06/2009)	12/2012 (12/2025)	2915 (5909)	4453.29	94
415	City Gas Distribution Maharashtra Natural Gas Limited (Ministry of Petroleum & Natural Gas) (701338)	Multi-States (Karnataka, Maharashtra)	NA (01/2006)	06/2031 (06/2031)	5535 (5535)	3861.49	0
416	Dhamra Haldia Pipeline Project (Ministry of Petroleum & Natural Gas) (701344)	Multi-States (Odisha, West Bengal)	NA (03/2020)	11/2022 (12/2025)	1030.65 (1125)	854.6	87
417	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (Bharat Petroleum Corporation Limited [BPCL]) (709794)	Multi-States (Punjab, Rajasthan)	NA (12/2022)	06/2030 (06/2030)	3207 (3207)	339.57	24
418	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum & Natural Gas) (709786)	Nagaland	NA (08/2023)	11/2027 (11/2027)	227.62 (227.62)	9.12	22
419	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (Ministry of Petroleum & Natural Gas) (604859)	Odisha	NA (07/2020)	01/2024 (08/2026)	13805 (11783)	8310.16	90
420	CUF POL Depot at Sadashibpur [Meramundali], Odisha (Ministry of Petroleum & Natural Gas) (709800)	Odisha	NA (04/2021)	03/2026 (03/2026)	393.54 (393.54)	104.55	44
421	Life Extension of 48 well platforms of Mumbai High & Heera Fields (Oil and Natural Gas Corporation Limited [ONGC]) (400119)	Offshore	NA (12/2015)	04/2018 (12/2025)	3190.69 (3375.9)	3074.25	89
422	PRP-VIII [Group-A] (Ministry of Petroleum & Natural Gas) (616950)	Offshore	NA (09/2024)	02/2026 (02/2026)	1486.4 (1486.4)	272.3	19
423	Daman Upside Development Project (Oil and Natural Gas Corporation Limited [ONGC]) (709839)	Offshore	NA (06/2022)	10/2025 (02/2026)	4144.41 (6406.9)	3894.53	85
424	MHN TCPBP PGC BGC Project [MTPBP] (Ministry of Petroleum & Natural Gas) (709848)	Offshore	NA (06/2022)	05/2026 (05/2026)	2329.45 (2354.23)	820.24	53
425	PRP-VIII Group B [NH & BS Asset] (Ministry of Petroleum & Natural Gas) (709849)	Offshore	NA (06/2024)	02/2026 (02/2026)	2379.84 (3165.53)	1675.65	62
426	Integrated Development of 4 Contract Areas under DSF-II (Ministry of Petroleum & Natural Gas) (709851)	Offshore	NA (05/2023)	04/2027 (04/2027)	6183.79 (6183.79)	474	20
427	2G Ethanol Biorefinery at Bathinda (Hindustan Petroleum Corporation Limited [HPCL]) (400171)	Punjab	NA (05/2020)	02/2023 (03/2026)	1421.46 (1421.46)	1182.4	95

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
428	Bathinda Sangrur Pipeline (Ministry of Petroleum and Natural Gas) (612998)	Punjab	NA (11/2021)	05/2024 (09/2025)	367 (397)	346.18	93
429	City Gas Distribution Project at Pathankot District (Ministry of Petroleum and Natural Gas) (709770)	Punjab	NA (03/2022)	09/2033 (09/2033)	151 (151)	8.73	2
430	CBR 9 MMTPA Project (Chennai Petroleum Corporation Limited [CPCL]) (604795)	Tamil Nadu	NA (09/2021)	06/2025 (10/2028)	31580 (36354)	1342.27	10
431	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore (Chennai Petroleum Corporation Limited [CPCL]) (709750)	Tamil Nadu	NA (01/2024)	09/2025 (12/2025)	205 (205)	38.14	42
432	City Gas Distribution Projects at the Nilgiris and Erode districts (Bharat Petroleum Corporation Limited [BPCL]) (709796)	Tamil Nadu	NA (12/2022)	03/2030 (03/2030)	3685 (3685)	226.87	17
433	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	NA (03/2022)	05/2024 (12/2025)	209.33 (131.51)	68.88	62
434	PP Project, Pata (Gas Authority of India Limited [GAIL]) (400161)	Uttar Pradesh	NA (03/2019)	01/2024 (09/2025)	910.56 (1299.02)	1019	97
435	Revamping / Augmentation of Facilities at Mathura Bitumen Plant (Ministry of Petroleum and Natural Gas) (709781)	Uttar Pradesh	NA (04/2022)	06/2027 (12/2026)	260.12 (260.12)	1.11	26
436	City Gas Distribution Projects at Lakhimpur Kheri, Sitapur, Bahraich, Shravasti, Balrampur, Siddharth Nagar & Maharajganj districts (Bharat Petroleum Corporation Limited [BPCL]) (709795)	Uttar Pradesh	NA (12/2022)	06/2030 (06/2030)	16654 (16654)	558.33	11
437	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] (Ministry of Petroleum & Natural Gas) (617302)	West Bengal	NA (03/2017)	12/2020 (12/2025)	1740 (2493.15)	2239.7	90
438	Haldia Panagarh Pipeline Project (Hindustan Petroleum Corporation Limited) (709753)	West Bengal	NA (11/2022)	11/2025 (11/2025)	1010 (1010)	645.07	82
439	CGD Project in Malda, Birbhum, Murshidabad, Dakshin Dinajpur GA ID 11A.03 (Hindustan Petroleum Corporation Limited) (709758)	West Bengal	NA (06/2022)	06/2030 (06/2030)	2628 (2628)	335.96	27
440	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts (Ministry of Petroleum and Natural Gas) (709772)	West Bengal	NA (03/2022)	06/2031 (06/2031)	609 (609)	56.35	2
441	City Gas Distribution Projects at Alipurduar and Cooch Behar (Bharat Petroleum Corporation Limited [BPCL]) (709791)	West Bengal	NA (12/2022)	03/2030 (03/2030)	1017 (1017)	184.13	39
Total (90)					351248.78	184032.26	
Ministry of Health & Family Welfare							
Healthcare							
442	AIIMS Majra Rewari Haryana (Ministry of Health & Family Welfare) (701173)	Haryana	NA (02/2019)	02/2023 (12/2026)	1299 (1299)	349.41	28
443	AIIMS Kashmir at Awantipora Jammu & Kashmir (Central Public Works Department [CPWD]) (701167)	Jammu and Kashmir	01/2019 (01/2019)	01/2025 (12/2025)	1828 (1828)	1531.86	66
444	AIIMS Bibinagar (Ministry of Health & Family Welfare) (701171)	Telangana	12/2018 (12/2018)	09/2022 (12/2025)	1028 (1365.95)	812.95	84
Total (3)					4155	2694.22	
Ministry of Ports, Shipping and Waterways							
Healthcare							
445	Establishment of 600 bed super specialty hospital with optional development of Medical college and further expansion on PPP basis. (Mumbai Port Trust [MPT]) (708662)	Maharashtra	08/2019 (01/2022)	06/2026 (12/2027)	693 (693)	58	0
Total (1)					693	58	
Inland Waterways							
446	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust [DPT]) (609424)	Gujarat	NA (12/2023)	12/2026 (-)	4243.64 (4243.64)	366.2	10
447	Jal Marg Vikas Project (Inland Waterways Authority of India [IWAI]) (701565)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	01/2018 (02/2018)	12/2023 (12/2025)	5369.18 (5061.15)	3510.72	71
Total (2)					9612.82	3876.92	
Shipping							
448	Setting up of a Floating Storage and Regasification Unit [FSRU] - Mumbai (Mumbai Port Trust [MPT]) (701586)	Maharashtra	NA (04/2021)	11/2026 (11/2026)	900 (900)	65	0
449	Operationalization of Coastal Berth & Shallow Water Berth through PPP (Jawaharlal Nehru Port Authority [JNPA]) (708655)	Maharashtra	NA (07/2021)	01/2026 (-)	366.8 (366.8)	376.86	25
450	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574)	Odisha	05/2022 (01/2023)	12/2027 (10/2028)	3004.63 (3004.63)	1149.79	40
451	Berth No. 2 [previously Berth 3] of HDC Mechanization Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701576)	West Bengal	NA (03/2023)	09/2025 (01/2026)	298.26 (298.26)	420	91

All Ongoing Projects							AUGUST 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
452	Shalukkhali Liquid Cargo Handling Facility Development Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701577)	West Bengal	NA (08/2022)	08/2025 (-)	253.65 (253.65)	9.28	0
	Total (5)				4823.34	2020.93	
	Tourism, Hospitality & Wellness						
453	National Maritime Heritage Complex [NMHC] Phase-I (Indian Port Rail & Ropeway Corporation Ltd. [IPRCL]) (707215)	Gujarat	02/2019 (01/2022)	03/2024 (09/2025)	573 (1238.05)	496.63	66
	Total (1)				573	496.63	
	Ministry of Steel						
	Metals & Mining						
454	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul (National Mineral Development Corporation Limited [NMDC]) (615202)	Chhattisgarh	08/2021 (07/2022)	12/2028 (03/2028)	1700 (1756.2)	65.44	3
	Total (1)				1700	65.44	
	Steel						
455	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617243)	Chhattisgarh	07/2024 (08/2024)	07/2026 (-)	198.62 (198.62)	10.9	10
456	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617255)	Chhattisgarh	NA (12/2023)	06/2026 (-)	471.83 (471.83)	130.66	40
457	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617256)	Chhattisgarh	NA (01/2024)	10/2025 (-)	884.1 (884.1)	466.31	77
458	NMDC Slurry Pipeline Project Phase-1 (National Mineral Development Corporation Limited [NMDC]) (706811)	Chhattisgarh	11/2015 (09/2020)	06/2023 (12/2025)	2907 (5427)	3038.85	85
459	SCREENING PLANT-III AT KIRANDUL (National Mineral Development Corporation Limited [NMDC]) (709826)	Chhattisgarh	NA (10/2021)	01/2026 (-)	2718.84 (2718.84)	1341.08	72
460	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (National Mineral Development Corporation Limited [NMDC]) (709827)	Chhattisgarh	NA (10/2022)	12/2025 (-)	349.75 (349.75)	282.52	88
461	New Sinter Plant at BSL, SAIL (Steel Authority of India Limited [SAIL]) (400174)	Jharkhand	03/2015 (05/2015)	10/2017 (06/2027)	1034.01 (1752.3)	883.44	51
462	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617249)	Jharkhand	01/2025 (02/2025)	01/2027 (-)	211.94 (211.94)	15.04	10
463	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617250)	Jharkhand	NA (02/2025)	10/2026 (-)	207.13 (207.13)	15.76	8
464	Revamping of old sub-systems of Blast Furnace 3 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617253)	Jharkhand	09/2023 (10/2023)	07/2025 (11/2025)	513.82 (513.82)	234.54	71
465	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617254)	Jharkhand	NA (04/2024)	06/2026 (-)	260.37 (260.37)	44.25	22
466	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617257)	Jharkhand	NA (12/2023)	11/2026 (-)	627.31 (627.31)	91.96	38
467	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. (National Mineral Development Corporation Limited [NMDC]) (400121)	Karnataka	11/2014 (06/2024)	08/2026 (-)	1043.63 (1043.63)	229.77	29
468	Installation of 4th Slab Caster along with its Auxiliaries and a New Ladle Furnace in SMS-II at Rourkela Steel Plant (Steel Authority of India Limited [SAIL]) (400065)	Odisha	01/2022 (02/2022)	05/2025 (09/2025)	1105.23 (1105.23)	769.08	97
469	Rebuilding of COB 4 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (612781)	West Bengal	11/2023 (12/2023)	12/2026 (-)	916.78 (916.78)	126.25	14
470	Installation of New Bar Mill at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617242)	West Bengal	09/2024 (10/2024)	06/2027 (-)	2115.44 (2115.44)	209.11	27
471	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617246)	West Bengal	09/2024 (10/2024)	06/2026 (-)	758.09 (758.09)	63.81	4
472	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617248)	West Bengal	NA (12/2024)	07/2026 (-)	227.96 (227.96)	16.24	29
473	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617251)	West Bengal	11/2024 (12/2024)	05/2026 (-)	196.4 (196.4)	0.19	3
	Total (19)				16748.25	7969.76	
	Ministry of Railways						
	Railways						
474	Nadikudi - Srikalahasti New Line (South Central Railway [SCR] - II) (400298)	Andhra Pradesh	03/2012 (12/2016)	05/2027 (03/2028)	2312 (5200)	2179	54
475	Malugur- Palasamudram New Line Project [17.975 Km] (South Western Railway [SWR] - II) (611615)	Andhra Pradesh	09/2022 (11/2025)	11/2027 (12/2027)	342 (342.14)	0	0

All Ongoing Projects							AUGUST 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
476	GOOTY-PENDEKALLU DOUBLING 29.225 Km (South Central Railway [SCR] - II) (611752)	Andhra Pradesh	03/2023 (06/2023)	03/2027 (03/2027)	351.83 (351.83)	18	25
477	GUNTAKAL WEST-MALLAPPA GATE RAIL OVER RAIL - ROR TRACK (South Central Railway [SCR] - II) (611754)	Andhra Pradesh	NA (07/2023)	07/2026 (-)	293.3 (293.3)	0	0
478	Kurnool - Setting up facilities for coach midlife rehabilitation workshop (WPO/Patna) (611927)	Andhra Pradesh	01/2014 (10/2017)	12/2023 (-)	560.72 (560.72)	276.66	65
479	Flyover between Pendurthi and Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB 73 of 2023 24 NR (East Coast Railway [ECor] - II) (612827)	Andhra Pradesh	NA (05/2024)	04/2027 (-)	183.65 (183.65)	4.2	11
480	3rd & 4th line between Vadlapudi -Gate Jn. cabin and Tie line between Gate Junction to Gangavaram port (East Coast Railway [ECor] - II) (616697)	Andhra Pradesh	NA (03/2024)	06/2026 (-)	154.28 (154.28)	10.98	16
481	Tiupati Katpadi 104.39 kms (South Central Railway [SCR] - II) (617210)	Andhra Pradesh	04/2025 (04/2025)	03/2029 (-)	1215.56 (1215.56)	0	0
482	3rd Line between Gudur Renigunta 83.17 Km (South Central Railway [SCR] - II) (617216)	Andhra Pradesh	10/2024 (10/2024)	03/2027 (-)	877.34 (877.34)	2.97	0
483	Kurnool Coach Midlife Rehabilitation Project (WPO/Patna) (705253)	Andhra Pradesh	NA (07/2014)	12/2020 (-)	563 (563)	120	0
484	Kotapalli - Narasapur New Line (South Central Railway [SCR] - II) (705436)	Andhra Pradesh	03/2009 (09/2013)	03/2028 (03/2028)	2501 (2501)	1303.41	29
485	Guntur-Guntakal Doubling Project (South Central Railway [SCR] - II) (705633)	Andhra Pradesh	03/2017 (11/2017)	12/2025 (12/2026)	3733 (4295)	4213.01	92
486	Vijaywada-Gudur 3rd Line (RVNL - II) (705648)	Andhra Pradesh	08/2016 (04/2018)	11/2024 (12/2025)	6654 (6654)	5922	90
487	Penukonda - Dharmavaram Doubling Project [41.5 Km] (South Western Railway [SWR] - II) (705789)	Andhra Pradesh	04/2019 (12/2018)	03/2026 (03/2026)	307.66 (307.66)	270.52	61
488	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3683.75	93
489	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
490	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	NA (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
491	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	NA (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
492	Sakri -Hasanpur [via Harnagar - Kusheshwar Asthan] New Railway line (East Central Railway [ECR] - I) (400254)	Bihar	12/2023 (08/1997)	12/2024 (03/2027)	735.2 (735.2)	585.84	82
493	Khagaria-Kusheshwar Asthan [42Km] new line project (East Central Railway [ECR] - I) (705364)	Bihar	04/2019 (12/1998)	12/2024 (03/2027)	614 (1384)	484.29	55
494	Hajipur-Sagauli New line (East Central Railway [ECR] - I) (705366)	Bihar	10/2007 (10/2004)	03/2020 (12/2026)	2067 (2087)	1968.45	74
495	Araria Supaul New BG Line (East Central Railway [ECR] - I) (705368)	Bihar	06/2018 (03/2009)	03/2024 (01/2027)	1605 (2514)	1490.2	35
496	Fatuha-Islampur incl. MM for extn.of NL from Neora to Daniawan , Daniawan to Biharsharif, Biharsharif to Barbiga , Barbiga to Shekhpura (East Central Railway [ECR] - I) (705373)	Bihar	08/2002 (03/2002)	03/2023 (08/2025)	1473 (2882)	2522.41	94
497	Jogbani-Biratnagar New Rail Line project (Indian Railway Construction International Limited [IRCON]) (705450)	Bihar	06/2010 (01/2011)	03/2022 (12/2026)	402 (486)	367.54	86
498	Samastipur-Darbhanga Doubling Railway Project (East Central Railway [ECR] - I) (705526)	Bihar	NA (12/2015)	03/2025 (10/2025)	519 (519)	344.23	84
499	Sagauli-Valmikinagar (East Central Railway [ECR] - I) (705527)	Bihar	03/2018 (03/2017)	12/2025 (12/2025)	1216 (2222)	2044.54	91
500	Muzaffarpur-Sugauli (East Central Railway [ECR] - I) (705528)	Bihar	03/2018 (03/2017)	06/2024 (08/2025)	1586 (1586)	1463.45	99
501	Rampur Dumra-Tal-Rajendrapul Additional Bridge and Railway Line Doubling (Indian Railway Construction International Limited [IRCON]) (706759)	Bihar	03/2016 (05/2017)	12/2024 (12/2025)	2373.64 (1700.24)	1402.95	95
502	Barauni-Bachwara [16 km] - 3rd & 4th line incl. Barauni yard remodelling [32 km] (East Central Railway [ECR] - I) (706860)	Bihar	10/2022 (08/2025)	08/2025 (10/2026)	645 (645)	0.77	55
503	Kharsia-Dharamjaygarh with Spur line [East Corridor-Phase 1] (Indian Railway Construction International Limited [IRCON]) (400220)	Chhattisgarh	03/2016 (01/2014)	09/2018 (03/2026)	3055 (3438)	2574.54	94
504	Doubling of Kirandul-Jagdalpur Line [150 km] (East Coast Railway [ECor] - II) (400291)	Chhattisgarh	02/2013 (03/2013)	03/2020 (12/2025)	1589 (1798)	1542.79	92
505	Gauge Conversion of Kendri-Dhamtari including Abhanpur - Rajim Branch line 67.20 Kms - 2nd Material Modification to Raipur Titlagarh doubling. (SECR) (602792)	Chhattisgarh	07/2011 (05/2021)	02/2025 (11/2025)	1171 (1171)	848	82

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
506	4th line between Nipania Bhatapara 14.4 Km (South East Central Railway [SECR] - II) (612815)	Chhattisgarh	NA (05/2024)	03/2027 (-)	170.49 (170.49)	0	0
507	Dharamjaigarh-Korba 63 km (CERL) (613003)	Chhattisgarh	NA (07/2022)	08/2026 (-)	1686.26 (1686.26)	288.83	18.5
508	KHARSIA- NAYA RAIPUR-PARMALKASA 5th and 6th Line [278KM] (CAO/C/SECR) (617200)	Chhattisgarh	04/2025 (04/2025)	03/2031 (-)	7853.84 (7853.84)	0	0
509	Dallirajhra- Rowghat New Railway Line - Phase I [95 km] (RVNL - II) (705433)	Chhattisgarh	07/2009 (12/2009)	09/2025 (12/2025)	1628 (1628)	1440.85	82
510	Gevra Road-Pendra Road New Railway Line [135 km] (Indian Railway Construction International Limited [IRCON]) (705444)	Chhattisgarh	NA (04/2014)	03/2022 (12/2025)	4970 (4970)	4346.55	73
511	Chirimiri-Nagpur Halt New Railway Line Project (South East Central Railway [SECR] - II) (705756)	Chhattisgarh	10/2018 (06/2020)	06/2030 (06/2030)	241 (656.52)	71	0
512	Boridand - Ambikapur Doubling Line Project (South East Central Railway [SECR] - II) (706854)	Chhattisgarh	06/2022 (04/2022)	06/2030 (06/2030)	1376 (1576.23)	218	18
513	NIPANIA-BHATAPRA [14.4 KM] 4TH LINE [PB-72/NR/2022-23] (SECR) (709814)	Chhattisgarh	NA (05/2024)	12/2026 (12/2026)	170 (184)	0	0
514	4TH LINE - BHATAPARA-HATHBAND [8.8 KM] [PB-72/NR/2022-23] (SECR) (709815)	Chhattisgarh	NA (05/2024)	01/2027 (12/2027)	177.03 (177.03)	0	2
515	4TH LINE - BHILAI-BHILAI NAGAR [8.8 KM] [PB-72/NR/2022-23] (SECR) (709816)	Chhattisgarh	NA (05/2024)	02/2027 (02/2027)	177.34 (177.34)	1.16	2
516	4TH LINE - DADHAPARA-BELHA [9.2 KM] [PB-72/NR/2022-23] (SECR) (709817)	Chhattisgarh	NA (05/2024)	11/2026 (11/2026)	169.06 (169.06)	14.42	60
517	4TH LINE RAJNANDGAON-DONGARHGARH [31.2 KM] [PB-72/NR/2022-23] (SECR) (709818)	Chhattisgarh	NA (05/2024)	01/2027 (01/2027)	328.34 (328.34)	50.58	25
518	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (709819)	Chhattisgarh	09/2022 (05/2025)	12/2026 (12/2026)	167.64 (167.64)	0	2
519	Redevelopment of New Delhi Railway Station and construction of associated infrastructure (Ministry of Railways) (613785)	Delhi	01/2023 (06/2024)	12/2028 (-)	4744 (4744)	35.09	0
520	North Region Video Surveillance Project (RCIL) (705298)	Delhi	NA (04/2023)	03/2024 (-)	274.39 (274.39)	0	0
521	Anand Vihar-Tilak Bridge 3rd & 4th line (CAO/C/NR) (705583)	Delhi	03/2013 (03/2013)	03/2023 (12/2027)	667 (667)	285.44	62
522	Provision of Work-site Tampers [WST] Railway Project (EDTK[MC]/RB) (705694)	Delhi	NA (01/2016)	12/2023 (01/2026)	187.72 (187.72)	141.91	100
523	WST Machine Procurement Project (EDTK[MC]/RB) (705708)	Delhi	NA (06/2018)	03/2024 (12/2027)	176 (176)	0	0
524	PCT Machine Procurement Project (EDTK[MC]/RB) (705710)	Delhi	NA (04/2019)	04/2024 (06/2027)	336 (336)	74.32	85
525	RBMV Machine Procurement Project (EDTK[MC]/RB) (705712)	Delhi	NA (10/2019)	06/2024 (12/2027)	480 (480)	0.33	7
526	SRGM Machine Procurement Project (EDTK[MC]/RB) (705717)	Delhi	NA (10/2019)	12/2023 (03/2026)	440 (440)	390.03	90
527	WST Machine Procurement Project (EDTK[MC]/RB) (705720)	Delhi	NA (12/2019)	04/2024 (12/2026)	384 (384)	0	0
528	DTS Machine Procurement Project (EDTK[MC]/RB) (705721)	Delhi	NA (12/2019)	12/2024 (12/2026)	447.6 (447.6)	0	0
529	BRM Machine Procurement Project (EDTK[MC]/RB) (705722)	Delhi	NA (09/2019)	06/2024 (12/2027)	210 (210)	0.02	0
530	Track Machine Procurement Project (EDTK[MC]/RB) (705726)	Delhi	NA (04/2020)	03/2025 (01/2028)	6339 (6339)	4166.47	41
531	Kosamba Umarpada 70 Km (PCE/WR) (611918)	Gujarat	NA (07/2022)	03/2027 (-)	468 (468)	20	8
532	Adraj Moti Vijapur 40 Kms (Western Railway [WR] - II) (611937)	Gujarat	05/2022 (05/2022)	05/2026 (05/2026)	417.53 (417.53)	223	86
533	Vijapur Ambliyan 42 km (PCE/WR) (611938)	Gujarat	05/2022 (05/2022)	05/2026 (05/2026)	415.38 (415.38)	364	96
534	Himatnagar Khedbrahma 55 km (Railway) (611939)	Gujarat	06/2022 (04/2017)	06/2001 (06/2026)	482.42 (482.42)	461	96
535	New broad gauge line between Naliya Jakhau Port 25 Kms (PCE/WR) (611943)	Gujarat	02/2023 (02/2023)	01/2028 (01/2028)	410.26 (410.26)	6	4

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
536	Quadrupling between Gandhidham Adipur with Y connection at Adipur for providing direct entry towards Mundra Port and Bhuj and high level platform at Gopalpur 11Kms (PCE/WR) (611944)	Gujarat	02/2023 (02/2023)	03/2026 (03/2026)	152.44 (152.44)	20	68
537	Petlad Bhadran 23 Kms (PCE/WR) (611945)	Gujarat	05/2022 (05/2022)	05/2030 (05/2030)	307.11 (307.11)	82	17
538	Choranda Motikoral 18 Kms (PCE/WR) (611969)	Gujarat	NA (08/2023)	10/2026 (-)	246 (246)	0	0
539	Samlaya Timba Road 54 km (PCE/WR) (611970)	Gujarat	02/2023 (02/2023)	03/2030 (03/2030)	670.17 (670.17)	102	12
540	Samni Jambusar 24 km (PCE/WR) (611971)	Gujarat	05/2022 (05/2022)	03/2030 (03/2030)	350 (349.93)	87	31
541	Jambusar Kavi 26 Kms (PCE/WR) (611972)	Gujarat	NA (04/2023)	12/2026 (-)	318 (318)	0	0
542	miyagam karjan Choranda maalsar 37 kms (PCE/WR) (611973)	Gujarat	NA (06/2023)	12/2026 (-)	450 (450)	0	0
543	Western Railway Samakhiali Gandhidham Quadrupiling 53 Kms (PCE/WR) (611974)	Gujarat	08/2023 (08/2023)	12/2026 (-)	1430 (1430)	0	0
544	Dahod Creation of Infrastructure facilities for 9000 HP Electric locomotives Manufacturing at (PCE/WR) (611977)	Gujarat	NA (02/2023)	02/2025 (-)	487 (487)	108.69	0
545	Dahod Rolling Stock Workshop Provision of Infrastructure for CBS at (PCE/WR) (611978)	Gujarat	NA (03/2023)	03/2025 (-)	158 (158)	47.31	0
546	Sabarmati Setting up of Maintenance Facilities for Train Sets Phase ii (PCE/WR) (611979)	Gujarat	NA (04/2023)	06/2025 (-)	250 (250)	0	0
547	4th LINE BETWEEN BAREJADI NANDEJ-SANAND-AHMEDABAD BYPASS (Western Railway) (612072)	Gujarat	02/2023 (02/2023)	03/2027 (03/2027)	961.67 (961.67)	327.53	17
548	Redevelopment of Ahmedabad railway station and associated infrastructure on engineering, procurement and construction mode (Ministry of Railways) (613786)	Gujarat	01/2023 (11/2023)	03/2028 (-)	2379 (2379)	656.84	16
549	Miyagam-Karjan-Dabhoi-Samlaya [GC] (Western Railway [WR] - II) (705458)	Gujarat	01/2017 (01/2017)	03/2021 (12/2026)	483.88 (844.1)	620.98	41
550	Modasa-Shamlaji Road Railway Line Project (SECR) (706757)	Gujarat	09/2012 (04/2008)	03/2025 (03/2027)	262 (262)	203	58
551	Rajkot - Kanalus Doubling Project [111.2 Kms] (Western Railway [WR] - II) (706763)	Gujarat	10/2021 (12/2021)	10/2026 (10/2026)	1080.58 (1080.58)	787.69	76
552	NADIAD-PETLAD [37.26 KM] (Railway) (709812)	Gujarat	NA ()	06/2030 (06/2030)	461.91 (461.91)	75	7
553	NEW BG LINE INTERSECTION [5 NOS] BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD [16.51 KM] [PB#29/NR/202 (SECR) (709813)	Gujarat	NA ()	10/2027 (10/2027)	437.21 (437.21)	43	15
554	Bhiwani - Dobh Bahali Doubling Project [42.30 Km] (North Western Railway [NWR]) (611884)	Haryana	02/2023 (02/2023)	02/2028 (02/2028)	471 (471)	191.39	59
555	Gomoh - Flyover for DN trains (East Central Railway [ECR] - I) (705765)	Jharkhand	01/2018 (01/2018)	03/2026 (03/2026)	686 (686)	538.66	59
556	Lodhma - Piska - Link Line bypassing Hatia/Ranchi with Y connection (South Eastern Railway [SER] - I) (705785)	Jharkhand	08/2021 (03/2019)	06/2026 (05/2027)	473 (473)	284.34	4
557	Pradhan Kuntha Jn Line Doubling Project (East Central Railway [ECR] - I) (706837)	Jharkhand	11/2022 (11/2022)	11/2027 (11/2027)	349.22 (349.22)	90.64	60
558	Construction of New BG line between Hassan to Belur [27 Km] (South Western Railway [SWR] - II) (400023)	Karnataka	03/2019 (12/2025)	04/2028 (04/2027)	749 (749)	0	0
559	Yeshvanthpur - Channasandra Doubling Project [21.70 Km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703585)	Karnataka	NA (10/2019)	03/2024 (08/2025)	314.1 (683.57)	151.11	52
560	New Railway Line between Ginigera and Raichur [165.57 km] (South Western Railway [SWR] - II) (705434)	Karnataka	03/2008 (05/2009)	03/2019 (03/2027)	2565 (3034.98)	2073.98	66
561	Gadag-Wadi New Railway Line [257 km] (South Western Railway [SWR] - II) (705490)	Karnataka	04/2013 (08/2017)	03/2027 (12/2027)	2842 (6700)	1735.22	30
562	Kadur - Chickamagalur - Sakleshpur [93km] (South Western Railway [SWR] - II) (705492)	Karnataka	01/2014 (11/2016)	06/2025 (12/2025)	825 (825)	788.13	83
563	Bagalkot-Kudachi New Railway Line [142 km] (South Western Railway [SWR] - II) (705495)	Karnataka	11/2021 (11/2012)	03/2027 (01/2027)	1378 (1649)	683.48	35
564	Tumkur-Chitradurga-Davangere New Rail Line Project [191 km] (South Western Railway [SWR] - II) (705496)	Karnataka	10/2013 (01/2017)	03/2019 (12/2027)	1876 (1876)	523.07	13
565	Bangalore-Whitefield-Bangalore City-Krishnarajapuram [23.08 km] - Quadrupling (South Western Railway [SWR] - II) (705663)	Karnataka	02/2018 (06/2022)	02/2026 (02/2026)	493 (493)	252.45	82

All Ongoing Projects

AUGUST 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
566	SHIMOGA - SHIKARIPURA - RANEBENNUR [96 Km] (South Western Railway [SWR] - II) (705761)	Karnataka	NA (02/2023)	12/2027 (06/2028)	1454 (1454)	69.82	11
567	Belgaum-Dharwad via Kittur [73.10Km] (South Western Railway [SWR] - II) (706835)	Karnataka	09/2020 (03/2025)	12/2027 (03/2029)	1591 (1591)	0.75	0
568	Kumbalam-Turavur doubling project [15.59 Km] (Southern Railway [SR] - II) (705638)	Kerala	04/2023 (04/2023)	03/2027 (03/2027)	813 (813)	292.15	15
569	Ernakulam-Kumbalam doubling project [7.71 Km] (SR-ERS) (705639)	Kerala	04/2023 (04/2023)	03/2028 (03/2028)	601 (601)	283	17
570	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho (North Central Railway) (705480)	Madhya Pradesh	01/2007 (03/1998)	03/2027 (12/2027)	8914 (8914)	5013.49	72
571	Katni - Bina Third Railway Line [279 km] (West Central Railway WCR I) (705651)	Madhya Pradesh	06/2016 (01/2017)	03/2022 (12/2025)	2478.23 (4127.23)	3301.89	90
572	Satna-Rewa Railway Line Doubling Project (West Central Railway [WCR] - II) (705659)	Madhya Pradesh	11/2015 (08/2017)	03/2026 (03/2026)	500 (584)	561.38	80
573	Doubling of Katni - Singrauli Railway Line [261 km] (Indian Railway Construction International Limited [IRCON]) (705660)	Madhya Pradesh	03/2016 (03/2017)	12/2025 (12/2025)	2445 (4377)	3201.67	100
574	Katni Grade Separator/Bye Pass (Indian Railway Construction International Limited [IRCON]) (705661)	Madhya Pradesh	03/2016 (09/2017)	09/2024 (03/2026)	1248 (1248)	1587.21	94
575	Indore - Budni New Railway Line [198 kms] (RVNL - II) (705763)	Madhya Pradesh	08/2019 (10/2020)	09/2030 (09/2030)	7474 (7474)	1685.25	23
576	Nimach-Ratlam Doubling [133 Km] (Western Railway [WR] - II) (705933)	Madhya Pradesh	10/2021 (10/2021)	10/2027 (10/2027)	1095.88 (1095.88)	1067.49	89
577	DHULE [BORVIHIR] - NARDANA NEW LINE [50.60 KMS] (CR) (400019)	Maharashtra	01/2019 (04/2023)	12/2026 (09/2027)	492.76 (1170.83)	245.11	16
578	Wardha-Nanded Via Yavatmal New BG Line (Central Railway [CR] - II) (400271)	Maharashtra	12/2017 (04/2008)	03/2028 (03/2028)	3445 (3445)	3002.93	50
579	AURANGABAD-ANKAI - DOUBLING PROJECT 98.25 Km (South Central Railway [SCR] - II) (611751)	Maharashtra	05/2023 (05/2023)	03/2027 (-)	960.64 (960.64)	0	0.01
580	Western Railway Vasai bypass double line between Naigaon Juchandra 6 km (PCE/WR) (611975)	Maharashtra	NA (07/2023)	03/2026 (-)	176 (176)	0	0
581	Jogeshwari AT Development of JOS-AT as Trainset Maintenance Depot for energy efficient Vande Bharat Sleeper Trains (PCE/WR) (611976)	Maharashtra	NA (06/2023)	10/2025 (-)	221 (221)	0	0
582	Redevelopment of Chhatrapati Shivaji Maharaj Terminus [CSMT] and construction of associated infrastructure (Ministry of Railways) (613015)	Maharashtra	04/2023 (07/2023)	03/2027 (-)	1813 (1813)	569.08	13
583	Gondia-Balharshah [Chanda Fort] Doubling [240 Km] (South East Central Railway) (617201)	Maharashtra	04/2025 (04/2025)	04/2030 (-)	4373.04 (4373.04)	0	0
584	Doubling between Parbhani Parli Vajjanath stations 64.71 Km (South Central Railway [SCR] - II) (617215)	Maharashtra	12/2023 (12/2023)	03/2028 (-)	769.93 (769.93)	0	0
585	Western Region Video Surveillance Project (RCIL) (705300)	Maharashtra	NA (04/2023)	12/2023 (-)	227.59 (227.59)	0	0
586	Ahmednagar - Beed - Parli - Vajinath New Broad Gauge Line Railway Project [261.3 km] (Central Railways) (705356)	Maharashtra	01/1999 (10/2002)	03/2026 (03/2026)	2538.67 (4957.27)	4975.74	98
587	Baramati Lonand New Line Project (Central Railway [CR] - II) (705357)	Maharashtra	03/2016 (03/1999)	03/2027 (03/2027)	138.48 (1843.9)	735.33	51
588	Wadsa-Gadchiroli (South East Central Railway) (705479)	Maharashtra	05/2017 (03/2012)	03/2027 (03/2027)	1886 (1886)	925.28	50
589	3rd Line Kalyan - Kasara [67.35 Kilometres] (Central Railway [CR] - II) (705498)	Maharashtra	09/2015 (09/2015)	12/2026 (12/2026)	792.89 (1395.79)	899.47	51
590	3rd Line Wardha - Sewagram - Nagpur (Central Railway [CR] - II) (705500)	Maharashtra	09/2015 (05/2016)	12/2025 (12/2025)	540.02 (944.24)	754.27	81
591	3rd Line Wardha - Ballarshah [132 Kilometres] (Central Railway [CR] - II) (705502)	Maharashtra	03/2016 (12/2016)	12/2025 (02/2026)	1384.72 (2033.59)	1655.88	68
592	Pune - Miraj-Londa [467 Kilometres] (Central Railway [CR] - II) (705503)	Maharashtra	06/2016 (06/2016)	02/2025 (08/2025)	4027.53 (4872.52)	4833.04	85
593	Doubling of Daund Manmad Line [247.6 km] (Central Railway [CR] - II) (705504)	Maharashtra	10/2017 (03/2017)	12/2025 (03/2026)	2081.27 (3267.06)	2816.46	88
594	4th Line Wardha - Nagpur [78.7 Kilometres] (Central Railway [CR] - II) (705505)	Maharashtra	04/2017 (05/2018)	12/2025 (02/2026)	637.95 (1341.28)	983.16	81
595	3rd Line Manmad - Jalgaon [160 Kilometres] (Central Railway [CR] - II) (705506)	Maharashtra	NA (04/2018)	12/2024 (08/2025)	1035.16 (1558.75)	1726.94	95



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
596	Solapur-tuljapur-Osmanabad (Railway) (705735)	Maharashtra	NA (12/2023)	03/2027 (03/2028)	904.92 (3295.74)	1127.14	12
597	Nagpur- Nagbhir Railway Line Gauge Conversion Project (MRIDC) (705799)	Maharashtra	10/2019 (04/2020)	12/2025 (12/2025)	1400 (1400)	1472	80
598	Mumbai Urban Transport Project [MUTP] - PHASE II (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706779)	Maharashtra	05/2008 (04/2008)	03/2014 (12/2027)	8087 (8087)	7364	87
599	Mumbai Urban Transport Project [MUTP] Phase-III A (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706780)	Maharashtra	04/2019 (04/2019)	12/2027 (12/2027)	33690 (33690)	2303.4	16
600	Mumbai Urban Transport Project Phase-III (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706781)	Maharashtra	11/2016 (12/2016)	03/2022 (12/2026)	10947 (10947)	5152.7	60
601	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (709808)	Maharashtra	NA (01/2022)	08/2027 (03/2028)	955.39 (2093.82)	130.42	11
602	KALYAN-MURBAD VIA ULHASNAGAR [UMBRELLA WORK] (Central Railway [CR] - II) (709809)	Maharashtra	NA (04/2023)	03/2027 (03/2027)	726.46 (836.12)	9.29	0
603	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15598.11	69
604	Marikuppam - Kuppam New Line Project [23.70 Km] (South Western Railway [SWR] - II) (705491)	Multi-States (Andhra Pradesh, Karnataka)	04/2012 (10/2018)	06/2026 (06/2026)	297 (297)	123.38	15
605	Rayadurg-Tumkur via Kalyandurg New Line [207 km] (South Western Railway [SWR] - II) (705494)	Multi-States (Andhra Pradesh, Karnataka)	03/2008 (07/2010)	09/2015 (02/2028)	2496 (2496)	1706.31	68
606	Renigunta, Wadi & Gooty Bypass Railway Project (South Central Railway [SCR] - I) (705610)	Multi-States (Andhra Pradesh, Karnataka)	04/2016 (04/2016)	12/2025 (12/2025)	302 (543)	381	50
607	Doubling between Mudkhed Medchal & Mahbubnagar Dhone section 417.88 Km (South Central Railway [SCR] - II) (617212)	Multi-States (Andhra Pradesh, Maharashtra, Telangana)	08/2023 (08/2023)	03/2029 (-)	4686.09 (4686.09)	0	0
608	Vizianagaram - Titlagarh 3rd line [272 Km including By - pass line of 7.68 KM] (RVNL - II) (400253)	Multi-States (Andhra Pradesh, Odisha)	06/2016 (11/2016)	12/2026 (12/2026)	4803 (6670)	5722.01	89
609	Doubling of Kottavalasa-Koraput Rail Line [189 KM] (East Coast Railway [ECOR] - II) (705512)	Multi-States (Andhra Pradesh, Odisha)	12/2015 (01/2016)	03/2022 (03/2028)	2500 (2500)	1987.17	70
610	Vizianagaram-Sambhalpur 3rd Line Project (RVNL) (705520)	Multi-States (Andhra Pradesh, Odisha)	NA (12/2016)	03/2025 (-)	4803.16 (4803.16)	2979.23	0
611	Malkangiri Pandurangapuram new railway line project (Indian Railways) (616702)	Multi-States (Andhra Pradesh, Odisha, Telangana)	08/2024 (01/2027)	11/2031 (-)	3591.76 (3591.76)	0	0
612	Tindivanam-Nagari New Line Project [184.5 km] (Southern Railway [SR] - II) (400275)	Multi-States (Andhra Pradesh, Tamil Nadu)	07/2008 (10/2008)	09/2016 (03/2028)	3631 (3631)	1113.53	18
613	Doubling between Motumari Vishnupuram - 88.81 Km and Rail over Rail - RoR at Motumari - 10.877 Km (South Central Railway [SCR] - II) (616857)	Multi-States (Andhra Pradesh, Telangana)	NA (03/2025)	03/2029 (-)	1595.55 (1595.55)	7.69	1
614	Doubling of Guntur Bibinagar 239 Km (South Central Railway [SCR] - II) (617211)	Multi-States (Andhra Pradesh, Telangana)	08/2023 (08/2023)	03/2029 (-)	2853.23 (2853.23)	43.88	1
615	Rail Connectivity to Errupalem Amravati Namburu 57 Km (South Central Railway [SCR] - II) (617214)	Multi-States (Andhra Pradesh, Telangana)	11/2024 (11/2024)	03/2027 (-)	2047.4 (2047.4)	0	0
616	Kazipet-Vijayawada 3rd line with electrification [220 km] (South Central Railway [SCR] - II) (705612)	Multi-States (Andhra Pradesh, Telangana)	03/2013 (08/2014)	02/2025 (12/2025)	1953 (3363)	3073.74	91
617	Vijayawada - Kazipet Bypass line (South Central Railway [SCR] - II) (705632)	Multi-States (Andhra Pradesh, Telangana)	04/2016 (04/2016)	01/2025 (12/2025)	647 (904)	888.91	91
618	Murkongselek-Pasighat (Northeast Frontier Railway [NFR] - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	NA (03/2012)	03/2025 (12/2025)	435 (1250)	901	56
619	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	NA (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
620	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5312.26	80
621	New Delhi- Howrah Speed Booster[160Kmph] Project (PCE/NCR) (705794)	Multi-States (Bihar, Delhi, Jharkhand, Uttar Pradesh, West Bengal)	NA (09/2019)	03/2024 (-)	6684.81 (6684.81)	127.03	0
622	Third Railway Line between Patratu-Sonnagar [281 kms] (RVNL - II) (400234)	Multi-States (Bihar, Jharkhand)	11/2016 (08/2018)	03/2026 (07/2026)	8975 (8975)	4950	88
623	Multi tracking of Son Nagar-Andal 374.53 rkm & 814.38 tkm (East Central Railway [ECR] - I) (616699)	Multi-States (Bihar, Jharkhand)	08/2023 (08/2023)	03/2028 (-)	12333.57 (12333.6)	467.55	11
624	Koderma-Tilaiya New Line (East Central Railway [ECR] - I) (705375)	Multi-States (Bihar, Jharkhand)	11/2004 (03/2002)	02/2025 (02/2026)	1626 (2020)	2000.4	95

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
625	Pirpainti - Jasidih [100.52 Km] New BG line (Eastern Railway [ER] - I) (705385)	Multi-States (Bihar, Jharkhand)	03/2014 (03/2022)	03/2028 (03/2028)	2555 (2555)	767.04	48
626	NER Provision of Automatic Block Signalling on Gorakhpur Cantt[Excl] Chhapra Gramin & Burhwal Jn [Excl] Sitapur Jn section of high density routes (North Eastern Railway [NER]) (611669)	Multi-States (Bihar, Uttar Pradesh)	NA (06/2023)	03/2027 (-)	380.47 (380.47)	24.53	0
627	Gorakhpur-Valmikinagar Doubling project (NER) (617224)	Multi-States (Bihar, Uttar Pradesh)	NA (03/2024)	12/2027 (-)	1120 (1120)	204.59	20
628	Chhapra-Ballia Patch Doubling (North Eastern Railway [NER]) (705562)	Multi-States (Bihar, Uttar Pradesh)	03/2013 (11/2015)	02/2025 (03/2025)	963 (1046)	911.66	95
629	Katihar - Kumedpur Doubling Line Project (GM/C/ NFR) (706844)	Multi-States (Bihar, West Bengal)	08/2022 ()	08/2027 (08/2027)	942 (942)	356	45
630	Rajnandgaon - Nagpur [Kalumna] Third Railway Line [228.30 km] (South East Central Railway [SECR] - II) (705617)	Multi-States (Chhattisgarh, Maharashtra)	09/2016 (12/2016)	12/2024 (06/2026)	3545 (3545)	3428.26	95
631	Jagdulpur-Koraput (East Coast Railway [ECoR] - II) (705511)	Multi-States (Chhattisgarh, Odisha)	12/2015 (03/2016)	03/2024 (12/2026)	1547 (1547)	1323.05	90
632	Jharsuguda-Bilaspur Fourth Railway Line [206 km] (SECR) (705616)	Multi-States (Chhattisgarh, Odisha)	09/2016 (09/2016)	10/2024 (12/2025)	2140 (2979)	2143.64	89
633	Mumbai-Ahmedabad High Speed Rail Project- 508 km (National High Speed Rail Corporation [NHSRC]) (705728)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	03/2015 (09/2017)	08/2027 (12/2029)	108000 (108000)	79918.89	53
634	New Delhi- Mumbai Speed Booster[160Kmph] Project (PCE/WR) (705793)	Multi-States (Delhi, Gujarat, Madhya Pradesh, Maharashtra, Rajasthan)	NA (09/2019)	03/2024 (-)	6806.44 (6806.44)	135.65	0
635	Hospet - Tinaighat - Vasco Rail Doubling Project (RVNL - II) (705650)	Multi-States (Goa, Karnataka)	03/2010 (07/2012)	03/2027 (12/2027)	5060 (5060)	5007.82	86
636	Hospet-Hubli-Vasco da Gama Line Electrification Project (RVNL) (706950)	Multi-States (Goa, Karnataka)	NA (05/2018)	03/2023 (03/2024)	744.49 (1122.62)	969.05	95
637	Western Dedicated Freight Corridor (DFCCIL) (705237)	Multi-States (Gujarat, Haryana, Maharashtra, Rajasthan, Uttar Pradesh)	02/2008 (01/2012)	03/2022 (12/2025)	51101 (124005)	124623	96
638	New line Dahod-Indore via Sardarpur, Jabuwa and Dhar (Western Railway [WR] - II) (705453)	Multi-States (Gujarat, Madhya Pradesh)	06/2012 (06/2012)	02/2027 (02/2027)	456.07 (1873.1)	3412.33	46
639	Chhota Udaipur - Dhar New Line Project [157 km] (Western Railway [WR] - II) (705454)	Multi-States (Gujarat, Madhya Pradesh)	11/2008 (01/2014)	12/2025 (12/2025)	1794 (1794)	1804.05	80
640	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (Western Railway) (611452)	Multi-States (Gujarat, Maharashtra)	09/2019 (03/2023)	12/2025 (06/2025)	311 (311)	208	92
641	Taranga Hill-Abu Road via Ambaji (North Western Railway [NWR]) (400022)	Multi-States (Gujarat, Rajasthan)	07/2022 (07/2022)	07/2030 (07/2030)	2798 (2798)	1915.38	15
642	LUNI- SAMDARI- BHILDI DOUBLING (North Western Railway [NWR]) (616842)	Multi-States (Gujarat, Rajasthan)	02/2024 (02/2024)	07/2027 (-)	3085.59 (3085.59)	171.32	7
643	Chandigarh-Baddi New Rail Line- 36 km (Northern Railway [NR]) (705424)	Multi-States (Haryana, Himachal Pradesh)	02/2018 (02/2018)	12/2026 (12/2026)	1540 (1540.13)	506.73	31
644	Rewari - Kathuwas Doubling Project [27.72 Km] (North Western Railway [NWR]) (611861)	Multi-States (Haryana, Rajasthan)	02/2023 (12/2022)	06/2027 (06/2027)	352 (352)	246.11	63
645	Nangal Dam-Talwara New Broad Gauge Line [84 KM] and Taking Over Siding Mukerian-Talwara [29 KM] (Northern Railway [NR]) (705410)	Multi-States (Himachal Pradesh, Punjab)	03/1983 (05/1985)	12/2025 (01/2027)	2018 (2018)	2053.9	45
646	Bhanupalli-Bilaspur-Beri New Railway Line Project (RVNL - II) (705428)	Multi-States (Himachal Pradesh, Punjab)	03/2009 (04/2015)	12/2026 (12/2027)	13447 (13447)	6805.81	60
647	Doubling of Hatia [Ranchi]-Bondamunda Rail Line - 159 km (South Eastern Railway - JH) (705628)	Multi-States (Jharkhand, Odisha)	03/2016 (02/2017)	06/2025 (06/2026)	3029 (3029)	2470.12	85
648	Buramara-Chakulia new line [59.96 km] (South Eastern Railway [SER] - I) (616588)	Multi-States (Jharkhand, Odisha, West Bengal)	08/2024 (12/2024)	12/2029 (-)	1459.13 (1459.13)	2.11	0
649	Chandil - Anara - Damodar - 3rd line [121.26 km] (CAO/C/SER) (616227)	Multi-States (Jharkhand, West Bengal)	NA (07/2025)	09/2029 (-)	1932.01 (1932.01)	0.03	0
650	KHARAGPUR-ADITYAPUR THIRD RAIL LINE- 132 KM (RVNL - II) (705668)	Multi-States (Jharkhand, West Bengal)	09/2016 (01/2018)	03/2025 (12/2025)	3250 (3250)	3176.46	97
651	Hotgi-Kudgi-Gadag Doubling Project (South Western Railway [SWR] - II) (705662)	Multi-States (Karnataka, Maharashtra)	04/2014 (01/2016)	12/2024 (03/2026)	1878 (2459)	2642.04	92
652	Baiyyappanahalli - Hosur Doubling Project [48 km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703586)	Multi-States (Karnataka, Tamil Nadu)	04/2019 (02/2019)	12/2024 (01/2026)	499 (499)	595	97

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
653	Trivandrum- Kanyakumari (Southern Railway [SR] - I) (705635)	Multi-States (Kerala, Tamil Nadu)	08/2017 (03/2016)	03/2024 (12/2027)	1432 (3785)	2451	46
654	Ratlam-Mhow-Khandwa-Akola Gauge Conversion (Western Railway [WR] - II) (705457)	Multi-States (Madhya Pradesh, Maharashtra)	04/2008 (03/2010)	03/2027 (09/2028)	1656.25 (5735.88)	4428.77	80
655	Itarsi - Nagpur Third Railway Line [280 km] (Central Railway [CR] - II) (705507)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016 (09/2016)	03/2027 (03/2027)	2449.91 (2506.68)	1843.76	51
656	Gwalior - Seopurkala with extension to Kota [Gauge Conversion] (North Central Railway) (705419)	Multi-States (Madhya Pradesh, Rajasthan)	03/2011 (07/2018)	03/2025 (02/2026)	2913 (2913)	2097.51	78
657	Ramganjmandi-Bhopal New Line Project [262 km] (West Central Railway [WCR] - II) (705481)	Multi-States (Madhya Pradesh, Rajasthan)	03/2001 (10/2004)	12/2025 (12/2027)	3032 (5073)	3621.79	70
658	Nimach-Badi Sadri New Rail Line Project (Western Railway [WR] - II) (705764)	Multi-States (Madhya Pradesh, Rajasthan)	04/2017 (09/2021)	03/2026 (06/2026)	495 (825)	79.55	53
659	Mathura-Jhansi Third Railway Line [274 Km] (RVNL - II) (705667)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	12/2015 (03/2018)	12/2024 (12/2026)	5961 (5961)	4928.62	94
660	Jhansi - Bina Third Railway Line [153 Km] (CAO/C/NCR) (705598)	Multi-States (Madhya Pradesh, Uttar Pradesh)	09/2016 (03/2018)	03/2022 (03/2026)	2002 (2002)	1795.86	93
661	Jhansi-Khairar-Manikpur & Khirar-Bhimsen (North Central Railway) (705608)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2018 (03/2017)	03/2026 (03/2026)	4330 (4330)	2184.56	55
662	Third Line [new] between Kazipet - Balharshah with electrification [201.04 Km] (South Central Railway [SCR] - II) (705613)	Multi-States (Maharashtra, Telangana)	09/2016 (10/2016)	01/2025 (11/2025)	2595 (3071)	3223.67	93
663	Narayangarh-Bhadrak 3rd line (South Eastern Railway [SER] - I) (705629)	Multi-States (Odisha, West Bengal)	03/2019 (03/2017)	12/2025 (06/2026)	2400 (2400)	2236.9	65
664	Nagapattinam-Tiruturaipundi and Karaikal-Peralam New Line (Southern Railway [SR] - II) (400223)	Multi-States (Puducherry, Tamil Nadu)	07/2008 (01/2019)	03/2026 (03/2027)	713 (981)	598.38	80
665	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Multi-States (Sikkim, West Bengal)	10/2009 (05/2010)	05/2015 (12/2027)	7877 (12133)	9039.91	84
666	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass Line Project (Eastern Railway [ER] - I) (602797)	Multi-States (Uttar Pradesh, West Bengal)	08/2017 (12/2017)	03/2027 (03/2027)	461.64 (461.64)	186.03	7
667	Proposed 6 nos Road Over Bridge [ROB] at different locations under MCL Talcher Under Deposit Scheme. (East Coast Railway [ECoR] - II) (400045)	Odisha	08/2022 (07/2022)	03/2025 (01/2025)	168.32 (168.32)	69.85	82
668	Brundamal-Jharsuguda- flyover connection for joining downline (East Coast Railway [ECoR] - II) (400232)	Odisha	01/2014 (01/2014)	12/2026 (12/2026)	297 (297)	193.22	30
669	3rd & 4th line between Sarla - Sason [8 km] [PB 73/2023-24/NR] (East Coast Railway [ECoR] - II) (612834)	Odisha	04/2023 (04/2023)	12/2025 (-)	252 (252)	79.55	45
670	Bangriposi-Gorumahisani new line [85.60 km] (CAO/C/SER) (616586)	Odisha	08/2024 (09/2025)	12/2029 (-)	2269.49 (2269.49)	2.31	0
671	Badampahar-Kendujhargarh new line [82.06 km] (CAO/C/SER) (616587)	Odisha	08/2024 (09/2025)	12/2029 (-)	1875.72 (1875.72)	0.53	0
672	Flyover between Siju and Paradeep coaching Yard to avoid Surface crossing of trains (East Coast Railway [ECoR] - II) (616694)	Odisha	04/2023 (10/2025)	07/2028 (-)	200.77 (200.77)	0	0
673	Paradeep - Badabandha 3rd & 4th Line / 18.51kms (East Coast Railway [ECoR] - II) (616695)	Odisha	08/2023 (04/2025)	11/2028 (-)	300.15 (300.15)	0.01	0
674	Khurda-Bolangir New Broad Gauge Rail Link [301km] (East Coast Railway [ECoR] - II) (705358)	Odisha	03/1994 (03/2001)	12/2026 (12/2026)	3792 (5089)	5027.62	89
675	Talcher-Bimlagarh New Railway Line (East Coast Railway [ECoR] - II) (705359)	Odisha	03/2004 (12/2004)	03/2025 (03/2027)	1928 (1928)	1934.28	48
676	Bhadrak-Nergundi Third Line (East Coast Railway [ECoR] - II) (705510)	Odisha	10/2015 (04/2015)	11/2024 (01/2026)	1284 (1284)	1298	80
677	Koraput - Singapur Railway Doubling (East Coast Railway [ECoR] - II) (705513)	Odisha	12/2015 (12/2015)	12/2027 (03/2028)	2362 (2362)	1798.71	68
678	Jarapada- Budhapank with flyover at Talcher road 3rd and 4th Line (East Coast Railway [ECoR] - II) (705514)	Odisha	NA (12/2015)	11/2018 (03/2026)	1000 (810.02)	401.61	36
679	3rd & 4th Railway Line Project from Salegaon to Budhapank via Rajathgarh. (East Coast Railway [ECoR] - II) (705515)	Odisha	07/2013 (12/2015)	03/2026 (03/2026)	1173 (2092)	1971	80
680	Jeypore-Navarangpur New Rail Line Project (East Coast Railway [ECoR] - II) (705741)	Odisha	07/2017 (04/2023)	07/2028 (12/2029)	748 (748)	10.56	1
681	Jeypore-Malkanagiri New Railway Line Project (East Coast Railway [ECoR] - II) (705742)	Odisha	02/2018 (12/2023)	07/2033 (07/2033)	2344 (2344)	225.84	8
682	Talcher-Angul New Line with Y-Connection at Talcher (CAO/C/ECoR) (705743)	Odisha	07/2018 (0)	05/2027 (05/2028)	495 (495)	29.5	1

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
683	Baghuapal Flyover Construction Project (CAO/C/ECoR) (705767)	Odisha	08/2019 (10/2022)	03/2028 (03/2028)	257.97 (258)	0.83	0
684	Khurda Road - Balangir Electrification of Railway Track Project (Ministry of Railways) (706898)	Odisha	NA (09/2019)	03/2021 (-)	267.61 (267.61)	0	0
685	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (Indian Railway) (709810)	Odisha	08/2022 (01/2026)	08/2027 (08/2027)	190.9 (190.9)	0	0
686	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION/12.76kms (East Coast Railway [ECoR] - II) (709811)	Odisha	09/2022 (05/2025)	09/2027 (09/2027)	190 (190)	0	0
687	Junagarh Visavadar 42 Kms (Railway) (611980)	Offshore	06/2022 (02/2023)	09/2028 (09/2028)	492.83 (492.83)	3	1
688	Jaynagar-Bijalpura, incl. extn. Bet, Bijalpura-Bardibas [Nepal] (East Central Railway [ECR] - I) (705362)	Offshore	08/2015 (03/2011)	03/2022 (03/2026)	819 (819)	580.6	75
689	Ludhiana- Killa Raipur Railway Doubling Project (Railway) (705783)	Punjab	03/2019 (12/2022)	03/2025 (03/2026)	237.64 (237.64)	118	55
690	Dedicated Test Track for RDSO Phase II (North Western Railway [NWR]) (611614)	Rajasthan	11/2021 (11/2021)	11/2026 (11/2026)	819.48 (967.06)	471	86
691	Devgarh Madariya - Nathdwara Gauge Conversion [82.54 Km] part of Marwar - Mavli Gauge Conversion [152 Km] (North Western Railway [NWR]) (611849)	Rajasthan	01/2023 (01/2023)	06/2028 (06/2028)	968.92 (968.92)	98.62	51
692	Maintenance cum workshop depot for Vande Bharat Sleeper Trains as per conditions under WTA 527 (WPO/Patna) (611929)	Rajasthan	NA (06/2023)	12/2024 (-)	166.86 (166.86)	0	0
693	RINGUS KHATUSHYAMJI NEW LINE (North Western Railway [NWR]) (616696)	Rajasthan	03/2024 (03/2024)	03/2028 (-)	254.06 (254.06)	2.94	0
694	RAS- MERTA CITY NEW LINE INCL BYPASS AT MERTA ROAD (North Western Railway [NWR]) (616840)	Rajasthan	NA (02/2024)	03/2028 (-)	947 (947)	1.36	0
695	PUSHKAR- MERTA CITY NEW LINE (North Western Railway [NWR]) (616841)	Rajasthan	02/2024 (02/2024)	12/2026 (-)	799.64 (799.64)	14.5	4
696	AJMER- CHANDERIYA DOUBLING (North Western Railway [NWR]) (616843)	Rajasthan	02/2024 (02/2024)	06/2027 (-)	1634.79 (1634.79)	74.43	6
697	Dholpur - Sirmuttra Gauge Conversion (North Central Railway) (705482)	Rajasthan	03/2022 (04/2020)	02/2019 (02/2027)	747 (747)	355.13	43
698	Gudha-Thatha Mithri Construction of Railway Track Project (North Western Railway [NWR]) (705752)	Rajasthan	04/2019 (04/2019)	11/2026 (11/2026)	819.48 (967.06)	471	98
699	Sawai Madhopur-Jaipur Railway Line Project (North Western Railway [NWR]) (705912)	Rajasthan	NA (04/2023)	03/2027 (-)	1203.89 (1203.89)	46.07	7
700	Agra Fort-Bandikui Doubling Line Project (CAO/C/NCR) (705919)	Rajasthan	06/2022 (02/2021)	06/2027 (06/2027)	1390 (1390)	123	25
701	Sawaimadhopur Bye Pass Line Project (North Western Railway [NWR]) (706866)	Rajasthan	12/2022 (01/2023)	03/2026 (05/2027)	304 (304)	43.07	44
702	Ph II extension of MRTS from Velachery to St Thomas Mount (Southern Railways [SR] - construction) (400280)	Tamil Nadu	11/2007 (11/2008)	07/2024 (08/2025)	734 (982)	475.73	99
703	Redevelopment of Chennai Egmore Station (Railway) (613002)	Tamil Nadu	NA (10/2022)	03/2026 (-)	842 (842)	340	0
704	Coach Production Factory Upgradation Project (CPM/ICF) (705244)	Tamil Nadu	NA (07/2018)	12/2021 (-)	520 (520)	192.25	0
705	Morappur - Dharmपुरi New Railway Line Project (Southern Railway [SR] - I) (705755)	Tamil Nadu	05/2019 (12/2016)	03/2028 (03/2028)	359 (359)	40	1
706	Doubling between Bhadrachalam Road and Dornakal (South Central Railway [SCR] - II) (616856)	Telangana	NA (04/2025)	04/2029 (-)	770.12 (770.12)	0	0
707	Kazipet Wagon Overhauling Project (RVNL) (705252)	Telangana	NA (07/2017)	12/2023 (-)	385 (385)	0	0
708	Manoharabad-Kothapalli New Rail Line [151 km] (South Central Railway [SCR] - II) (705437)	Telangana	07/2016 (01/2017)	03/2027 (12/2027)	1160 (2781)	1771.32	71
709	Bahraich-Shravasti-Balrampur-Siddharthnagar -Santkabar nagar (North Eastern Railway [NER]) (400204)	Uttar Pradesh	10/2018 (03/2017)	10/2030 (10/2030)	4939.78 (4939.78)	1232.64	8
710	Sahjanwa-Dohrighat (North Eastern Railway [NER]) (400205)	Uttar Pradesh	08/2019 (03/2017)	03/2029 (03/2029)	1319.75 (1319.75)	460.2	3
711	Anandnagar - Ghugli via Maharajganj New line 52.7 km (Construction NER) (617252)	Uttar Pradesh	10/2023 (11/2023)	03/2028 (-)	958.27 (958.27)	436.95	23
712	Chunar-Chopan doubling project (North Central Railway) (617284)	Uttar Pradesh	08/2023 (01/2025)	03/2028 (-)	1423.96 (1423.96)	49.57	2

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
713	Domingarh-Gorakhpur-Gorakhpur Cantt.-Kusumhi - 3rd Railway Line Project (North Eastern Railway [NER]) (705566)	Uttar Pradesh	11/2016 (06/2018)	02/2025 (09/2025)	351 (521.47)	495.86	98
714	Burhwal Gonda 3rd line (North Eastern Railway [NER]) (705567)	Uttar Pradesh	11/2017 (07/2019)	03/2025 (09/2025)	1016 (1118)	1373.8	73
715	Janghai-Pratapgarh- Amethi (CAO/C/II/INR) (705588)	Uttar Pradesh	11/2017 (03/2017)	03/2025 (03/2026)	722 (1194)	1550	70
716	Lalitpur-Birari with flyover at Lalitpur- 16 Km (North Central Railway) (705766)	Uttar Pradesh	03/2017 (03/2017)	12/2024 (11/2025)	304.44 (356)	220.8	72
717	Allahabad-Bamhrauli Flyover Construction & 4th Railway Line Project (North Central Railway) (705771)	Uttar Pradesh	04/2019 (10/2020)	03/2026 (03/2026)	494 (494)	333	70
718	Mughalsarai-Allahabad, 3rd line (North Central Railway) (705772)	Uttar Pradesh	12/2015 (03/2016)	12/2026 (03/2027)	2649 (2649.44)	1561.89	62
719	Aligarh -Daud Khan Flyover Construction & 3rd Railway Line Project (CAO/C/INCR) (705774)	Uttar Pradesh	04/2019 (09/2020)	01/2025 (03/2027)	758 (779.49)	315.37	55
720	Bhandai - Flyover for Etawah bound down train- 10 Km (North Central Railway (NCR) - II) (705777)	Uttar Pradesh	07/2020 (04/2021)	02/2026 (02/2027)	250.18 (250.18)	113.94	3
721	Phephna-Indara, Mau-Shahganj doubling excluding Indara-Mau (South Eastern Railway [SER] - I) (705779)	Uttar Pradesh	05/2017 (03/2017)	12/2024 (03/2026)	1178 (1777)	1489.5	85
722	Bhatni-Aurnihar with electrification excluding Indara-Mau (RVNL - II) (705780)	Uttar Pradesh	03/2018 (03/2017)	12/2024 (10/2025)	2529 (2529.46)	2051.69	94
723	Barabanki-Malhaur 3rd & 4th Railway Line Project (CAO/C/INR) (705782)	Uttar Pradesh	01/2019 (04/2017)	03/2025 (03/2026)	407 (407)	317	75
724	Janghai-Phaphamau Doubling Rail Line Project (RVNL) (705784)	Uttar Pradesh	11/2018 (03/2020)	03/2025 (03/2025)	357 (978.77)	579	95
725	Bahraich - Nanpara - Nepalganj Road Gauge Conversion (North Eastern Railway [NER]) (705863)	Uttar Pradesh	07/2020 (04/2021)	07/2025 (09/2025)	950 (550)	511.18	90
726	Allahabad division - Aligarh - Harduaganj Flyover (North Central Railway) (705918)	Uttar Pradesh	04/2020 (02/2021)	06/2026 (03/2027)	1457 (1457)	50	14
727	DOUBLING BETWEEN JAUNPUR JN-ZAFFARABAD [6.28 KM] (Northen Railway [NR]) (900872)	Uttar Pradesh	01/2023 ()	01/2027 (12/2028)	177 (177)	41	10
728	Rishikesh-Karnaprayag New Rail Line- 125 km (RVNL - II) (705429)	Uttarakhand	11/2016 (08/2018)	12/2025 (03/2027)	38953 (38953)	24645.15	65
729	Kalinarayanpur-Krishnanagar Doubling Alongwith Krishnanagar - Chapra New Line. And Naihati-Ranaghat 3rd Line. (Eastern Railway [ER] - I) (400247)	West Bengal	07/2015 (11/2005)	02/2027 (02/2027)	1000 (1000)	1031.21	67
730	Tarakeshwar-Bishnupur New Line [82.47 km] (Eastern Railway [ER] - I) (400273)	West Bengal	03/2001 (02/2008)	03/2019 (02/2026)	1189 (1542)	1307.52	90
731	Dum Dum Airport-New Garia via Rajarhat-Construction of Metro Railway (RVNL - II) (400277)	West Bengal	03/2010 (10/2011)	12/2025 (03/2026)	8964 (8964)	8097.47	80
732	Construction of Balurghat-Hilli new BG Line (Northeast Frontier Railway [NFR]) (612096)	West Bengal	12/2010 (12/2010)	03/2027 (03/2025)	1209 (1209)	405.31	9
733	Kalipahari Bakhtarnagar 5th line (Eastern Railway [ER] - I) (617322)	West Bengal	08/2024 (07/2025)	06/2027 (06/2027)	350.46 (350.46)	0	0
734	Joka-BBD Bag new metro project (RVNL - II) (705730)	West Bengal	03/2010 (04/2010)	12/2026 (12/2028)	4835 (10362)	4373.24	60
735	Noapara-Barasat via Bimanbandar - Construction of Metro railway [18 km] (Metro Railway, Kolkata) (706776)	West Bengal	11/2010 (03/2010)	08/2026 (03/2029)	4830 (4830)	2764.13	32
736	Baranagar-Barrackpore and Dakshineshwar- Construction of Metro Railway (RVNL - II) (706777)	West Bengal	03/2010 (03/2010)	12/2026 (12/2025)	2298 (2734)	393	17
Total (263)					691320.92	524256.16	
Department for Promotion of Industry & Internal Trade							
Real Estate							
737	Krishnapatnam Node - Phase 1 - Roads and Services Development (National Industrial Corridor Development Corporation) (701658)	Andhra Pradesh	12/2020 (02/2024)	02/2028 (-)	2139.44 (2139.44)	406.05	17
738	Tumakuru Node - Phase 1 - Roads and Services Development (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (701657)	Karnataka	12/2020 (02/2023)	09/2026 (-)	1701.81 (1701.81)	88.25	8
Total (2)					3841.25	494.3	
Department of Telecommunications							
Telecommunication							
739	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance (Erstwhile NICF)) (709859)	Delhi	10/2014 (04/2018)	02/2020 (10/2025)	248.2 (248.2)	236.91	98

All Ongoing Projects							
AUGUST 2025							
SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
740	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya <i>(Department of Telecommunications [DoT])</i> (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (09/2025)	971.96 (971.96)	208.25	99
741	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 <i>(Department of Telecommunications [DoT])</i> (701599)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	NA (09/2021)	03/2023 (11/2025)	1577.57 (1577.57)	598.31	87
742	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha <i>(Department of Telecommunications [DoT])</i> (701602)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	11/2021 (05/2022)	11/2023 (11/2025)	3685 (3685)	1101.44	79
743	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam <i>(Department of Telecommunications [DoT])</i> (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (09/2025)	1255.49 (1255.49)	284.04	89
744	354 Uncovered Villages Scheme <i>(Department of Telecommunications [DoT])</i> (701600)	Multi-States (Bihar, Gujarat, Himachal Pradesh, Jammu and Kashmir, Ladakh, Rajasthan, Uttar Pradesh)	12/2019 (04/2020)	10/2021 (08/2025)	336.89 (301.13)	227.82	97
745	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajastha and Uttar Pradesh <i>(Department of Telecommunications [DoT])</i> (704495)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	NA (03/2021)	03/2022 (12/2025)	421.65 (228.94)	134.08	96
746	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART <i>(BSNL)</i> (709749)	Multi-States (Maharashtra, Telangana)	NA (03/2020)	06/2021 (12/2025)	461.42 (461.42)	166.02	81
747	Saturation 4G mobile coverage of Uncovered Villages through USOF <i>(Department of Telecommunications [DoT])</i> (400013)	PAN India	07/2022 (07/2022)	06/2024 (03/2026)	26316 (30620)	9791.8	73
748	4G Services by BSNL <i>(Department of Telecommunications [DoT])</i> (701593)	PAN India	11/2020 (11/2020)	03/2024 (03/2026)	28466 (19592)	8390.32	96
749	BharatNet <i>(Department of Telecommunications [DoT])</i> (706775)	PAN India	07/2017 (10/2011)	08/2023 (03/2027)	61109 (188000)	41486.14	81
750	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT <i>(BSNL)</i> (709856)	PAN India	NA (05/2023)	08/2024 (10/2025)	645.13 (645.13)	364.34	91
751	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. <i>(BSNL)</i> (709857)	PAN India	NA (06/2023)	06/2025 (03/2026)	24544.55 (24544.5)	8391.17	96
752	OPTICAL TRANSPORT NETWORK [OTN] PH-4 IN BSNL <i>(BSNL)</i> (709858)	PAN India	NA (02/2024)	08/2025 (10/2025)	810.99 (810.99)	741.9	100
	Total (14)				150849.85	72122.54	
	Department of Water Resources, River Development & GR						
	Waste & Water						
753	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616600)	Bihar	10/2017 (03/2022)	02/2025 (12/2025)	413.29 (413.29)	126.67	97
754	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616611)	Bihar	08/2017 (07/2019)	12/2025 (-)	824 (824)	396.71	56
755	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh-Patna under Hybrid annuity based PPP mode-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616612)	Bihar	08/2017 (07/2019)	12/2025 (-)	578.89 (578.89)	171.79	54
756	Sewer Network, SPS and STP at Begusarai <i>(National Mission for Clean Ganga)</i> (616615)	Bihar	03/2010 (03/2018)	04/2025 (12/2025)	230.06 (230.06)	261.82	97
757	Sewer Networks, SPS and STP at Hajipur <i>(National Mission for Clean Ganga)</i> (616616)	Bihar	03/2010 (03/2018)	06/2025 (12/2025)	305.19 (305.19)	346.46	95
758	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616594)	Uttar Pradesh	05/2020 (04/2023)	04/2025 (12/2025)	842.25 (842.25)	208.64	73
759	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP <i>(National Mission for Clean Ganga)</i> (616605)	Uttar Pradesh	05/2020 (11/2024)	12/2024 (05/2027)	690.71 (690.71)	34.79	27
760	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP <i>(National Mission for Clean Ganga)</i> (616604)	West Bengal	05/2018 (12/2021)	03/2025 (12/2025)	154.73 (154.73)	96.17	92

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (8)				4039.12	1643.05	
	Water Resources						
761	Sardar Gouthu Latchanna Thotapalli Barrage Project (<i>Water Resources-AP</i>) (400100)	Andhra Pradesh	NA (01/2006)	12/2019 (06/2026)	353.05 (1023.24)	869.11	95
762	Gundlakamma project (<i>Water Resources-AP</i>) (400101)	Andhra Pradesh	NA (04/2005)	12/2019 (03/2027)	397.41 (697.39)	610.89	98
763	Polavaram Irrigation Project (<i>Water Resources-AP</i>) (701415)	Andhra Pradesh	02/2009 (11/2004)	04/2022 (03/2026)	10151.04 (55548.9)	24347.76	83
764	Borolia Irrigation Project (<i>Department of Water Resources, River Development & GR</i>) (701370)	Assam	NA (12/1996)	12/2022 (03/2026)	256.16 (256.16)	0	55
765	Punpun Barrage Project (<i>Water Resources-BR</i>) (400104)	Bihar	NA (04/2007)	12/2019 (03/2026)	571.07 (658.12)	469.66	44
766	Durgawati Reservoir Project (<i>Irrigation and CAD-TG</i>) (701371)	Bihar	NA (04/1997)	12/2019 (12/2024)	691.15 (971.96)	978.51	87
767	Kelo Irrigation Project (<i>Water Resources-CT</i>) (400111)	Chhattisgarh	NA (04/2008)	12/2019 (06/2026)	459.97 (727.04)	616.93	71
768	Kudali Irrigation Project (<i>Department of Water Resources, River Development & GR</i>) (701399)	Chhattisgarh	NA (12/2009)	12/2025 (-)	382.29 (382.29)	0	86
769	Sardar Sarovar CADWM Project (<i>Narmada and Water Resources, Water Supply and Kalpsar Department-GJ</i>) (400097)	Gujarat	NA (04/2004)	12/2019 (03/2025)	5021.76 (6670.31)	4954.99	90.3
770	Sardar Sarovar Project (<i>Narmada and Water Resources, Water Supply and Kalpsar Department-GJ</i>) (701372)	Gujarat	NA (04/1996)	12/2019 (12/2025)	20718.17 (33412.5)	31767.59	93
771	Subernarekha Multipurpose Project, Jharkhand (<i>Department of Water Resources-JH</i>) (701376)	Jharkhand	NA (01/2012)	12/2019 (03/2026)	3807.77 (9579.58)	5561.97	69
772	Upper Tunga Irrigation Project (<i>Water Resources-KA</i>) (701377)	Karnataka	NA (04/2014)	12/2019 (12/2025)	770.16 (1606.07)	1511.22	99
773	Omkareshwar CADWM Project (<i>Water resource-mp</i>) (400096)	Madhya Pradesh	NA (04/2015)	12/2019 (03/2026)	648.09 (648.09)	172.56	3
774	Bargi Diversion Project Phase - IV [km. 154 to km 197] (<i>Water Resources-MP</i>) (400115)	Madhya Pradesh	NA (01/2009)	12/2019 (03/2025)	751.03 (893.35)	746.19	75
775	Bargi Diversion Project Phase - III [km. 104 to km 154] (<i>Water Resources-MP</i>) (400116)	Madhya Pradesh	NA (04/2007)	12/2019 (12/2025)	1229.15 (1399.7)	1807.2	79
776	Gosikhurd CADWM Project (<i>Department of water resources-MH - II</i>) (400095)	Maharashtra	04/2017 (04/2017)	12/2019 (06/2026)	743.73 (743.73)	252	50
777	Urmodi Irrigation Project (<i>Department of water resources-MH - II</i>) (400105)	Maharashtra	NA (04/2018)	06/2022 (12/2026)	580.79 (895.81)	713.46	76
778	Sulwade-Jamphal-Kanoli Lift Irrigation Scheme (<i>Department of water resources-MH - II</i>) (400107)	Maharashtra	NA (02/2019)	06/2023 (06/2027)	2407.67 (2407.67)	2436.43	80
779	Purna Barrage-2 [Ner Dhamana] Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (400109)	Maharashtra	NA (04/2018)	06/2020 (06/2026)	848.07 (888.43)	690.49	69
780	Jigaon Irrigation Project (<i>Department of water resources-MH - II</i>) (400112)	Maharashtra	NA (04/2018)	06/2028 (-)	7222.95 (7222.95)	8501.45	90
781	Waghur Project (<i>Department of water resources-MH - II</i>) (701383)	Maharashtra	NA (04/1996)	12/2019 (03/2026)	1058.99 (1758.51)	1530.45	89
782	Gosikhurd Project (<i>Department of water resources-MH - II</i>) (701386)	Maharashtra	12/2017 (04/2008)	12/2019 (06/2026)	7196.47 (12770.1)	13533.29	72
783	Aruna Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (701391)	Maharashtra	NA (01/2010)	12/2019 (12/2025)	210.45 (1472.14)	1697.94	97
784	Lower Pedhi Project (<i>Department of water resources-MH - II</i>) (701396)	Maharashtra	NA (04/2008)	12/2019 (06/2026)	255.97 (1480.7)	1324.78	64
785	Nardave Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (701398)	Maharashtra	NA (04/2009)	12/2019 (06/2026)	211.46 (781.85)	623.5	72
786	Thoubal Multipurpose Project (<i>Water Resources Department-MN</i>) (701400)	Manipur	01/2022 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
787	North Koel Reservoir Project (<i>Department of Water Resources, River Development & GR</i>) (701412)	Multi-States (Bihar, Jharkhand)	NA (01/2021)	03/2021 (03/2026)	1622.27 (2430.76)	142.1	32
788	Integrated Anandpur Barrage Project (<i>Water Resources-OR</i>) (603945)	Odisha	NA (01/1998)	12/2019 (06/2026)	567.03 (2990.05)	2629.74	62
789	Kanupur Irrigation Project (<i>Irrigation and CAD-TG</i>) (701404)	Odisha	NA (01/2004)	12/2019 (12/2024)	989.43 (2301.28)	2563.56	79
790	Relining of Rajasthan feeder and Sirhind Feeder canal (<i>Department of Water Resources-PB</i>) (701410)	Punjab	02/2016 (04/2018)	06/2021 (06/2026)	1441.26 (2462.16)	3000.36	80

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
791	Shahpur Kandi Dam Project (Department of Water Resources-PB) (701411)	Punjab	02/2010 (04/2018)	06/2022 (10/2025)	2285.81 (2715.7)	2072.33	80
792	Sri Ram Sagar Project Stage - II (Irrigation and CAD-TG) (400102)	Telangana	NA (04/2005)	12/2019 (03/2026)	736.13 (949.87)	940.7	96
793	Indiramma Flood Flow Canal Project (Irrigation and CAD-TG) (400103)	Telangana	NA (01/2006)	12/2019 (12/2026)	1331.3 (5940.09)	4491.08	92
794	J. Chokka Rao Devadula Lift Irrigation Scheme (Irrigation and CAD-TG) (701405)	Telangana	NA (04/2006)	12/2019 (12/2025)	8200.71 (14730)	4558.89	87
795	Rajiv Bhima Lift Irrigation Scheme (Irrigation and CAD-TG) (701406)	Telangana	NA (01/2008)	12/2019 (03/2026)	1402 (2509.66)	1839.76	100
796	Saryu Nahar CADWM Project (Irrigation & Water Resources-UP) (400093)	Uttar Pradesh	NA (04/2017)	12/2019 (03/2026)	1672.7 (1672.7)	0	0
797	Arjun Sahayak Project (Irrigation & Water Resources-UP) (400117)	Uttar Pradesh	NA (04/2009)	12/2019 (12/2019)	741.38 (2465.68)	3218.3	100
798	Morna [Gureghar] Irrigation Project (Department of Water Resources, River Development & GR) (701395)	Uttar Pradesh	NA (12/2007)	12/2025 (-)	219.9 (219.9)	0	0
799	Madhya Ganga canal Phase-II (Irrigation & Water Resources-UP) (701408)	Uttar Pradesh	NA (07/2007)	12/2019 (12/2025)	1060.67 (4417.21)	4415.24	82
800	Jamrani Dam Multipurpose Project (Irrigation-UK) (613787)	Uttarakhand	10/2023 (04/2023)	06/2029 (-)	2584.1 (2584.1)	968.52	16
Total (40)					93248.95	138396.86	



सत्यमेव जयते

Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.ipm.mospi.gov.in>
