



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation

477th Flash Report on Central Sector Infrastructure Projects



Scan the QR code to access
the PAIMANA Portal.

(Rs. 150 crore
& above)

JULY 2025



CONTENTS

I. Overview*	2-4
II. North Eastern Region	5-6
III. As per Harmonized Master List (HML) 2022	7-13
IV. Major Infrastructure Central Ministries & Departments	14-19
V. Appendix : <i>List of Tables</i>	20 onwards
Table 1: Ministry-wise Ongoing Projects	
Table 2: State-wise Ongoing Projects	
Table 3: Ongoing Projects of North Eastern Region	
Table 4: All Ongoing Projects	

**Note: This report is web-generated from the PAIMANA portal (ipm.mospi.gov.in) as of July 2025, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies (excluding Ministry of Road Transport & Highways, may reflect from next month onwards) on the IPM portal (indiainvestmentgrid.gov.in) latest by 21st August 2025.*





Overview





Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above

JULY 2025

791 | 14

Ongoing Projects |
Line Ministries & Departments

₹ 23,86,335

Original Cost
(crores)

₹ 28,99,509

Revised Cost
(crores)


₹ 15,10,700

(52.1% of Revised Cost)

Expenditure
(crores)


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

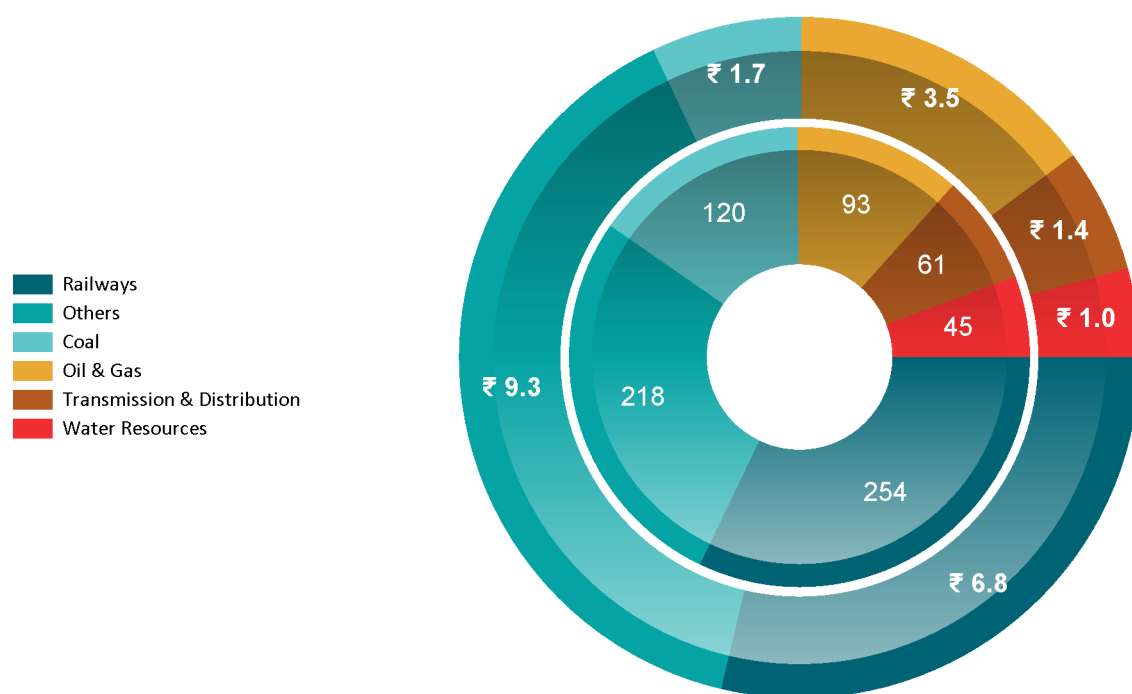


Ministry Comparison : Major Ministries*


[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

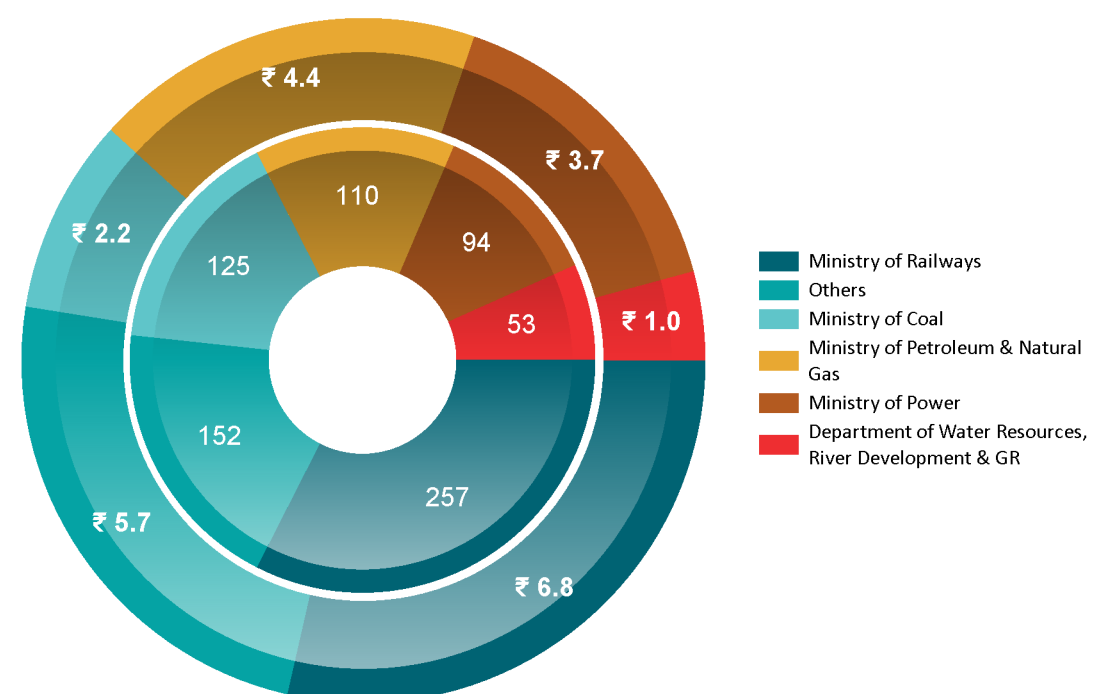

Cost Analytics : Major Sectors*

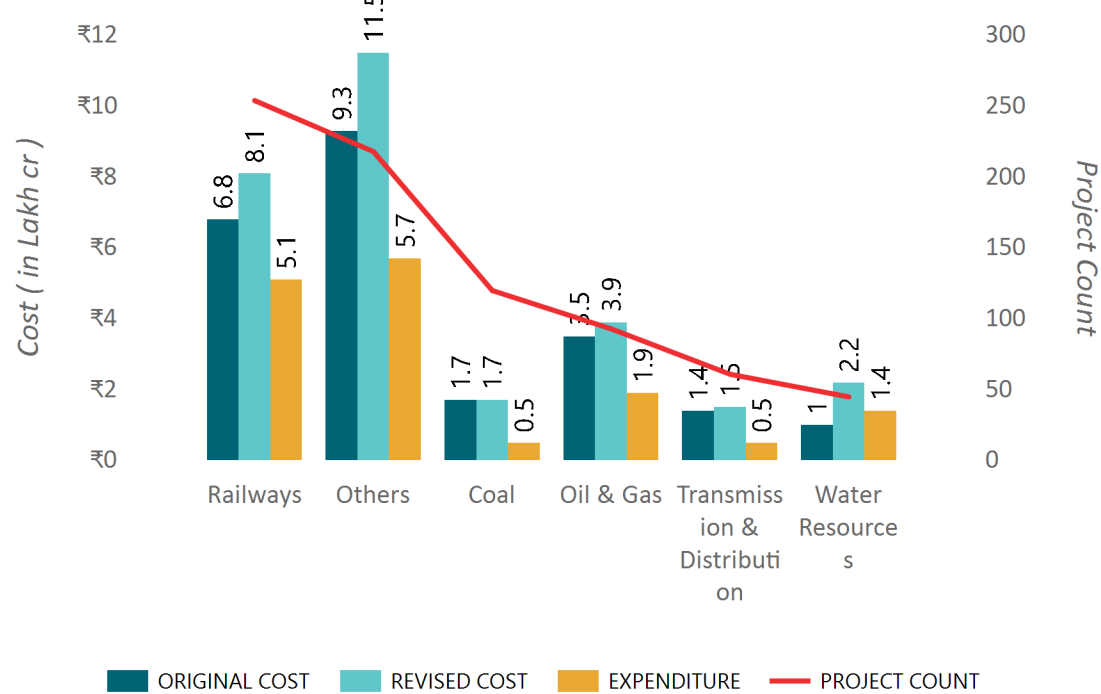


Cost Analytics : Major Ministries*

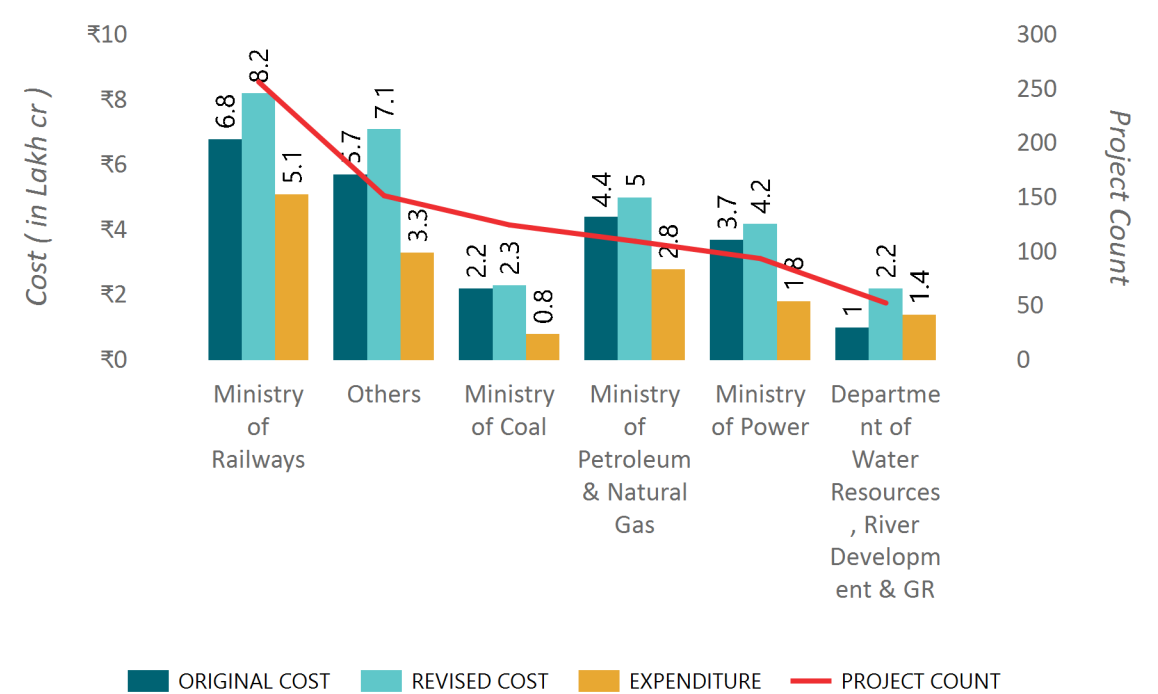


Note: * as per Project Count

Analytics: as per HML

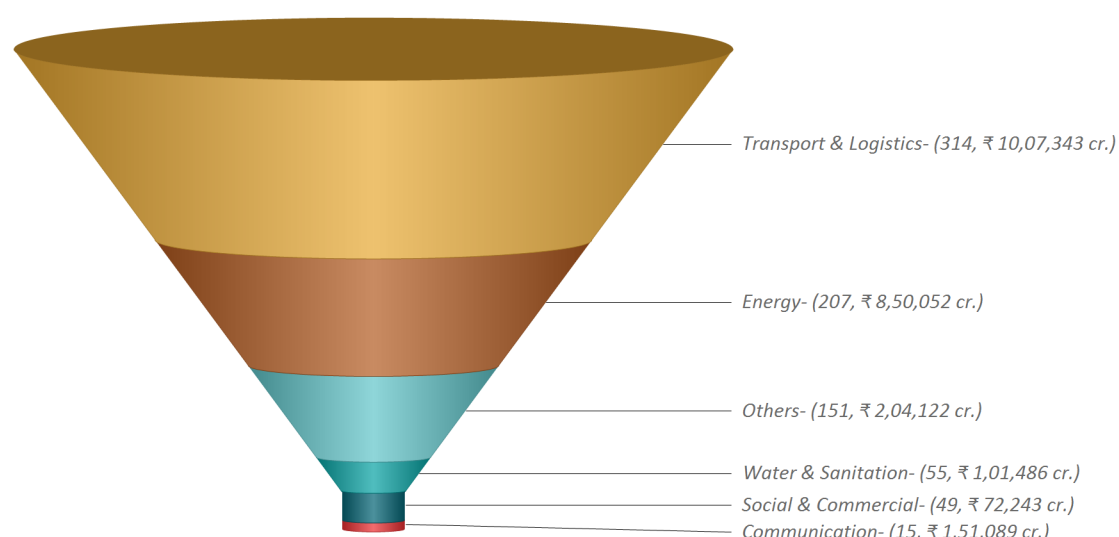


Note: all indicated legends are in format (Project count, Original Cost in crores)

Physical & Financial progress (%) : Project count

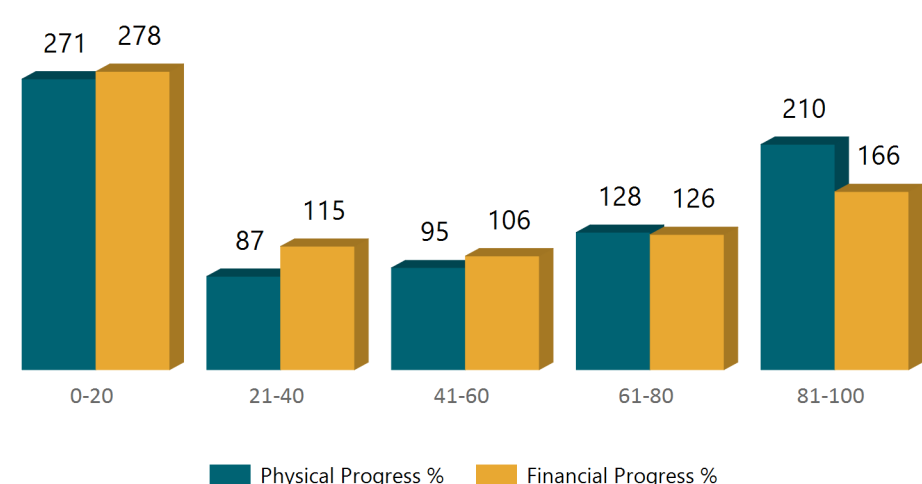




State Comparison : Major States*

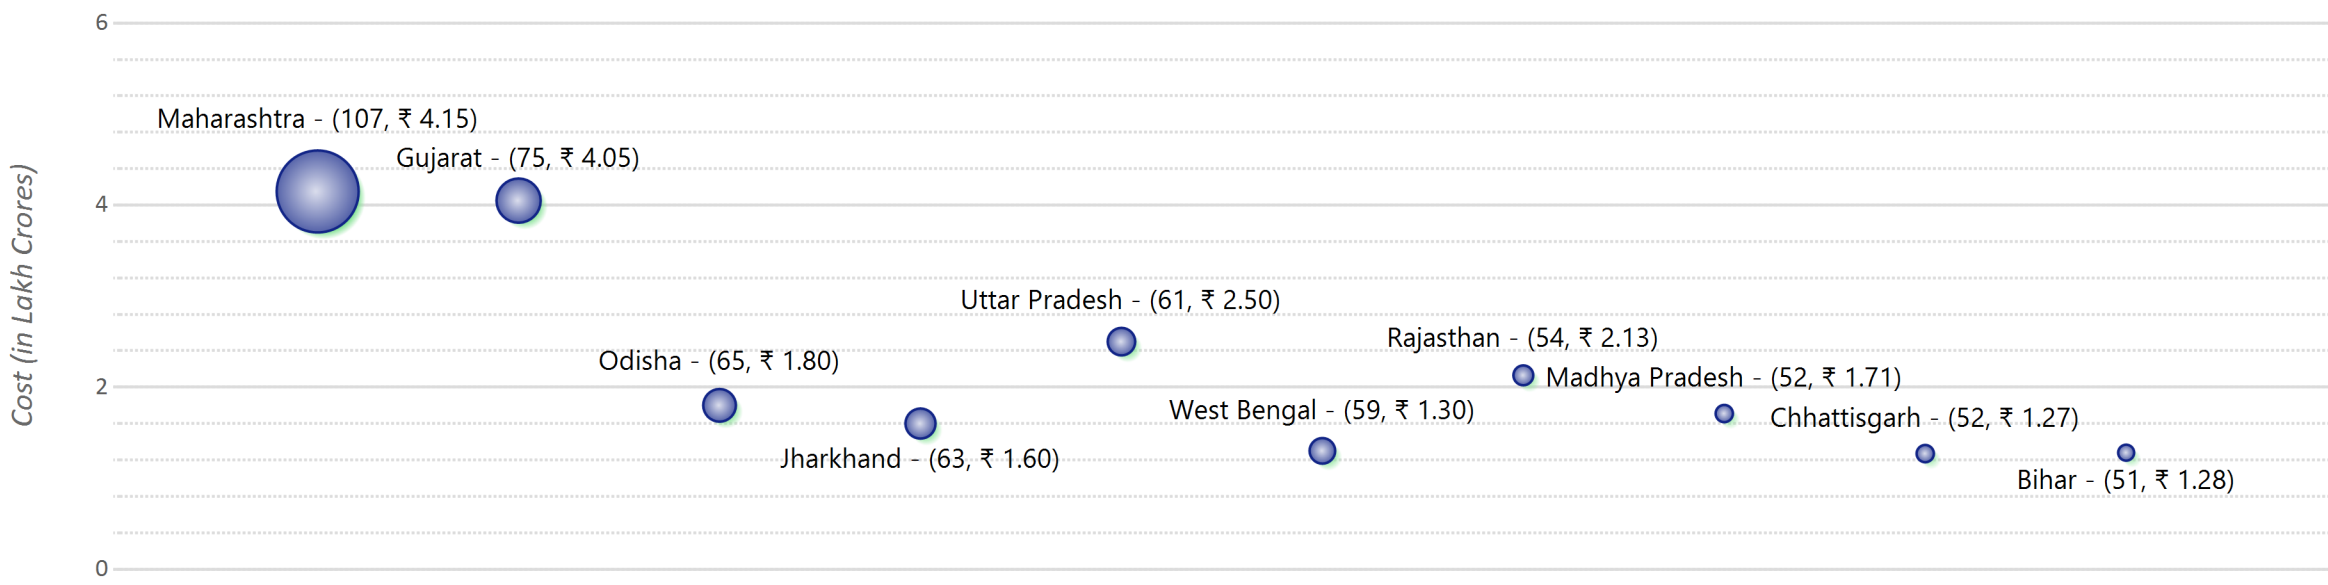


Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count

Ministry-wise Distribution of total 210 projects
with reported Physical Progress between 81-100%

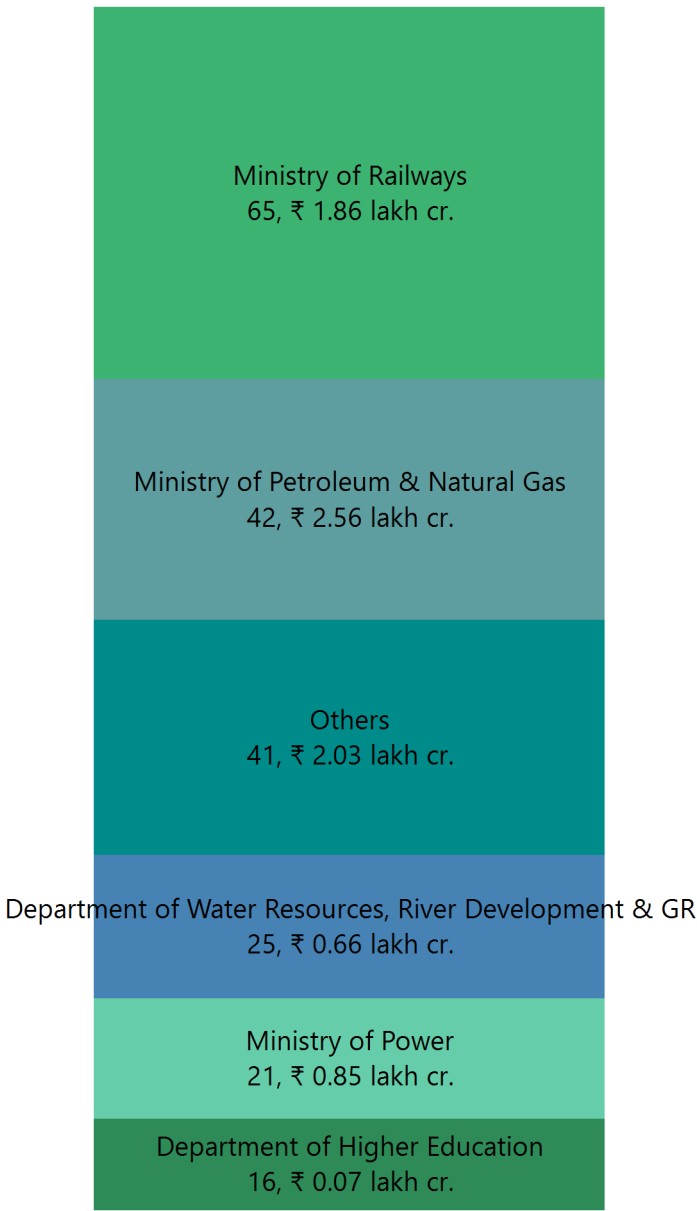

Total Ongoing Projects: Mega & Major

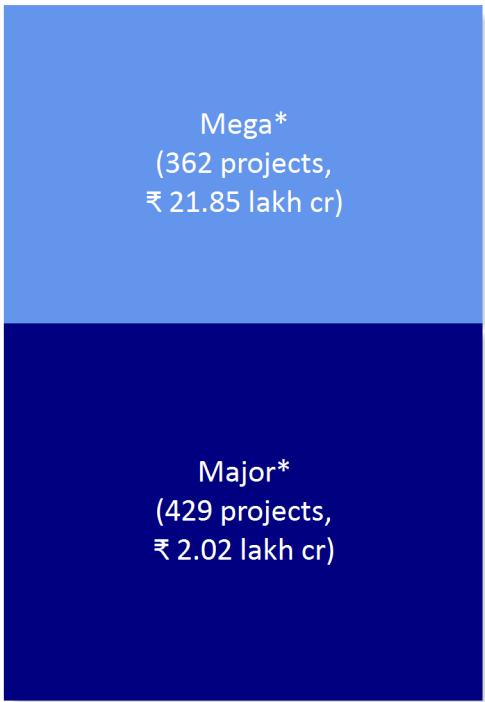


Total North East Region Ongoing Projects: Mega & Major




Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost >= 1000 crore
* Major project if having original cost < 1000 crore

Project volume (nos.)

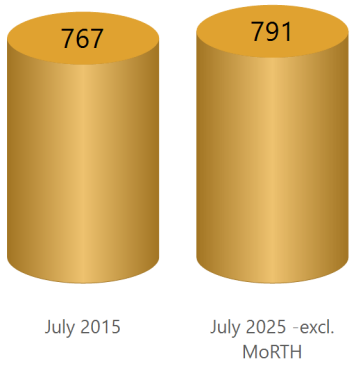


Change in Project Count : +3%

Total Project value (in lakh crore)

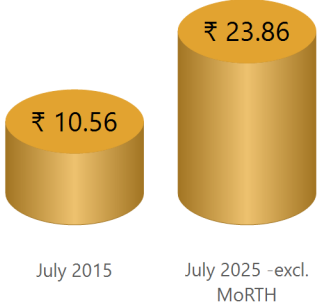

Change in Total Value : +121%

Cumulative Expenditure (in lakh crore)

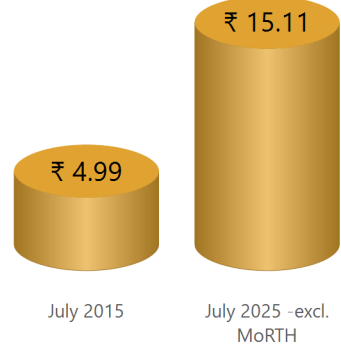

Change in Expenditure : +202%



North Eastern Region





Special Focus : North Eastern Region

JULY 2025

51 | 8

Ongoing Projects |
Line Ministries & Departments

₹ 1,74,842

Original Cost
(crores)

₹ 2,47,094

Revised Cost
(crores)


₹ 1,70,863

(69.15% of Revised Cost)


Expenditure
(crores)

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

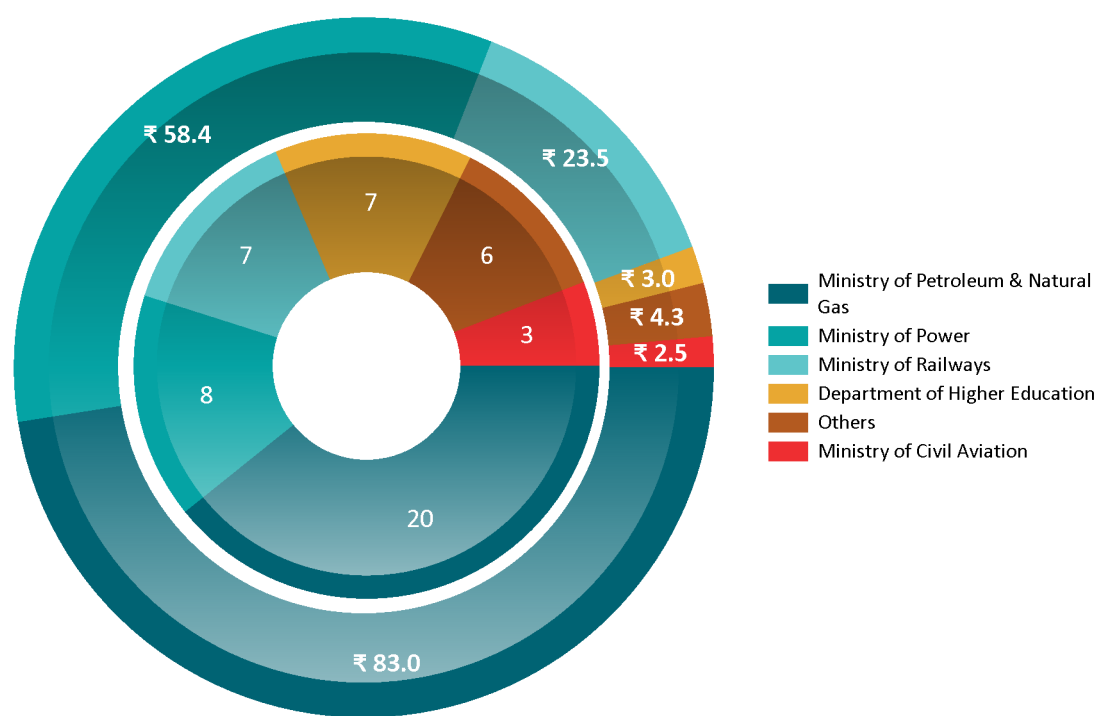


Cost Analytics : Major Ministries*

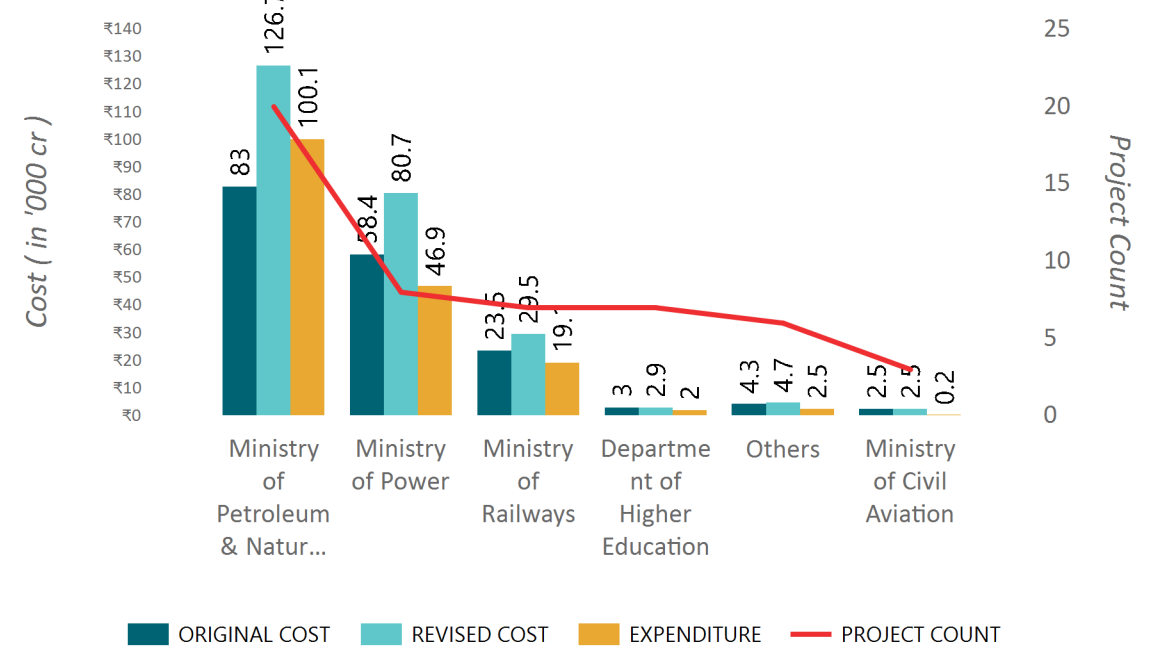


Note: * as per Project Count

Analytics: as per HML

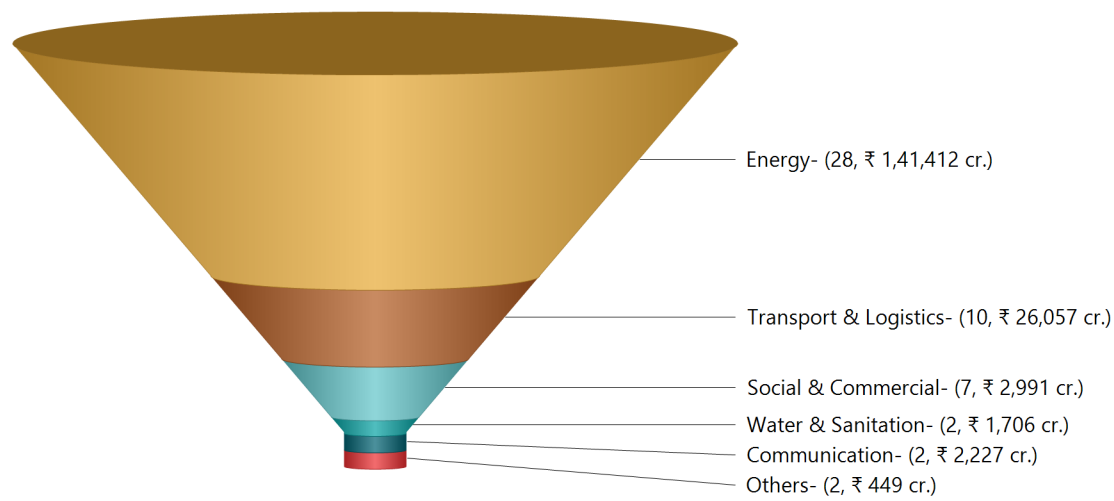


Physical & Financial progress (%) : Project count

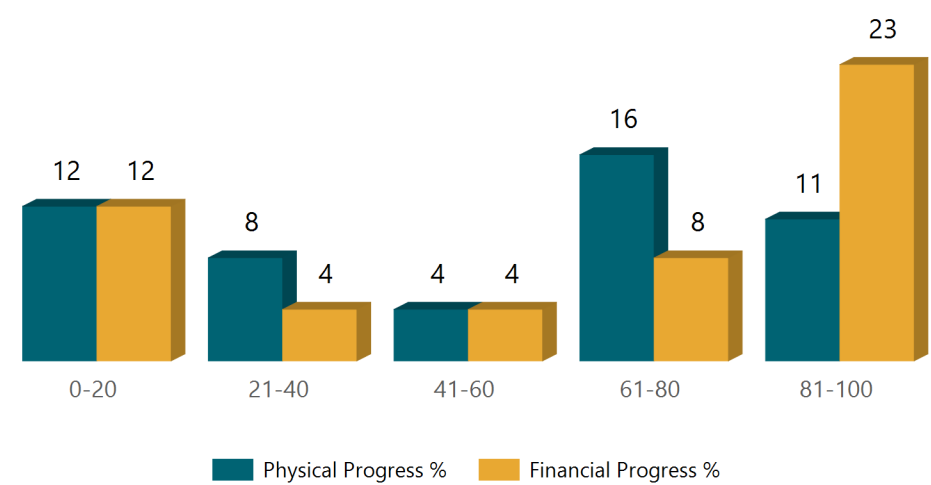

Note: all indicated legends are in format (Project count, Original Cost in crores)

State Comparison : All States

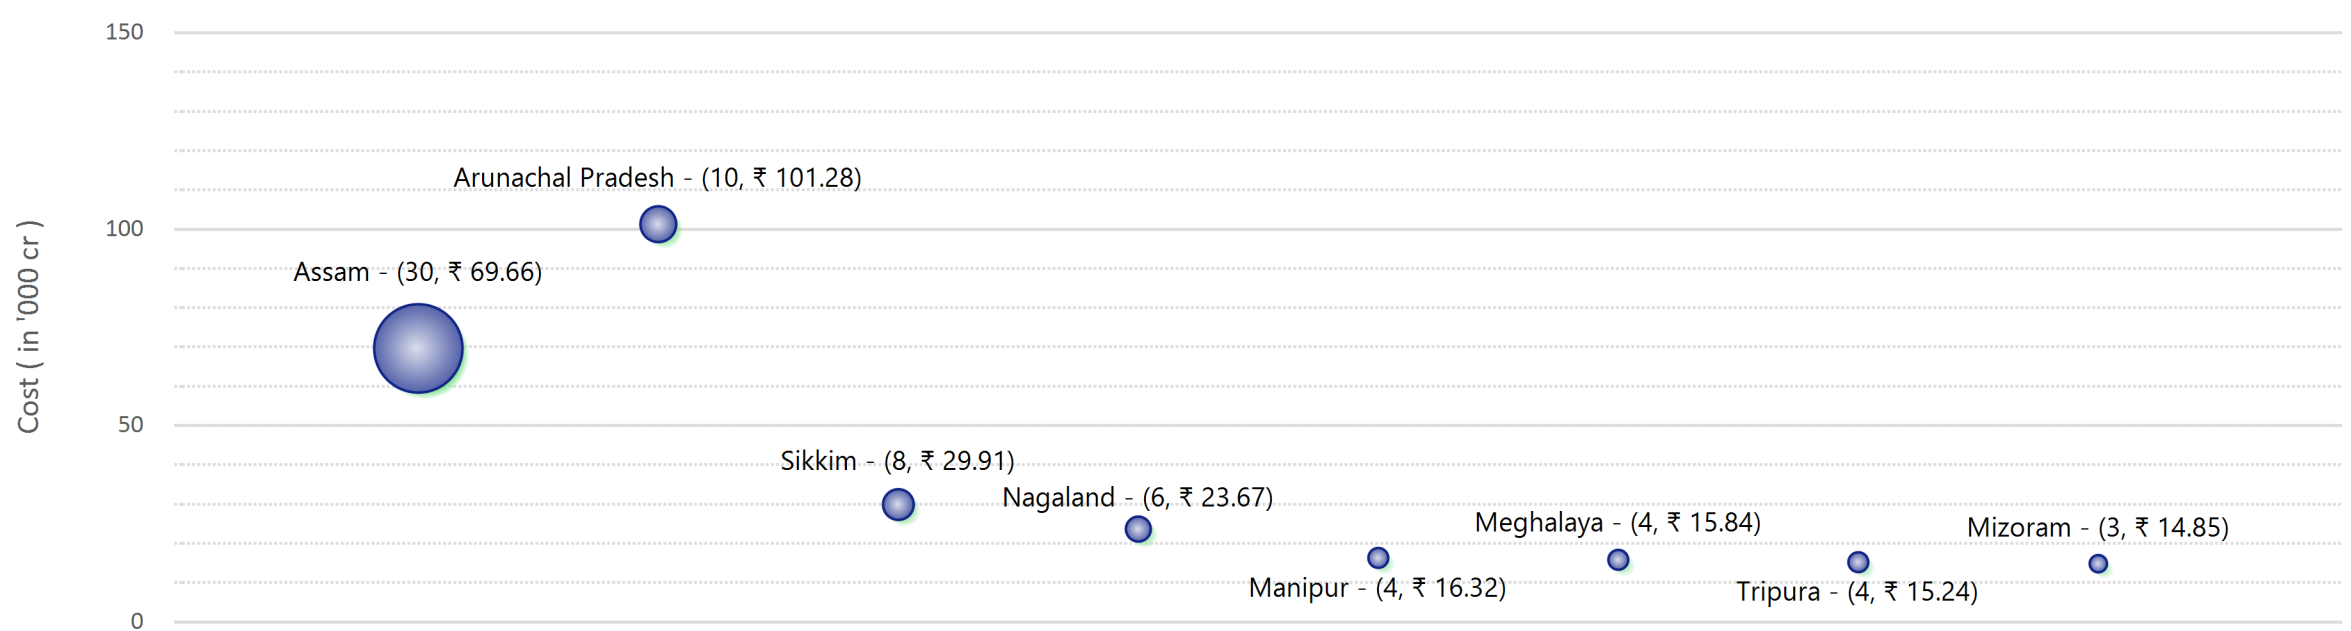

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022



HML Category 1 : Transport & Logistics

JULY 2025


314
Ongoing Projects

₹ 10,07,343
Original Cost
(crores)


₹ 11,52,546
Revised Cost
(crores)

₹ 7,24,223
(62.84% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

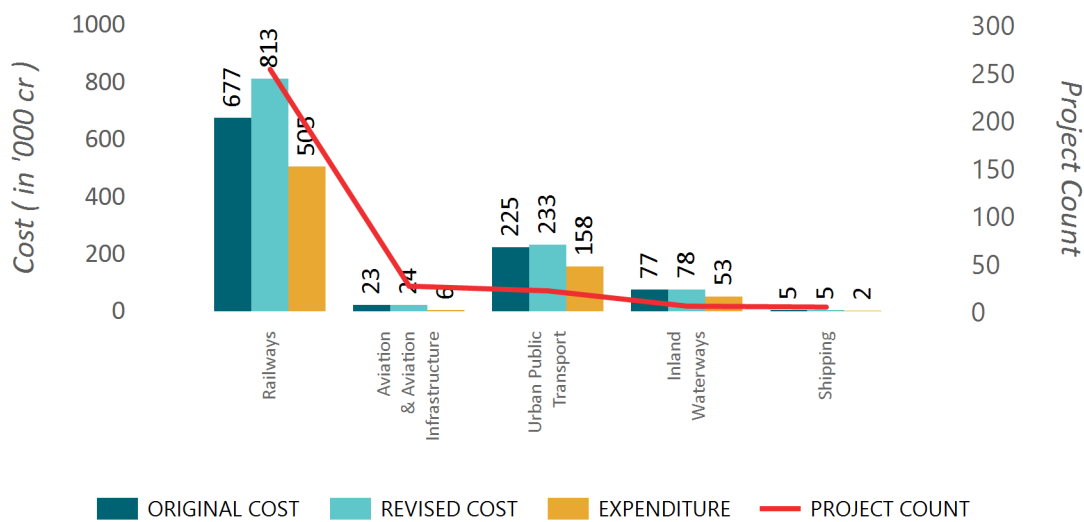

Physical & Financial progress (%) : Project count

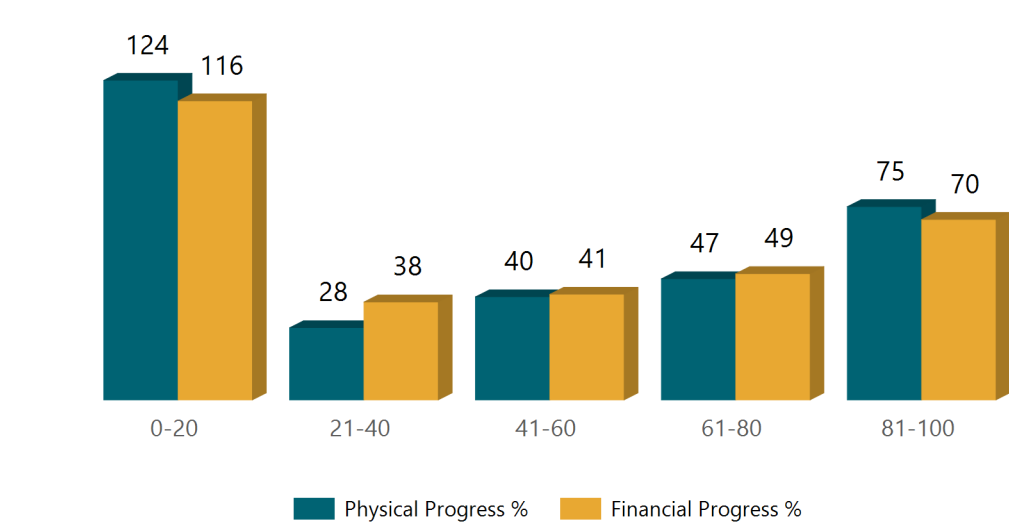

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Railways	254	676,816	813,264	505,345
2	Aviation & Aviation Infrastructure	27	23,265	23,726	5,884
3	Urban Public Transport	22	225,315	232,998	158,062
4	Inland Waterways	6	77,124	77,735	53,119
5	Shipping	5	4,823	4,823	1,812

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	78,691	53
2	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		47,163	0
3	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
4	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
5	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,246	16

HML Category 2 : Energy



JULY 2025

207
Ongoing Projects

₹ 8,50,052
Original Cost
(crores)

₹ 9,69,946
Revised Cost
(crores)

₹ 4,78,496
(49.33% of Revised Cost)
Expenditure
(crores)

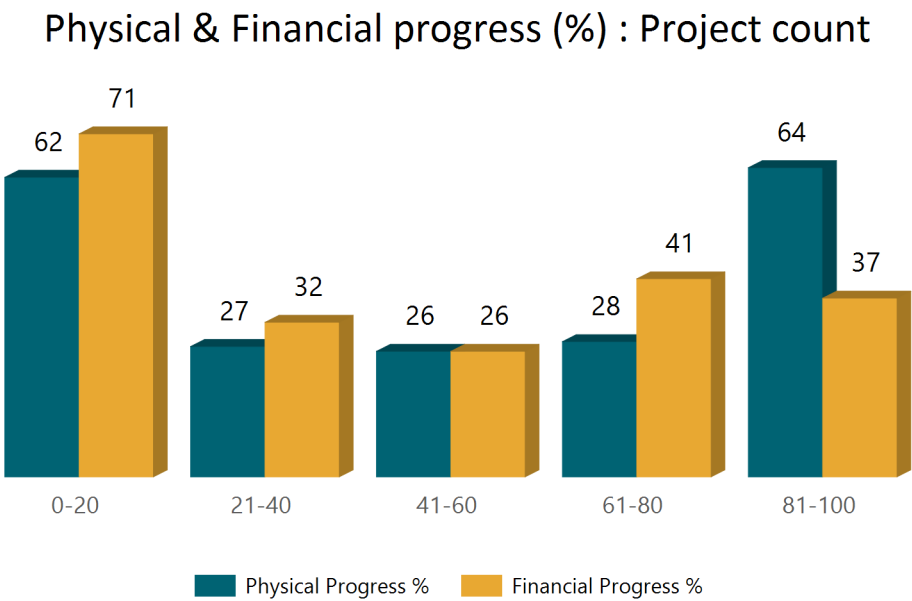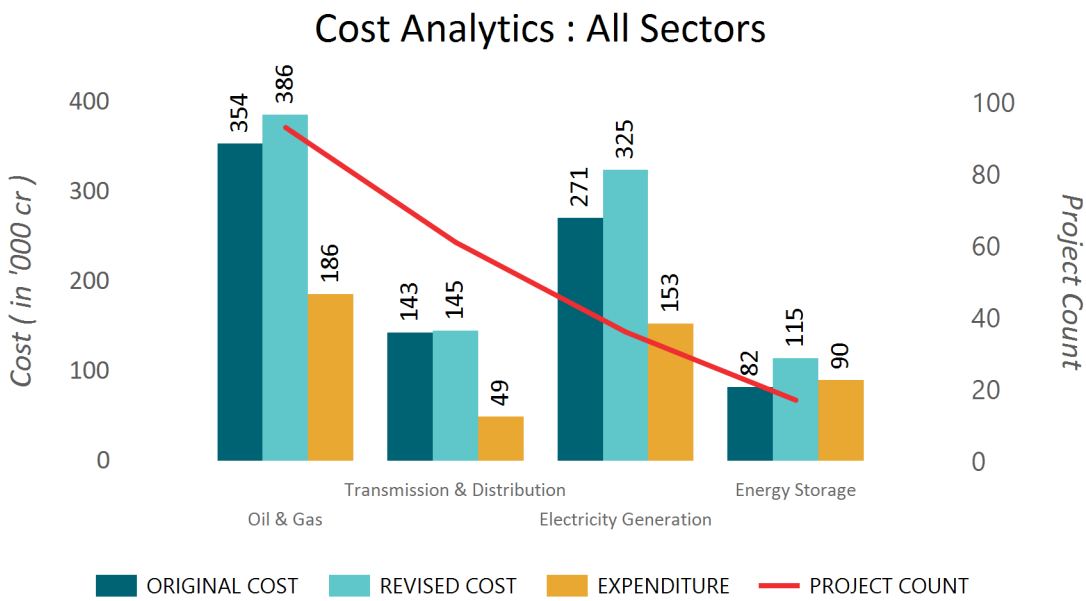

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	93	353,990	385,767	186,037
2	Transmission & Distribution	61	142,977	145,116	49,396
3	Electricity Generation	36	270,930	324,546	152,918
4	Energy Storage	17	82,155	114,517	90,144

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,789	13
2	701263	RAJASTHAN REFINERY PROJECT	43,129	72,937	59,524	87
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA	34,627	36,225	23,977	88
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	35,498	96
5	602182	DIBANG MULTIPURPOSE PROJECT	31,876		3,436	16



HML Category 3 : Water & Sanitation

JULY 2025

55

Ongoing Projects

₹ 1,01,486

Original Cost
(crores)


₹ 2,19,723

Revised Cost
(crores)


₹ 1,44,876

(65.94% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

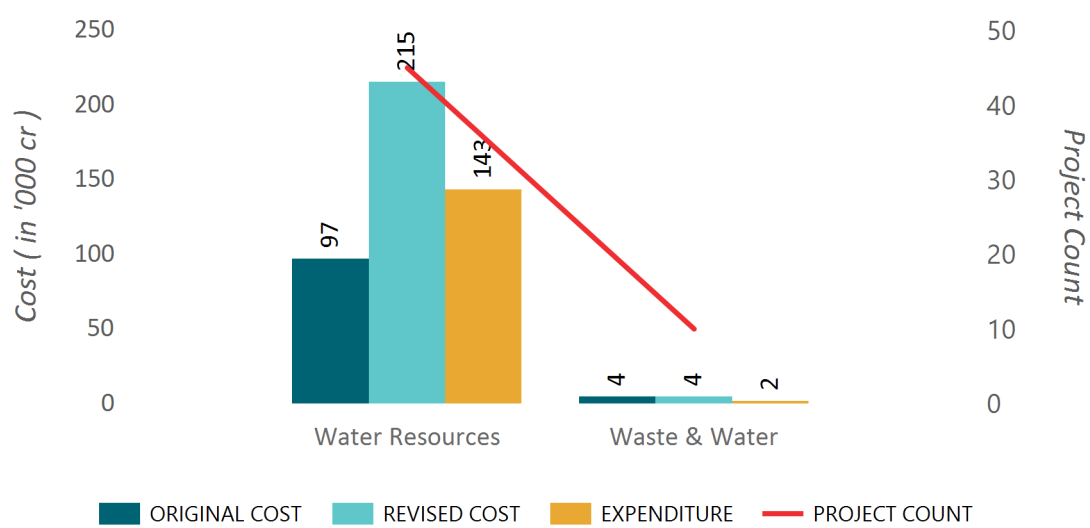

Physical & Financial progress (%) : Project count

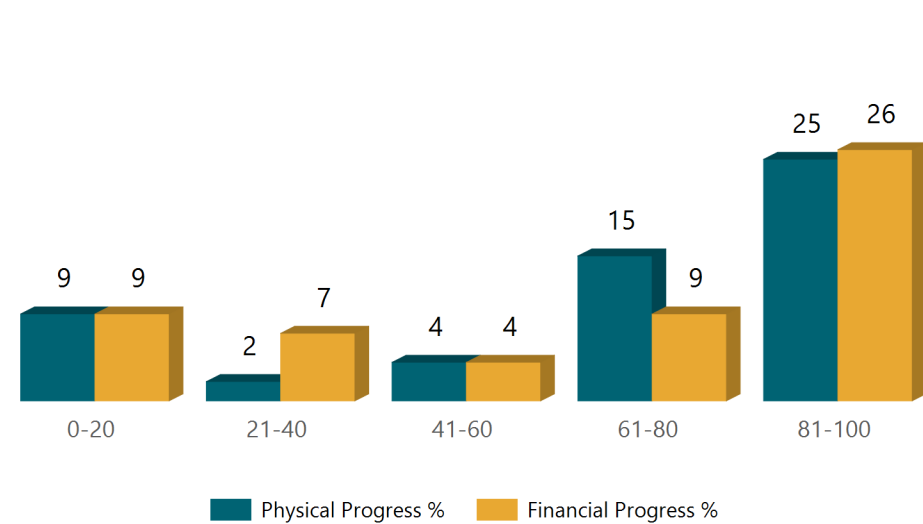

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	45	97,037	215,274	143,186
2	Waste & Water	10	4,449	4,449	1,691

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,768	93
2	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	24,348	83
3	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,559	87
4	400112	JIGAON IRRIGATION PROJECT	7,223		8,501	90
5	701386	GOSIKHURD PROJECT	7,196	12,770	13,533	72

HML Category 4 : Communication

JULY 2025


15
Ongoing Projects

₹ 1,51,089
Original Cost
(crores)


₹ 2,73,182
Revised Cost
(crores)

₹ 71,833
(26.29% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

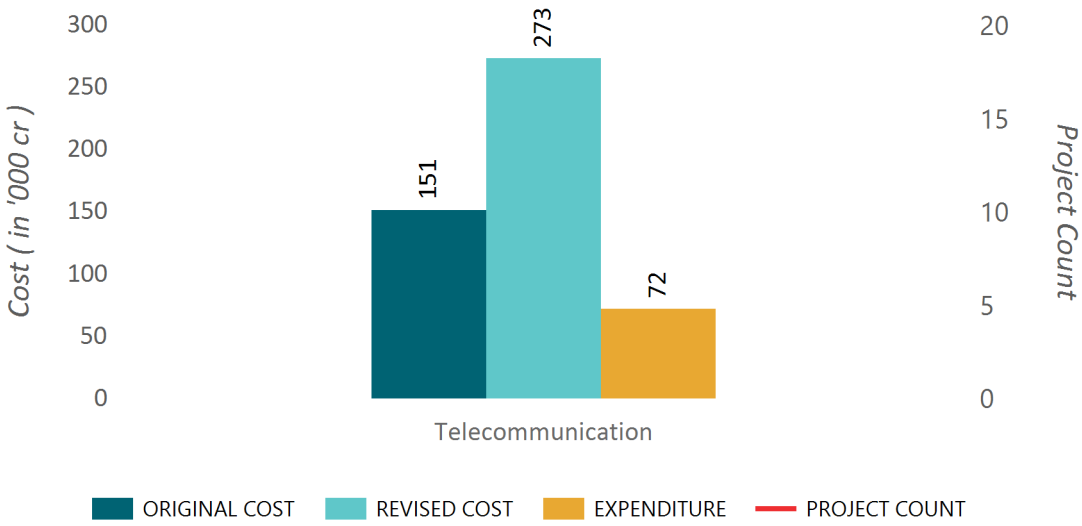

Physical & Financial progress (%) : Project count

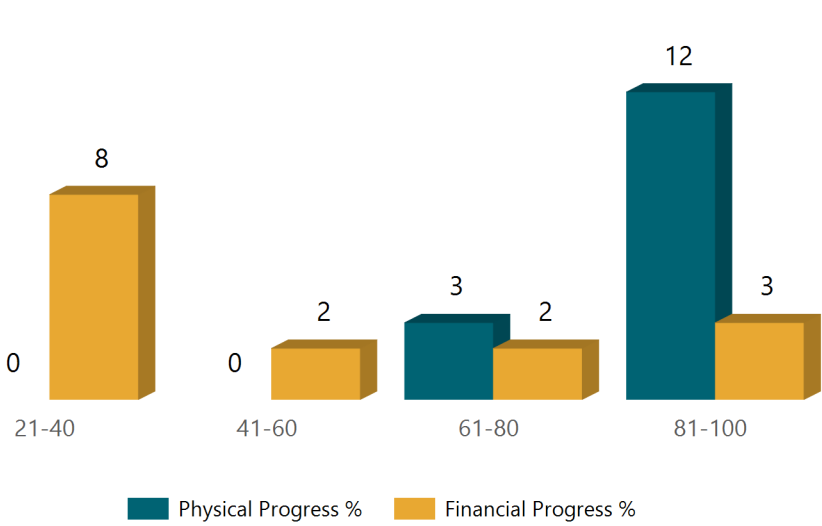

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	15	151,089	273,182	71,833

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	706775	BHARATNET	61,109	188,000	41,486	80.52
2	701593	4G SERVICES BY BSNL	28,466	19,592	8,333	92
3	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	30,620	9,292	72
4	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		8,333	96
5	701602	PROVISION OF 4G BASED MOBILE SERVICES IN 7,287 UNCOVERED VILLAGES OF 44 ASPIRATIONAL DISTRICT ACROSS 5 STATES OF ANDHRA PRADESH, CHHATTISGARH, JHARKHAND, MAHARASHTRA & ODISHA	3,685		1,101	79



HML Category 5 : Social & Commercial

JULY 2025

49

Ongoing Projects

₹ 72,243

Original Cost
(crores)


₹ 73,400

Revised Cost
(crores)


₹ 22,918

(31.22% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

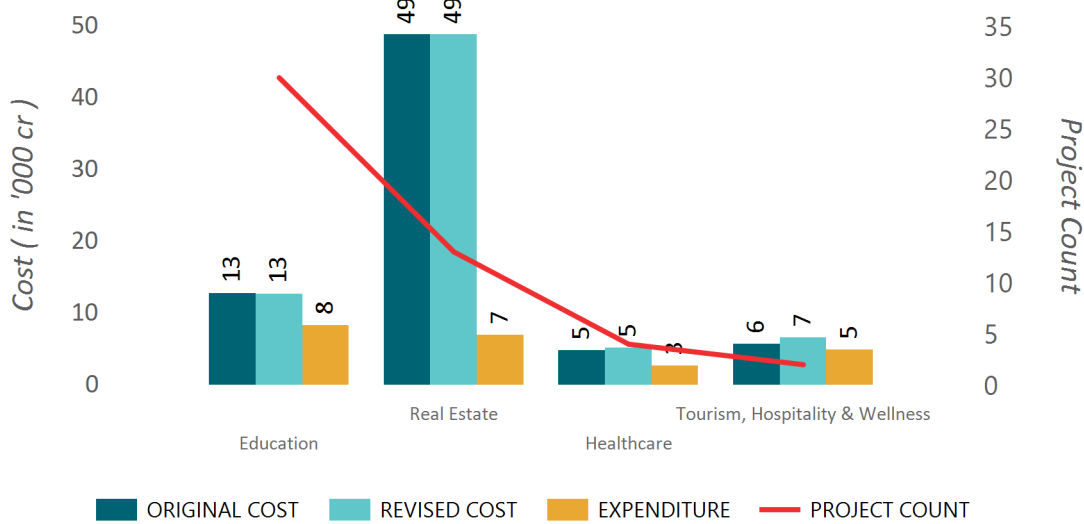

Physical & Financial progress (%) : Project count

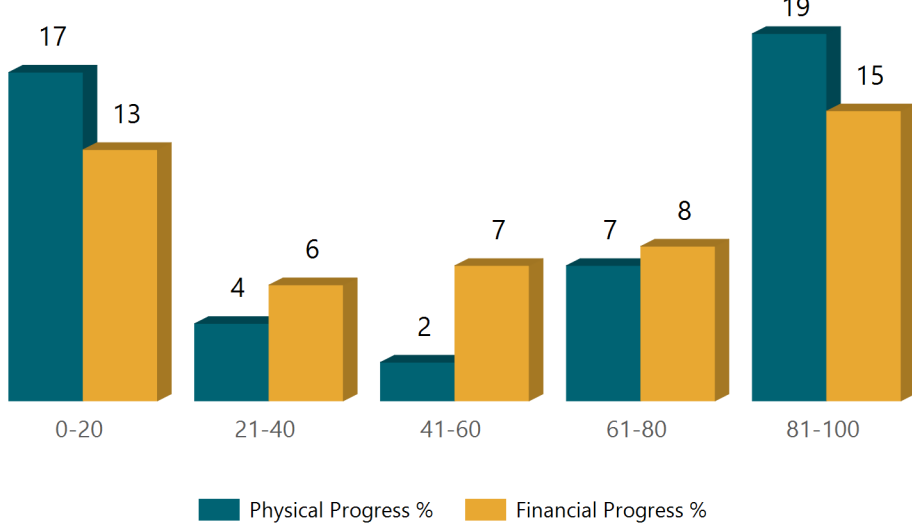

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Education	30	12,754	12,685	8,277
2	Real Estate	13	48,889	48,889	6,979
3	Healthcare	4	4,848	5,186	2,705
4	Tourism, Hospitality & Wellness	2	5,751	6,639	4,957

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850		0	0
2	702540	IN-SITU SLUM REDEVELOPMENT PROJECT IN GUJARAT	5,477		3,036	0
3	400429	EXHIBITION CUM CONVENTION CENTRE DWARKA [PHASE I]	5,178	5,401	4,470	97.4
4	702524	AFFORDABLE HOUSING CONSTRUCTION PROJECT IN CHHATTISGARH	3,798		2,694	0
5	701658	KRISHNAPATNAM NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	2,139		328	14

Other Sectors

JULY 2025


151
Ongoing Projects

₹ 2,04,122
Original Cost
(crores)

₹ 2,10,711
Revised Cost
(crores)

₹ 68,354
(32.44% of Revised Cost)
Expenditure
(crores)

Physical & Financial progress (%) : Project count

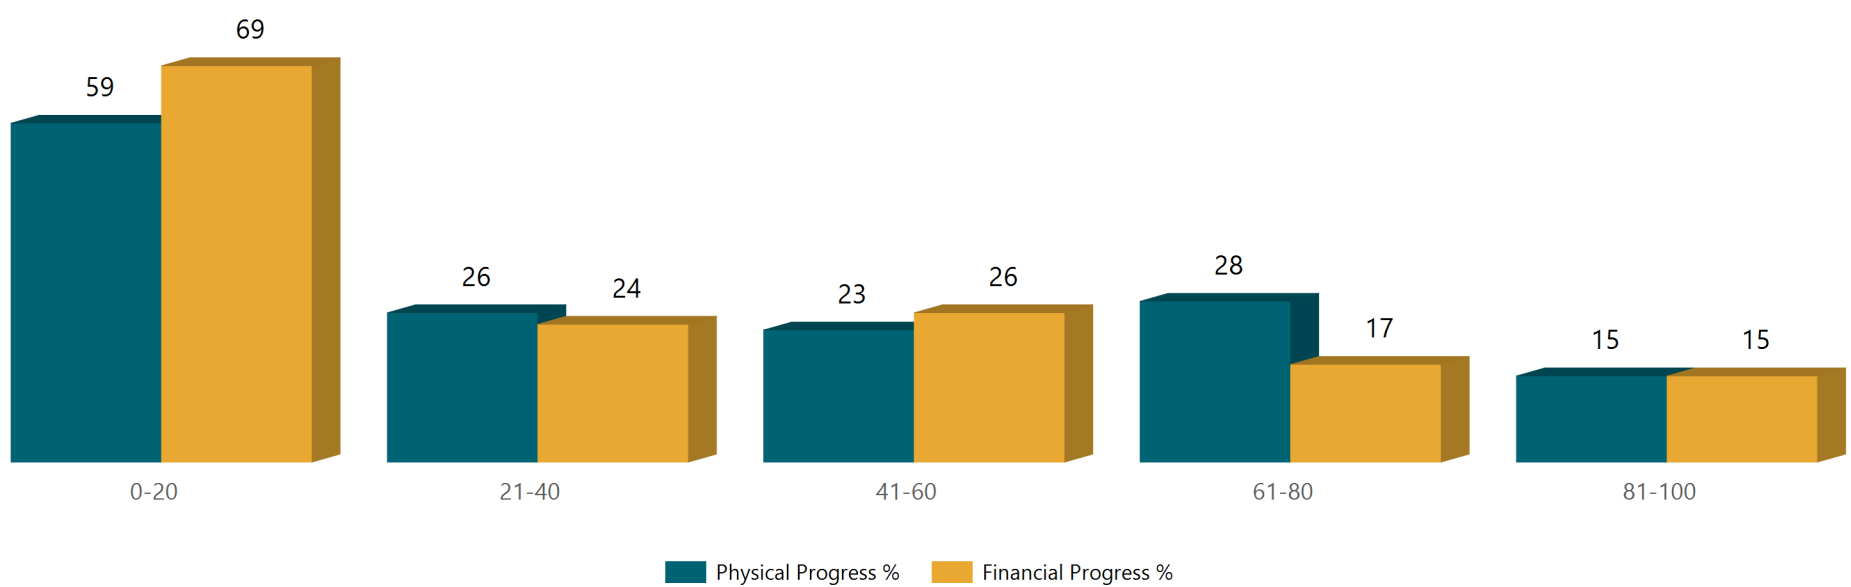

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	120	172,035	172,950	53,892
2	Steel	19	16,748	19,987	7,760
3	Metals & Mining	10	14,436	16,873	6,106
4	Construction	2	902	902	597

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400424	GEVRA OC [70 MTY]	11,816		5,329	77
2	400185	GOPALJI KANIHA OCP [10 TO 30 MTY]	8,416	6,108	1,694	17
3	400147	KUSMUNDA OC EXPANSION [15 TO 50 MTY]	7,612		4,698	81
4	612838	DIPKA OC	7,580		3,091	65
5	400150	RPR MAGADH EXP OCP	7,254		1,535	38



Major Infrastructure Central Ministries & Departments



Ministry of Railways

JULY 2025

257
Ongoing Projects

₹ 6,80,386
Original Cost
(crores)


₹ 8,18,189
Revised Cost
(crores)

₹ 5,06,532
(61.91% of Revised Cost)
Expenditure
(crores)


129 | ₹ 618,379
Mega Projects
Count | Original Cost (crores)

128 | ₹ 62,007
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

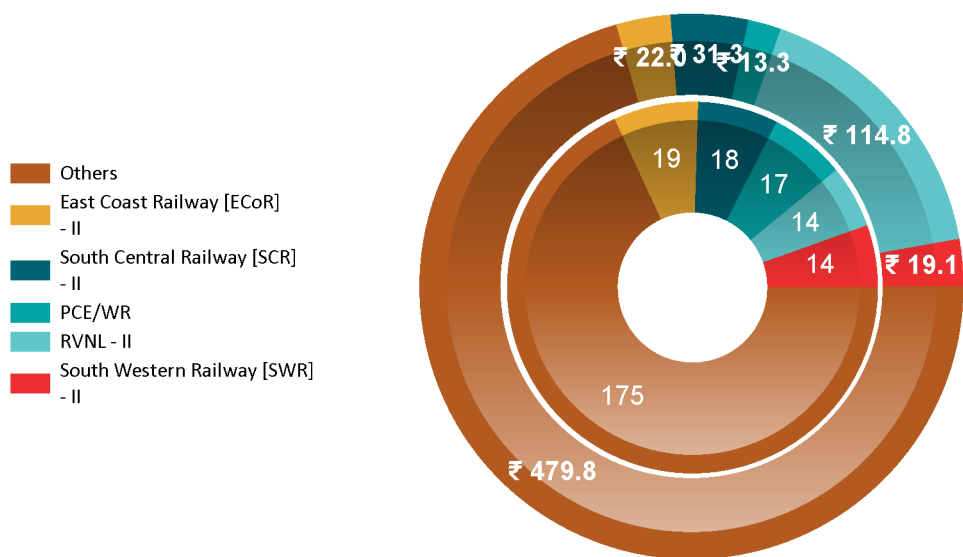


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

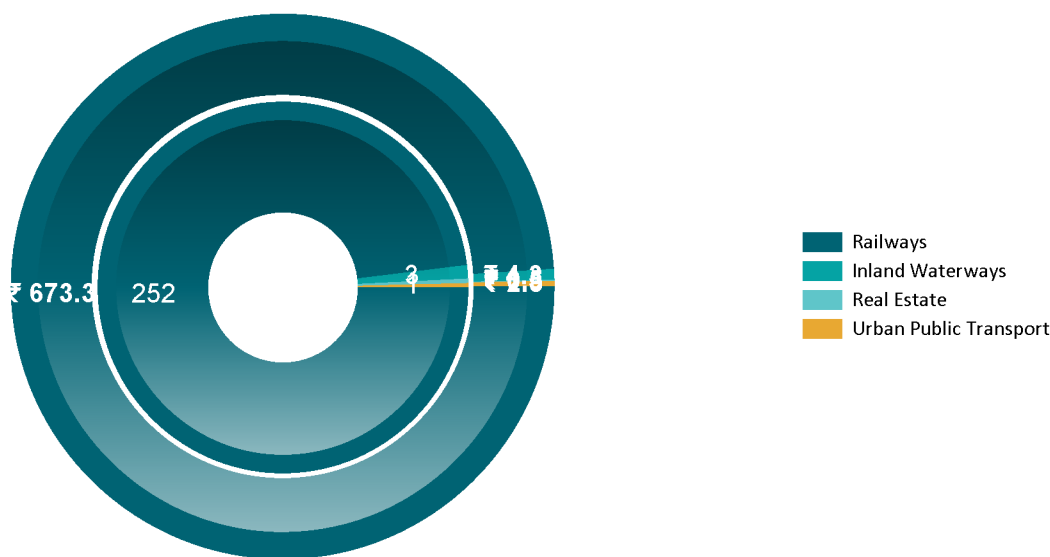


Physical & Financial progress (%) : Project count

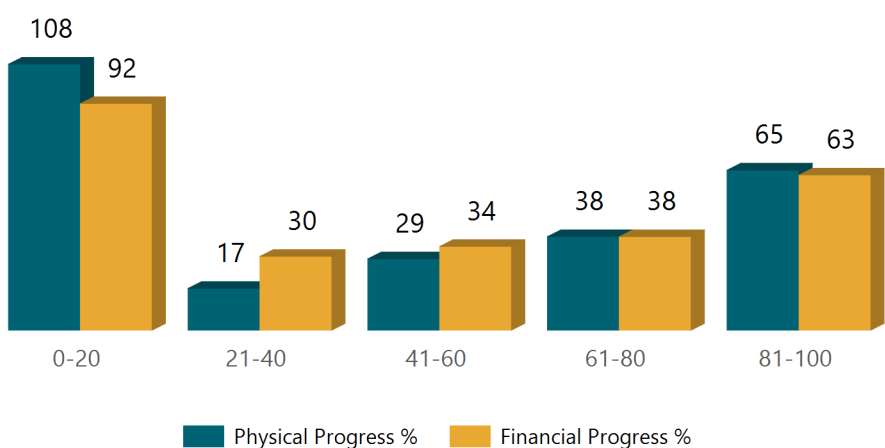

Cost Analytics : Major Sectors*

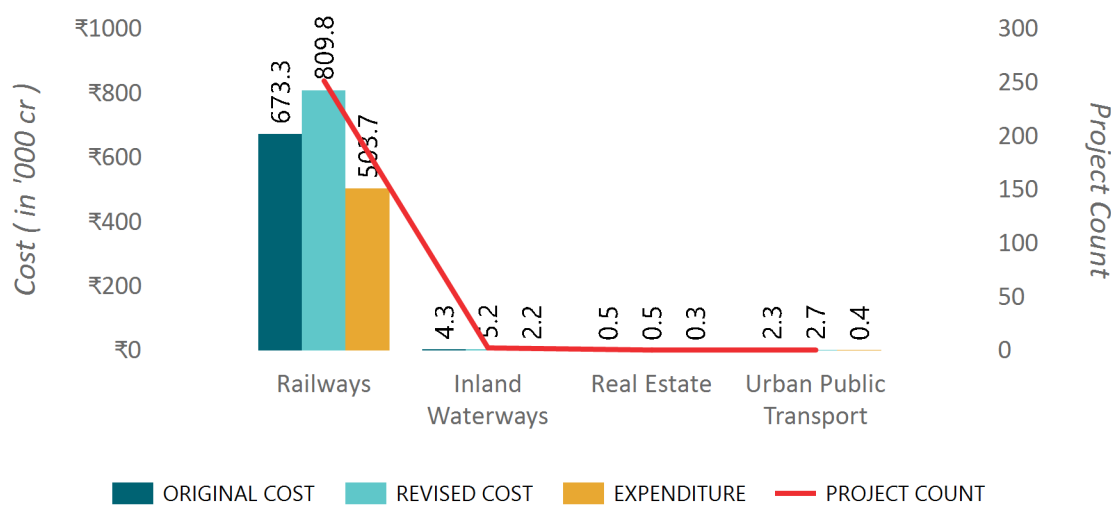

State Comparison : Major States*

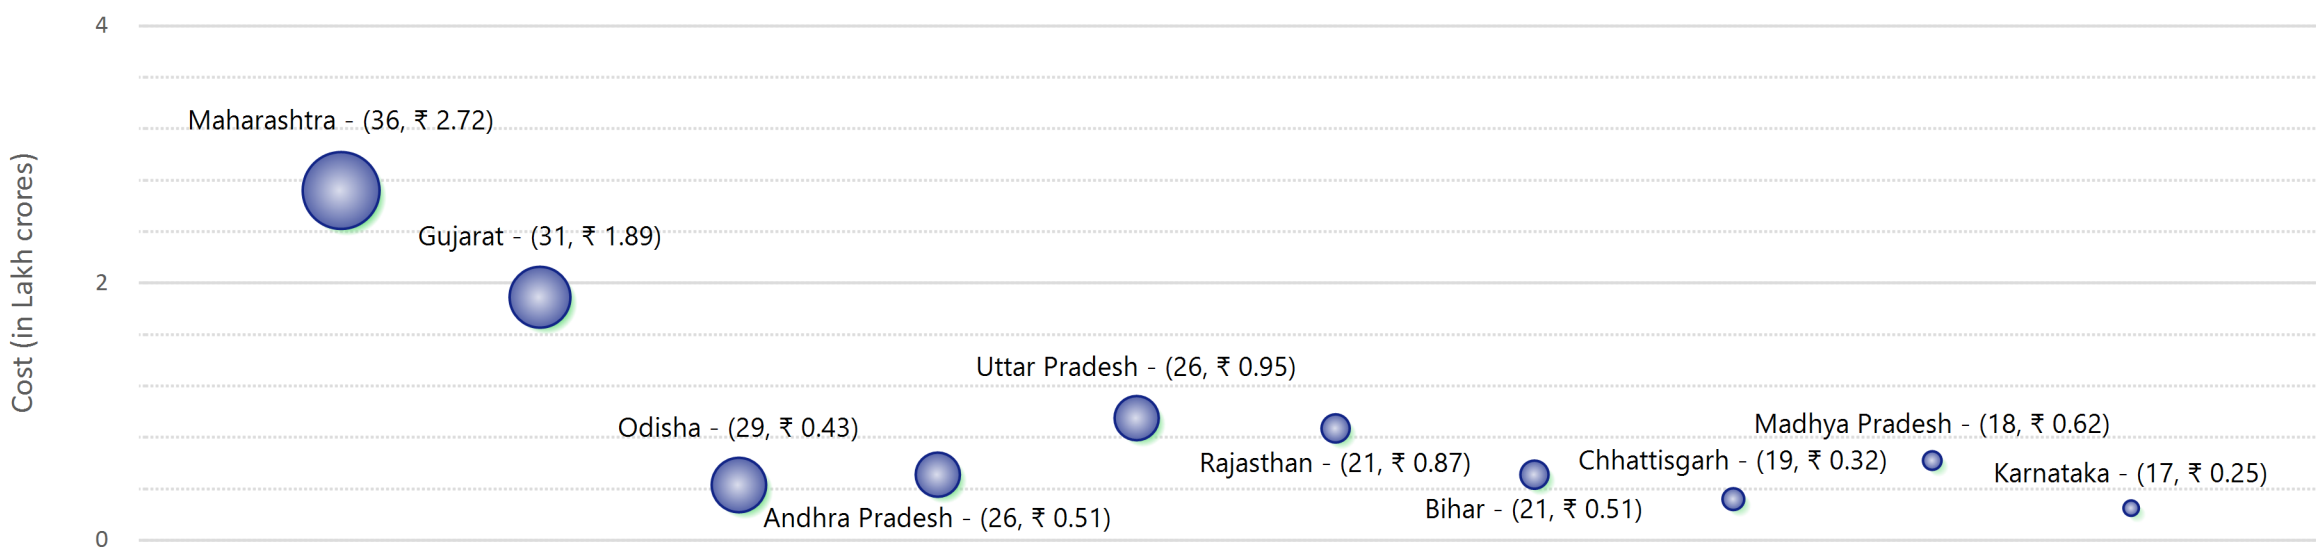

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	78,691	53
2	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
3	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
4	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,246	16
5	705428	BHANUPALLI-BILASPUR-BERI NEW RAILWAY LINE PROJECT	13,447	13,447	6,391	59



Ministry of Coal

JULY 2025

125
Ongoing Projects

₹ 2,20,304
Original Cost
(crores)

₹ 2,25,479
Revised Cost
(crores)


₹ 77,935
(34.56% of Revised Cost)
Expenditure
(crores)

40 | ₹ 178,547
Mega Projects
Count | Original Cost (crores)

85 | ₹ 41,757
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

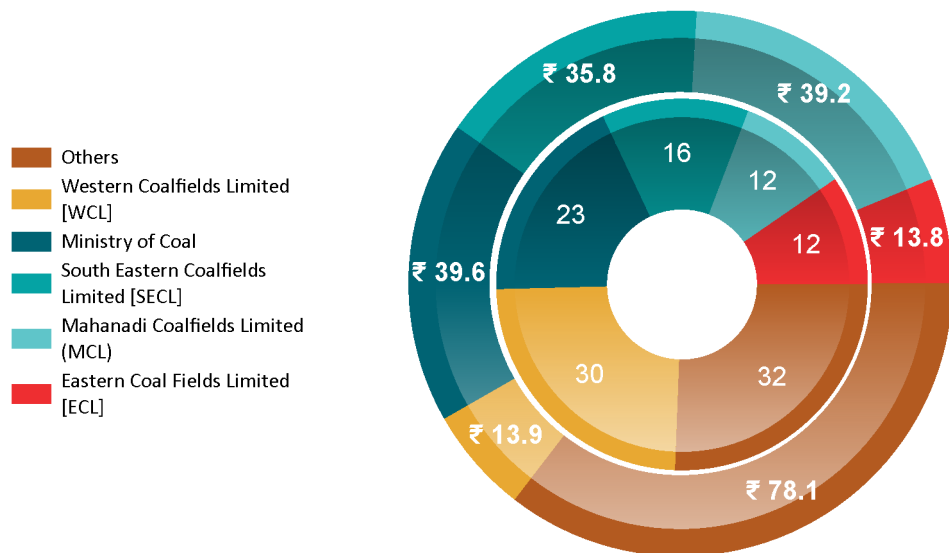


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

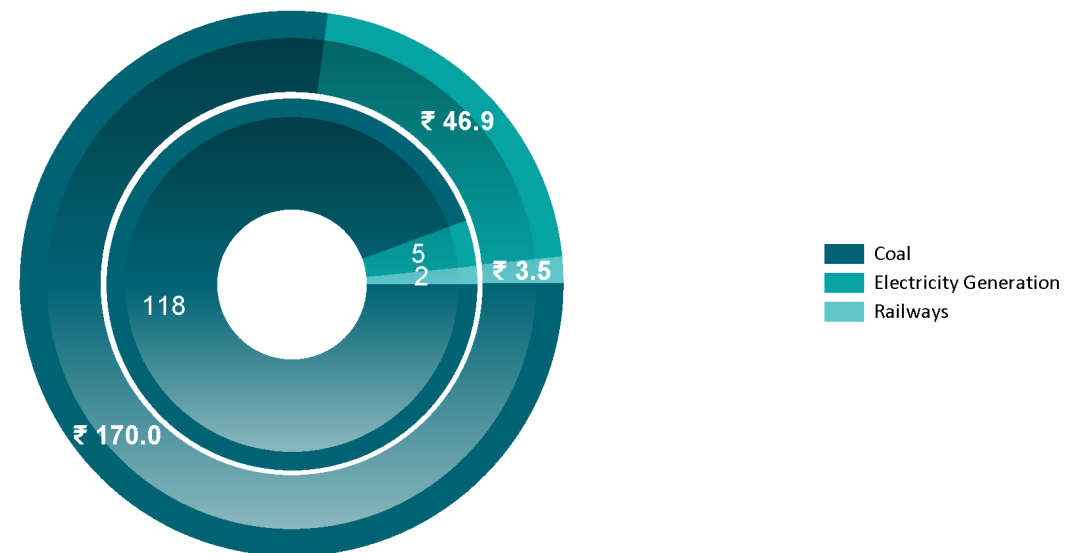


Physical & Financial progress (%) : Project count

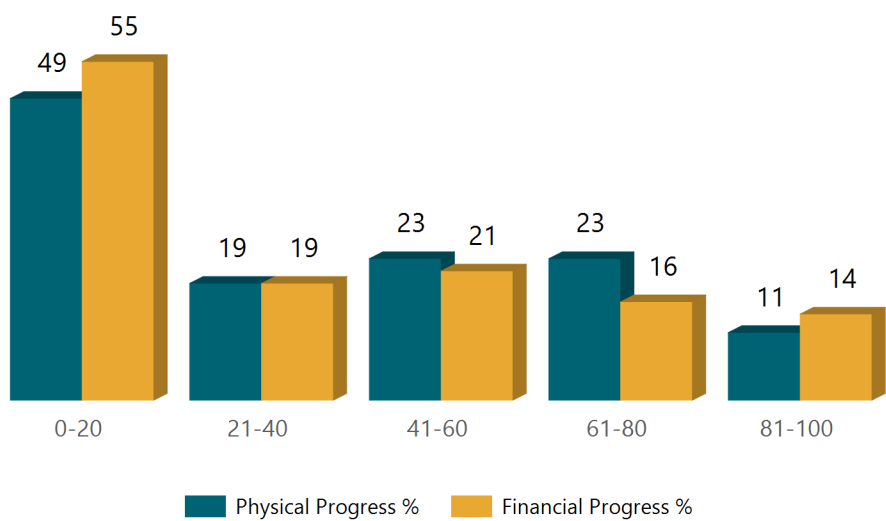

Cost Analytics : Major Sectors*

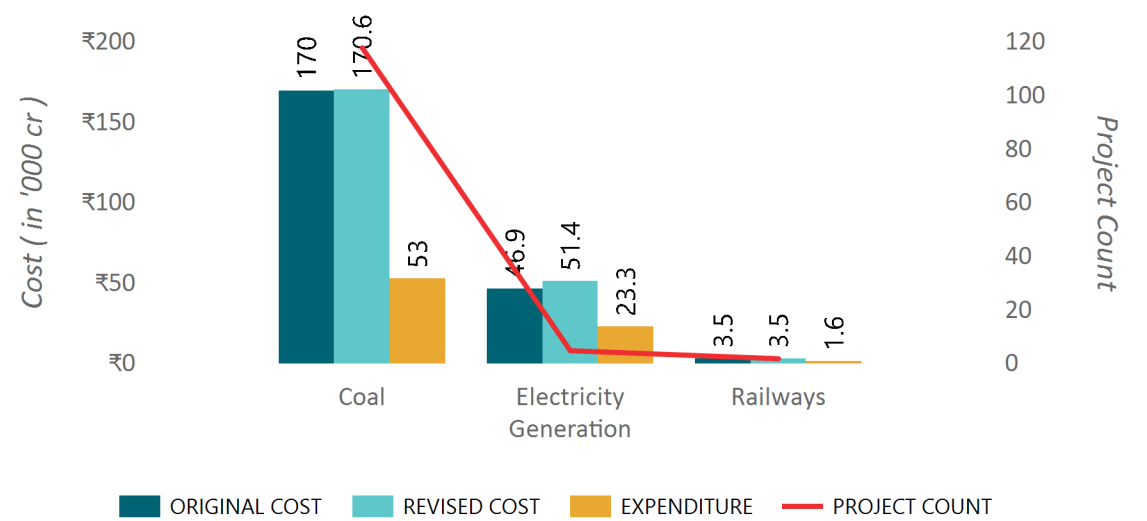

State Comparison : Major States*

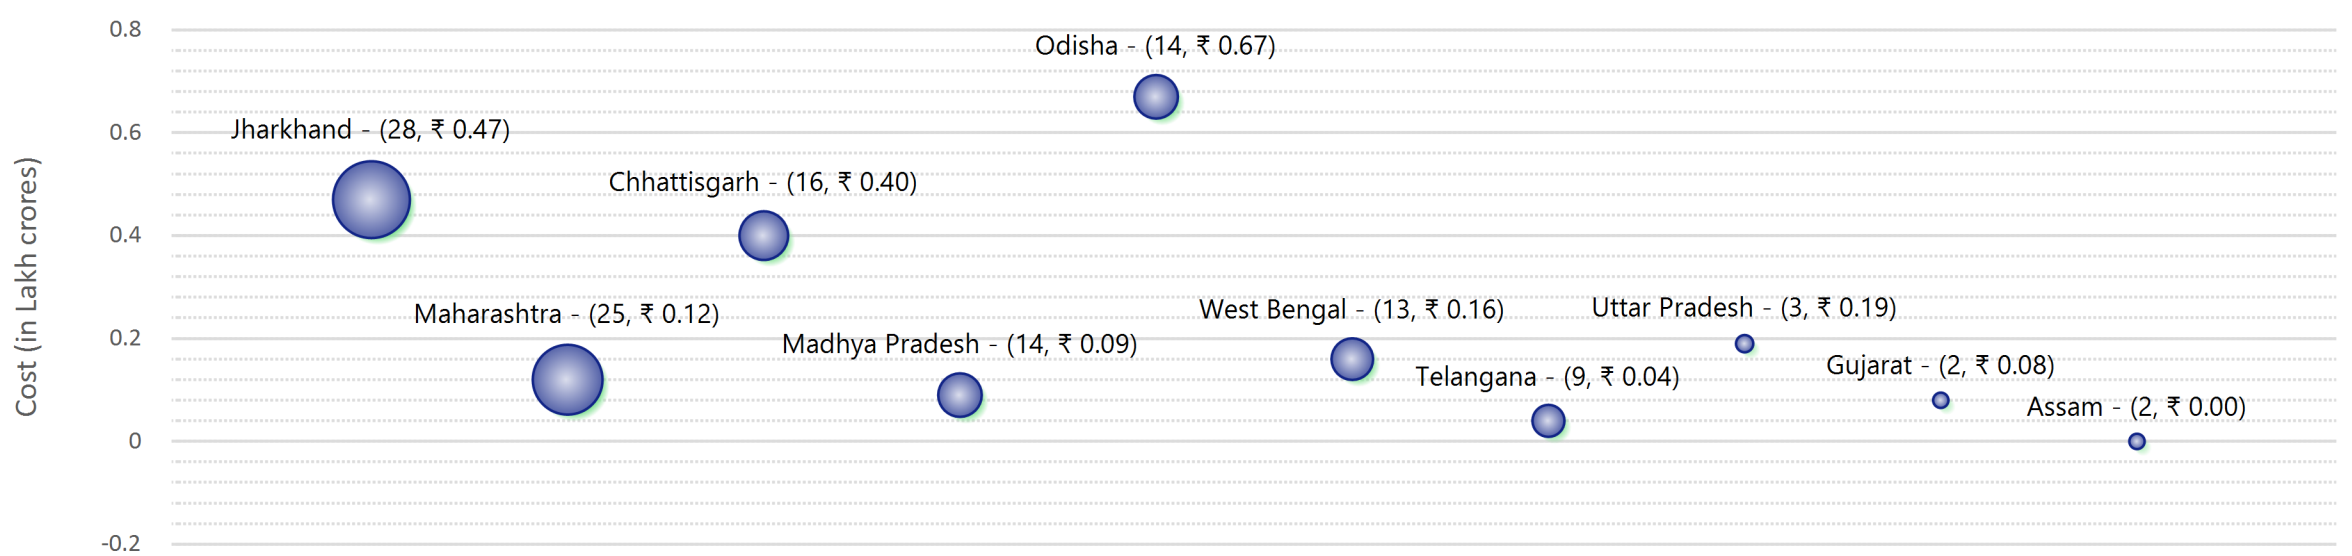

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	1,939	1
2	400259	GHATAMPUR THERMAL POWER PLANT 3 X 660 MW	17,238	21,781	20,135	92
3	400424	GEVRA OC [70 MTY]	11,816	11,816	5,329	77
4	400185	GOPALJI KANIHA OCP [10 TO 30 MTY]	8,416	6,108	1,694	17
5	400147	KUSMUNDA OC EXPANSION [15 TO 50 MTY]	7,612	7,612	4,698	81

Ministry of Petroleum & Natural Gas

JULY 2025

110
Ongoing Projects

₹ 4,36,146
Original Cost
(crores)


₹ 5,00,284
Revised Cost
(crores)

₹ 2,76,181
(55.2% of Revised Cost)
Expenditure
(crores)


50 | ₹ 409,237
Mega Projects
Count | Original Cost (crores)

60 | ₹ 26,908
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

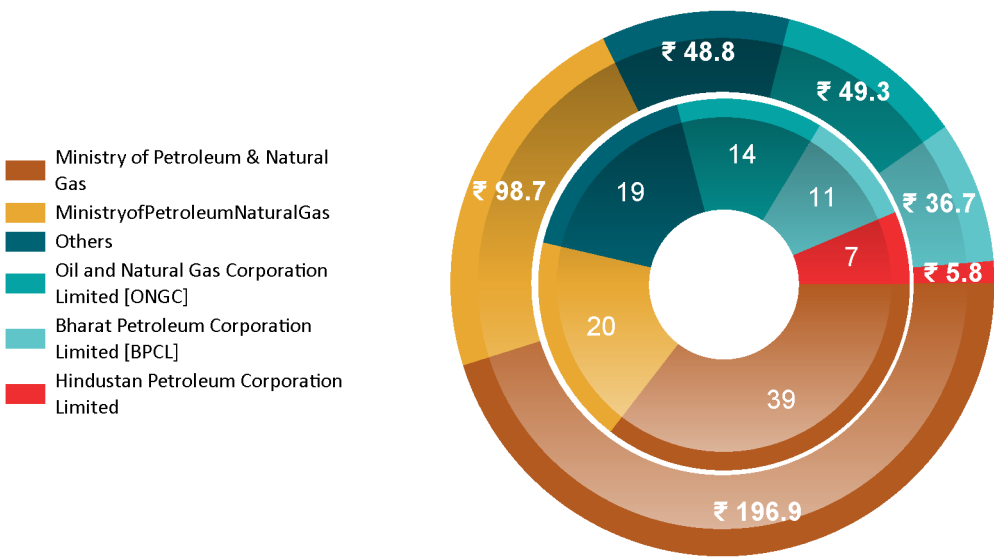


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

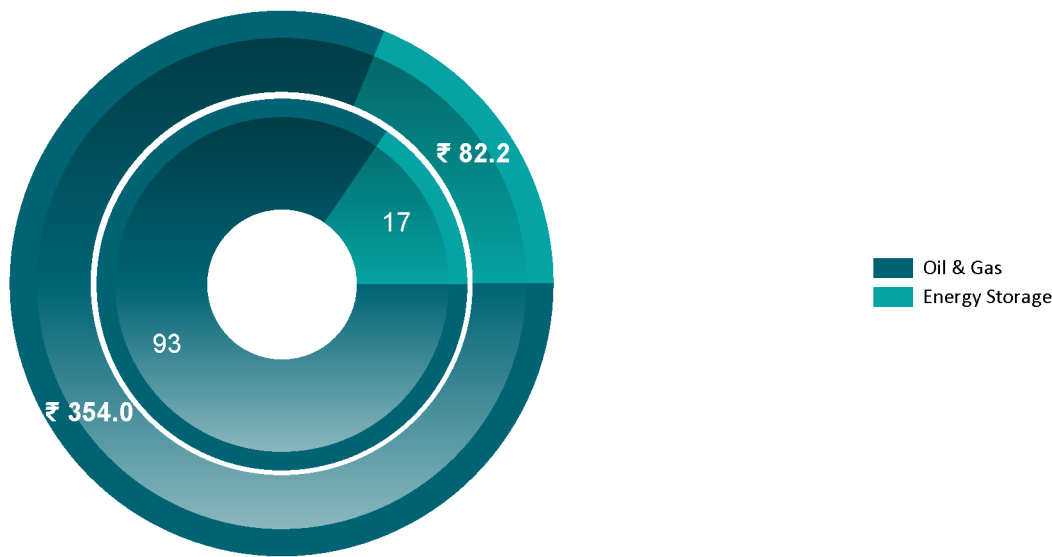


Physical & Financial progress (%) : Project count

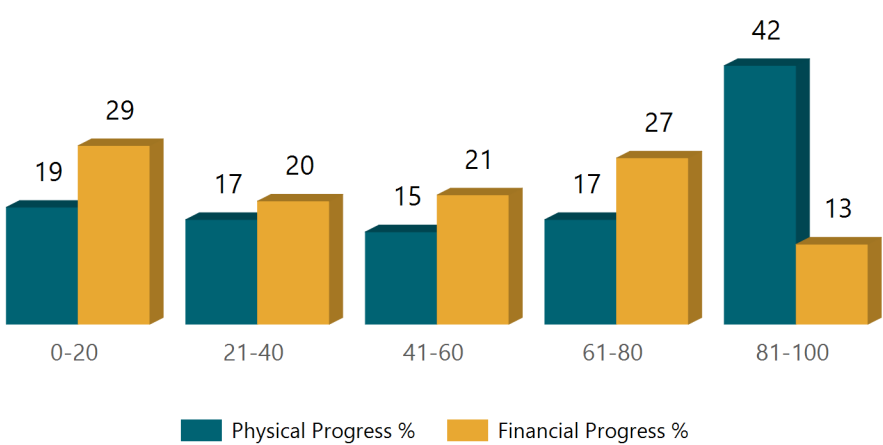

Cost Analytics : Major Sectors*

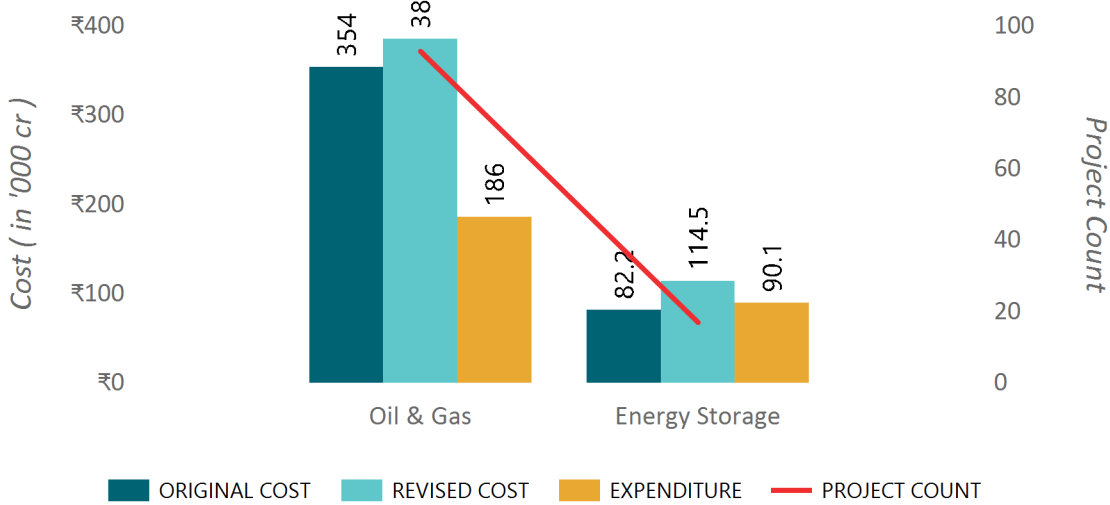

State Comparison : Major States*

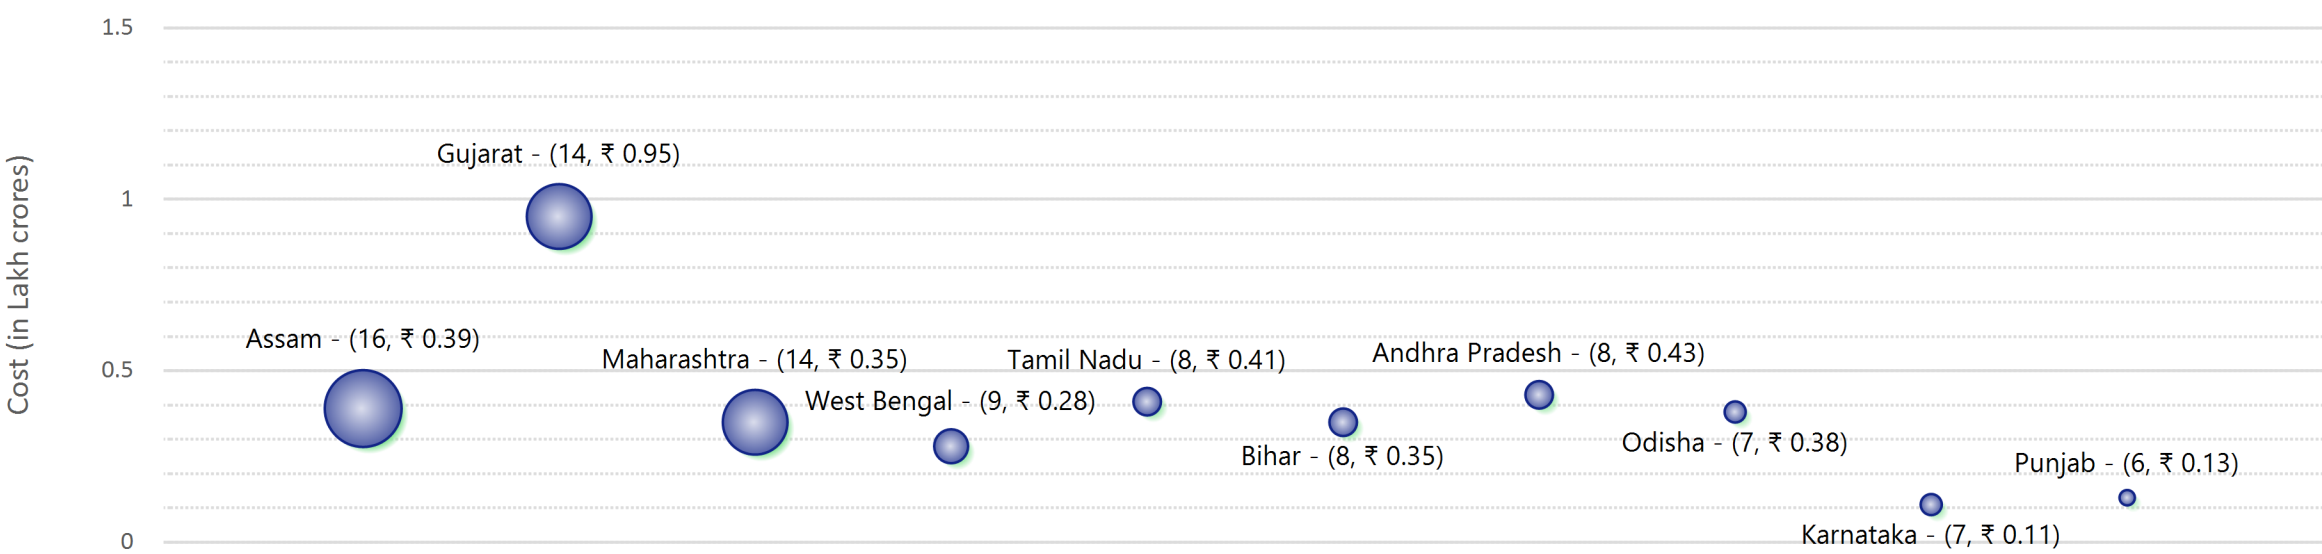

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,789	13
2	701263	RAJASTHAN REFINERY PROJECT	43,129	72,937	59,524	87
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	23,977	88
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	35,498	96
5	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,342	10



Ministry of Power

JULY 2025

94

Ongoing Projects

₹ 3,69,124

Original Cost
(crores)

₹ 4,20,618

Revised Cost
(crores)

₹ 1,79,908

(42.77% of Revised Cost)

Expenditure
(crores)

63 | ₹ 355,654


Mega Projects
Count | Original Cost (crores)

31 | ₹ 13,470

Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

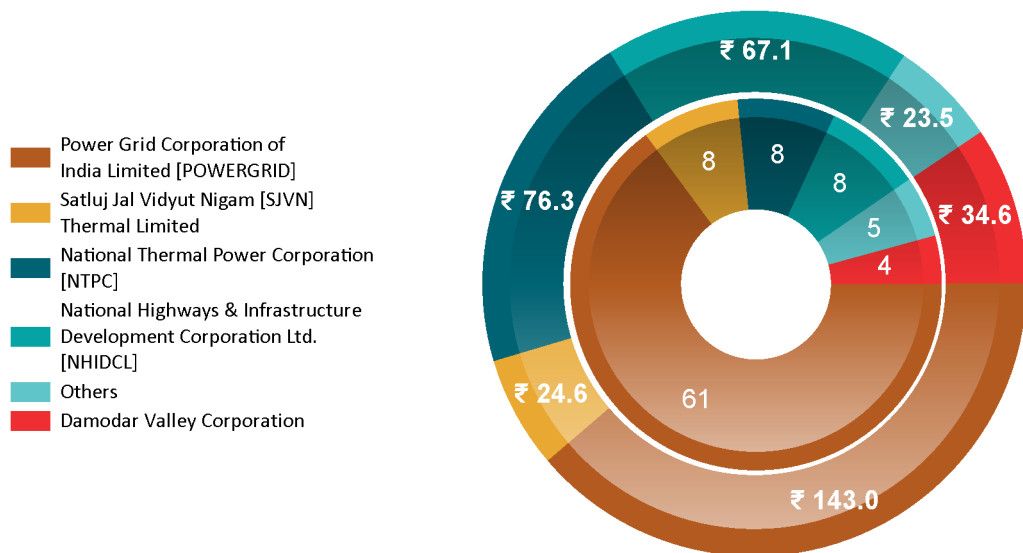


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

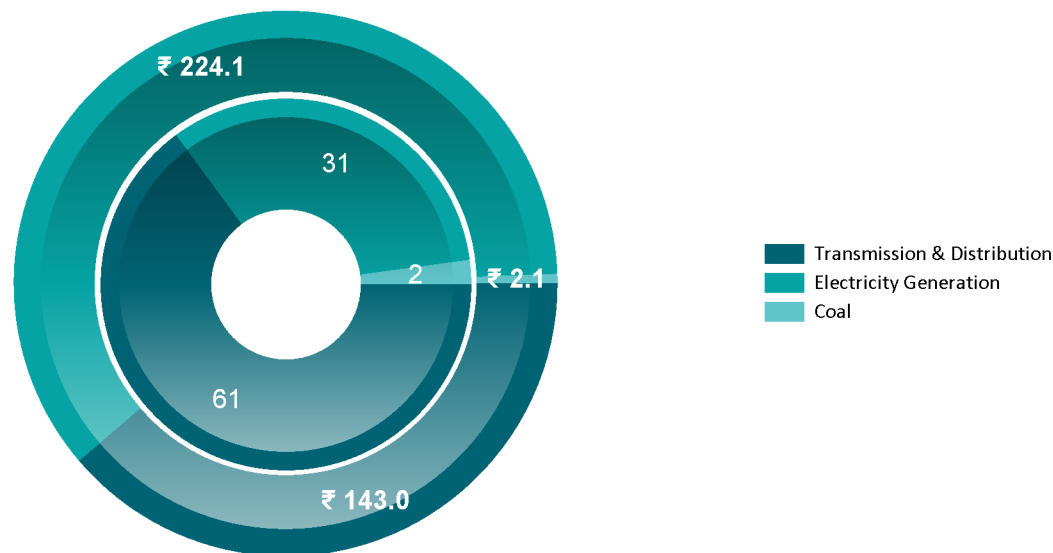


Physical & Financial progress (%) : Project count

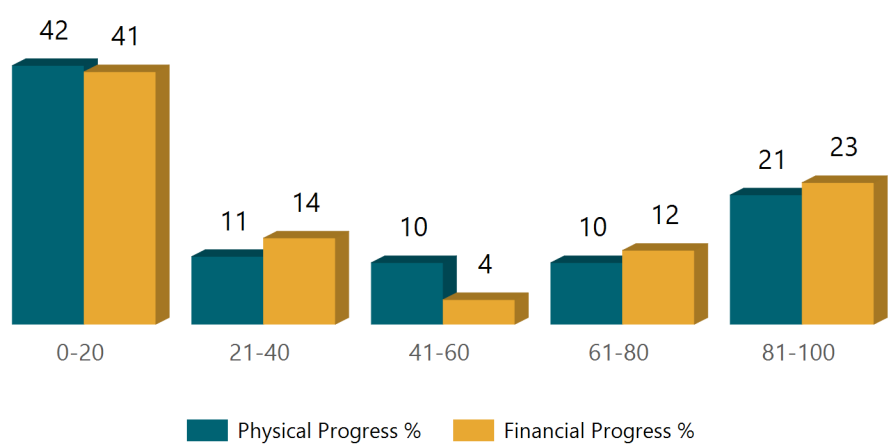

Cost Analytics : Major Sectors*

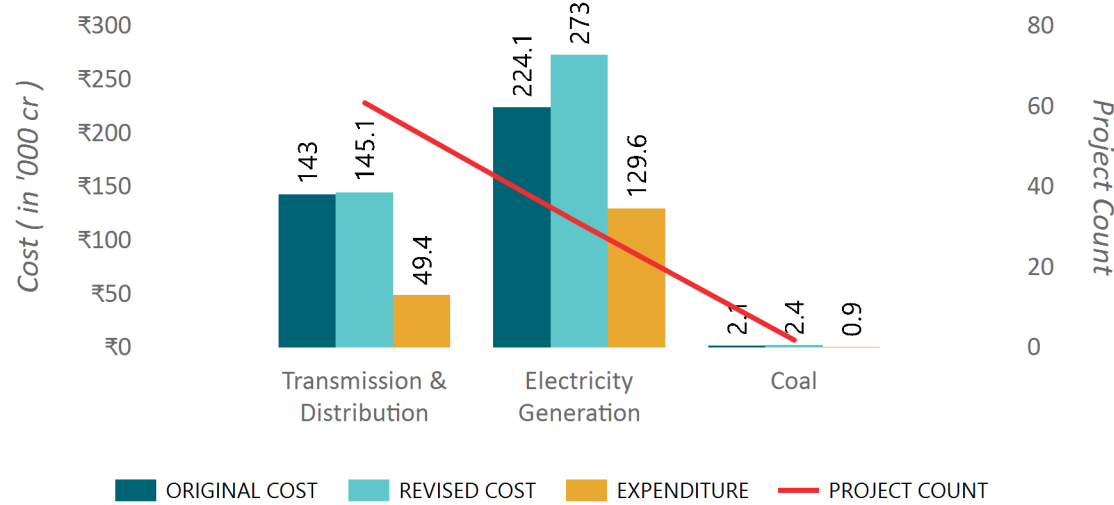

State Comparison : Major States*

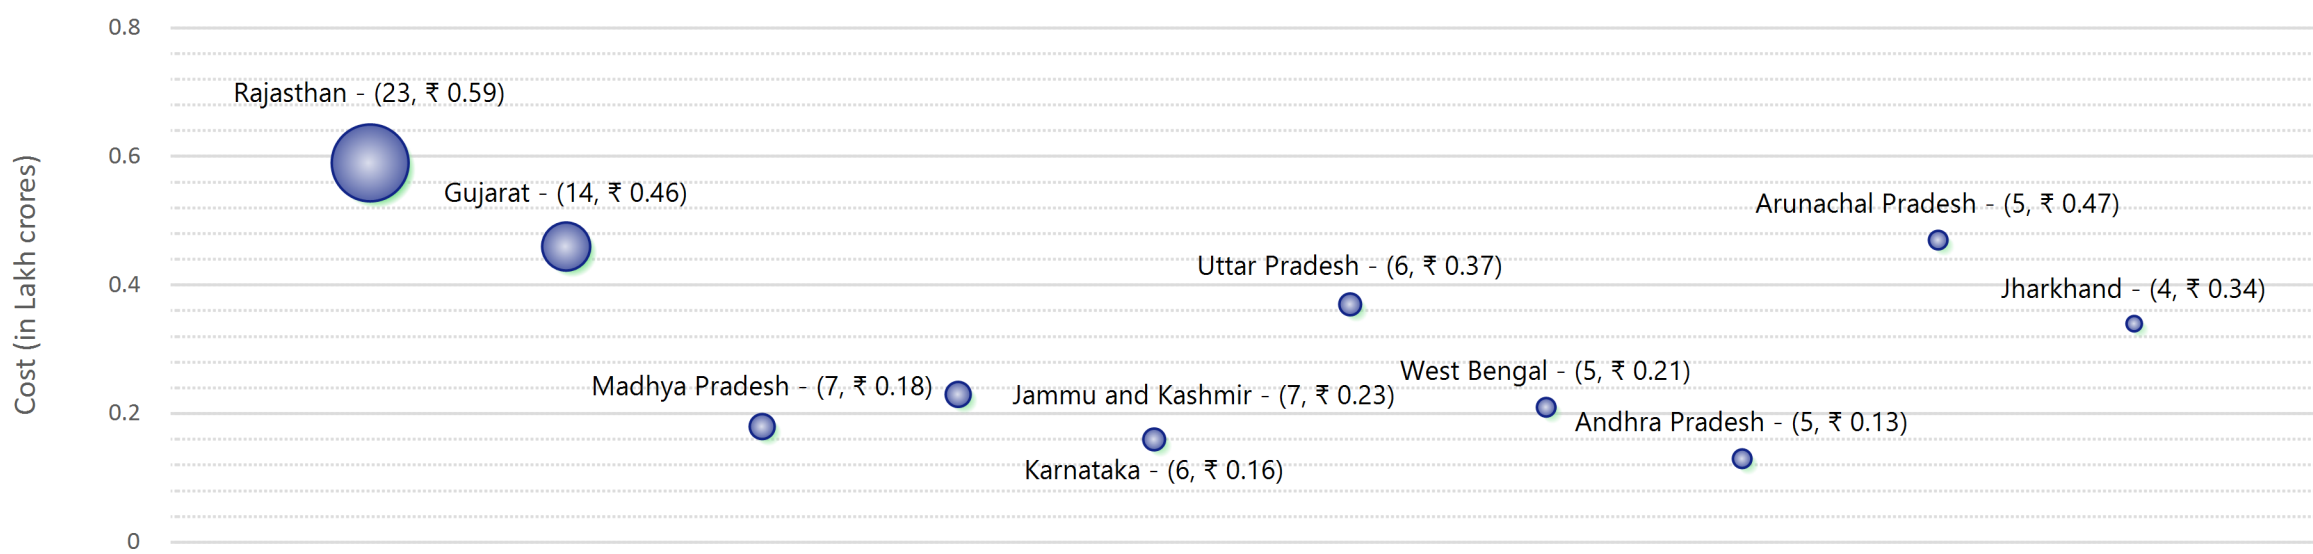

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)

Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	3,436	16
2	615347	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV NAME POWERGRID WEST CENTRAL TRANSMISSION LIMITED]	24,819	24,819	1,489	1
3	400062	RAGHUNATHPUR THERMAL POWER STATION PHASE II [2X660 MW] AT RAGHUNATHPUR, PURULIA, WEST BENGAL	17,673	17,673	1,184	1
4	612142	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III [2X800 MW]	17,195	17,195	1,626	8
5	400261	PATRATU THERMAL POWER STATION EXPANSION PROJECT PHASE-I [3X800 MW]	17,112	20,302	17,365	81



Department of Water Resources, River Development & GR

JULY 2025

53

Ongoing Projects

₹ 1,01,076

Original Cost
(crores)

₹ 2,19,313

Revised Cost
(crores)

₹ 1,44,776

(66.01% of Revised Cost)

Expenditure
(crores)

20 | ₹ 83,217


Mega Projects
Count | Original Cost (crores)

33 | ₹ 17,860

Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

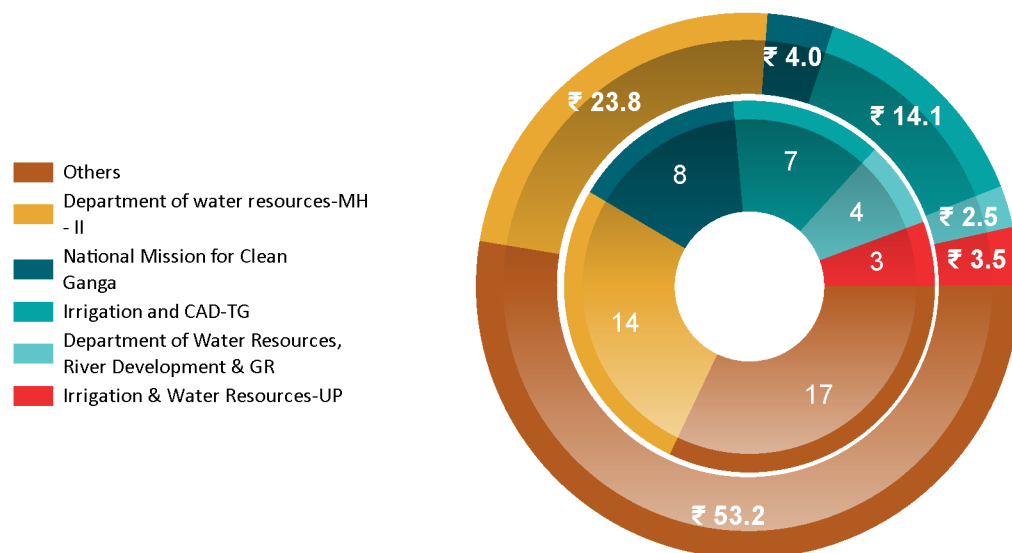


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

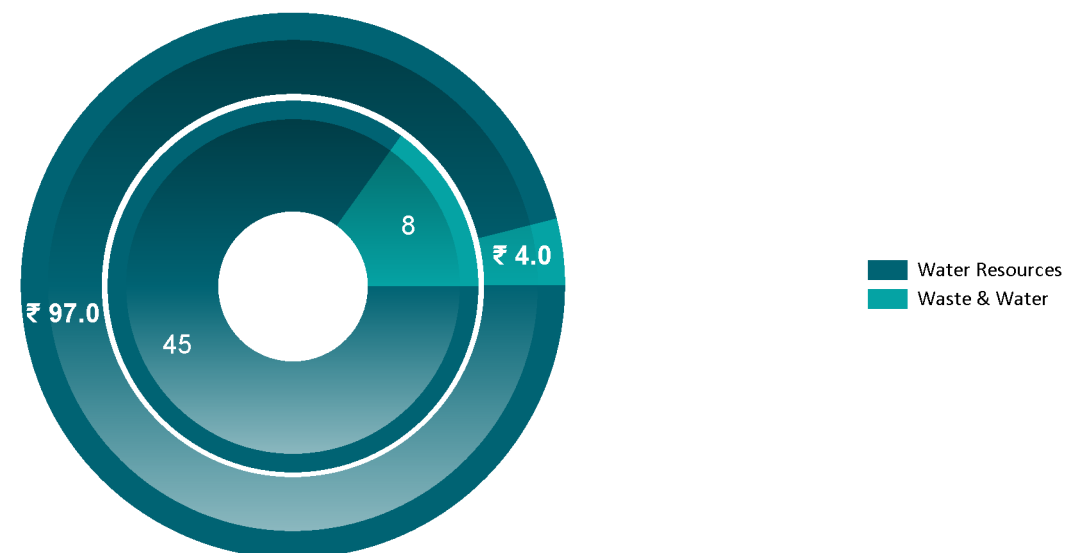


Physical & Financial progress (%) : Project count

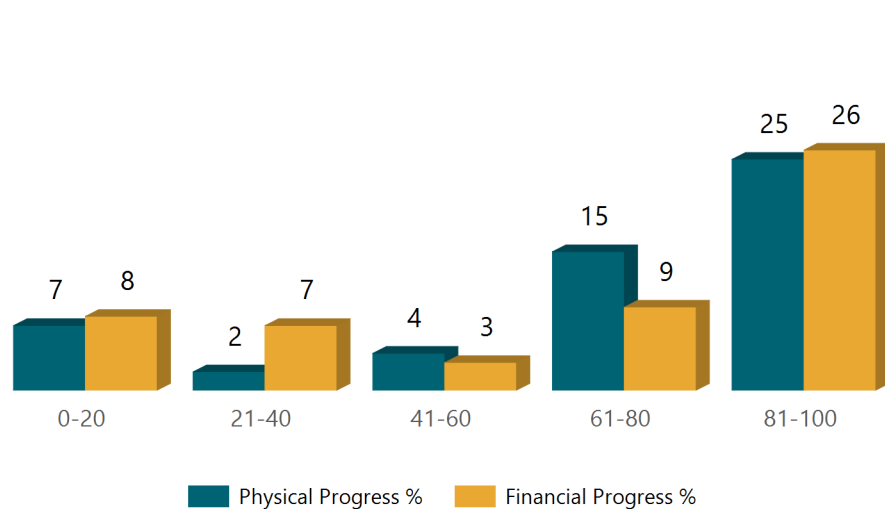

Cost Analytics : Major Sectors*

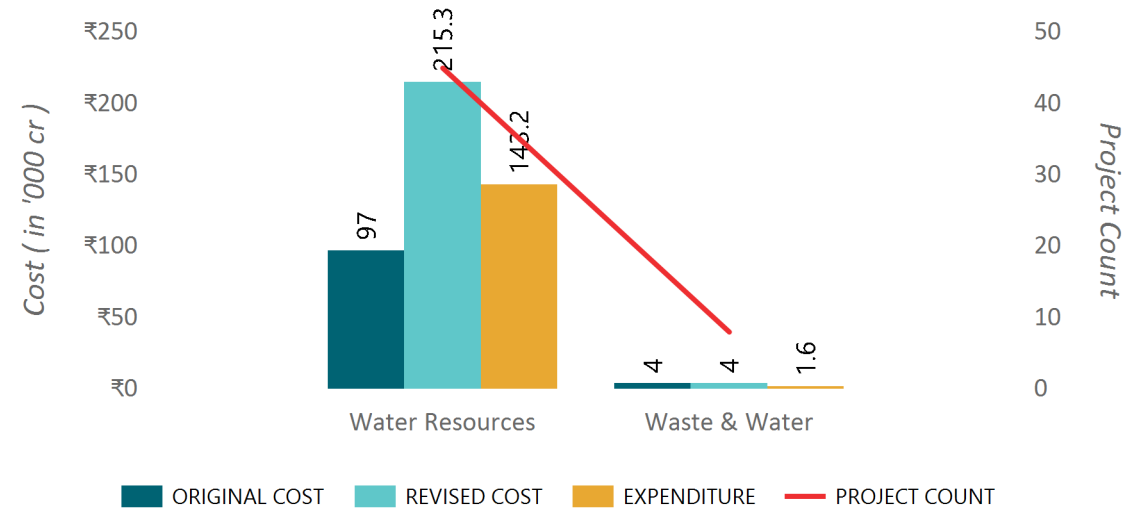

State Comparison : Major States*

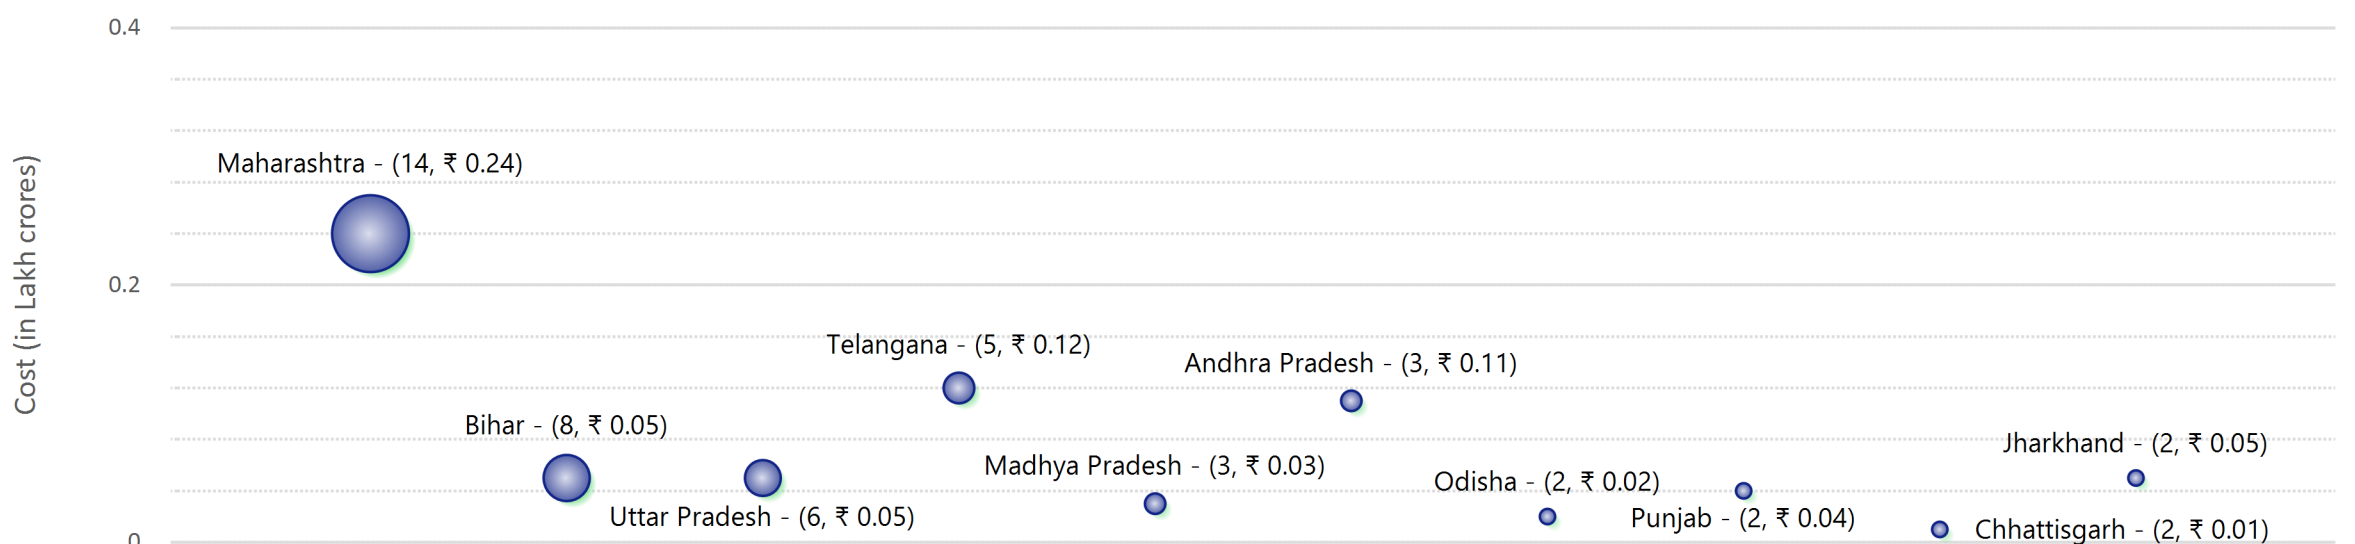

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,768	93
2	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	24,348	83
3	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,559	87
4	400112	JIGAON IRRIGATION PROJECT	7,223	7,223	8,501	90
5	701386	GOSIKHURD PROJECT	7,196	12,770	13,533	72



List of Tables



Table 1: Ministry-wise Ongoing Projects





Ministry-wise Ongoing Projects

JULY 2025

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Real Estate	2	3841.25 3841.25	422.99
		Tourism, Hospitality & Wellness	1	5178 5401	4470
2	Department of Higher Education	Education	30	12754.41 12685.5	8277.36
3	Department of Telecommunications	Telecommunication	15	151089.45 273182	71833.2
4	Department of Water Resources, River Development & GR	Waste & Water	8	4039.12 4039.12	1590.56
		Water Resources	45	97037.25 215274	143186
5	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	27	23265.01 23726.2	5883.97
6	Ministry of Coal	Coal	118	169952.27 170585	52990.5
		Electricity Generation	5	46865.63 51408.8	23308.2
		Railways	2	3485.86 3485.86	1636.67
7	Ministry of Health & Family Welfare	Healthcare	3	4155 4492.95	2646.56
8	Ministry of Housing & Urban Affairs	Construction	1	646.53 646.52	518.46
		Inland Waterways	1	63246 63246	47162.7
		Real Estate	10	44555.17 44555.2	6303.55
		Urban Public Transport	21	223016.77 230264	157669
		Waste & Water	2	410 410	100
9	Ministry of Mines	Construction	1	255.37 255.37	78.34
		Metals & Mining	9	12736.35 15116.5	6040.77
10	Ministry of Petroleum & Natural Gas	Energy Storage	17	82155.48 114517	90143.8
		Oil & Gas	93	353990.1 385767	186037
11	Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58
		Inland Waterways	2	9612.82 9304.79	3778.54
		Shipping	5	4823.34 4823.34	1812.05
		Tourism, Hospitality & Wellness	1	573 1238.05	487.35
12	Ministry of Power	Coal	2	2083 2365	901.38
		Electricity Generation	31	224064.24 273137	129610
		Transmission & Distribution	61	142976.51 145116	49396.5
13	Ministry of Railways	Inland Waterways	3	4265 5184	2178.18
		Railways	252	673330.1 809778	503708
		Real Estate	1	493 493	252.45
		Urban Public Transport	1	2298 2734	393
14	Ministry of Steel	Metals & Mining	1	1700 1756.2	65.44
		Steel	19	16748.25 19986.5	7759.53
Total			791	2,386,335.28	1,510,700.05



Table 2: State-wise Ongoing Projects





Ongoing Projects State-Wise

JULY 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	6	19714.58 22972.8	9861.58
		Ministry of Railways	Railways	2	1311.83 1311.83	591.32
	PAN India	Department of Telecommunications	Telecommunication	7	142131.27 264452	68888.24
	Total			15	163157.68	79341.14
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 209.88	0.00
		Total			1	209.88
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	2139.44 2139.44	327.99
		Department of Higher Education	Education	1	305 305	83.33
		Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1697.56
		Department of Water Resources, River Development & GR	Water Resources	3	10901.5 57269.5	25827.76
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	4	1440.03 1440.03	696.24
		Ministry of Petroleum & Natural Gas	Energy Storage	2	2898.34 3050	2223.91
			Oil & Gas	6	39929 40265	37302.20
		Ministry of Power	Transmission & Distribution	5	13395.24 13395.2	4132.14
		Ministry of Railways	Railways	26	50889.37 58114.5	28960.14
	Total			50	127160.49	101251.27
4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 592.61	549.96
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Ministry of Petroleum & Natural Gas	Energy Storage	1	43129 72937	59524.37
			Oil & Gas	1	9265 9265	6375.02
		Ministry of Power	Electricity Generation	4	41850.64 61640.8	28273.61
			Transmission & Distribution	1	4754.42 4754.42	7321.07
		Ministry of Railways	Railways	1	435 1250	901.00
	Total			10	101282.16	103229.07
5	Assam	Department of Higher Education	Education	1	153.71 153.71	288.87
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 256.16	0.00
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1712 1712	0.00
		Ministry of Coal	Coal	2	449.23 449.23	186.31
		Ministry of Petroleum & Natural Gas	Energy Storage	3	10768.4 11947.4	9862.17
			Oil & Gas	13	28019.15 40824	30217.38
		Ministry of Power	Electricity Generation	1	6285.33 26075.5	24685.13
			Transmission & Distribution	1	5111.33 6700	5253.47
	Ministry of Railways	Railways	6	15645.83 17360.8	10192.51	
Total			30	69656.63	80969.88	
6	Bihar	Department of Higher Education	Education	1	499.21 499.21	425.47
		Department of Telecommunications	Telecommunication	3	2336.11 2107.64	948.33
		Department of Water Resources, River Development & GR	Waste & Water	5	2351.43 2351.43	1285.75
			Water Resources	3	2884.49 4060.84	1590.27
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	4	3756.73 3756.73	1284.41
		Ministry of Housing & Urban Affairs	Real Estate	1	454.65 454.65	204.64
			Urban Public Transport	1	13365.77 13365.8	4039.77
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9701.95
			Oil & Gas	7	24636.5 26501.2	13077.01
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3432.34
		Ministry of Power	Electricity Generation	1	10439.09 13756.6	11970.96

Ongoing Projects State-Wise

JULY 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Ministry of Power	Transmission & Distribution	2	751.63 751.63	0.40
		Ministry of Railways	Railways	21	51225.79 57662.8	27425.45
	Total		51	128298.58	75386.75	
7	Chandigarh	Ministry of Housing & Urban Affairs	Real Estate	1	285.85 285.85	127.58
	Total		1	285.85	127.58	
8	Chhattisgarh	Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1697.56
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 1109.33	616.93
		Ministry of Coal	Coal	15	38654.89 38654.9	15299.54
			Railways	1	1686.22 1686.22	342.96
		Ministry of Housing & Urban Affairs	Real Estate	1	3797.69 3797.69	2694.00
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	10056.25 10467	6507.12
		Ministry of Power	Electricity Generation	2	25321 25321	2288.00
			Transmission & Distribution	1	385.84 385.84	378.16
		Ministry of Railways	Railways	19	32171.36 34232.1	17908.81
		Ministry of Steel	Metals & Mining	1	1700 1756.2	65.44
	Steel		6	7530.14 10050.1	5162.03	
Total		52	127408.22	52960.55		
9	Dadra & Nagar Haveli and Daman & Diu	Ministry of Housing & Urban Affairs	Waste & Water	1	210 210	0.00
		Ministry of Power	Transmission & Distribution	1	4546.26 4546.26	4148.46
		Ministry of Railways	Railways	1	108000 108000	78690.89
	Total		3	112756.26	82839.35	
10	Delhi	Department for Promotion of Industry & Internal Trade	Tourism, Hospitality & Wellness	1	5178 5401	4470.00
		Department of Higher Education	Education	2	706.49 706.49	290.98
		Department of Telecommunications	Telecommunication	1	248.2 248.2	236.91
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	215.17 215.17	104.92
		Ministry of Housing & Urban Affairs	Construction	1	646.53 646.52	518.46
			Real Estate	1	32850 32850	0.00
			Urban Public Transport	4	69853.45 69853.4	41241.03
		Ministry of Power	Transmission & Distribution	4	4356.47 4908.47	3860.71
	Ministry of Railways	Railways	13	27509.96 27510	5067.53	
Total		28	141564.27	55790.54		
11	Goa	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	756.17 756.17	436.21
		Ministry of Railways	Railways	2	5804.49 6182.62	5976.87
	Total		4	6560.66	6413.08	
12	Gujarat	Department of Higher Education	Education	1	490.63 490.63	301.44
		Department of Telecommunications	Telecommunication	1	336.89 301.13	225.71
		Department of Water Resources, River Development & GR	Water Resources	2	25739.93 40082.8	36722.58
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1520.17 1766.17	771.34
		Ministry of Coal	Coal	1	7580 7580	3091.00
			Electricity Generation	1	383.84 383.84	303.50
		Ministry of Housing & Urban Affairs	Real Estate	2	6016.4 6016.4	3075.44
			Urban Public Transport	3	28177.49 30329	23395.89
			Waste & Water	1	200 200	100.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	62245 92053	74193.58
			Oil & Gas	11	32704.12 32178.7	22543.16
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	4243.64 4243.64	346.20

Ongoing Projects State-Wise						JULY 2025
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
12	Gujarat	Ministry of Ports, Shipping and Waterways	Tourism, Hospitality & Wellness	1	573 1238.05	487.35
		Ministry of Power	Electricity Generation	1	339.35 339.35	317.59
			Transmission & Distribution	13	45319.41 45318.9	12189.63
		Ministry of Railways	Railways	31	189276.71 263686	214924.05
		Total		75	405146.58	392988.46
13	Haryana	Ministry of Health & Family Welfare	Healthcare	1	1299 1299	349.41
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	6230.99 6230.99	0.14
		Ministry of Petroleum & Natural Gas	Energy Storage	1	9028 9028	7071.08
			Oil & Gas	5	45925.07 49596.1	33255.25
		Ministry of Power	Transmission & Distribution	4	13362 13914	2575.26
		Ministry of Railways	Railways	4	53464 126368	125556.07
		Total		16	129309.06	168807.21
14	Himachal Pradesh	Department of Higher Education	Education	3	811.15 921.89	576.20
		Department of Telecommunications	Telecommunication	1	336.89 301.13	225.71
		Ministry of Power	Electricity Generation	4	7728.04 12252.1	4103.90
		Ministry of Railways	Railways	3	17005 17005	8745.88
		Total		11	25881.08	13651.69
15	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 500.91	484.52
		Department of Telecommunications	Telecommunication	1	336.89 301.13	225.71
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 861.37	154.30
		Ministry of Health & Family Welfare	Healthcare	1	1828 1828	1504.91
		Ministry of Petroleum & Natural Gas	Energy Storage	1	676.89 676.89	518.22
			Oil & Gas	2	1059.9 1059.9	194.19
		Ministry of Power	Electricity Generation	4	22207.77 22207.8	12060.37
			Transmission & Distribution	3	825.43 825.43	488.41
		Total		14	28221.18	15630.63
16	Jharkhand	Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1697.56
		Department of Water Resources, River Development & GR	Water Resources	2	5430.04 12010.3	5692.84
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	215.17 215.17	104.92
		Ministry of Coal	Coal	27	45414.48 45178.8	10320.88
			Railways	1	1799.64 1799.64	1293.71
		Ministry of Housing & Urban Affairs	Real Estate	1	212.74 212.74	41.00
		Ministry of Mines	Metals & Mining	2	3370.02 3370.02	13.33
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9701.95
			Oil & Gas	3	2010.07 2010.07	596.23
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3432.34
		Ministry of Power	Coal	2	2083 2365	901.38
			Electricity Generation	2	31470 34660	18481.70
		Ministry of Railways	Railways	12	43938.71 44332.7	14801.80
		Ministry of Steel	Steel	6	2854.58 3572.87	1251.51
		Total		63	159658.2	68331.15
17	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1701.81 1701.81	95.00
		Department of Higher Education	Education	1	420.41 420.41	360.72
		Department of Water Resources, River Development & GR	Water Resources	1	770.16 1606.07	1511.22
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	4	1358.57 1358.57	583.49
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	41193.24 45483.2	37902.51



Ongoing Projects State-Wise

JULY 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	Karnataka	Ministry of Petroleum & Natural Gas	Energy Storage	2	1532 2586	1387.55
			Oil & Gas	5	9662 12693.6	8687.98
		Ministry of Power	Transmission & Distribution	6	15682.01 15682	2377.07
		Ministry of Railways	Railways	16	24870.49 30669.6	17352.85
			Real Estate	1	493 493	252.45
		Ministry of Steel	Steel	1	1043.63 1043.63	214.48
		Total		40	98727.32	70725.32
18	Kerala	Department of Higher Education	Education	1	1006.45 1217.4	615.95
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	699.74 699.74	179.59
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1957.05 1957.05	306.45
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	7996.87 10990.9	4880.20
		Ministry of Railways	Railways	3	2846 5199	3026.15
		Total		10	14506.11	9008.34
19	Ladakh	Department of Telecommunications	Telecommunication	1	336.89 301.13	225.71
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480 640	427.04
		Ministry of Power	Transmission & Distribution	1	288.71 288.71	202.10
		Total		3	1105.6	854.85
20	Madhya Pradesh	Department of Higher Education	Education	1	496.28 496.28	138.60
		Department of Telecommunications	Telecommunication	2	1999.22 1806.51	722.62
		Department of Water Resources, River Development & GR	Water Resources	3	2628.27 2941.14	2757.75
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	215.17 215.17	104.92
		Ministry of Coal	Coal	14	8634.02 8634.02	3268.58
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	14442.2 14442.2	6956.02
		Ministry of Mines	Metals & Mining	1	1856.36 1856.36	924.98
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10088 10088	7598.13
			Oil & Gas	2	51211.25 51622	8284.20
		Ministry of Power	Electricity Generation	1	646.17 646.17	0.00
			Transmission & Distribution	6	17446 17446	2423.32
		Ministry of Railways	Railways	18	61558.55 69197.5	43133.73
		Total		52	171221.49	76312.85
21	Maharashtra	Department of Higher Education	Education	2	250.33 446.26	154.59
		Department of Telecommunications	Telecommunication	3	5723.99 5723.99	1863.58
		Department of Water Resources, River Development & GR	Water Resources	14	23764.91 37142.8	36591.47
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	306.21
		Ministry of Coal	Coal	25	12455.88 12455.9	2983.36
		Ministry of Housing & Urban Affairs	Urban Public Transport	6	34571.47 35377.5	28692.48
		Ministry of Petroleum & Natural Gas	Energy Storage	1	281.35 389.67	227.54
			Oil & Gas	13	34264.24 37660.4	20460.79
		Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58.00
			Shipping	2	1266.8 1266.8	253.46
		Ministry of Power	Transmission & Distribution	3	29589.67 29589.7	5660.04
		Ministry of Railways	Railways	36	271609.73 360035	260743.99
		Total		107	414971.85	357995.51
22	Manipur	Department of Water Resources, River Development & GR	Water Resources	1	1449.44 1822.24	1837.91
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499 499	160.48
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6375.02



Ongoing Projects State-Wise

JULY 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
22	Manipur	Ministry of Power	Transmission & Distribution	1	5111.33 6700	5253.47
		Total		4	16324.77	13626.88
23	Meghalaya	Department of Higher Education	Education	1	494.52 494.52	413.57
		Department of Telecommunications	Telecommunication	1	971.96 971.96	208.25
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6375.02
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5253.47
		Total		4	15842.81	12250.31
24	Mizoram	Department of Higher Education	Education	1	474.23 474.23	167.55
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6375.02
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5253.47
		Total		3	14850.56	11796.04
25	Nagaland	Department of Higher Education	Education	1	275.63 275.63	257.82
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	9492.62 9492.62	6384.03
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5253.47
		Ministry of Railways	Railways	2	8786.7 8786.7	5216.03
		Total		6	23666.28	17111.35
26	Odisha	Department of Higher Education	Education	1	1229.32 773.76	835.55
		Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1697.56
		Department of Water Resources, River Development & GR	Water Resources	2	1556.46 5291.33	5193.30
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	215.17 215.17	104.92
		Ministry of Coal	Coal	13	39671.73 40539.7	13423.80
			Electricity Generation	1	27212.96 27213	1938.68
		Ministry of Mines	Metals & Mining	5	7343.97 9724.14	4967.46
		Ministry of Petroleum & Natural Gas	Energy Storage	2	12886.34 14217	11894.63
			Oil & Gas	5	25285.44 23768.5	15711.67
		Ministry of Ports, Shipping and Waterways	Shipping	1	3004.63 3004.63	1149.79
		Ministry of Power	Electricity Generation	1	11843.75 12543	3975.00
			Transmission & Distribution	1	342.69 342.69	0.20
		Ministry of Railways	Inland Waterways	3	4265 5184	2178.18
			Railways	25	38578.21 42391.3	26663.28
			Railways	1	267.61 267.61	0.00
		Ministry of Steel	Steel	1	1105.23 1105.23	736.47
		Total		65	180071.08	90470.49
27	Puducherry	Department of Higher Education	Education	1	618.34 544.34	509.24
		Ministry of Railways	Railways	1	713 981	598.38
		Total		2	1331.34	1107.62
28	Punjab	Department of Higher Education	Education	2	559.3 559.3	290.39
		Department of Water Resources, River Development & GR	Water Resources	2	3727.07 5177.86	5035.32
		Ministry of Petroleum & Natural Gas	Oil & Gas	6	13060.36 13090.4	8357.79
		Ministry of Power	Transmission & Distribution	1	5969 5969	167.13
		Ministry of Railways	Railways	3	15702.64 15702.6	8357.15
		Total		14	39018.37	22207.78
29	Rajasthan	Department of Telecommunications	Telecommunication	2	758.54 530.07	352.16
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1367 1367	567.11
		Ministry of Coal	Electricity Generation	1	1813 1813	769.57
		Ministry of Petroleum & Natural Gas	Energy Storage	3	52618.05 82426.1	66707.02



Ongoing Projects State-Wise

JULY 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
29	Rajasthan	Ministry of Petroleum & Natural Gas	Oil & Gas	2	10599 10599	6638.82
		Ministry of Power	Electricity Generation	1	5491.89 5491.89	4606.84
			Transmission & Distribution	22	53646.51 54198.2	15938.13
		Ministry of Railways	Railways	21	86599.23 162169	140736.04
		Total		54	212893.22	236315.69
30	Sikkim	Department of Higher Education	Education	2	999.82 924.82	359.78
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 323.26	29.69
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6375.02
		Ministry of Power	Electricity Generation	2	6686.33 7576.15	6049.43
			Transmission & Distribution	1	4754.42 4754.42	7321.07
		Ministry of Railways	Railways	1	7877 12133	8883.60
		Total		8	29905.83	29018.59
31	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1422.17 1422.17	481.39
		Ministry of Coal	Electricity Generation	1	218.03 218.03	160.93
		Ministry of Housing & Urban Affairs	Inland Waterways	1	63246 63246	47162.73
		Ministry of Mines	Metals & Mining	1	166 166	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	2334 3448.71	1592.52
			Oil & Gas	5	38886 46654	6139.70
		Ministry of Power	Transmission & Distribution	1	548 548	10.96
		Ministry of Railways	Railways	8	8730 11599	5805.89
		Total		22	115550.2	61489.12
32	Telangana	Department of Higher Education	Education	1	262 262	164.40
		Department of Telecommunications	Telecommunication	2	2038.99 2038.99	762.19
		Department of Water Resources, River Development & GR	Water Resources	5	12430.08 37575	11830.43
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	715.65 715.65	411.13
		Ministry of Coal	Coal	9	3890.03 3890.03	2423.61
		Ministry of Health & Family Welfare	Healthcare	1	1028 1365.95	792.24
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	1932 2208	1552.37
		Ministry of Power	Transmission & Distribution	2	5694.56 5694.56	4189.95
		Ministry of Railways	Railways	10	21899.15 25663.2	8692.79
		Total		33	49890.46	30819.11
33	Tripura	Ministry of Petroleum & Natural Gas	Energy Storage	1	656 656	465.73
			Oil & Gas	2	9474.33 9396.51	6440.99
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5253.47
		Total		4	15241.66	12160.19
34	Uttar Pradesh	Department of Higher Education	Education	1	246 246	185.83
		Department of Telecommunications	Telecommunication	3	2336.11 2107.64	948.33
		Department of Water Resources, River Development & GR	Waste & Water	2	1532.96 1532.96	208.64
			Water Resources	4	3694.65 8775.49	7633.54
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	5	6983 7038.2	687.85
		Ministry of Coal	Coal	2	1328.09 1328.09	980.95
			Electricity Generation	1	17237.8 21780.9	20135.48
		Ministry of Housing & Urban Affairs	Real Estate	1	576.99 576.99	141.94
			Urban Public Transport	3	49730.1 49730.1	40947.26
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11068.45 11068.5	7834.35
			Oil & Gas	4	18133 18521.5	1791.69



Ongoing Projects State-Wise

JULY 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
34	Uttar Pradesh	Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3432.34
		Ministry of Power	Electricity Generation	2	28284.42 30471.2	14055.05
			Transmission & Distribution	4	8474.28 8474.28	1903.49
		Ministry of Railways	Railways	26	94574.3 169600	146724.15
		Total		61	249569.33	247610.89
35	Uttarakhand	Department of Higher Education	Education	1	650.85 650.85	130.00
		Department of Water Resources, River Development & GR	Water Resources	1	2584.1 2584.1	486.52
		Ministry of Housing & Urban Affairs	Real Estate	1	150.97 150.97	18.95
		Ministry of Power	Electricity Generation	3	11663.95 26070	19892.29
		Ministry of Railways	Railways	1	38953 38953	24645.15
		Total		7	54002.87	45172.91
36	West Bengal	Department of Higher Education	Education	2	787.2 729.2	692.60
		Department of Telecommunications	Telecommunication	1	1577.57 1577.57	596.17
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 154.73	96.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	2092.47 2092.47	465.48
		Ministry of Coal	Coal	13	15863.74 15863.7	2781.17
		Ministry of Mines	Construction	1	255.37 255.37	78.34
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9701.95
			Oil & Gas	8	18159.65 19007.2	11226.34
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3432.34
			Shipping	2	551.91 551.91	408.80
		Ministry of Power	Electricity Generation	3	20091.84 20160.8	3535.09
			Transmission & Distribution	2	751.63 751.63	0.40
		Ministry of Railways	Railways	15	47377.24 57513.2	32499.77
			Urban Public Transport	1	2298 2734	393.00
		Ministry of Steel	Steel	5	4214.67 4214.67	395.04
		Total		59	129773.2	66302.66




Table 3: Ongoing Projects North Eastern Region



Ongoing Projects of North-East Region							JULY 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	03/2018	03/2025 (-)	1712 (1712)	0	94.1
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	07/2022	07/2024 12/2026	499 (499)	160.48	41
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	12/2023	02/2026 (-)	323.26 (323.26)	29.69	12
	Total (3)				2534.26	190.17	
	Ministry of Coal						
	Coal						
4	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022	07/2031 (-)	159.77 (159.77)	80.84	0
5	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022	11/2030 (-)	289.46 (289.46)	105.47	0
	Total (2)				449.23	186.31	
	Department of Higher Education						
	Education						
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	03/2013	08/2026 (-)	592.61 (592.61)	549.96	75
7	Tezpur University Projects (Tezpur University) (606112)	Assam	06/2021	11/2023 08/2025	153.71 (153.71)	288.87	93
8	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2014	03/2022 07/2025	494.52 (494.52)	413.57	86
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (Ministry of Education) (612876)	Mizoram	05/2014	12/2029 12/2029	474.23 (474.23)	167.55	4
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2012	12/2025 (-)	275.63 (275.63)	257.82	93
11	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	01/2022	01/2025 09/2025	314.06 (314.06)	238.22	82
12	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (Ministry of Education) (612883)	Sikkim	03/2024	02/2028 12/2026	685.76 (610.76)	121.56	7
	Total (7)				2990.52	2037.55	
	Ministry of Power						
	Electricity Generation						
13	Dibang Multipurpose Project (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602182)	Arunachal Pradesh	02/2023	02/2032 02/2032	31876.39 (31876.4)	3436.38	16
14	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	05/2025	07/2029 (-)	1938.85 (1938.85)	49.31	3
15	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	05/2025	07/2029 (-)	1750.07 (1750.07)	102.79	2
16	Subansiri Lower HE Project [2000 MW] (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003	09/2010 05/2026	6285.33 (26075.5)	24685.13	96
17	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602181)	Sikkim	03/2019	03/2024 12/2027	5748.04 (5748.04)	4495.28	68
18	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (605156)	Sikkim	03/2021	05/2024 12/2025	938.29 (1828.11)	1554.15	90
	Total (6)				48536.97	34323.04	
	Transmission & Distribution						
19	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Meghalaya, Manipur, Mizoram, Tripura, Nagaland, Assam)	03/2016	12/2018 09/2025	5111.33 (6700)	5253.47	96
20	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Sikkim, Arunachal Pradesh)	01/2016	12/2018 03/2027	4754.42 (4754.42)	7321.07	81

Ongoing Projects of North-East Region

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (2)				9865.75	12574.54	
	Ministry of Petroleum & Natural Gas						
	Energy Storage						
21	Rajasthan Refinery Project (MinistryofPetroleumNaturalGas) (701263)	Arunachal Pradesh	10/2017	10/2022 03/2026	43129 (72937)	59524.37	87
22	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Assam	01/2019	07/2024 09/2025	10228 (11407)	9701.95	86
23	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023	07/2027 07/2027	156.36 (156.36)	49.78	39
24	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023	07/2027 07/2027	384.04 (384.04)	110.44	48
25	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	06/2022	09/2025 09/2025	656 (656)	465.73	84
	Total (5)				54553.4	69852.27	
	Oil & Gas						
26	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	07/2020	07/2024 12/2025	12366 (22494)	16502.36	75
27	Assam Bio Refinery, ABRPL (Ministry of Petroleum & Natural Gas) (604792)	Assam	02/2018	09/2021 07/2025	1750 (4200)	4650	99
28	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	01/2018	02/2020 12/2025	682.9 (726.93)	488.37	94
29	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	05/2021	10/2023 05/2026	412.3 (577)	430.83	84
30	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	12/2020	03/2024 12/2025	430.76 (430.76)	326.12	85
31	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Assam	06/2021	12/2024 10/2025	860 (860)	566.18	98
32	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (MinistryofPetroleumNaturalGas) (709776)	Assam	04/2022	09/2026 09/2026	277 (323.09)	185.18	67
33	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (MinistryofPetroleumNaturalGas) (709779)	Assam	06/2022	03/2026 03/2026	768 (740)	99.02	35
34	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023	04/2026 04/2026	344.99 (344.99)	210.89	46
35	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	09/2023	05/2026 05/2026	198.7 (198.7)	36.78	29
36	DCU Revamp Project (NRL) (709864)	Assam	08/2021	07/2024 10/2025	370 (370)	249.41	57
37	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	04/2023	12/2024 10/2025	293.5 (293.5)	97.22	93
38	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Sikkim, Arunachal Pradesh, Nagaland, Meghalaya, Assam, Mizoram, Tripura, Manipur)	04/2020	03/2024 03/2026	9265 (9265)	6375.02	85
39	Augmentation/ Revamping of Dimapur Depot, Dimapur (MinistryofPetroleumNaturalGas) (709786)	Nagaland	08/2023	11/2027 11/2027	227.62 (227.62)	9.01	20
40	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022	05/2024 12/2025	209.33 (131.51)	65.97	62
	Total (15)				28456.1	30292.36	
	Ministry of Railways						
	Railways						
41	AGTHORI KAMAKHYA SECTION WITH CONSTRUCTION OF NEW RAIL CUM-ROAD BRIDGE AT SARAIGHAT - 7.062KM (Northeast Frontier Railway [NFR]) (613788)	Assam	05/2025	12/2029 (-)	1473.77 (1473.77)	0	0
42	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016	03/2026 03/2026	4060 (4961)	3683.75	93
43	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2018	09/2020 06/2024	890.36 (889.36)	391.73	89
44	Murkongselek-Pasighat (Northeast Frontier Railway [NFR]) (705401)	Multi-States (Arunachal Pradesh, Assam)	03/2012	03/2025 12/2025	435 (1250)	901	56

Ongoing Projects of North-East Region

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
45	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	01/2025	02/2028 (-)	2123.7 (2123.7)	13.74	0
46	Dimapur [Dhansirij-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Nagaland, Assam)	02/2016	03/2025 12/2025	6663 (6663)	5202.29	79
47	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Sikkim	05/2010	05/2015 12/2027	7877 (12133)	8883.6	80
	Total (7)				23522.83	19076.11	
	Department of Telecommunications						
	Telecommunication						
48	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications [DoT]) (701598)	Meghalaya	09/2020	03/2022 03/2025	971.96 (971.96)	208.25	98
49	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications [DoT]) (701597)	Multi-States (Assam, Arunachal Pradesh)	10/2021	04/2023 09/2025	1255.49 (1255.49)	284.04	89
	Total (2)				2227.45	492.29	
	Department of Water Resources, River Development & GR						
	Water Resources						
50	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	12/1996	12/2022 03/2025	256.16 (256.16)	0	0
51	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997	12/2019 03/2026	1449.44 (1822.24)	1837.91	98
	Total (2)				1705.6	1837.91	




Table 4: All Ongoing Projects



All Ongoing Projects							JULY 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Orignal Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport (Airport Authority of India [AAI]) (612786)	Andhra Pradesh	01/2024	01/2026 03/2026	265.91 (265.91)	45.54	31
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. (Airport Authority of India [AAI]) (701107)	Andhra Pradesh	09/2020	09/2022 12/2025	611.8 (611.8)	464.55	77
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. (Airport Authority of India [AAI]) (701121)	Andhra Pradesh	08/2023	08/2025 12/2025	347.15 (347.15)	81.23	49
4	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	03/2018	03/2025 (-)	1712 (1712)	0	94.1
5	Development of New Civil Enclave at Bihta (Airport Authority of India [AAI]) (612183)	Bihar	03/2025	09/2027 (-)	1413 (1413)	0	1
6	Development of New Civil Enclave and associated works at Darbhanga Airport (Airport Authority of India [AAI]) (612194)	Bihar	07/2024	01/2026 (-)	911.66 (911.66)	133.01	23
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna (Airport Authority of India [AAI]) (701101)	Bihar	10/2018	07/2023 11/2025	1216.9 (1216.9)	1046.48	94
8	Goa Airport Terminal Building Extension Project (Airport Authority of India [AAI]) (701105)	Goa	12/2019	12/2021 09/2025	255.69 (255.69)	130	88
9	Development of Dholera International Greenfield Airport , Gujarat (Airport Authority of India [AAI]) (701126)	Gujarat	07/2022	06/2026 06/2026	1305 (1551)	666.42	63
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. (Airport Authority of India [AAI]) (611047)	Jammu and Kashmir	07/2023	06/2026 06/2026	861.37 (861.37)	154.3	30
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport (Airport Authority of India [AAI]) (612787)	Karnataka	01/2024	01/2026 03/2026	320.47 (320.47)	56.54	36
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. (Airport Authority of India [AAI]) (612788)	Karnataka	02/2024	01/2026 01/2026	322.45 (322.45)	115.82	48
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 (Airport Authority of India [AAI]) (612789)	Kerala	02/2024	09/2025 03/2026	484.57 (484.57)	74.67	19
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh (Airport Authority of India [AAI]) (400010)	Ladakh	09/2018	09/2021 10/2025	480 (640)	427.04	67
15	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	07/2022	07/2024 12/2026	499 (499)	160.48	41
16	Procurement of 30 Nos ACFTs of WT Capacity 10KL at Various Airports (Airport Authority of India [AAI]) (611440)	Multi-States (Andhra Pradesh, Bihar, Delhi, Gujarat, Jharkhand, Karnataka, Kerala, Madhya Pradesh, Odisha, Tamil Nadu, Telangana, Uttar Pradesh, West Bengal)	05/2023	06/2025 (-)	215.17 (215.17)	104.92	53
17	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, MOPA [without ASMGCS], HIAL & BIAL (Airport Authority of India [AAI]) (611570)	Multi-States (Goa, Karnataka, Maharashtra, Telangana)	10/2022	09/2025 (-)	500.48 (500.48)	306.21	74
18	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. (Airport Authority of India [AAI]) (701127)	Rajasthan	04/2023	11/2024 10/2025	480 (480)	254.71	77
19	Construction of New Integrated Passenger Terminal Building at Udaipur Airport (Airport Authority of India [AAI]) (701128)	Rajasthan	11/2022	03/2026 10/2026	887 (887)	312.4	44
20	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	12/2023	02/2026 (-)	323.26 (323.26)	29.69	12
21	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAI]) (611602)	Tamil Nadu	06/2023	07/2025 03/2026	1207 (1207)	376.47	21
22	Construction of New Terminal Building, Second Link Taxi Track, Apron Expansion, and associated works at Prayagraj Airport- On Design & Build Basis. (Airport Authority of India [AAI]) (612063)	Uttar Pradesh	08/2023	11/2024 08/2025	219.18 (274.38)	206.33	97
23	Lucknow Airport-Terminal 3- Phase 1 & Other Associated Works (Adani Airport Holdings Limited) (701091)	Uttar Pradesh	09/2018	03/2026 (-)	3100 (3100)	0	99.96



All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
24	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAI]) (701113)	Uttar Pradesh	07/2024	07/2027 07/2027	2869.65 (2869.65)	302.3	14
25	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAI]) (701122)	Uttar Pradesh	07/2024	07/2026 (-)	579 (579)	74.3	14
26	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAI]) (611495)	West Bengal	10/2023	01/2027 01/2027	1549 (1549)	262.41	10
27	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCB I Airport Kolkata. (Airport Authority of India [AAI]) (612791)	West Bengal	12/2023	02/2025 08/2026	328.3 (328.3)	98.15	44
Total (27)					23265.01	5883.97	
Ministry of Coal							
Coal							
28	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022	07/2031 (-)	159.77 (159.77)	80.84	0
29	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022	11/2030 (-)	289.46 (289.46)	105.47	0
30	PORDA CHIMTAPANI OCP [10 MTY] (South Eastern Coalfields Limited [SECL]) (400144)	Chhattisgarh	12/2020	03/2029 (-)	2310.12 (2310.12)	83.66	10
31	CHHAL OC SEAM III [6 MTY] (South Eastern Coalfields Limited [SECL]) (400145)	Chhattisgarh	12/2013	03/2022 09/2025	610.63 (610.63)	577.46	85
32	KUSMUNDA OC EXPANSION [15 TO 50 MTY] (South Eastern Coalfields Limited [SECL]) (400147)	Chhattisgarh	08/2013	03/2023 03/2030	7612.33 (7612.33)	4697.95	81
33	BAROUD OC EXPANSION [3.0-10.0MTY] (South Eastern Coalfields Limited [SECL]) (400149)	Chhattisgarh	08/2020	03/2029 (-)	2309.8 (2309.8)	913.03	47
34	DIPKA EXPANSION OCP [40 MTY] (South Eastern Coalfields Limited [SECL]) (400354)	Chhattisgarh	12/2020	03/2029 (-)	5241.4 (5241.4)	2675	37
35	GEVRA OC [70 MTY] (South Eastern Coalfields Limited [SECL]) (400424)	Chhattisgarh	03/2016	03/2023 03/2026	11816.4 (11816.4)	5328.96	77
36	JAMPALI OC RCE [2.0 MTY] (SECL - CIL) (613795)	Chhattisgarh	05/2020	03/2025 06/2025	278.64 (278.64)	210.07	82
37	AMERA OC RCE [1.0 MTY] (South Eastern Coalfields Limited [SECL]) (613798)	Chhattisgarh	02/2015	03/2026 (-)	335.97 (335.97)	87.47	42
38	AMGAON OC RCE [1.0 MTY] (South Eastern Coalfields Limited [SECL]) (613799)	Chhattisgarh	07/2015	03/2026 (-)	316.11 (316.11)	188.53	71
39	JAGANNATHPUR OC RCE PROJECT[3.0 MTY] (South Eastern Coalfields Limited [SECL]) (613800)	Chhattisgarh	07/2016	03/2025 03/2026	459.49 (459.49)	274.35	92
40	MAHAMAYA OCP [1.50 MTY] (South Eastern Coalfields Limited [SECL]) (613801)	Chhattisgarh	05/2018	03/2026 (-)	410.26 (410.26)	169.3	38
41	KATKONA RO UG MINE (South Eastern Coalfields Limited [SECL]) (615191)	Chhattisgarh	01/2023	03/2029 (-)	329.21 (329.21)	60.3	2
42	PELMA OC MDO (South Eastern Coalfields Limited [SECL]) (616234)	Chhattisgarh	10/2022	03/2033 (-)	1725.04 (1725.04)	15.63	17
43	KUSMUNDA OC EXPANSION PROJECT 50-75 MTY (SECL - CIL) (617287)	Chhattisgarh	11/2024	03/2030 (-)	4516.88 (4516.88)	16.97	3
44	MANIKPUR OC EXPANSION PROJECT 7 MTY (South Eastern Coalfields Limited [SECL]) (617288)	Chhattisgarh	01/2025	03/2029 (-)	382.61 (382.61)	0.86	1
45	DIPKA OC (SECL - CIL) (612838)	Gujarat	01/2017	03/2025 (-)	7580 (7580)	3091	65
46	HURA C OCP (ECL - CIL) (400018)	Jharkhand	08/2022	03/2029 (-)	859.41 (859.41)	450.47	62
47	KONAR EXPANSION OCP (Ministry of Coal) (400073)	Jharkhand	01/2022	03/2032 (-)	799.34 (799.34)	426.16	46
48	KARO EXPANSION OCP (Ministry of Coal) (400074)	Jharkhand	01/2022	03/2029 (-)	908.47 (908.47)	251.79	22
49	SANGHMITRA OC (Ministry of Coal) (400136)	Jharkhand	03/2027	03/2032 (-)	2660 (2660)	0	0
50	CHANDRAGUPT OCP (Ministry of Coal) (400138)	Jharkhand	08/2020	03/2032 (-)	973.5 (973.5)	440.32	15
51	KOTRE BASANTPUR PACHMO OCP (Ministry of Coal) (400139)	Jharkhand	08/2020	03/2032 (-)	861.06 (625.4)	441.05	41
52	Pachwara South Coal Block (NLC India Limited [NLCIL]) (400142)	Jharkhand	12/2019	09/2028 (-)	2242.9 (2242.9)	1165.64	54



All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
53	RPR MAGADH EXP OCP (Ministry of Coal) (400150)	Jharkhand	08/2020	03/2028 (-)	7254.37 (7254.37)	1534.64	38
54	NORTH URIMARI EXPANSION OCP (Ministry of Coal) (400151)	Jharkhand	07/2021	03/2029 (-)	778.8 (778.8)	695.11	67
55	EPR ROHINI - KARKETTA OCP (Ministry of Coal) (400153)	Jharkhand	01/2021	03/2028 (-)	1020.42 (1020.42)	83.95	20
56	EPR PUNDI OCP (Ministry of Coal) (400154)	Jharkhand	11/2020	03/2027 (-)	713.35 (713.35)	236.57	10
57	EPR ASHOK OC (Ministry of Coal) (400155)	Jharkhand	05/2021	03/2028 (-)	2898.28 (2898.28)	176.6	21
58	EPR AMRAPALI OCP (Ministry of Coal) (400156)	Jharkhand	02/2020	03/2028 (-)	5136.15 (5136.15)	1125.18	43
59	RAJRAPPA RCE OCP (Ministry of Coal) (400160)	Jharkhand	12/2009	03/2016 03/2027	510.85 (510.85)	488.57	76
60	CHITRA EAST OC (Eastern Coal Fields Limited [ECL]) (400172)	Jharkhand	08/2018	03/2026 (-)	513.99 (513.99)	228.71	51
61	JHARKHAND-LAIYO OCP (Ministry of Coal) (400352)	Jharkhand	08/2020	03/2031 (-)	764.57 (764.57)	145.81	25
62	MOONIDIH XV SEAM UG (BCCL - CIL) (400425)	Jharkhand	08/2011	03/2019 05/2026	1230.27 (1230.27)	624.17	81
63	2.5 MTPA PATHERDIH NLW WASHERY (Ministry of Coal) (611017)	Jharkhand	04/2016	04/2018 03/2026	334.27 (334.27)	138.69	48
64	AMALAGAMATED NTST KUJAMA OCP 8.5MTY (Ministry of Coal) (611864)	Jharkhand	01/2023	03/2030 (-)	4011.85 (4011.85)	398.5	28
65	MURADIDH UG PROJECT (Ministry of Coal) (613808)	Jharkhand	02/2011	04/2014 12/2026	339.87 (339.87)	190.65	70
66	TAPIN SOUTH EXPN (Ministry of Coal) (615349)	Jharkhand	11/2020	03/2028 (-)	230.41 (230.41)	21	20
67	SIRKA OC (Ministry of Coal) (615822)	Jharkhand	05/2020	03/2028 (-)	222.82 (222.82)	139.31	60
68	TETARIAKHAR OC (Ministry of Coal) (615843)	Jharkhand	11/2019	03/2025 03/2027	243.52 (243.52)	44.64	28
69	CHUPERBHITA SIMLONG OCP MDO 6 MTY (Eastern Coal Fields Limited [ECL]) (616225)	Jharkhand	12/2023	03/2037 (-)	979.08 (979.08)	0	0
70	JARANGDIH EXPN. OCP 1.5 MTY (CCL - CIL) (616236)	Jharkhand	02/2020	03/2029 (-)	414.37 (414.37)	85.6	26
71	BLOCK E OCP (Ministry of Coal) (616253)	Jharkhand	03/2024	03/2029 (-)	5850.83 (5850.83)	0	2
72	AMADAND OCP[4.0MTY] (Ministry of Coal) (400148)	Madhya Pradesh	03/2016	03/2021 03/2027	869.44 (869.44)	274.45	75
73	RAMPUR BATURA OCP [4.0MTY] (South Eastern Coalfields Limited [SECL]) (400152)	Madhya Pradesh	07/2019	03/2026 (-)	1248.93 (1248.93)	495.4	44
74	BLOCK B EXPANSION [3.5 TO 8.0 MTPA] OPENCAST COAL MINING PROJECT (Northern Coalfields Limited [NCL]) (400162)	Madhya Pradesh	07/2019	03/2023 03/2027	998.71 (998.71)	458.01	46
75	NIGAH I EXPANSION [15 TO 25 MTPA] OPENCAST MINING PROJECT (Northern Coalfields Limited [NCL]) (400321)	Madhya Pradesh	11/2020	03/2025 03/2028	1729.68 (1729.68)	772.91	44
76	KANCHAN OC EXP (South Eastern Coalfields Limited [SECL]) (613802)	Madhya Pradesh	12/2014	03/2026 (-)	371.04 (371.04)	144.61	47
77	JHIRIA WEST OCP [1.5 MTY] (South Eastern Coalfields Limited [SECL]) (613803)	Madhya Pradesh	01/2024	03/2026 (-)	366.94 (366.94)	25.07	41
78	RPR TAWA-III UG 0.84 MTY (WCL - CIL) (613804)	Madhya Pradesh	12/2021	03/2027 (-)	314.09 (314.09)	5.7	17
79	AMALGAMATED DHANKASA & JAMUNIA UG (Western Coalfields Limited [WCL]) (615185)	Madhya Pradesh	09/2022	03/2027 (-)	399.2 (399.2)	72.21	67
80	RPR OF VISHNUPURI UG TO OC (Western Coalfields Limited [WCL]) (615187)	Madhya Pradesh	11/2022	03/2029 (-)	220.62 (220.62)	0	11
81	URDHAN EXPANSION OC COST PLUS (Western Coalfields Limited [WCL]) (615194)	Madhya Pradesh	01/2023	03/2031 (-)	206.88 (206.88)	23.22	1
82	SHARDA UG MINE (Western Coalfields Limited [WCL]) (615195)	Madhya Pradesh	09/2023	03/2028 (-)	166.25 (166.25)	2.78	9
83	GANDHIGRAM UG MINE (Western Coalfields Limited [WCL]) (615206)	Madhya Pradesh	08/2019	03/2026 (-)	414.15 (414.15)	13.27	57



All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
84	BHATADI EXPANSION OC (<i>Western Coalfields Limited [WCL]</i>) (400033)	Maharashtra	05/2022	03/2028 (-)	580.61 (580.61)	20.52	26
85	AMALGAMATED YEKONA I & YEKONA II OC (<i>Western Coalfields Limited [WCL]</i>) (400177)	Maharashtra	08/2015	03/2025 03/2026	727.28 (727.28)	524.54	80
86	DINESH[MAKARDHOKRA-III] OC (<i>Western Coalfields Limited [WCL]</i>) (400178)	Maharashtra	02/2020	03/2027 (-)	822.88 (822.88)	621.73	35
87	DHUPTALA OC [SASTI UG TO OC] (<i>Western Coalfields Limited [WCL]</i>) (400353)	Maharashtra	10/2021	03/2028 (-)	711.01 (711.01)	80.33	17
88	SAONER UG MINE -1 EXPANSION 1.2 MTY (<i>Western Coalfields Limited [WCL]</i>) (615184)	Maharashtra	01/2022	03/2028 (-)	228.64 (228.64)	139.81	68
89	SASTI EXPANSION OPENCAST (<i>Western Coalfields Limited [WCL]</i>) (615186)	Maharashtra	08/2020	03/2026 (-)	319.04 (319.04)	90.96	20
90	NEW MAJRI UG TO OC 3 MTY COST PLUS (<i>Western Coalfields Limited [WCL]</i>) (615188)	Maharashtra	09/2022	03/2027 (-)	402.27 (402.27)	41.08	24
91	MAKARDHOKRA EXPN OC 4.9 MTY (<i>Western Coalfields Limited [WCL]</i>) (615189)	Maharashtra	06/2022	03/2026 (-)	361.87 (361.87)	67.64	12
92	SINGHORI DEEP OC MIN 2.0 MTY (<i>Western Coalfields Limited [WCL]</i>) (615190)	Maharashtra	05/2022	03/2029 (-)	335.75 (335.75)	26.64	6
93	GOKUL EXTENSION OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615192)	Maharashtra	04/2021	03/2026 (-)	309.58 (309.58)	29.85	8
94	KOLGAON EXPANSION DEEP OC MINE 0.80 MTY (<i>Western Coalfields Limited [WCL]</i>) (615199)	Maharashtra	09/2023	03/2027 (-)	198.71 (198.71)	0.71	3
95	BALLARPUR NORTH WEST OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615330)	Maharashtra	12/2022	03/2029 (-)	360.81 (360.81)	0	4
96	GADEGAON OC 3 MTY (<i>Western Coalfields Limited [WCL]</i>) (615331)	Maharashtra	10/2023	03/2030 (-)	497.41 (497.41)	0	0
97	GHONSA EXPANSION DEEP OC MINE 1.5 MTY (<i>Western Coalfields Limited [WCL]</i>) (615914)	Maharashtra	03/2021	03/2029 (-)	184.71 (184.71)	10.48	6
98	AMLG GAURI PAUNI EXPANSION OC - 9.0 MTY (<i>Western Coalfields Limited [WCL]</i>) (615916)	Maharashtra	04/2024	03/2030 (-)	1225.21 (1225.21)	78.41	1
99	GAURIDEEP/GAURI CENTRAL OCP 7.00 MTY CP (<i>Western Coalfields Limited [WCL]</i>) (615917)	Maharashtra	06/2024	03/2030 (-)	973.07 (973.07)	0.11	0
100	RPR OF BHANEGAON OC (<i>Western Coalfields Limited [WCL]</i>) (615918)	Maharashtra	09/2022	03/2028 (-)	405.2 (405.2)	11.71	8
101	N. EXTN. MUNGOLI NIRGUDA D OCP 6.125 MTY (<i>Western Coalfields Limited [WCL]</i>) (615919)	Maharashtra	06/2024	03/2030 (-)	1024.91 (1024.91)	165.54	0
102	NILJAI EXPANSION DEEP OCP (<i>Western Coalfields Limited [WCL]</i>) (615982)	Maharashtra	08/2016	03/2022 03/2026	319.75 (319.75)	367.6	79
103	UKNI DEEP OC MINE -COST PLUS (<i>Western Coalfields Limited [WCL]</i>) (616044)	Maharashtra	01/2019	03/2021 03/2026	237.06 (237.06)	159.21	87
104	AMALGAMATED INDER-KAMPTEE DEEP OC (<i>Western Coalfields Limited [WCL]</i>) (616050)	Maharashtra	09/2018	03/2024 03/2026	235.9 (235.9)	237.12	98
105	ADASA UG TO OC MINE (<i>Western Coalfields Limited [WCL]</i>) (616223)	Maharashtra	11/2018	03/2024 03/2026	316 (316)	308.84	86
106	AMAL GONDEGAON GHATROHANA EXPN OCP (<i>Western Coalfields Limited [WCL]</i>) (616229)	Maharashtra	09/2024	03/2030 (-)	668.54 (668.54)	0.53	0
107	WAGHODA UG MINE [1.02 MTY] (<i>Western Coalfields Limited [WCL]</i>) (617233)	Maharashtra	01/2025	03/2030 (-)	379.3 (379.3)	0	0
108	KOLARPIMPRI EXPANSION OC [2.5 MTY] (<i>Western Coalfields Limited [WCL]</i>) (617278)	Maharashtra	02/2025	03/2030 (-)	630.37 (630.37)	0	0
109	Master Plan for Jharia and Raniganj Coalfields (<i>Bharat Coking Coal Limited [BCCL]</i>) (400313)	Multi-States (Jharkhand, West Bengal)	08/2009	08/2019 12/2028	2661.73 (2661.73)	787.75	43
110	BINA KAKRI AMALGAMATION EXPANSION OPENCAST MINING PROJECT [14 MTPA] (<i>Northern Coalfields Limited [NCL]</i>) (400369)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020	03/2024 03/2027	836.42 (836.42)	778.77	89
111	KHADIA EXPANSION [10 TO 16 MTPA] OPENCAST MINING PROJECT (<i>Northern Coalfields Limited [NCL]</i>) (615183)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021	03/2025 03/2027	491.67 (491.67)	202.18	40
112	SUBHADRA OCP (<i>Mahanadi Coalfields Limited (MCL)</i>) (400165)	Odisha	05/2021	03/2029 03/2029	1693.81 (1693.81)	1278.66	42
113	SIARMAL OCP (<i>Mahanadi Coalfields Limited (MCL)</i>) (400166)	Odisha	02/2021	03/2029 03/2028	5194.95 (5194.95)	3455.65	54
114	BHUBANESWARI EXPANSION OCP (<i>Mahanadi Coalfields Limited (MCL)</i>) (400179)	Odisha	01/2023	03/2031 (-)	3145.45 (6321.73)	1250.66	21



All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
115	BALARAM EXPANSION OCP (<i>Mahanadi Coalfields Limited (MCL)</i>) (400183)	Odisha	08/2020	03/2029 (-)	3504.21 (3504.21)	1027.23	52
116	GOPALJI KANIHA OCP [10 TO 30 MTY] (<i>Mahanadi Coalfields Limited (MCL)</i>) (400185)	Odisha	04/2022	03/2030 (-)	8416.19 (6107.87)	1694.31	17
117	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP (<i>Mahanadi Coalfields Limited (MCL)</i>) (400187)	Odisha	05/2018	03/2027 (-)	2434.75 (2434.75)	1805.65	61
118	BHARATPUR RE-ORGANIZATION OCP (<i>Mahanadi Coalfields Limited (MCL)</i>) (400392)	Odisha	11/2018	03/2029 (-)	2838.86 (2838.86)	1748.9	47
119	BASUNDHARA WEST EXTENSION OPENCAST PRO (<i>Mahanadi Coalfields Limited (MCL)</i>) (615193)	Odisha	05/2014	03/2027 (-)	479.15 (479.15)	259.2	62
120	Naini Coal Mine (<i>Singareni Collieries Company Limited [SCCL]</i>) (615857)	Odisha	03/2020	03/2026 (-)	494.3 (494.3)	491.33	80
121	INTEGRATED KULDA GARJANBAHAL OCP 40 MTY (<i>Mahanadi Coalfields Limited (MCL)</i>) (616226)	Odisha	04/2023	03/2033 (-)	3563.5 (3563.5)	150.7	3
122	BHUBANESWARI EXPN OCP 50 MTY (<i>Mahanadi Coalfields Limited (MCL)</i>) (616231)	Odisha	03/2024	03/2033 (-)	5366.27 (5366.27)	0	3
123	HINGULA II OC EXPN PH III 15 MTY (<i>Mahanadi Coalfields Limited (MCL)</i>) (616232)	Odisha	11/2022	03/2029 (-)	1561.85 (1561.85)	50.15	23
124	BALABHADRA OCP (<i>Mahanadi Coalfields Limited (MCL)</i>) (616233)	Odisha	04/2023	03/2030 (-)	978.44 (978.44)	211.36	8
125	Jawahar Khani Open Cast Mine (<i>Singareni Collieries Company Limited [SCCL]</i>) (615818)	Telangana	12/2021	03/2025 03/2027	297.88 (297.88)	46.39	20
126	Kalyanikhani Opencast Project (<i>Singareni Collieries Company Limited [SCCL]</i>) (615858)	Telangana	05/2017	03/2026 (-)	384.32 (384.32)	281.83	75
127	Kakathiya Khani Opencast - III Project Phase - I (<i>Singareni Collieries Company Limited [SCCL]</i>) (615859)	Telangana	05/2017	03/2026 (-)	413.84 (413.84)	397.55	79
128	Godavarikhani Coal Mine - 5 (<i>Singareni Collieries Company Limited [SCCL]</i>) (615860)	Telangana	05/2019	03/2025 03/2026	607.04 (607.04)	178.82	71
129	Indaram Opencast Project (<i>Singareni Collieries Company Limited [SCCL]</i>) (615861)	Telangana	12/2022	03/2025 03/2026	424.81 (424.81)	402.64	80
130	Goleti Opencast Mine (<i>Singareni Collieries Company Limited [SCCL]</i>) (615862)	Telangana	08/2021	03/2026 (-)	345.6 (345.6)	73.25	20
131	Venkatesh Khani Coal Mine (<i>Singareni Collieries Company Limited [SCCL]</i>) (615863)	Telangana	06/2020	03/2026 (-)	484.5 (484.5)	434.44	75
132	Ramagundam OC-II Extension Project (<i>Singareni Collieries Company Limited [SCCL]</i>) (615864)	Telangana	06/2015	03/2026 (-)	489.62 (489.62)	405.54	77
133	Kakatiyakhani OC - 2 Project (<i>Singareni Collieries Company Limited [SCCL]</i>) (615865)	Telangana	09/2017	03/2025 03/2026	442.42 (442.42)	203.15	63
134	MOHANPUR EXPANSION OC -PHASE II (<i>Eastern Coal Fields Limited [ECL]</i>) (400173)	West Bengal	11/2020	03/2026 (-)	888.99 (888.99)	85.51	30
135	BONJEMEHARI EXPANSION OCP (<i>Eastern Coal Fields Limited [ECL]</i>) (400180)	West Bengal	08/2021	03/2026 03/2026	570.11 (570.11)	81.29	16
136	NAKRAKONDA KUMARDIH- B OCP (<i>Eastern Coal Fields Limited [ECL]</i>) (400181)	West Bengal	08/2018	03/2029 (-)	502.68 (502.68)	70.97	25
137	SIDULI [OC & UG] (<i>ECL - CIL</i>) (400182)	West Bengal	05/2018	03/2027 (-)	535.18 (535.18)	5.05	14
138	TILABONI UG (<i>Eastern Coal Fields Limited [ECL]</i>) (400186)	West Bengal	03/2023	03/2029 03/2029	749.08 (749.08)	51.73	10
139	JHANJRA EXPANSION UG (<i>Eastern Coal Fields Limited [ECL]</i>) (400312)	West Bengal	04/2020	03/2029 (-)	1210.12 (1210.12)	514.93	40
140	SONEPUR BAZARI EXPANSION OCP [12 MTY] (<i>Eastern Coal Fields Limited [ECL]</i>) (400315)	West Bengal	07/2021	03/2029 (-)	5365.88 (5365.88)	571.02	17
141	2.0 MTPA BHOJUDIH NLW WASHERY (<i>Ministry of Coal</i>) (611016)	West Bengal	03/2019	09/2020 09/2025	384.57 (384.57)	353.21	97
142	ITAPARA OCP (<i>Eastern Coal Fields Limited [ECL]</i>) (612816)	West Bengal	12/2023	03/2030 (-)	929.1 (929.1)	65.61	7
143	SHYAMSUNDARPUR UG INCLUDING SARPI (<i>Eastern Coal Fields Limited [ECL]</i>) (613793)	West Bengal	04/2020	03/2026 (-)	483.65 (483.65)	55.89	12
144	PARASEA-BELBAID UG PROJECT (<i>Eastern Coal Fields Limited [ECL]</i>) (613794)	West Bengal	01/2023	03/2028 (-)	389.1 (389.1)	131.42	16
145	PARASCOLE JAMBAD OCP (<i>Eastern Coal Fields Limited [ECL]</i>) (616230)	West Bengal	11/2024	03/2037 (-)	1193.55 (1193.55)	6.79	0

All Ongoing Projects							JULY 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Orignal Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (118)				169952.27	52990.5	
	Electricity Generation						
146	50 MW Wind Power Project (NLC India Limited [NLCIL]) (617299)	Gujarat	02/2024	06/2025 01/2026	383.84 (383.84)	303.5	41
147	NLC Talabira Thermal Power Project (NLC India Limited [NLCIL]) (400231)	Odisha	01/2024	03/2030 (-)	27212.96 (27213)	1938.68	1
148	300 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (612819)	Rajasthan	03/2023	09/2024 09/2025	1813 (1813)	769.57	68
149	50 MW Solar PP Minedout Area (NLC India Limited [NLCIL]) (615327)	Tamil Nadu	02/2024	03/2025 09/2025	218.03 (218.03)	160.93	46
150	Ghatampur Thermal Power Plant 3 X 660 MW (NLC India Limited [NLCIL]) (400259)	Uttar Pradesh	08/2016	11/2020 10/2025	17237.8 (21780.9)	20135.48	92
	Total (5)				46865.63	23308.16	
	Railways						
151	Dharamjaigarh-Korba (WR) (400203)	Chhattisgarh	03/2017	12/2026 08/2026	1686.22 (1686.22)	342.96	40
152	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] (Ministry of Coal) (400416)	Jharkhand	05/2022	06/2025 (-)	1799.64 (1799.64)	1293.71	60
	Total (2)				3485.86	1636.67	
	Ministry of Power						
	Coal						
153	Tubed Coal Mine (Damodar Valley Corporation) (400192)	Jharkhand	10/2016	05/2026 05/2026	1581 (1581)	599.18	34
154	Badam Coal Mining project of NTPC (National Thermal Power Corporation [NTPC]) (603293)	Jharkhand	09/2019	12/2056 04/2027	502 (784)	302.2	59
	Total (2)				2083	901.38	
	Electricity Generation						
155	Dibang Multipurpose Project (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602182)	Arunachal Pradesh	02/2023	02/2032 02/2032	31876.39 (31876.4)	3436.38	16
156	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	05/2025	07/2029 (-)	1938.85 (1938.85)	49.31	3
157	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	05/2025	07/2029 (-)	1750.07 (1750.07)	102.79	2
158	Buxar Thermal Power Project [1320 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602579)	Bihar	06/2019	01/2024 11/2025	10439.09 (13756.6)	11970.96	92
159	Lara Super Thermal Power Project Stage-II [2 x 800 MW] (National Thermal Power Corporation [NTPC]) (611930)	Chhattisgarh	08/2023	06/2028 (-)	15530 (15530)	2288	14
160	Sipat Super Thermal Power Project, Stage-III [1x800 MW] (National Thermal Power Corporation [NTPC]) (617188)	Chhattisgarh	09/2024	09/2029 (-)	9791 (9791)	0	0
161	Bagodara Solar Power Project (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709747)	Gujarat	05/2021	12/2025 12/2025	339.35 (339.35)	317.59	51
162	Dhaultasidh Hydro Electric Project [66 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602582)	Himachal Pradesh	05/2021	11/2025 03/2027	687.97 (1511.87)	908.65	67
163	Luhri Stage-I Hydro Electric Project [210 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602593)	Himachal Pradesh	11/2020	01/2026 08/2029	1810.56 (3584.53)	1742.92	51
164	382 MW Sunni Dam HEP (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602633)	Himachal Pradesh	04/2018	03/2027 (-)	2615 (2615)	495.57	0.5
165	Sunni Dam Hydro Electric Project [382 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (611586)	Himachal Pradesh	01/2023	04/2028 12/2028	2614.51 (4540.71)	956.76	29
166	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602525)	Jammu and Kashmir	02/2018	04/2020 09/2026	8112.12 (8112.12)	6916.1	71
167	Kiru HE Project (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602532)	Jammu and Kashmir	03/2019	09/2023 03/2026	4287.59 (4287.59)	3055.87	66
168	Ratle HE Project - 850 MW, Ratle Hydroelectric Power Corporation Limited. (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602535)	Jammu and Kashmir	02/2021	02/2026 08/2029	5281.94 (5281.94)	1009.79	24
169	Kwar HE Project (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (605155)	Jammu and Kashmir	05/2022	11/2026 (-)	4526.12 (4526.12)	1078.61	23
170	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] (National Thermal Power Corporation [NTPC]) (400261)	Jharkhand	11/2017	03/2023 11/2026	17112 (20302)	17365	81
171	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand (Damodar Valley Corporation) (611509)	Jharkhand	11/2024	03/2029 (-)	14358 (14358)	1116.7	1

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
172	OMKARESHWAR FLOATING SOLAR POWER PROJECT [90 MW] <i>(Satluj Jal Vidyut Nigam [SJVN] Thermal Limited)</i> (709820)	Madhya Pradesh	11/2022	08/2024 (-)	646.17 (646.17)	0	0
173	Subansiri Lower HE Project [2000 MW] <i>(National Highways & Infrastructure Development Corporation Ltd. [NHIDCL])</i> (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003	09/2010 05/2026	6285.33 (26075.5)	24685.13	96
174	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion <i>(National Thermal Power Corporation [NTPC])</i> (602961)	Odisha	09/2022	05/2027 03/2028	11843.75 (12543)	3975	26
175	BIKANER SOLAR POWER PROJECT <i>(Satluj Jal Vidyut Nigam [SJVN] Thermal Limited)</i> (709748)	Rajasthan	05/2022	04/2024 12/2025	5491.89 (5491.89)	4606.84	82
176	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] <i>(National Highways & Infrastructure Development Corporation Ltd. [NHIDCL])</i> (602181)	Sikkim	03/2019	03/2024 12/2027	5748.04 (5748.04)	4495.28	68
177	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] -A wholly owned subsidiary of NHPC Ltd. acquired through NCLT <i>(National Highways & Infrastructure Development Corporation Ltd. [NHIDCL])</i> (605156)	Sikkim	03/2021	05/2024 12/2025	938.29 (1828.11)	1554.15	90
178	Khurja super Thermal Power Plant [2X660 MW] <i>(THDC India Limited)</i> (602194)	Uttar Pradesh	08/2019	02/2024 08/2025	11089.42 (13276.2)	12429.05	96
179	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] <i>(National Thermal Power Corporation [NTPC])</i> (612142)	Uttar Pradesh	03/2024	02/2030 (-)	17195 (17195)	1626	8
180	Tapovan-Vishnugad HEP [4x130 MW] <i>(National Thermal Power Corporation [NTPC])</i> (602185)	Uttarakhand	11/2006	03/2013 04/2029	2978 (10907.3)	7123.58	77
181	Tehri Pumped Storage Plant Project [4x250 MW] <i>(THDC India Limited)</i> (602193)	Uttarakhand	06/2011	06/2022 11/2025	4825.6 (8339)	7939.82	98
182	Vishnugad Pipalkoti Hydro Electric Project [444 MW] <i>(THDC India Limited)</i> (602195)	Uttarakhand	01/2014	12/2022 03/2027	3860.35 (6823.72)	4828.89	72
183	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal <i>(Damodar Valley Corporation)</i> (400062)	West Bengal	02/2025	06/2029 (-)	17673 (17673)	1183.7	1
184	Rammam-III HEPP [3x40 MW] <i>(National Thermal Power Corporation [NTPC])</i> (602184)	West Bengal	09/2014	09/2019 03/2029	1381.84 (1381.84)	1266	45
185	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 <i>(Damodar Valley Corporation)</i> (602538)	West Bengal	02/2021	01/2024 12/2025	1037 (1106)	1085.39	91
Total (31)					224064.24	129609.83	
Transmission & Distribution							
186	Transmission Scheme for Solar Energy Zone in Ananthpuram 2500MW and Kurnool 1000MW <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (611967)	Andhra Pradesh	09/2023	09/2025 04/2026	1248.69 (1248.69)	820.26	78
187	Augmentation of 1x1500 MVA 3rd 765/400 kV transformation capacity at Kurnool New Substation <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (612856)	Andhra Pradesh	12/2023	09/2025 11/2025	163.61 (163.61)	50.72	39
188	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (617183)	Andhra Pradesh	03/2025	12/2027 (-)	2886 (2886)	28.86	0
189	Western Region Expansion Scheme-XXV <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (611737)	Chhattisgarh	02/2023	11/2023 09/2025	385.84 (385.84)	378.16	96
190	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part B <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (611656)	Gujarat	03/2023	03/2025 10/2025	1167.55 (1167)	1013.39	91
191	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part C <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (611657)	Gujarat	03/2023	03/2025 11/2025	2820.99 (2820.99)	2454.26	84
192	Establishment of Khavda Pooling Station-2 KPS2 in Khavda RE Park KPS2 TRANSMISSION SYSTEM LIMITED <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (611660)	Gujarat	03/2023	12/2024 08/2025	966.79 (966.79)	894.76	95
193	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (612139)	Gujarat	12/2023	12/2025 06/2026	3751.82 (3751.82)	1500.72	21
194	Transmission System for Evacuation of Power from potential Renewable Energy zone in Khavda Area of Gujarat under Phase IV [7 GW] Part E3 <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (612151)	Gujarat	07/2023	07/2025 10/2025	334 (334)	70.44	22
195	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (612855)	Gujarat	05/2024	05/2026 02/2026	679 (679)	81.48	18
196	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (615342)	Gujarat	10/2024	07/2026 (-)	329 (329)	9.97	1
197	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (615343)	Gujarat	11/2024	11/2026 (-)	501 (501)	5.01	1

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
198	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345)	Gujarat	10/2024	10/2026 (-)	4766 (4766)	513.29	5
199	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069)	Gujarat	02/2025	02/2027 (-)	466 (466)	6.99	0
200	Augmentation of Banaskantha [Raghnesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182)	Gujarat	03/2025	03/2027 (-)	172 (172)	1.72	0
201	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272)	Haryana	06/2024	12/2026 (-)	370 (370)	1	1
202	Transmission system for evacuation of Power from Pakaldul HEP in Chenab Valley HEPs - LTA System (Power Grid Corporation of India Limited [POWERGRID]) (608302)	Jammu and Kashmir	02/2022	04/2025 08/2025	318.12 (318.12)	286.31	99
203	Transmission Scheme for evacuation of Power from Ratle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179)	Jammu and Kashmir	07/2024	07/2026 (-)	218.6 (218.6)	0	0
204	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140)	Karnataka	12/2023	12/2025 (-)	2889.39 (2889.39)	1154.31	37
205	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672)	Karnataka	01/2025	06/2027 (-)	1354 (1354)	16.65	0
206	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068)	Karnataka	02/2025	06/2027 (-)	288 (288)	5.76	0
207	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184)	Karnataka	03/2025	09/2027 (-)	3453 (3453)	20.7	0
208	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344)	Madhya Pradesh	10/2024	10/2026 (-)	3674 (3674)	408.18	13
209	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346)	Madhya Pradesh	08/2024	08/2026 (-)	2708 (2708)	649.92	26
210	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279)	Madhya Pradesh	06/2025	12/2027 (-)	558 (558)	5.58	0
211	Transmission System for Evacuation of power from Potential RE Zone in Khavda Area of Gujarat under phase IV 7GW-Part E4 (Power Grid Corporation of India Limited [POWERGRID]) (611966)	Maharashtra	11/2023	07/2025 11/2025	224.41 (224.41)	22.44	9
212	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185)	Multi-States (Andhra Pradesh, Karnataka)	03/2025	03/2027 (-)	5550 (5550)	111	0
213	Transmission System for Kurnool Wind Energy Zone/ Solar Energy Zone Part-A and Part-B (Power Grid Corporation of India Limited [POWERGRID]) (900808)	Multi-States (Andhra Pradesh, Telangana)	03/2023	11/2024 12/2025	3546.94 (3546.94)	3121.3	94
214	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	01/2016	12/2018 03/2027	4754.42 (4754.42)	7321.07	81
215	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	03/2016	12/2018 09/2025	5111.33 (6700)	5253.47	96
216	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271)	Multi-States (Bihar, Odisha, West Bengal)	09/2024	03/2026 (-)	342.69 (342.69)	0.2	0
217	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270)	Multi-States (Bihar, West Bengal)	11/2024	05/2026 (-)	408.94 (408.94)	0.2	0
218	Transmission Network Expansion in Gujarat to increase its ATC from ISTS Part B (Power Grid Corporation of India Limited [POWERGRID]) (400005)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	07/2022	06/2023 12/2025	4546.26 (4546.26)	4148.46	93
219	Transmission System Strengthening Scheme for evacuation of power from SEZ in Rajasthan 8.1 GW under Phase II Part G (Power Grid Corporation of India Limited [POWERGRID]) (608922)	Multi-States (Delhi, Haryana, Rajasthan)	05/2022	11/2023 11/2025	1666 (2218)	2139.28	95

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
220	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735)	Multi-States (Delhi, Rajasthan)	12/2022	03/2025 04/2026	331 (331)	75.92	28
221	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132)	Multi-States (Delhi, Rajasthan)	02/2024	08/2025 05/2026	2000 (2000)	1314.8	59
222	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan 8.1 GW under Phase II- Part- G1 (Power Grid Corporation of India Limited [POWERGRID]) (608301)	Multi-States (Delhi, Uttar Pradesh)	02/2022	09/2023 11/2025	359.47 (359.47)	330.71	93
223	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347)	Multi-States (Gujarat, Maharashtra)	11/2024	05/2029 (-)	24819 (24819)	1489.14	1
224	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024	11/2026 (-)	5969 (5969)	167.13	4
225	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Siwani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340)	Multi-States (Haryana, Rajasthan)	11/2024	11/2026 (-)	5357 (5357)	267.85	8
226	Transmission System for Strengthening of Srinagar-Leh Tr. System (Power Grid Corporation of India Limited [POWERGRID]) (606781)	Multi-States (Jammu and Kashmir, Ladakh)	03/2022	12/2024 09/2025	288.71 (288.71)	202.1	59
227	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138)	Multi-States (Karnataka, Telangana)	02/2024	02/2026 (-)	2147.62 (2147.62)	1068.65	55
228	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024	08/2026 (-)	2227 (2227)	534.48	19
229	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024	08/2026 (-)	3251 (3251)	685.96	17
230	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [Rajasthan V Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025	03/2027 (-)	5028 (5028)	139.2	1
231	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023	12/2025 06/2026	2056 (2056)	1336.4	55
232	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024	12/2026 (-)	5846 (5846)	236.18	3
233	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan[8.1 GW] under phase-II- Part E (Power Grid Corporation of India Limited [POWERGRID]) (611659)	Rajasthan	03/2023	09/2024 10/2025	1433.28 (1433)	1341.7	93
234	Transmission System for Evacuation of Power from REZ in Rajasthan 20GW under Phase III- Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (611947)	Rajasthan	11/2023	06/2025 09/2025	428.3 (428.3)	107.07	46
235	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part H (Power Grid Corporation of India Limited [POWERGRID]) (611948)	Rajasthan	10/2023	04/2025 12/2025	2211.29 (2211.29)	1780.53	72
236	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949)	Rajasthan	10/2023	04/2025 10/2025	1796.02 (1796.02)	1201.17	79
237	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part B1 (Power Grid Corporation of India Limited [POWERGRID]) (611950)	Rajasthan	09/2023	04/2025 12/2025	2190.54 (2190.54)	1740.6	77
238	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part E1 (Power Grid Corporation of India Limited [POWERGRID]) (611951)	Rajasthan	08/2023	02/2025 09/2025	688.74 (688.74)	585.42	93
239	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134)	Rajasthan	12/2023	12/2025 03/2026	2998.34 (2998.34)	1592.11	49
240	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332)	Rajasthan	08/2024	08/2026 (-)	3279 (3279)	547.59	19
241	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615335)	Rajasthan	08/2024	08/2026 (-)	1382 (1382)	41.46	2

All Ongoing Projects							JULY 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
242	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615337)	Rajasthan	08/2024	02/2026 (-)	369 (369)	17.82	6
243	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615338)	Rajasthan	11/2024	11/2026 (-)	2735 (2735)	81.42	5
244	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617181)	Rajasthan	03/2025	12/2026 (-)	404 (404)	4.04	0
245	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Tarnsmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616671)	Tamil Nadu	01/2025	12/2026 12/2026	548 (548)	10.96	4
246	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex (Power Grid Corporation of India Limited [POWERGRID]) (617269)	Uttar Pradesh	12/2024	06/2026 (-)	212.81 (212.81)	0.2	0
Total (61)					142976.51	49396.47	
Ministry of Housing & Urban Affairs							
Construction							
247	C/o 184 MS Flats for Hon'ble MPs at BKS Marg, New Delhi (Central Public Works Department [CPWD]) (617282)	Delhi	05/2022	05/2025 08/2025	646.53 (646.52)	518.46	98
Total (1)					646.53	518.46	
Inland Waterways							
248	Chennai Metro Rail Phase-II Development Project (Chennai Metro Rail Limited [CMRL]) (702668)	Tamil Nadu	11/2020	08/2029 (-)	63246 (63246)	47162.73	0
Total (1)					63246	47162.73	
Real Estate							
249	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System (Smart City Mission) (707229)	Andaman & Nicobar	11/2021	05/2023 (-)	209.88 (209.88)	0	0
250	In-Situ Slum Redevelopment Project in Bihar (PMAY, Ministry of Housing and Urban Affairs) (702522)	Bihar	06/2015	03/2024 (-)	454.65 (454.65)	204.64	0
251	In-Situ Slum Redevelopment Project in Haryana (PMAY, Ministry of Housing and Urban Affairs) (702544)	Chandigarh	06/2015	03/2024 (-)	285.85 (285.85)	127.58	0
252	Affordable Housing Construction Project in Chhattisgarh (PMAY, Ministry of Housing and Urban Affairs) (702524)	Chhattisgarh	06/2015	03/2024 (-)	3797.69 (3797.69)	2694	0
253	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi (National Buildings Construction Corporation [NBCC]) (400188)	Delhi	05/2018	12/2022 12/2025	32850 (32850)	0	0
254	Rehabilitation in Junavadaj Area Smart City Project (Ministry of Housing & Urban Affairs) (701719)	Gujarat	06/2016	07/2022 (-)	539 (539)	39.63	50
255	In-Situ Slum Redevelopment Project in Gujarat (PMAY, Ministry of Housing and Urban Affairs) (702540)	Gujarat	06/2015	03/2024 (-)	5477.4 (5477.4)	3035.81	0
256	In-Situ Slum Redevelopment Project in Jharkhand (PMAY, Ministry of Housing and Urban Affairs) (702555)	Jharkhand	06/2015	03/2024 (-)	212.74 (212.74)	41	0
257	In-Situ Slum Redevelopment Project in Uttar Pradesh (PMAY, Ministry of Housing and Urban Affairs) (702612)	Uttar Pradesh	06/2015	03/2024 (-)	576.99 (576.99)	141.94	0
258	Green Building Development Project (Ministry of Housing & Urban Affairs) (701766)	Uttarakhand	08/2019	11/2023 (-)	150.97 (150.97)	18.95	0
Total (10)					44555.17	6303.55	
Urban Public Transport							
259	Patna Metro Rail Project (Patna Metro Rail Corporation Ltd. [PMRCL]) (702627)	Bihar	02/2019	02/2024 06/2027	13365.77 (13365.8)	4039.77	40.07
260	Delhi Metro Rail Phase-IV [2 Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (617207)	Delhi	03/2024	03/2029 (-)	8399.81 (8399.81)	5.57	0
261	DMRTS Phase - IV [3 Priority Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (702632)	Delhi	07/2019	03/2025 03/2026	24948.65 (24948.7)	15423.06	68
262	Surat Metro Rail Project (Gujarat Metro Rail Corporation Limited [GMRCL]) (702630)	Gujarat	04/2019	03/2024 06/2026	12020.32 (12020.3)	7386.41	68
263	Ahmedabad Metro Rail Project, Phase-II (Gujarat Metro Rail Corporation Limited [GMRCL]) (702631)	Gujarat	03/2019	03/2024 12/2025	5384.17 (5384.17)	4151.57	87
264	Ahmedabad Metro Rail Project [Phase-I] (Gujarat Metro Rail Corporation Limited [GMRCL]) (702639)	Gujarat	03/2018	03/2018 08/2025	10773 (12924.5)	11857.91	99.34
265	Construction of Bangalore Metro Rail Project Phase 2. (Bengaluru Metro Rail) (702635)	Karnataka	02/2016	03/2021 09/2026	26405.14 (30695.1)	29477.97	94

All Ongoing Projects

JULY 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
266	Construction Bangalore Metro Rail Project Phase-2A & 2B (<i>Bengaluru Metro Rail</i>) (702665)	Karnataka	01/2019	06/2026 06/2026	14788.1 (14788.1)	8424.54	53
267	Kochi Metro Rail Phase 2 Development Project (<i>CSPCC Projects</i>) (702664)	Kerala	11/2022	11/2026 11/2026	1957.05 (1957.05)	306.45	10
268	Bhopal Metro Rail Project (<i>Madhya Pradesh Metro Rail Co Limited [MPMRCL]</i>) (702625)	Madhya Pradesh	11/2018	11/2022 06/2028	6941.4 (6941.4)	3116.75	43
269	Indore Metro Rail Project (<i>Madhya Pradesh Metro Rail Co Limited [MPMRCL]</i>) (702626)	Madhya Pradesh	11/2018	11/2022 12/2028	7500.8 (7500.8)	3839.27	54
270	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 (<i>Maharashtra Metro Rail Corporation Limited [MMRCL]</i>) (617225)	Maharashtra	10/2023	01/2027 (-)	910.18 (910.18)	110.33	21
271	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj (<i>Maharashtra Metro Rail Corporation Limited [MMRCL]</i>) (617226)	Maharashtra	09/2024	03/2029 (-)	2954.53 (2954.53)	18.66	3
272	New Suburba Station Development Project (<i>Ministry of Housing & Urban Affairs</i>) (701745)	Maharashtra	03/2019	07/2022 (-)	262.76 (262.76)	17.62	6
273	Kalyan Station Precinct Imporvement Project (<i>Ministry of Housing & Urban Affairs</i>) (701991)	Maharashtra	07/2020	07/2023 (-)	600 (600)	49.42	0
274	Mumbai Metro Line 3 (<i>Mumbai Metro Rail Corporation Limited [MMRC]</i>) (702637)	Maharashtra	06/2016	03/2023 06/2024	23136 (23942)	27519.07	91.9
275	Nagpur Metro Rail Phase II Development Project (<i>Maharashtra Metro Rail Corporation Limited [MMRCL]</i>) (702658)	Maharashtra	12/2022	12/2027 (-)	6708 (6708)	977.38	24
276	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] (<i>Delhi Metro Rail Corporation Limited [DMRC]</i>) (617206)	Multi-States (Delhi, Haryana)	01/2025	01/2029 (-)	6230.99 (6230.99)	0.14	0
277	Delhi-Ghaziabad-Meerut Regional Rapid Transit System [RRTS] corridor (<i>National Capital Region Transport Corporation [NCRTC]</i>) (702633)	Multi-States (Delhi, Uttar Pradesh)	03/2019	06/2025 (-)	30274 (30274)	25812.26	86
278	Kanpur Metro Rail Project (<i>Uttar Pradesh metro rail corporation [UPMRC]</i>) (702628)	Uttar Pradesh	11/2019	05/2024 03/2027	11076.48 (11076.5)	9079.81	73
279	Agra Metro Rail Project (<i>Uttar Pradesh metro rail corporation [UPMRC]</i>) (702629)	Uttar Pradesh	12/2020	05/2024 06/2027	8379.62 (8379.62)	6055.19	57
Total (21)					223016.77	157669.15	
Waste & Water							
280	Storm water drainag Development Project (<i>Ministry of Housing & Urban Affairs</i>) (702355)	Dadra & Nagar Haveli and Daman & Diu	12/2021	03/2024 (-)	210 (210)	0	0
281	Upgradation of Sewerage system in Gandhinagar City (<i>Smart City Mission</i>) (707267)	Gujarat	03/2021	06/2023 (-)	200 (200)	100	10
Total (2)					410	100	
Ministry of Mines							
Construction							
282	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata (<i>Central Public Works Department (CPWD)</i>) (617280)	West Bengal	02/2020	08/2026 (-)	255.37 (255.37)	78.34	35
Total (1)					255.37	78.34	
Metals & Mining							
283	Rakha Underground Mining Project (<i>Hindustan Copper Limited [HCL]</i>) (611798)	Jharkhand	03/2024	03/2033 (-)	2705 (2705)	0	0
284	Surda Underground Copper Mining Project (<i>Hindustan Copper Limited [HCL]</i>) (611800)	Jharkhand	03/2024	03/2028 (-)	665.02 (665.02)	13.33	1
285	Expansion of Malanjkhanda Copper Project (<i>Hindustan Copper Limited [HCL]</i>) (400426)	Madhya Pradesh	04/2015	04/2020 04/2026	1856.36 (1856.36)	924.98	79
286	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonne Per Annum (<i>National Aluminium Company Limited [NALCO]</i>) (400141)	Odisha	04/2017	12/2022 09/2025	4103 (5677.4)	3913.98	75
287	Pottangi Bauxite Mines Project (<i>National Aluminium Company Limited [NALCO]</i>) (400299)	Odisha	05/2018	03/2025 05/2026	1381 (1960.77)	650.04	51
288	UTKAL D AND E COAL BLOCK (<i>National Aluminium Company Limited [NALCO]</i>) (709829)	Odisha	02/2016	03/2025 (-)	1021.97 (1021.97)	0	0
289	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (<i>Ministry of Mines</i>) (709830)	Odisha	04/2017	11/2026 (-)	355 (581)	0	0
290	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (<i>National Aluminium Company Limited [NALCO]</i>) (709831)	Odisha	11/2019	05/2025 06/2026	483 (483)	403.44	90
291	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (<i>National Aluminium Company Limited [NALCO]</i>) (709832)	Tamil Nadu	12/2017	03/2025 03/2026	166 (166)	135	65
Total (9)					12736.35	6040.77	

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Department of Higher Education						
	Education						
292	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008)	Andhra Pradesh	12/2023	06/2027 (-)	305 (305)	83.33	24
293	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	03/2013	08/2026 (-)	592.61 (592.61)	549.96	75
294	Tezpur University Projects (Tezpur University) (606112)	Assam	06/2021	11/2023 08/2025	153.71 (153.71)	288.87	93
295	Additional Campus of NIT Patna (NIT Patna) (606013)	Bihar	08/2022	07/2024 01/2026	499.21 (499.21)	425.47	91
296	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis (Ministry of Education) (612851)	Delhi	11/2022	09/2025 (-)	333.49 (333.49)	272.95	88
297	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886)	Delhi	01/2025	10/2026 (-)	373 (373)	18.03	15
298	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Gujarat) (612916)	Gujarat	02/2021	03/2025 03/2026	490.63 (490.63)	301.44	76
299	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099)	Himachal Pradesh	08/2020	10/2023 02/2026	392.51 (454.78)	320.75	92
300	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128)	Himachal Pradesh	03/2024	03/2026 03/2026	166.66 (166.66)	72.09	58
301	Construction of Permanent Campus of Central University of Himachal Pradesh at Dehra, District - Kangra, [H.P.] on Engineering. Procurement and Construction [EPC Mode 1] Basis. (Central University, Himachal Pradesh) (612894)	Himachal Pradesh	08/2022	11/2024 11/2025	251.98 (300.45)	183.36	78
302	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098)	Jammu and Kashmir	10/2020	06/2023 08/2025	424.93 (500.91)	484.52	96
303	Additional Infrastructure at IISc Bangalore-RCC Monolithic for Men Hostel S14, Women Hostel S11, Postdoctoral Hostel S12 2 Block, International Hostel S 12, D&E Block S 12 2 Block FR. (IISC Bangalore) (610940)	Karnataka	08/2021	03/2024 09/2025	420.41 (420.41)	360.72	99
304	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431)	Kerala	03/2020	06/2022 11/2026	1006.45 (1217.4)	615.95	66
305	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] (Indian Institute of Technology, Indore) (611957)	Madhya Pradesh	11/2023	12/2026 (-)	496.28 (496.28)	138.6	30
306	Hostel 4 -Earlier Known as Hostel 20 (Indian Institute of Technology, Bombay) (612135)	Maharashtra	05/2022	09/2025 (-)	182.33 (182.33)	132.44	94
307	Academic Block 1 & 2 (Indian Institute of Technology, Bombay) (612203)	Maharashtra	01/2023	07/2026 03/2027	68 (263.93)	22.15	16
308	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2014	03/2022 07/2025	494.52 (494.52)	413.57	86
309	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (Ministry of Education) (612876)	Mizoram	05/2014	12/2029 12/2029	474.23 (474.23)	167.55	4
310	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2012	12/2025 (-)	275.63 (275.63)	257.82	93
311	IISER BERHAMPUR (Indian Institutes of Science Education and Research, Behrampur) (610315)	Odisha	09/2019	03/2021 11/2025	1229.32 (773.76)	835.55	97
312	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] (National Institute of Technology, Puducherry) (612877)	Puducherry	07/2013	12/2024 08/2025	618.34 (544.34)	509.24	94
313	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I (Indian intitue of Management, Amritsar) (605292)	Punjab	07/2020	06/2023 12/2025	348.31 (348.31)	290.39	91
314	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment (Central University of Punjab) (617221)	Punjab	04/2025	10/2027 (-)	210.99 (210.99)	0	0
315	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	01/2022	01/2025 09/2025	314.06 (314.06)	238.22	82
316	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (Ministry of Education) (612883)	Sikkim	03/2024	02/2028 12/2026	685.76 (610.76)	121.56	7

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
317	Construction of Precast housing and hostels at IIT Hyderabad <i>(Indian Institute of Technology, Hyderabad)</i> (609996)	Telangana	11/2022	10/2024 01/2026	262 (262)	164.4	71
318	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] <i>(Banaras Hindu University)</i> (606479)	Uttar Pradesh	06/2020	09/2022 03/2026	246 (246)	185.83	93
319	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal <i>(National Institute of Technology Uttarakhand)</i> (611963)	Uttarakhand	04/2024	09/2027 (-)	650.85 (650.85)	130	24
320	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur <i>(Indian Institute of Technology, Kharagpur)</i> (609019)	West Bengal	04/2019	03/2023 03/2026	500 (442)	382.6	87
321	IoE Projects [Civil Works], IIT Kharagpur <i>(Indian Institute of Technology, Kharagpur)</i> (609041)	West Bengal	04/2019	03/2023 12/2026	287.2 (287.2)	310	86
Total (30)					12754.41	8277.36	
Ministry of Petroleum & Natural Gas							
Energy Storage							
322	Construction of Aviation Fuel farm Facilities at Bhogapuram Airport <i>(Ministry of Petroleum & Natural Gas)</i> (616235)	Andhra Pradesh	08/2024	03/2026 03/2026	240 (240)	31.23	50
323	Construction of LPG Facilities at Kamardanga, Assam <i>(Hindustan Petroleum Corporation Limited)</i> (709754)	Assam	03/2023	07/2027 07/2027	156.36 (156.36)	49.78	39
324	Setting up of new rail fed POL facility at Kamardanga, Assam <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (709755)	Assam	03/2023	07/2027 07/2027	384.04 (384.04)	110.44	48
325	Setting up a common user Petroleum Terminal at Jammu, J&K for resitement of existing PSU OMC's Depots from Jammu City <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (400235)	Jammu and Kashmir	04/2023	03/2025 09/2025	676.89 (676.89)	518.22	77
326	Construction of 80,000 MT LPG Cavern at Mangalore <i>(Ministry of Petroleum & Natural Gas)</i> (701269)	Karnataka	12/2018	12/2022 08/2025	854 (854)	712.3	99
327	Andheri Residential Towers, Mumbai <i>(Ministry of Petroleum & Natural Gas)</i> (604833)	Maharashtra	06/2017	05/2025 06/2026	281.35 (389.67)	227.54	50
328	Srikakulam Angul Gas Pipeline Project <i>(Ministry of Petroleum & Natural Gas)</i> (701343)	Multi-States (Andhra Pradesh, Odisha)	09/2019	07/2022 12/2025	2658.34 (2810)	2192.68	94
329	Rajasthan Refinery Project <i>(Ministry of Petroleum & Natural Gas)</i> (701263)	Multi-States (Arunachal Pradesh, Gujarat, Rajasthan)	10/2017	10/2022 03/2026	43129 (72937)	59524.37	87
330	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip <i>(Ministry of Petroleum & Natural Gas)</i> (701349)	Multi-States (Assam, Bihar, Jharkhand, Odisha, West Bengal)	01/2019	07/2024 09/2025	10228 (11407)	9701.95	86
331	New Mundra Panipat Crude Oil Pipeline <i>(Ministry of Petroleum & Natural Gas)</i> (400078)	Multi-States (Gujarat, Haryana, Rajasthan)	12/2021	12/2024 12/2025	9028 (9028)	7071.08	84
332	Kandla Gorakhpur LPG Pipeline <i>(Ministry of Petroleum & Natural Gas)</i> (400012)	Multi-States (Gujarat, Madhya Pradesh, Uttar Pradesh)	12/2018	12/2021 12/2025	10088 (10088)	7598.13	92
333	Multi Product Pipeline from Irugur to Devangonthi <i>(Department of Water Resources, River Development & GR)</i> (400301)	Multi-States (Karnataka, Tamil Nadu)	11/2012	02/2017 10/2025	678 (1732)	675.25	67
334	Petrochemical evacuation marketing terminal at Barmer, Rajasthan <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (709759)	Rajasthan	12/2023	12/2026 12/2026	461.05 (461.05)	111.57	51
335	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] <i>(Ministry of Petroleum & Natural Gas)</i> (400043)	Tamil Nadu	01/2022	05/2026 05/2026	829 (829)	297.77	62
336	Grass root POL Terminal at Vallur, Chennai <i>(Indian Oil Corporation Limited [IOCL])</i> (400077)	Tamil Nadu	01/2022	12/2024 03/2026	827 (887.71)	619.5	85
337	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot <i>(Indian Oil Corporation Limited [IOCL])</i> (400035)	Tripura	06/2022	09/2025 09/2025	656 (656)	465.73	84
338	Grass-root Terminal at Mirzapur, Uttar Pradesh <i>(Ministry of Petroleum & Natural Gas)</i> (604852)	Uttar Pradesh	09/2022	11/2026 11/2026	980.45 (980.45)	236.22	50
Total (17)					82155.48	90143.76	
Oil & Gas							
339	KG-DWN-98/2 Cluster - II Development Project - NELP Block <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400120)	Andhra Pradesh	03/2016	06/2020 06/2026	34012 (34012)	35498.35	96
340	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery <i>(Hindustan Petroleum Corporation Limited)</i> (709752)	Andhra Pradesh	09/2021	06/2024 03/2026	160 (220)	77.06	64
341	HP Trijet Unit in Visakh Refinery <i>(Hindustan Petroleum Corporation Limited)</i> (709761)	Andhra Pradesh	07/2024	07/2027 07/2027	193 (193)	0.43	23
342	City Gas Distribution Project at Kurnool, Guntur & Prakasam Districts <i>(Ministry of Petroleum & Natural Gas)</i> (709766)	Andhra Pradesh	03/2022	03/2030 03/2030	1420 (1420)	162.47	6

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
343	Numaligarh Refinery Expansion Project <i>(Ministry of Petroleum & Natural Gas)</i> (604791)	Assam	07/2020	07/2024 12/2025	12366 (22494)	16502.36	75
344	Assam Bio Refinery, ABRPL <i>(Ministry of Petroleum & Natural Gas)</i> (604792)	Assam	02/2018	09/2021 07/2025	1750 (4200)	4650	99
345	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija <i>(Ministry of Petroleum & Natural Gas)</i> (604863)	Assam	01/2018	02/2020 12/2025	682.9 (726.93)	488.37	94
346	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery <i>(Ministry of Petroleum & Natural Gas)</i> (607701)	Assam	05/2021	10/2023 05/2026	412.3 (577)	430.83	84
347	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field <i>(Ministry of Petroleum & Natural Gas)</i> (616858)	Assam	12/2020	03/2024 12/2025	430.76 (430.76)	326.12	85
348	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi <i>(MinistryofPetroleumNaturalGas)</i> (709776)	Assam	04/2022	09/2026 09/2026	277 (323.09)	185.18	67
349	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA <i>(MinistryofPetroleumNaturalGas)</i> (709779)	Assam	06/2022	03/2026 03/2026	768 (740)	99.02	35
350	Pipeline Network Project Rudrasagar <i>(Ministry of Petroleum & Natural Gas)</i> (709847)	Assam	01/2023	04/2026 04/2026	344.99 (344.99)	210.89	46
351	Borholla GGS Life Extension Project [BLEP] <i>(Ministry of Petroleum & Natural Gas)</i> (709850)	Assam	09/2023	05/2026 05/2026	198.7 (198.7)	36.78	29
352	DCU Revamp Project <i>(NRL)</i> (709864)	Assam	08/2021	07/2024 10/2025	370 (370)	249.41	57
353	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme <i>(NRL)</i> (709865)	Assam	04/2023	12/2024 10/2025	293.5 (293.5)	97.22	93
354	City Gas Distribution Project at Khagaria, Saharsa and Madhepura <i>(Ministry of Petroleum & Natural Gas)</i> (617303)	Bihar	03/2019	03/2030 03/2030	163 (163)	95.54	40
355	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar <i>(MinistryofPetroleumNaturalGas)</i> (617304)	Bihar	10/2023	03/2027 03/2027	340.15 (340.15)	88.08	24
356	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (701324)	Bihar	01/2020	04/2023 08/2026	14810 (16724)	11728.01	87
357	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery <i>(MinistryofPetroleumNaturalGas)</i> (709777)	Bihar	01/2022	04/2025 10/2026	389.35 (340)	46.94	37
358	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709792)	Bihar	12/2022	03/2030 03/2030	3638 (3638)	396.42	21
359	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709793)	Bihar	12/2022	06/2030 06/2030	3919 (3919)	392.59	14
360	Redevelopment of Sobhasan Complex <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400087)	Gujarat	08/2021	02/2026 02/2026	885.63 (1286.67)	765.43	73
361	Redevelopment of Santhal Field [Onshore-Mehsana Asset] <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400167)	Gujarat	02/2017	03/2026 03/2026	1162.56 (1162.56)	1156.9	94
362	Redevelopment of Linch Field <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (400169)	Gujarat	04/2021	03/2025 10/2025	631.03 (860.04)	505.07	77
363	Petrochemical and Lube Integration Project at Gujarat Refinery <i>(Ministry of Petroleum & Natural Gas)</i> (701329)	Gujarat	09/2020	08/2024 12/2025	18936 (17825)	12190.08	83
364	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery <i>(MinistryofPetroleumNaturalGas)</i> (709778)	Gujarat	01/2022	08/2025 09/2026	328.29 (287)	144.16	55
365	Commercial Polymer Flooding Project in Bechraji field <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709838)	Gujarat	01/2022	11/2024 11/2025	621.4 (621.4)	137.71	21
366	Restoration of Gas Terminal, Phase-I [Part-A], Hazira <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709840)	Gujarat	05/2022	02/2025 12/2025	249.43 (249.43)	209.42	93
367	Old Pipe Line Replacement [OPRP] Group-A <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709841)	Gujarat	07/2021	07/2025 03/2026	173.03 (169.84)	148	87
368	Kalol Redevelopment Project, Ahmedabad Asset <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709842)	Gujarat	08/2022	03/2027 03/2027	1487.41 (1487.41)	776.61	61
369	Revamping of SV Stations, Gas Terminal & Kribhco Terminal <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709845)	Gujarat	11/2022	08/2026 08/2026	837.34 (837.34)	205.78	49
370	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad <i>(Ministry of Petroleum & Natural Gas)</i> (604853)	Haryana	06/2019	12/2022 03/2026	2281.94 (3200)	1800.61	63
371	Poly Butadiene Rubber plant at Panipat <i>(Indian Oil Corporation Limited [IOCL])</i> (611917)	Haryana	03/2022	03/2025 06/2026	1459 (2531.44)	1043.9	70

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
372	Capacity Expansion of Panipat Refinery from 15 to 25 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (701289)	Haryana	02/2021	09/2024 12/2025	34627 (36225)	23977.47	88
373	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. <i>(Ministry of Petroleum & Natural Gas)</i> (709783)	Haryana	12/2020	06/2023 06/2026	165.13 (247.69)	129.27	70
374	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts <i>(Ministry of Petroleum & Natural Gas)</i> (709773)	Jammu and Kashmir	03/2022	03/2032 03/2032	538 (538)	4.09	0
375	Development of Jharia CBM Block [Phase-1] <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (610984)	Jharkhand	11/2019	01/2024 08/2025	431 (431)	211.34	58
376	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] <i>(Ministry of Petroleum & Natural Gas)</i> (709785)	Jharkhand	02/2023	02/2026 02/2026	202.07 (202.07)	55.46	45
377	Power System Upgradation Project <i>(Mangalore Refinery and Petrochemicals Limited)</i> (612790)	Karnataka	10/2023	11/2025 11/2025	385 (385)	132.73	63
378	Demo Bio-ATF Project <i>(Ministry of Petroleum & Natural Gas)</i> (616879)	Karnataka	03/2024	01/2027 01/2027	364 (364)	22.82	10
379	Revamping/ Augmentation of facilities at existing port terminal at Mangalore <i>(Ministry of Petroleum & Natural Gas)</i> (709774)	Karnataka	01/2022	12/2025 12/2025	463 (500.62)	264.44	82
380	Replacement and Extension of Jetty Pipelines [REJP] at KR <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709790)	Kerala	03/2023	03/2026 03/2026	621.87 (621.87)	192.66	83
381	Setting up Polypropylene Unit at Kochi Refinery <i>(Ministry of Petroleum & Natural Gas)</i> (709799)	Kerala	12/2023	10/2027 10/2027	4460 (4460)	255.64	12
382	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery <i>(Ministry of Petroleum & Natural Gas)</i> (709798)	Madhya Pradesh	05/2023	05/2028 05/2028	43367 (43367)	1788.6	13
383	Debottlenecking and Augmentation of Cryogenic facilities at Uran LPG Import Terminal <i>(Department of Water Resources, River Development & GR)</i> (400158)	Maharashtra	04/2021	02/2024 12/2025	1164.69 (1629.86)	901.73	84
384	500 KTA PDHPP Project, Usar <i>(Ministry of Petroleum & Natural Gas)</i> (400168)	Maharashtra	04/2021	04/2025 10/2025	8797 (11256)	6768.36	85
385	Construction of lube oil blending plant at Rasayani <i>(Ministry of Petroleum & Natural Gas)</i> (610985)	Maharashtra	05/2022	12/2023 12/2025	423.39 (526.26)	287.49	78
386	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery <i>(Ministry of Petroleum & Natural Gas)</i> (616933)	Maharashtra	12/2024	03/2028 03/2028	4679 (4679)	188.88	4
387	HP TDAE Unit in Mumbai Refinery <i>(Hindustan Petroleum Corporation Limited)</i> (709760)	Maharashtra	06/2024	04/2026 04/2026	240 (240)	34.4	37
388	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts <i>(Ministry of Petroleum & Natural Gas)</i> (709771)	Maharashtra	03/2022	09/2031 09/2031	865 (865)	68.01	2
389	Construction of Additional Tankages and Allied Facilities at JNPT Terminal <i>(Ministry of Petroleum & Natural Gas)</i> (709780)	Maharashtra	04/2022	08/2026 08/2026	341.43 (436.14)	279.19	50
390	ATF Pipeline from Jawaharlal Nehru Port Trust to Navi Mumbai International Airport <i>(Indian Oil Corporation Limited [IOCL])</i> (709782)	Maharashtra	08/2022	08/2025 03/2026	165 (165)	89.94	72
391	Installation of Independent De- Aromatized Solvents [DAS] production facilities at MR <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709789)	Maharashtra	03/2023	07/2025 12/2025	405 (343)	201.28	84
392	POL & LOBS Installations with Receipt Pipelines at Rasayani <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709797)	Maharashtra	05/2023	05/2026 05/2026	2585 (2585)	564.58	58
393	Part Replacement Pipeline Project [PRPP] <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709846)	Maharashtra	11/2022	05/2024 11/2025	1219.48 (1145.1)	745.24	90
394	Visakh Raipur Pipeline Project <i>(Ministry of Petroleum & Natural Gas)</i> (616254)	Multi-States (Andhra Pradesh, Chhattisgarh, Odisha)	09/2024	09/2027 09/2027	2212 (2212)	11.52	7
395	Multi-product Pipeline from Krishnapatnam Coastal Installation to the proposed Installation at Hyderabad [Malkapur] <i>(Ministry of Petroleum & Natural Gas)</i> (701341)	Multi-States (Andhra Pradesh, Telangana)	09/2019	03/2025 08/2025	1932 (2208)	1552.37	98
396	North East Gas Grid <i>(Ministry of Petroleum & Natural Gas)</i> (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura, West Bengal)	04/2020	03/2024 03/2026	9265 (9265)	6375.02	85
397	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (701350)	Multi-States (Assam, West Bengal)	06/2021	12/2024 10/2025	860 (860)	566.18	98
398	CGD Project in Banka, Dumka, Godda, Jamtara, Pakur, Sahibganj GA ID 11A.02 <i>(Hindustan Petroleum Corporation Limited)</i> (709757)	Multi-States (Bihar, Jharkhand)	06/2022	06/2030 06/2030	1377 (1377)	329.43	26

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
399	Mumbai Nagpur Jharsuguda Pipeline Project (<i>Ministry of Petroleum & Natural Gas</i>) (701354)	Multi-States (Chhattisgarh, Madhya Pradesh, Maharashtra, Odisha)	06/2020	05/2023 09/2025	7844.25 (8255)	6495.6	95
400	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (<i>Ministry of Petroleum & Natural Gas</i>) (701330)	Multi-States (Gujarat, Haryana, Punjab, Rajasthan)	07/2011	06/2024 12/2025	7392 (7392)	6304	90
401	Gurdaspur Jammu Pipeline (<i>Gas Authority of India Limited [GAIL]</i>) (612853)	Multi-States (Jammu and Kashmir, Punjab)	07/2023	07/2026 07/2026	521.9 (521.9)	190.1	36
402	Kochi - Kootanad - Bangalore - Mangalore Pipeline Phase-II (<i>Ministry of Petroleum & Natural Gas</i>) (701228)	Multi-States (Karnataka, Kerala, Tamil Nadu)	06/2009	12/2012 12/2025	2915 (5909)	4431.9	94
403	City Gas Distribution Maharashtra Natural Gas Limited (<i>Ministry of Petroleum & Natural Gas</i>) (701338)	Multi-States (Karnataka, Maharashtra)	01/2006	06/2031 06/2031	5535 (5535)	3836.09	0
404	Dhamra Haldia Pipeline Project (<i>Ministry of Petroleum & Natural Gas</i>) (701344)	Multi-States (Odisha, West Bengal)	03/2020	11/2022 12/2025	1030.65 (1125)	853.7	87
405	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (<i>Bharat Petroleum Corporation Limited [BPCL]</i>) (709794)	Multi-States (Punjab, Rajasthan)	12/2022	06/2030 06/2030	3207 (3207)	334.82	22
406	Augmentation/ Revamping of Dimapur Depot, Dimapur (<i>Ministry of Petroleum & Natural Gas</i>) (709786)	Nagaland	08/2023	11/2027 11/2027	227.62 (227.62)	9.01	20
407	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (<i>Ministry of Petroleum & Natural Gas</i>) (604859)	Odisha	07/2020	01/2024 08/2026	13805 (11783)	8250.46	90
408	CUF POL Depot at Sadashibpur [Meramundali], Odisha (<i>Ministry of Petroleum & Natural Gas</i>) (709800)	Odisha	04/2021	03/2026 03/2026	393.54 (393.54)	100.39	43
409	Life Extension of 48 well platforms of Mumbai High & Heera Fields (<i>Oil and Natural Gas Corporation Limited [ONGC]</i>) (400119)	Offshore	12/2015	04/2018 12/2025	3190.69 (3375.9)	3074.01	89
410	PRP-VIII [Group-A] (<i>Ministry of Petroleum & Natural Gas</i>) (616950)	Offshore	09/2024	02/2026 02/2026	1486.4 (1486.4)	184.56	17
411	Daman Upside Development Project (<i>Oil and Natural Gas Corporation Limited [ONGC]</i>) (709839)	Offshore	06/2022	10/2025 02/2026	4144.41 (6406.9)	3770.15	83
412	MHN TCPP PGC BGC Project [MTPBP] (<i>Ministry of Petroleum & Natural Gas</i>) (709848)	Offshore	06/2022	05/2026 05/2026	2329.45 (2354.23)	820.24	48
413	PRP-VIII Group B [NH & BS Asset] (<i>Ministry of Petroleum & Natural Gas</i>) (709849)	Offshore	06/2024	02/2026 02/2026	2379.84 (3165.53)	1652.62	61
414	Integrated Development of 4 Contract Areas under DSF-II (<i>Ministry of Petroleum & Natural Gas</i>) (709851)	Offshore	05/2023	04/2027 04/2027	6183.79 (6183.79)	360	17
415	2G Ethanol Biorefinery at Bathinda (<i>Hindustan Petroleum Corporation Limited [HPCL]</i>) (400171)	Punjab	05/2020	02/2023 03/2026	1421.46 (1421.46)	1180.91	95
416	Bathinda Sangrur Pipeline (<i>Ministry of Petroleum and Natural Gas</i>) (612998)	Punjab	11/2021	05/2024 08/2025	367 (397)	339.19	93
417	City Gas Distribution Project at Pathankot District (<i>Ministry of Petroleum & Natural Gas</i>) (709770)	Punjab	03/2022	09/2033 09/2033	151 (151)	8.77	2
418	CBR 9 MMTA Project (<i>Chennai Petroleum Corporation Limited [CPCL]</i>) (604795)	Tamil Nadu	09/2021	06/2025 10/2028	31580 (36354)	1342.27	10
419	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore (<i>Chennai Petroleum Corporation Limited [CPCL]</i>) (709750)	Tamil Nadu	01/2024	09/2025 12/2025	205 (205)	19.86	39
420	City Gas Distribution Project at Dharmapuri and Krishnagiri Districts (<i>Ministry of Petroleum & Natural Gas</i>) (709768)	Tamil Nadu	03/2022	12/2030 12/2030	501 (501)	111.55	5
421	City Gas Distribution Projects at the Nilgiris and Erode districts (<i>Bharat Petroleum Corporation Limited [BPCL]</i>) (709796)	Tamil Nadu	12/2022	03/2030 03/2030	3685 (3685)	234.12	11
422	Creation of Gas Dehydration Facilities, Tripura Asset (<i>Oil and Natural Gas Corporation Limited [ONGC]</i>) (709837)	Tripura	03/2022	05/2024 12/2025	209.33 (131.51)	65.97	62
423	PP Project, Pata (<i>Gas Authority of India Limited [GAIL]</i>) (400161)	Uttar Pradesh	03/2019	01/2024 08/2025	910.56 (1299.02)	1004	97
424	Revamping / Augmentation of Facilities at Mathura Bitumen Plant (<i>Ministry of Petroleum & Natural Gas</i>) (709781)	Uttar Pradesh	04/2022	06/2027 12/2026	260.12 (260.12)	1.11	25
425	City Gas Distribution Projects at Lakhimpur Kheri, Sitapur, Bahraich, Shravasti, Balrampur, Siddharth Nagar & Maharajganj districts (<i>Bharat Petroleum Corporation Limited [BPCL]</i>) (709795)	Uttar Pradesh	12/2022	06/2030 06/2030	16654 (16654)	603.21	9
426	71 MWp [DC] Solar power project at Prayagraj (<i>Bharat Petroleum Corporation Limited [BPCL]</i>) (709801)	Uttar Pradesh	02/2024	08/2025 (-)	308.32 (308.32)	183.37	95
427	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] (<i>Ministry of Petroleum & Natural Gas</i>) (617302)	West Bengal	03/2017	12/2020 12/2025	1740 (2493.15)	2237.5	90

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
428	Haldia Panagarh Pipeline Project (Hindustan Petroleum Corporation Limited) (709753)	West Bengal	11/2022	11/2025 11/2025	1010 (1010)	627.12	81
429	CGD Project in Malda, Birbhum, Murshidabad, Dakshin Dinajpur GA ID 11A.03 (Hindustan Petroleum Corporation Limited) (709758)	West Bengal	06/2022	06/2030 06/2030	2628 (2628)	332.52	26
430	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts (Ministry of Petroleum Natural Gas) (709772)	West Bengal	03/2022	06/2031 06/2031	609 (609)	58.15	2
431	City Gas Distribution Projects at Alipurduar and Cooch Behar (Bharat Petroleum Corporation Limited [BPCL]) (709791)	West Bengal	12/2022	03/2030 03/2030	1017 (1017)	176.15	32
Total (93)					353990.1	186037.3	
Ministry of Health & Family Welfare							
Healthcare							
432	AIIMS Majra Rewari Haryana (Ministry of Health & Family Welfare) (701173)	Haryana	02/2019	02/2023 12/2026	1299 (1299)	349.41	28
433	AIIMS Kashmir at Awantipora Jammu & Kashmir (Central Public Works Department [CPWD]) (701167)	Jammu and Kashmir	01/2019	01/2025 12/2025	1828 (1828)	1504.91	65
434	AIIMS Bibinagar (Ministry of Health & Family Welfare) (701171)	Telangana	12/2018	09/2022 12/2025	1028 (1365.95)	792.24	83
Total (3)					4155	2646.56	
Ministry of Ports, Shipping and Waterways							
Healthcare							
435	Establishment of 600 bed super specialty hospital with optional development of Medical college and further expansion on PPP basis. (Mumbai Port Trust [MPT]) (708662)	Maharashtra	01/2022	06/2026 12/2027	693 (693)	58	0
Total (1)					693	58	
Inland Waterways							
436	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust [DPT]) (609424)	Gujarat	12/2023	12/2026 (-)	4243.64 (4243.64)	346.2	10
437	Jal Marg Vikas Project (Inland Waterways Authority of India [IWAI]) (701565)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	02/2018	12/2023 12/2025	5369.18 (5061.15)	3432.34	70
Total (2)					9612.82	3778.54	
Shipping							
438	Setting up of a Floating Storage and Regasification Unit [FSRU] - Mumbai (Mumbai Port Trust [MPT]) (701586)	Maharashtra	04/2021	11/2026 11/2026	900 (900)	65	0
439	Operationalization of Coastal Berth & Shallow Water Berth through PPP (Jawaharlal Nehru Port Authority [JNPA]) (708655)	Maharashtra	07/2021	01/2026 (-)	366.8 (366.8)	188.46	25
440	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574)	Odisha	01/2023	12/2027 10/2028	3004.63 (3004.63)	1149.79	40
441	Berth No. 2 [previously Berth 3] of HDC Mechanization Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701576)	West Bengal	03/2023	09/2025 01/2026	298.26 (298.26)	399.52	83
442	Shalukkhali Liquid Cargo Handling Facility Development Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701577)	West Bengal	08/2022	08/2025 (-)	253.65 (253.65)	9.28	0
Total (5)					4823.34	1812.05	
Tourism, Hospitality & Wellness							
443	National Maritime Heritage Complex [NMHC] Phase-I (Indian Port Rail & Ropeway Corporation Ltd. [IPRCL]) (707215)	Gujarat	01/2022	03/2024 09/2025	573 (1238.05)	487.35	66
Total (1)					573	487.35	
Ministry of Railways							
Inland Waterways							
444	3rd & 4th Railway Line Project from Salegaon to Budhapank via Rajathgarh. (East Coast Railway [ECOR] - II) (705515)	Odisha	12/2015	03/2026 03/2026	1173 (2092)	1971	80
445	Jeypore-Navarangpur New Rail Line Project (East Coast Railway [ECOR] - II) (705741)	Odisha	04/2023	07/2028 12/2029	748 (748)	10.43	1
446	Jeypore-Malkanagiri New Railway Line Project (East Coast Railway [ECOR] - II) (705742)	Odisha	12/2023	07/2033 07/2033	2344 (2344)	196.75	8
Total (3)					4265	2178.18	
Railways							
447	Khurda Road - Balangir Electrification of Railway Track Project (CORE) (706898)		09/2019	03/2021 (-)	267.61 (267.61)	0	0
448	Nadikudi - Srikalahasti New Line (South Central Railway [SCR] - II) (400298)	Andhra Pradesh	12/2016	05/2027 03/2028	2312 (5200)	2179	54
449	Malugur- Palasamudram New Line Project [17.975 Km] (South Western Railway [SWR] - II) (611615)	Andhra Pradesh	11/2025	11/2027 12/2027	342 (342.14)	0	0

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
450	GOOTY-PENDEKALLU DOUBLING 29.225 Km (South Central Railway [SCR] - II) (611752)	Andhra Pradesh	06/2023	03/2027 03/2027	351.83 (351.83)	18	25
451	GUNTAKAL WEST-MALLAPPA GATE RAIL OVER RAIL - ROR TRACK (South Central Railway [SCR] - II) (611754)	Andhra Pradesh	07/2023	07/2026 (-)	293.3 (293.3)	0	0
452	Kurnool - Setting up facilities for coach midlife rehabilitation workshop (WPO/Patna) (611927)	Andhra Pradesh	10/2017	12/2023 (-)	560.72 (560.72)	276.66	65
453	Flyover between Pendurthi and Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB 73 of 2023 24 NR (East Coast Railway [ECor] - II) (612827)	Andhra Pradesh	05/2024	04/2027 (-)	183.65 (183.65)	4.16	11
454	3rd & 4th line between Vadlapudi -Gate Jn. cabin and Tie line between Gate Junction to Gangavaram port (East Coast Railway [ECor] - II) (616697)	Andhra Pradesh	03/2024	06/2026 (-)	154.28 (154.28)	10.79	16
455	Tiupati Katpadi 104.39 kms (South Central Railway [SCR] - II) (617210)	Andhra Pradesh	04/2025	03/2029 (-)	1215.56 (1215.56)	0	0
456	3rd Line between Gudur Renigunta 83.17 Km (South Central Railway [SCR] - II) (617216)	Andhra Pradesh	10/2024	03/2027 (-)	877.34 (877.34)	2.97	0
457	Kotapalli - Narasapur New Line (South Central Railway [SCR] - II) (705436)	Andhra Pradesh	09/2013	03/2028 03/2028	2501 (2501)	1264.18	29
458	Guntur-Guntakal Doubling Project (South Central Railway [SCR] - II) (705633)	Andhra Pradesh	11/2017	12/2025 12/2026	3733 (4295)	4112.59	92
459	Vijaywada-Gudur 3rd Line (RVNL - II) (705648)	Andhra Pradesh	04/2018	11/2024 12/2025	6654 (6654)	5922	90
460	Penukonda - Dharmavaram Doubling Project [41.5 Km] (South Western Railway [SWR] - II) (705789)	Andhra Pradesh	12/2018	03/2026 03/2026	307.66 (307.66)	267.83	60
461	AGTHORI KAMAKHYA SECTION WITH CONSTRUCTION OF NEW RAIL CUM-ROAD BRIDGE AT SARAIGHAT - 7.062KM (Northeast Frontier Railway [NFR]) (613788)	Assam	05/2025	12/2029 (-)	1473.77 (1473.77)	0	0
462	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016	03/2026 03/2026	4060 (4961)	3683.75	93
463	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2018	09/2020 06/2024	890.36 (889.36)	391.73	89
464	Sakri -Hasanpur [via Harnagar - Kusheshwar Asthan] New Railway line (East Central Railway [ECR] - I) (400254)	Bihar	08/1997	12/2024 03/2027	735.2 (735.2)	585.09	81
465	Construction of Bulb line at Nabinagar Ankorah of East Central Railway (East Central Railway [ECR] - I) (617231)	Bihar	05/2026	06/2028 (-)	611.74 (611.74)	0	0
466	Sakri-Hasanpur Road New Rail Line Project (East Central Railway [ECR] - I) (705363)	Bihar	03/2011	12/2024 03/2025	735 (735)	605	78
467	Khagaria-Kusheshwar Asthan [42Km] new line project (East Central Railway [ECR] - I) (705364)	Bihar	12/1998	12/2024 03/2027	614 (1384)	479.22	55
468	Hajipur-Sagauli New line (East Central Railway [ECR] - I) (705366)	Bihar	10/2004	03/2020 12/2026	2067 (2087)	1908.49	74
469	Araria Supaul New BG Line (East Central Railway [ECR] - II) (705368)	Bihar	03/2009	03/2024 01/2027	1605 (2514)	1311.39	33
470	Fatuha-Islampur incl. MM for extn.of NL from Neora to Daniawan , Daniawan to Biharsharif, Biharsharif to Barbiga , Barbiga to Shekhpura (East Central Railway [ECR] - II) (705373)	Bihar	03/2002	03/2023 08/2025	1473 (2882)	2824.8	91
471	New B.G. Railway Line- Araria to Galgalia [Thakurgunj] (Northeast Frontier Railway [NFR]) (705400)	Bihar	06/2007	12/2024 07/2025	2650 (4412)	4152.4	96
472	Jogbani-Biratnagar New Rail Line project (Indian Railway Construction International Limited [IRCON]) (705450)	Bihar	01/2011	03/2022 12/2026	402 (486)	361	86
473	Samastipur-Darbhanga Doubling Railway Project (East Central Railway [ECR] - I) (705526)	Bihar	12/2015	03/2025 10/2025	519 (519)	337.03	82
474	Sagauli-Valmiknagar (East Central Railway [ECR] - II) (705527)	Bihar	03/2017	12/2025 12/2025	1216 (2222)	2039	91
475	Muzaffarpur-Sugauli (East Central Railway [ECR] - II) (705528)	Bihar	03/2017	06/2024 08/2025	1586 (1586)	1586.82	99
476	Rampur Dumra-Tal-Rajendrapul Additional Bridge and Railway Line Doubling (Indian Railway Construction International Limited [IRCON]) (706759)	Bihar	05/2017	12/2024 12/2025	2374 (2374)	1777	85
477	Kharsia-Dharamjaygarh with Spur line [East Corridor-Phase 1] (Indian Railway Construction International Limited [IRCON]) (400220)	Chhattisgarh	01/2014	09/2018 03/2026	3055 (3438)	2574.54	94
478	Doubling of Kirandul-Jagdalpur Line [150 km] (East Coast Railway [ECor] - II) (400291)	Chhattisgarh	03/2013	03/2020 12/2025	1589 (1798)	1541.7	92

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
479	Gauge Conversion of Kendri-Dhamtari including Abhanpur - Rajim Branch line 67.20 Kms - 2nd Material Modification to Raipur Titlagarh doubling. (SECR) (602792)	Chhattisgarh	05/2021	02/2025 11/2025	1171 (1171)	848	82
480	4th line between Nipania Bhatapara 14.4 Km (South East Central Railway [SECR] - II) (612815)	Chhattisgarh	05/2024	03/2027 (-)	170.49 (170.49)	0	0
481	Dharamjaigarh-Korba 63 km (CERL) (613003)	Chhattisgarh	07/2022	08/2026 (-)	1686.26 (1686.26)	288.83	18.5
482	KHARSIA- NAYA RAIPUR-PARMALKASA 5th and 6th Line [278KM] (CAO/C/SECR) (617200)	Chhattisgarh	04/2025	03/2031 (-)	7853.84 (7853.84)	0	0
483	Dallirajhra- Rowghat New Railway Line - Phase I [95 km] (RVNL - II) (705433)	Chhattisgarh	12/2009	09/2025 12/2025	1628 (1628)	1440.85	82
484	Gevra Road-Pendra Road New Railway Line [135 km] (Indian Railway Construction International Limited [IRCON]) (705444)	Chhattisgarh	04/2014	03/2022 12/2025	4970 (4970)	4271.55	72
485	Chirimiri-Nagpur Halt New Railway Line Project (South East Central Railway [SECR] - II) (705756)	Chhattisgarh	06/2020	06/2030 06/2030	241 (656.52)	71	0
486	Boridand - Ambikapur Doubling Line Project (South East Central Railway [SECR] - II) (706854)	Chhattisgarh	04/2022	06/2030 06/2030	1376 (1576.23)	218	18
487	NIPANIA-BHATAPRA [14.4 KM] 4TH LINE [PB-72/NR/2022-23] (SECR) (709814)	Chhattisgarh	05/2024	12/2026 12/2026	170 (184)	0	0
488	4TH LINE - BHATAPARA-HATHBAND [8.8 KM] [PB-72/NR/2022-23] (SECR) (709815)	Chhattisgarh	05/2024	01/2027 12/2027	177.03 (177.03)	0	0
489	4TH LINE - BHILAI-BHILAI NAGAR [8.8 KM] [PB-72/NR/2022-23] (SECR) (709816)	Chhattisgarh	05/2024	02/2027 02/2027	177.34 (177.34)	0.76	2
490	4TH LINE - DADHAPARA-BELHA [9.2 KM] [PB-72/NR/2022-23] (SECR) (709817)	Chhattisgarh	05/2024	11/2026 11/2026	169.06 (169.06)	10.13	4
491	4TH LINE RAJNANDGAON-DONGARHGARH [31.2 KM] [PB-72/NR/2022-23] (SECR) (709818)	Chhattisgarh	05/2024	01/2027 01/2027	328.34 (328.34)	48.02	25
492	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (709819)	Chhattisgarh	09/2022	12/2026 12/2026	177 (177)	0	0
493	Redevelopment of New Delhi Railway Station and construction of associated infrastructure (Ministry of Railways) (613785)	Delhi	06/2024	12/2028 (-)	4744 (4744)	31.77	0
494	North Region Video Surveillance Project (RCIL) (705298)	Delhi	04/2023	03/2024 (-)	274.39 (274.39)	0	0
495	Provision of Work-site Tampers [WST] Railway Project (EDTK[MC]/RB) (705694)	Delhi	01/2016	12/2023 01/2026	187.72 (187.72)	141.91	100
496	WST Machine Procurement Project (EDTK[MC]/RB) (705708)	Delhi	06/2018	03/2024 12/2027	176 (176)	0	0
497	PCT Machine Procurement Project (EDTK[MC]/RB) (705710)	Delhi	04/2019	04/2024 06/2027	336 (336)	74.32	81.25
498	RBMV Machine Procurement Project (EDTK[MC]/RB) (705712)	Delhi	10/2019	06/2024 12/2027	480 (480)	0.33	3.75
499	SRGM Machine Procurement Project (EDTK[MC]/RB) (705717)	Delhi	10/2019	12/2023 03/2026	440 (440)	390.03	75
500	WST Machine Procurement Project (EDTK[MC]/RB) (705720)	Delhi	12/2019	04/2024 12/2026	384 (384)	0	0
501	DTS Machine Procurement Project (EDTK[MC]/RB) (705721)	Delhi	12/2019	12/2024 12/2026	447.6 (447.6)	0	0
502	BRM Machine Procurement Project (EDTK[MC]/RB) (705722)	Delhi	09/2019	06/2024 12/2027	210 (210)	0.02	0
503	Track Machine Procurement Project (EDTK[MC]/RB) (705726)	Delhi	04/2020	03/2025 01/2028	6339 (6339)	4166.47	41
504	Kosamba Umarpada 70 Km (PCE/WR) (611918)	Gujarat	07/2022	03/2027 (-)	468 (468)	20	0
505	Adraj Moti Vijapur 40 Kms (Western Railway [WR] - II) (611937)	Gujarat	05/2022	05/2026 05/2026	417.53 (417.53)	223	86
506	Vijapur Ambliyasani 42 km (PCE/WR) (611938)	Gujarat	05/2022	05/2026 05/2026	415.38 (415.38)	364	96
507	Himatnagar Khedbrahma 55 km (WR) (611939)	Gujarat	04/2017	06/2001 06/2026	482.42 (482.42)	461	96
508	New broad gauge line between Naliya Jakhau Port 25 Kms (PCE/WR) (611943)	Gujarat	02/2023	01/2028 01/2028	410.26 (410.26)	6	4

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
509	Quadrupling between Gandhidham Adipur with Y connection at Adipur for providing direct entry towards Mundra Port and Bhuj and high level platform at Gopalpur 11Kms (PCE/WR) (611944)	Gujarat	02/2023	03/2026 03/2026	152.44 (152.44)	20	68
510	Petlad Bhadran 23 Kms (PCE/WR) (611945)	Gujarat	05/2022	05/2030 05/2030	307.11 (307.11)	82	8
511	Choranda Motikoral 18 Kms (PCE/WR) (611969)	Gujarat	08/2023	10/2026 (-)	246 (246)	0	0
512	Samlaya Timba Road 54 km (PCE/WR) (611970)	Gujarat	02/2023	03/2030 03/2030	670.17 (670.17)	102	12
513	Samni Jambusar 24 km (PCE/WR) (611971)	Gujarat	05/2022	03/2030 03/2030	350 (349.93)	87	32
514	Jambusar Kavi 26 Kms (PCE/WR) (611972)	Gujarat	04/2023	12/2026 (-)	318 (318)	0	0
515	miyagam karjan Choranda maalsar 37 kms (PCE/WR) (611973)	Gujarat	06/2023	12/2026 (-)	450 (450)	0	0
516	Western Railway Samakhiali Gandhidham Quadrupiling 53 Kms (PCE/WR) (611974)	Gujarat	08/2023	12/2026 (-)	1430 (1430)	0	0
517	Dahod Creation of Infrastructure facilities for 9000 HP Electric locomotives Manufacturing at (PCE/WR) (611977)	Gujarat	02/2023	02/2025 (-)	487 (487)	108.69	0
518	Dahod Rolling Stock Workshop Provision of Infrastructure for CBS at (PCE/WR) (611978)	Gujarat	03/2023	03/2025 (-)	158 (158)	47.31	0
519	Sabarmati Setting up of Maintenance Facilities for Train Sets Phase ii (PCE/WR) (611979)	Gujarat	04/2023	06/2025 (-)	250 (250)	0	0
520	4th LINE BETWEEN BAREJADI NANDEJ-SANAND-AHMEDABAD BYPASS (Western Railway) (612072)	Gujarat	02/2023	03/2027 03/2027	961.67 (961.67)	132.63	16
521	Redevelopment of Ahmedabad railway station and associated infrastructure on engineering, procurement and construction mode (Ministry of Railways) (613786)	Gujarat	11/2023	03/2028 (-)	2379 (2379)	607.69	15
522	Miyagam-Karjan-Dabhoi-Samlaya [GC] (Western Railway [WR] - II) (705458)	Gujarat	01/2017	03/2021 12/2026	844 (1600)	693	68
523	Modasa-Shamlaji Road Railway Line Project (SECR) (706757)	Gujarat	04/2008	03/2025 03/2027	262 (262)	203	58
524	Rajkot - Kanalus Doubling Project [111.2 Kms] (Western Railway [WR] - II) (706763)	Gujarat	12/2021	10/2026 10/2026	1080.58 (1080.58)	731	72
525	NADIAD-PETLAD [37.26 KM] (WR) (709812)	Gujarat		06/2030 06/2030	461.91 (461.91)	75	7
526	NEW BG LINE INTERSECTION [5 NOS] BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD [16.51 KM] [PB#29/NR/202 (SECR) (709813)	Gujarat		10/2027 10/2027	437.21 (437.21)	43	15
527	Bhiwani - Dobh Bahali Doubling Project [42.30 Km] (North Western Railway [NWR]) (611884)	Haryana	02/2023	02/2028 02/2028	471 (471)	187.33	57
528	Gomoh - Flyover for DN trains (East Central Railway [ECR] - II) (705765)	Jharkhand	01/2018	03/2026 03/2026	686 (686)	536.04	59
529	Lodhma - Piska - Link Line bypassing Hatia/Ranchi with Y connection (South Eastern Railway [SER] - I) (705785)	Jharkhand	03/2019	06/2026 05/2027	473 (473)	284.26	4
530	Construction of New BG line between Hassan to Belur [27 Km] (South Western Railway [SWR] - II) (400023)	Karnataka	12/2025	04/2028 04/2027	749 (749)	0	0
531	Yeshvanthpur - Channasandra Doubling Project [21.70 Km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703585)	Karnataka	10/2019	12/2024 06/2026	314 (314)	144	59
532	New Railway Line between Ginigera and Raichur [165.57 km] (South Western Railway [SWR] - II) (705434)	Karnataka	05/2009	03/2019 03/2027	2565 (3034.98)	2063.57	66
533	Gadag-Wadi New Railway Line [257 km] (South Western Railway [SWR] - II) (705490)	Karnataka	08/2017	03/2027 12/2027	2842 (6700)	1721.14	30
534	Kadur - Chickamagalur - Sakleshpur [93km] (South Western Railway [SWR] - II) (705492)	Karnataka	11/2016	06/2025 12/2025	825 (825)	770.18	83
535	Bagalkot-Kudachi New Railway Line [142 km] (South Western Railway [SWR] - II) (705495)	Karnataka	11/2012	03/2027 01/2027	1378 (1649)	670.74	35
536	Tumkur-Chitradurga-Davangere New Rail Line Project [191 km] (South Western Railway [SWR] - II) (705496)	Karnataka	01/2017	03/2019 12/2027	1876 (1876)	516.17	13
537	SHIMOGA - SHIKARIPURA - RANEBENNUR [96 Km] (South Western Railway [SWR] - II) (705761)	Karnataka	02/2023	12/2027 06/2028	1454 (1454)	69.58	11
538	Belgaum-Dharwad via Kittur [73.10Km] (South Western Railway [SWR] - II) (706835)	Karnataka	03/2025	12/2027 03/2029	1591 (1591)	0.75	0

All Ongoing Projects

JULY 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
539	Kumbalam-Turavur doubling project [15.59 Km] (Southern Railway [SR] - II) (705638)	Kerala	04/2023	03/2027 03/2027	813 (813)	292.15	15
540	Ernakulam-Kumbalam doubling project [7.71 Km] (SR-ERS) (705639)	Kerala	04/2023	03/2028 03/2028	601 (601)	283	17
541	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho (North Central Railway) (705480)	Madhya Pradesh	03/1998	03/2027 12/2027	8914 (8914)	4971.65	70
542	Katni - Bina Third Railway Line [279 km] (West Central Railway WCR I) (705651)	Madhya Pradesh	01/2017	03/2022 12/2025	2478.23 (4127.23)	3295.49	90
543	Satna-Rewa Railway Line Doubling Project (West Central Railway [WCR] - II) (705659)	Madhya Pradesh	08/2017	03/2026 03/2026	500 (584)	561.26	80
544	Doubling of Katni - Singrauli Railway Line [261 km] (Indian Railway Construction International Limited [IRCON]) (705660)	Madhya Pradesh	03/2017	12/2026 12/2027	2445 (4377)	3122	100
545	Katni Grade Separator/Bye Pass (Indian Railway Construction International Limited [IRCON]) (705661)	Madhya Pradesh	09/2017	09/2024 03/2026	1248 (1248)	1537.77	92
546	Indore - Budni New Railway Line [198 kms] (RVNL - II) (705763)	Madhya Pradesh	10/2020	09/2030 09/2030	7474 (7474)	1658.03	22
547	Nimach-Ratlam Doubling [133 Km] (Western Railway [WR] - II) (705933)	Madhya Pradesh	10/2021	10/2027 10/2027	1095.88 (1095.88)	1056.18	89
548	DHULE [BORVIHIR] - NARDANA NEW LINE [50.60 KMS] (CR) (400019)	Maharashtra	04/2023	12/2026 09/2027	493 (1171)	234.48	9
549	Wardha-Nanded Via Yavatmal New BG Line (Central Railway [CR] - II) (400271)	Maharashtra	04/2008	03/2028 03/2028	3445 (3445)	3002.93	50
550	AURANGABAD-ANKAI - DOUBLING PROJECT 98.25 Km (South Central Railway [SCR] - II) (611751)	Maharashtra	05/2023	03/2027 (-)	960.64 (960.64)	0	0.01
551	Western Railway Vasai bypass double line between Naigaon Juchandra 6 km (PCE/WR) (611975)	Maharashtra	07/2023	03/2026 (-)	176 (176)	0	0
552	Jogeshwari AT Development of JOS-AT as Trainset Maintenance Depot for energy efficient Vande Bharat Sleeper Trains (PCE/WR) (611976)	Maharashtra	06/2023	10/2025 (-)	221 (221)	0	0
553	Redevelopment of Chhatrapati Shivaji Maharaj Terminus [CSMT] and construction of associated infrastructure (Ministry of Railways) (613015)	Maharashtra	07/2023	03/2027 (-)	1813 (1813)	525.2	12
554	Gondia-Balharshah [Chanda Fort] Doubling [240 Km] (South East Central Railway) (617201)	Maharashtra	04/2025	04/2030 (-)	4373.04 (4373.04)	0	0
555	Doubling between Parbhani Parli Vajjanath stations 64.71 Km (South Central Railway [SCR] - II) (617215)	Maharashtra	12/2023	03/2028 (-)	769.93 (769.93)	0	0
556	Western Region Video Surveillance Project (RCIL) (705300)	Maharashtra	04/2023	12/2023 (-)	227.59 (227.59)	0	0
557	Ahmednagar - Beed - Parli - Vajinath New Broad Gauge Line Railway Project [261.3 km] (Central Railways) (705356)	Maharashtra	10/2002	03/2026 03/2026	2539 (4957)	4725.34	92
558	Baramati Lonand New Line Project (Central Railway [CR] - II) (705357)	Maharashtra	03/1999	03/2027 03/2027	736 (1844)	712	50
559	Wadsa-Gadchiroli (South East Central Railway) (705479)	Maharashtra	03/2012	03/2027 03/2027	1886 (1886)	706.28	49
560	3rd Line Kalyan - Kasara [67.35 Kilometres] (Central Railway [CR] - II) (705498)	Maharashtra	09/2015	12/2026 12/2026	793 (1432)	894.16	50
561	3rd Line Wardha - Sewagram - Nagpur (Central Railway [CR] - II) (705500)	Maharashtra	05/2016	12/2025 12/2025	540 (698)	724.75	80
562	3rd Line Wardha - Ballarshah [132 Kilometres] (Central Railway [CR] - II) (705502)	Maharashtra	12/2016	12/2025 02/2026	1385 (1385)	1102.48	77
563	Pune - Miraj-Londa [467 Kilometres] (Central Railway [CR] - II) (705503)	Maharashtra	06/2016	02/2025 08/2025	3627 (6689)	6548	84
564	Doubling of Daund Manmad Line [247.6 km] (Central Railway [CR] - II) (705504)	Maharashtra	03/2017	12/2025 12/2025	2081 (3075)	2769	88
565	4th Line Wardha - Nagpur [78.7 Kilometres] (Central Railway [CR] - II) (705505)	Maharashtra	05/2018	12/2025 02/2026	638 (1137)	969	80
566	3rd Line Manmad - Jalgaon [160 Kilometres] (Central Railway [CR] - II) (705506)	Maharashtra	04/2018	12/2024 08/2025	1035 (1559)	1692	97
567	Solapur-tuljapur-Osmanabad (WR) (705735)	Maharashtra	12/2023	03/2028 03/2028	905 (3296)	1150	10
568	Nagpur- Nagbhir Railway Line Gauge Conversion Project (MRIDC) (705799)	Maharashtra	04/2020	12/2025 12/2025	1400 (1400)	1472	80

All Ongoing Projects

JULY 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
569	Mumbai Urban Transport Project [MUTP] - PHASE II (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706779)	Maharashtra	04/2008	03/2014 12/2027	8087 (8087)	7364	87
570	Mumbai Urban Transport Project [MUTP] Phase-IIIA (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706780)	Maharashtra	04/2019	12/2027 12/2027	33690 (33690)	2246.15	16
571	Mumbai Urban Transport Project Phase-III (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706781)	Maharashtra	12/2016	03/2022 12/2026	10947 (10947)	5057.67	60
572	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (709808)	Maharashtra	01/2022	08/2027 03/2028	955 (2094)	118	2
573	KALYAN-MURBAD VIA ULHASNAGAR [UMBRELLA WORK] (Central Railway [CR] - II) (709809)	Maharashtra	04/2023	03/2027 03/2027	836 (836)	9.29	1
574	Marikuppam - Kuppam New Line Project [23.70 Km] (South Western Railway [SWR] - II) (705491)	Multi-States (Andhra Pradesh, Karnataka)	10/2018	06/2026 06/2026	297 (297)	123.17	15
575	Rayadurg-Tumkur via Kalyandurg New Line [207 km] (South Western Railway [SWR] - II) (705494)	Multi-States (Andhra Pradesh, Karnataka)	07/2010	09/2015 02/2028	2496 (2496)	1691.88	67
576	Renigunta, Wadi & Gooty Bypass Railway Project (South Central Railway [SCR] - I) (705610)	Multi-States (Andhra Pradesh, Karnataka)	04/2016	12/2025 12/2025	302 (543)	381	50
577	Doubling between Mudkhed Medchal & Mahbubnagar Dhone section 417.88 Km (South Central Railway [SCR] - II) (617212)	Multi-States (Andhra Pradesh, Maharashtra, Telangana)	08/2023	03/2029 (-)	4686.09 (4686.09)	0	0
578	Vizianagaram - Titlagarh 3rd line [272 Km including By - pass line of 7.68 KM] (RVNL - II) (400253)	Multi-States (Andhra Pradesh, Odisha)	11/2016	12/2026 12/2026	4803 (6670)	5722.01	89
579	Doubling of Kottavalasa-Koraput Rail Line [189 KM] (East Coast Railway [ECOR] - II) (705512)	Multi-States (Andhra Pradesh, Odisha)	01/2016	03/2022 03/2028	2500 (2500)	2033.31	70
580	Malkangiri Pandurangapuram new railway line project (Indian Railways) (616702)	Multi-States (Andhra Pradesh, Odisha, Telangana)	01/2027	11/2031 (-)	3591.76 (3591.76)	0	0
581	Tindivanam-Nagari New Line Project [184.5 km] (Southern Railway [SR] - II) (400275)	Multi-States (Andhra Pradesh, Tamil Nadu)	10/2008	09/2016 03/2028	3631 (3631)	1113.53	18
582	Doubling between Motumari Vishnupuram - 88.81 Km and Rail over Rail - RoR at Motumari - 10.877 Km (South Central Railway [SCR] - II) (616857)	Multi-States (Andhra Pradesh, Telangana)	03/2025	03/2029 (-)	1595.55 (1595.55)	7.69	1
583	Doubling of Guntur Bibinagar 239 Km (South Central Railway [SCR] - II) (617211)	Multi-States (Andhra Pradesh, Telangana)	08/2023	03/2029 (-)	2853.23 (2853.23)	43.88	1
584	Rail Connectivity to Errupalem Amravati Namburu 57 Km (South Central Railway [SCR] - II) (617214)	Multi-States (Andhra Pradesh, Telangana)	11/2024	03/2027 (-)	2047.4 (2047.4)	0	0
585	Kazipet-Vijayawada 3rd line with electrification [220 km] (South Central Railway [SCR] - II) (705612)	Multi-States (Andhra Pradesh, Telangana)	08/2014	02/2025 12/2025	1953 (3363)	2915.49	90
586	Vijayawada - Kazipet Bypass line (South Central Railway [SCR] - II) (705632)	Multi-States (Andhra Pradesh, Telangana)	04/2016	01/2025 12/2025	647 (904)	870	91
587	Murkongselek-Pasighat (Northeast Frontier Railway [NFR]) (705401)	Multi-States (Arunachal Pradesh, Assam)	03/2012	03/2025 12/2025	435 (1250)	901	56
588	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	01/2025	02/2028 (-)	2123.7 (2123.7)	13.74	0
589	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	02/2016	03/2025 12/2025	6663 (6663)	5202.29	79
590	New Delhi- Howrah Speed Booster[160Kmph] Project (PCE/NCR) (705794)	Multi-States (Bihar, Delhi, Jharkhand, Uttar Pradesh, West Bengal)	09/2019	03/2024 (-)	6684.81 (6684.81)	127.03	0
591	Third Railway Line between Patratu-Sonnagar [281 kms] (RVNL - II) (400234)	Multi-States (Bihar, Jharkhand)	08/2018	03/2026 07/2026	8975 (8975)	4950	88
592	Multi tracking of Son Nagar-Andal [374.53 rkm & 814.38 tkm] (East Central Railway [ECR] - I) (616699)	Multi-States (Bihar, Jharkhand)	08/2023	03/2028 (-)	12333.57 (12333.6)	444.74	10
593	Koderma-Tilaiya New Line (East Central Railway [ECR] - II) (705375)	Multi-States (Bihar, Jharkhand)	03/2002	02/2025 02/2026	1626 (2020)	2060.97	92
594	Pirpainti - Jasidih [100.52 Km] New BG line (Eastern Railway [ER] - I) (705385)	Multi-States (Bihar, Jharkhand)	03/2022	03/2028 03/2028	2555 (2555)	763.08	48
595	NER Provision of Automatic Block Signalling on Gorakhpur Cantt[Excl] Chhapra Gramin & Burhwal Jn [Excl] Sitapur Jn section of high density routes (North Eastern Railway [NER]) (611669)	Multi-States (Bihar, Uttar Pradesh)	06/2023	03/2027 (-)	380.47 (380.47)	24.53	0
596	Gorakhpur-Valmikinagar Doubling project (NER) (617224)	Multi-States (Bihar, Uttar Pradesh)	03/2024	12/2027 (-)	1120 (1120)	181.86	20
597	Chhapra-Ballia Patch Doubling (North Eastern Railway [NER]) (705562)	Multi-States (Bihar, Uttar Pradesh)	11/2015	02/2025 03/2026	963 (1046)	906	95.4

All Ongoing Projects

JULY 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
598	Rajnandgaon - Nagpur [Kalumna] Third Railway Line [228.30 km] (South East Central Railway [SECR] - II) (705617)	Multi-States (Chhattisgarh, Maharashtra)	12/2016	12/2024 06/2026	3545 (3545)	3163.08	95
599	Jagdalpur-Koraput (East Coast Railway [ECoR] - II) (705511)	Multi-States (Chhattisgarh, Odisha)	03/2016	03/2024 12/2026	1547 (1547)	1308.2	90
600	Jharsuguda-Bilaspur Fourth Railway Line [206 km] (SECR) (705616)	Multi-States (Chhattisgarh, Odisha)	09/2016	10/2024 12/2025	2140 (2979)	2124.15	88
601	Mumbai-Ahmedabad High Speed Rail Project- 508 km (National High Speed Rail Corporation [NHSRC]) (705728)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	09/2017	08/2027 12/2029	108000 (108000)	78690.89	53
602	New Delhi- Mumbai Speed Booster[160Kmph] Project (PCE/WR) (705793)	Multi-States (Delhi, Gujarat, Madhya Pradesh, Maharashtra, Rajasthan)	09/2019	03/2024 (-)	6806.44 (6806.44)	135.65	0
603	Hospet - Tinaighat - Vasco Rail Doubling Project (RVNL - II) (705650)	Multi-States (Goa, Karnataka)	07/2012	03/2027 12/2027	5060 (5060)	5007.82	86
604	Hospet-Hubli-Vasco da Gama Line Electrification Project (RVNL) (706950)	Multi-States (Goa, Karnataka)	05/2018	03/2023 03/2024	744.49 (1122.62)	969.05	95
605	Western Dedicated Freight Corridor (DFCCIL) (705237)	Multi-States (Gujarat, Haryana, Maharashtra, Rajasthan, Uttar Pradesh)	01/2012	03/2022 12/2025	51101 (124005)	124623	96
606	New line Dahod-Indore via Sardarpur, Jabuwa and Dhar (Western Railway [WR] - II) (705453)	Multi-States (Gujarat, Madhya Pradesh)	06/2012	02/2027 02/2027	1942 (2691)	3412.98	67
607	Chhota Udaipur - Dhar New Line Project [157 km] (Western Railway [WR] - II) (705454)	Multi-States (Gujarat, Madhya Pradesh)	01/2014	12/2025 12/2025	1794 (1794)	1800.85	80
608	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (Western Railway) (611452)	Multi-States (Gujarat, Maharashtra)	03/2023	12/2025 06/2025	311 (311)	208	92
609	Taranga Hill-Abu Road via Ambaji (North Western Railway [NWR]) (400022)	Multi-States (Gujarat, Rajasthan)	07/2022	07/2030 07/2030	2798 (2798)	1891.9	14
610	LUNI- SAMDARI- BHILDI DOUBLING (North Western Railway [NWR]) (616842)	Multi-States (Gujarat, Rajasthan)	02/2024	07/2027 (-)	3085.59 (3085.59)	154.46	7
611	Chandigarh-Baddi New Rail Line- 36 km (Northern Railway [NR]) (705424)	Multi-States (Haryana, Himachal Pradesh)	02/2018	12/2026 12/2026	1540 (1540)	506.73	31
612	Rewari - Kathuwas Doubling Project [27.72 Km] (North Western Railway [NWR]) (611861)	Multi-States (Haryana, Rajasthan)	12/2022	06/2027 06/2027	352 (352)	239.01	59
613	Nangal Dam-Talwara New Broad Gauge Line [84 KM] and Taking Over Siding Mukerian-Talwara [29 KM] (Northern Railway [NR]) (705410)	Multi-States (Himachal Pradesh, Punjab)	05/1985	12/2025 01/2027	2018 (2018)	1848	74
614	Bhanupalli-Bilaspur-Beri New Railway Line Project (RVNL - II) (705428)	Multi-States (Himachal Pradesh, Punjab)	04/2015	12/2026 12/2027	13447 (13447)	6391.15	59
615	Doubling of Hatia [Ranchi]-Bondamunda Rail Line - 159 km (South Eastern Railway - JH) (705628)	Multi-States (Jharkhand, Odisha)	02/2017	06/2025 06/2026	3029 (3029)	2458.15	85
616	Buramara-Chakulia new line [59.96 km] (South Eastern Railway [SER] - I) (616588)	Multi-States (Jharkhand, Odisha, West Bengal)	12/2024	12/2029 (-)	1459.13 (1459.13)	1.04	0
617	Chandil - Anara - Damodar - 3rd line [121.26 km] (CAO/C/SER) (616227)	Multi-States (Jharkhand, West Bengal)	07/2025	09/2029 (-)	1932.01 (1932.01)	0.03	0
618	Murarai - Barharwa 3rd line (Eastern Railway [ER] - II) (617240)	Multi-States (Jharkhand, West Bengal)	01/2026	05/2028 (-)	935.19 (935.19)	0	0
619	KHARAGPUR-ADITYAPUR THIRD RAIL LINE- 132 KM (RVNL - II) (705668)	Multi-States (Jharkhand, West Bengal)	01/2018	03/2025 12/2025	3250 (3250)	3176.46	97
620	Hotgi-Kudgi-Gadag Doubling Project (South Western Railway [SWR] - II) (705662)	Multi-States (Karnataka, Maharashtra)	01/2016	12/2024 03/2026	1878 (2459)	2628.8	89
621	Baiyyappanahalli - Hosur Doubling Project [48 km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703586)	Multi-States (Karnataka, Tamil Nadu)	02/2019	12/2024 01/2026	499 (499)	595	97
622	Trivandrum- Kanyakumari (SR-ERS) (705635)	Multi-States (Kerala, Tamil Nadu)	03/2016	03/2024 12/2027	1432 (3785)	2451	46
623	Ratlam-Mhow-Khandwa-Akola Gauge Conversion (Western Railway [WR] - II) (705457)	Multi-States (Madhya Pradesh, Maharashtra)	03/2010	03/2027 09/2028	5678 (6531.9)	4314	87
624	Itarsi - Nagpur Third Railway Line [280 km] (Central Railway [CR] - II) (705507)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016	03/2027 03/2027	2450 (2450)	1815.49	52
625	Gwalior - Seopurkala with extension to Kota [Gauge Conversion] (North Central Railway) (705419)	Multi-States (Madhya Pradesh, Rajasthan)	07/2018	03/2025 02/2026	2913 (2913)	2751	83

All Ongoing Projects

JULY 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
626	Ramganjmandi-Bhopal New Line Project [262 km] (West Central Railway [WCR] - II) (705481)	Multi-States (Madhya Pradesh, Rajasthan)	10/2004	12/2025 12/2027	3032 (5073)	3592.92	70
627	Nimach-Badi Sadri New Rail Line Project (Western Railway [WR] - II) (705764)	Multi-States (Madhya Pradesh, Rajasthan)	09/2021	03/2026 12/2025	495 (825)	306	46
628	Mathura-Jhansi Third Railway Line [274 Km] (RVNL - II) (705667)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	03/2018	12/2024 12/2026	5961 (5961)	4928.62	94
629	Jhansi - Bina Third Railway Line [153 Km] (CAO/C/NCR) (705598)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2018	03/2022 03/2026	2002 (2002)	1884.84	93
630	Jhansi-Khairar-Manikpur & Khirar-Bhimsen (North Central Railway) (705608)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2017	03/2026 03/2026	4330 (4330)	1989	53
631	Third Line [new] between Kazipet - Balharshah with electrification [201.04 Km] (South Central Railway [SCR] - II) (705613)	Multi-States (Maharashtra, Telangana)	10/2016	01/2025 11/2025	2595 (3071)	3142.35	92
632	Narayangarh-Bhadrak 3rd line (South Eastern Railway [SER] - I) (705629)	Multi-States (Odisha, West Bengal)	03/2017	12/2025 06/2026	2400 (2400)	2188	65
633	Nagapattinam-Tiruturaipundi and Karaikal-Peralam New Line (Southern Railway [SR] - II) (400223)	Multi-States (Puducherry, Tamil Nadu)	01/2019	03/2026 03/2027	713 (981)	598.38	80
634	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Multi-States (Sikkim, West Bengal)	05/2010	05/2015 12/2027	7877 (12133)	8883.6	80
635	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass Line Project (Eastern Railway [ER] - I) (602797)	Multi-States (Uttar Pradesh, West Bengal)	12/2017	03/2027 03/2027	461.64 (461.64)	178.45	6
636	Proposed 6 nos Road Over Bridge [ROB] at different locations under MCL Talcher Under Deposit Scheme. (East Coast Railway [ECoR] - II) (400045)	Odisha	07/2022	03/2025 01/2025	168.32 (168.32)	69.85	82
637	Brundamal-Jharsuguda- flyover connection for joining downline (East Coast Railway [ECoR] - II) (400232)	Odisha	01/2014	12/2026 12/2026	297 (297)	193.22	30
638	3rd & 4th line between Sarla - Sason [8 km] [PB 73/2023-24/NR] (East Coast Railway [ECoR] - II) (612834)	Odisha	04/2023	12/2025 (-)	252 (252)	79.55	45
639	Bangriposi-Gorumahisani new line [85.60 km] (CAO/C/SER) (616586)	Odisha	09/2025	12/2029 (-)	2269.49 (2269.49)	0	0
640	Badampahar-Kendujhargarh new line [82.06 km] (CAO/C/SER) (616587)	Odisha	09/2025	12/2029 (-)	1875.72 (1875.72)	0	0
641	Flyover between Siju and Paradeep coaching Yard to avoid Surface crossing of trains (East Coast Railway [ECoR] - II) (616694)	Odisha	10/2025	07/2028 (-)	200.77 (200.77)	0	0
642	Paradeep - Badabandha 3rd & 4th Line / 18.51kms (East Coast Railway [ECoR] - II) (616695)	Odisha	04/2025	11/2028 (-)	300.15 (300.15)	0.01	0
643	Khurda-Bolangir New Broad Gauge Rail Link [301km] (East Coast Railway [ECoR] - II) (705358)	Odisha	03/2001	12/2026 12/2026	3792 (5089)	4983.45	89
644	Talcher-Bimlagarh New Railway Line (East Coast Railway [ECoR] - II) (705359)	Odisha	12/2004	03/2025 03/2027	1928 (1928)	1902.91	47
645	Bhadrak-Nergundi Third Line (East Coast Railway [ECoR] - II) (705510)	Odisha	04/2015	11/2024 01/2026	1284 (1284)	1298	80
646	Koraput - Singapur Railway Doubling (East Coast Railway [ECoR] - II) (705513)	Odisha	12/2015	12/2027 03/2028	2362 (2362)	1787.49	68
647	Jarapada- Budhapank with flyover at Talcher road 3rd and 4th Line (East Coast Railway [ECoR] - II) (705514)	Odisha	12/2015	11/2018 03/2026	1000 (810.02)	401.61	36
648	Talcher-Angul New Line with Y-Connection at Talcher (CAO/C/ECoR) (705743)	Odisha		05/2027 05/2028	495 (495)	29.5	1
649	Baghuapal Flyover Construction Project (CAO/C/ECoR) (705767)	Odisha	10/2022	03/2028 03/2028	257.97 (258)	0.83	0
650	Rourkela - Bondamunda 5th Line Doubling Project (South Eastern Railway [SER] - I) (706856)	Odisha	03/2022	09/2026 09/2026	245 (245)	82	35
651	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (Indian Railway) (709810)	Odisha	01/2026	08/2027 08/2027	190.9 (190.9)	0	0
652	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION/12.76kms (East Coast Railway [ECoR] - II) (709811)	Odisha	05/2025	09/2027 09/2027	190 (190)	0	0
653	Junagarh Visavadar 42 Kms (WR) (611980)	Offshore	02/2023	09/2028 09/2028	492.83 (492.83)	3	1
654	Jaynagar-Bijalpura, incl. extn. Bet, Bijalpura-Bardibas [Nepal] (East Central Railway [ECR] - I) (705362)	Offshore	03/2011	03/2022 03/2026	819 (819)	588.32	75
655	Ludhiana- Killa Raipur Railway Doubling Project (CAO/C/NR) (705783)	Punjab	12/2022	03/2025 03/2026	237.64 (237.64)	118	55

All Ongoing Projects							
JULY 2025							
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
656	Dedicated Test Track for RDSO Phase II (North Western Railway [NWR]) (611614)	Rajasthan	11/2021	11/2026 11/2026	819.48 (967.06)	471	86
657	Devgarh Madariya - Nathdwara Gauge Conversion [82.54 Km] part of Marwar - Mavli Gauge Conversion [152 Km] (North Western Railway [NWR]) (611849)	Rajasthan	01/2023	06/2028 06/2028	969 (969)	411	45
658	Maintenance cum workshop depot for Vande Bharat Sleeper Trains as per conditions under WTA 527 (WPO/Patna) (611929)	Rajasthan	06/2023	12/2024 (-)	166.86 (166.86)	0	0
659	RINGUS KHATUSHYAMJI NEW LINE (North Western Railway [NWR]) (616696)	Rajasthan	03/2024	03/2028 (-)	254.06 (254.06)	1.65	0
660	RAS- MERTA CITY NEW LINE INCL BYPASS AT MERTA ROAD (North Western Railway [NWR]) (616840)	Rajasthan	02/2024	03/2028 (-)	947 (947)	1.36	0
661	PUSHKAR- MERTA CITY NEW LINE (North Western Railway [NWR]) (616841)	Rajasthan	02/2024	12/2026 (-)	799.64 (799.64)	13.91	3
662	AJMER- CHANDERIYA DOUBLING (North Western Railway [NWR]) (616843)	Rajasthan	02/2024	06/2027 (-)	1634.79 (1634.79)	59.51	5
663	Dholpur - Sirmuttra Gauge Conversion (North Central Railway) (705482)	Rajasthan	04/2020	02/2019 02/2027	747 (747)	392	39
664	Gudha-Thatha Mithri Construction of Railway Track Project (North Western Railway [NWR]) (705752)	Rajasthan	04/2019	11/2026 11/2026	819.48 (967.06)	471	98
665	Sawai Madhopur-Jaipur Railway Line Project (North Western Railway [NWR]) (705912)	Rajasthan	04/2023	03/2027 (-)	1203.89 (1203.89)	35.05	9
666	Agra Fort-Bandikui Doubling Line Project (CAO/C/NCR) (705919)	Rajasthan	02/2021	06/2027 06/2027	1390 (1390)	123	25
667	Sawaimadhopur Bye Pass Line Project (North Western Railway [NWR]) (706866)	Rajasthan	01/2023	03/2026 05/2027	304 (304)	134	35
668	Ph II extension of MRTS from Velachery to St Thomas Mount (Southern Railways [SR] - construction) (400280)	Tamil Nadu	11/2008	07/2024 08/2025	734 (982)	475.73	99
669	Redevelopment of Chennai Egmore Station (WR) (613002)	Tamil Nadu	10/2022	03/2026 (-)	842 (842)	340	0
670	Coach Production Factory Upgradation Project (CPM/ICF) (705244)	Tamil Nadu	07/2018	12/2021 (-)	520 (520)	192.25	0
671	Morappur - Dharmपुरi New Railway Line Project (Southern Railway [SR] - I) (705755)	Tamil Nadu	12/2016	03/2028 03/2028	359 (359)	40	1
672	Doubling between Bhadrachalam Road and Dornakal (South Central Railway [SCR] - II) (616856)	Telangana	04/2025	04/2029 (-)	770.12 (770.12)	0	0
673	Manoharabad-Kothapalli New Rail Line [151 km] (South Central Railway [SCR] - II) (705437)	Telangana	01/2017	03/2027 12/2027	1160 (2781)	1713.38	71
674	Bahraich-Shravasti-Balrampur-Siddharthnagar -Santkabinagar (North Eastern Railway [NER]) (400204)	Uttar Pradesh	03/2017	10/2030 10/2030	4939.78 (4939.78)	1217.13	8
675	Sahjanwa-Dohrighat (North Eastern Railway [NER]) (400205)	Uttar Pradesh	03/2017	03/2029 03/2029	1319.75 (1319.75)	457.35	3
676	Anandnagar - Ghugli via Maharajganj 50 km (Construction NER) (617252)	Uttar Pradesh	11/2023	03/2028 (-)	958.27 (958.27)	432.01	23
677	Chunar-Chopan doubling project (North Central Railway) (617284)	Uttar Pradesh	01/2025	03/2028 (-)	1423.96 (1423.96)	26	2
678	Domingarh-Gorakhpur-Gorakhpur Cantt.-Kusumhi - 3rd Railway Line Project (North Eastern Railway [NER]) (705566)	Uttar Pradesh	06/2018	02/2025 09/2025	351 (521.47)	494	98
679	Burhwal Gonda 3rd line (North Eastern Railway [NER]) (705567)	Uttar Pradesh	07/2019	03/2025 09/2025	1016 (1118)	1113.75	70
680	Janghai-Pratapgarh- Amethi (CAO/C/II/NCR) (705588)	Uttar Pradesh	03/2017	03/2025 03/2026	722 (1194)	1100	70
681	Lalitpur-Birari with flyover at Lalitpur- 16 Km (North Central Railway) (705766)	Uttar Pradesh	03/2017	12/2024 11/2025	304.44 (356)	214	65
682	Mughalsarai-Allahabad, 3rd line (North Central Railway) (705772)	Uttar Pradesh	03/2016	12/2026 03/2027	2649 (2649)	1399	62
683	Aligarh -Daud Khan Flyover Construction & 3rd Railway Line Project (CAO/C/NCR) (705774)	Uttar Pradesh	09/2020	01/2025 03/2027	758 (779.49)	315.37	55
684	Bhandai Flyover Construction Project (CAO/C/NCR) (705777)	Uttar Pradesh	04/2021	02/2026 02/2027	250.18 (250.18)	118	15
685	Phephna-Indara, Mau-Shahganj doubling excluding Indara-Mau (South Eastern Railway [SER] - I) (705779)	Uttar Pradesh	03/2017	12/2024 03/2026	1178 (1777)	1489.5	85

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
686	Bhatni-Aurnihar with electrification excluding Indara-Mau (RVNL - II) (705780)	Uttar Pradesh	03/2017	12/2024 10/2025	2529 (2529.46)	2051.69	94
687	Barabanki-Malhaur 3rd & 4th Railway Line Project (CAO/C/NR) (705782)	Uttar Pradesh	04/2017	03/2025 03/2026	407 (407)	317	75
688	Janghai-Phaphamau Doubling Rail Line Project (RVNL) (705784)	Uttar Pradesh	03/2020	03/2025 03/2025	357 (978.77)	579	95
689	Bahraich - Nanpara - Nepalganj Road Gauge Conversion (North Eastern Railway [NER]) (705863)	Uttar Pradesh	04/2021	07/2025 08/2025	950 (950)	507.02	86
690	Allahabad division - Aligarh - Harduaganj Flyover (North Central Railway) (705918)	Uttar Pradesh	02/2021	06/2026 03/2027	1457 (1457)	50	8
691	Rishikesh-Karnaprayag New Rail Line- 125 km (RVNL - II) (705429)	Uttarakhand	08/2018	12/2025 03/2027	38953 (38953)	24645.15	65
692	Kalinarayanpur-Krishnanagar Doubling Alongwith Krishnanagar - Chapra New Line And Naihati-Ranaghat 3rd Line. (Eastern Railway [ER] - I) (400247)	West Bengal	11/2005	02/2027 02/2027	1000 (1000)	1029.97	67
693	Tarakeshwar-Bishnupur New Line [82.47 km] (Eastern Railway [ER] - I) (400273)	West Bengal	02/2008	03/2019 02/2026	1189 (1542)	1287.05	90
694	Dum Dum Airport-New Garia via Rajarhat-Construction of Metro Railway (RVNL - II) (400277)	West Bengal	10/2011	12/2025 03/2026	8964 (8964)	8097.47	80
695	Construction of Balurghat-Hilli new BG Line (Northeast Frontier Railway [NFR]) (612096)	West Bengal	12/2010	03/2027 03/2025	1209 (1209)	405.31	9
696	Kalipahari Bakhtarnagar 5th line (Eastern Railway [ER] - I) (617322)	West Bengal	07/2025	06/2027 06/2027	350.46 (350.46)	0	0
697	Joka-BBD Bag new metro project (RVNL - II) (705730)	West Bengal	04/2010	12/2026 12/2028	4835 (10362)	4361.23	59
698	Noapara-Barasat via Bimanbandar - Construction of Metro railway [18 km] (Metro Railway, Kolkata) (706776)	West Bengal	03/2010	08/2026 03/2029	4830 (4830)	2764.13	32
Total (252)					673330.1	503708.43	
Real Estate							
699	Bangalore-Whitefield-Bangalore City-Krishnarajapuram [23.08 km] - Quadrupling (South Western Railway [SWR] - II) (705663)	Karnataka	06/2022	02/2026 02/2026	493 (493)	252.45	82
Total (1)					493	252.45	
Urban Public Transport							
700	Baranagar-Barrackpore and Dakshineswar- Construction of Metro Railway (RVNL - II) (706777)	West Bengal	03/2010	12/2026 12/2025	2298 (2734)	393	17
Total (1)					2298	393	
Ministry of Steel							
Metals & Mining							
701	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul (National Mineral Development Corporation Limited [NMDC]) (615202)	Chhattisgarh	07/2022	12/2028 03/2028	1700 (1756.2)	65.44	2
Total (1)					1700	65.44	
Steel							
702	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617243)	Chhattisgarh	08/2024	07/2026 (-)	198.62 (198.62)	10.53	8
703	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617255)	Chhattisgarh	12/2023	06/2026 (-)	471.83 (471.83)	111.75	35
704	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617256)	Chhattisgarh	01/2024	10/2025 (-)	884.1 (884.1)	453.2	75
705	NMDC Slurry Pipeline Project Phase-1 (National Mineral Development Corporation Limited [NMDC]) (706811)	Chhattisgarh	09/2020	06/2023 12/2025	2907 (5427)	3012.02	84
706	SCREENING PLANT-III AT KIRANDUL (National Mineral Development Corporation Limited [NMDC]) (709826)	Chhattisgarh	10/2021	01/2026 (-)	2718.84 (2718.84)	1327.11	72
707	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (National Mineral Development Corporation Limited [NMDC]) (709827)	Chhattisgarh	10/2022	12/2025 (-)	349.75 (349.75)	247.42	85
708	New Sinter Plant at BSL, SAIL (Steel Authority of India Limited [SAIL]) (400174)	Jharkhand	05/2015	10/2017 06/2027	1034.01 (1752.3)	883.23	51
709	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617249)	Jharkhand	02/2025	01/2027 (-)	211.94 (211.94)	7.52	6
710	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617250)	Jharkhand	02/2025	10/2026 (-)	207.13 (207.13)	7.91	6
711	Revamping of old sub-systems of Blast Furnace 3 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617253)	Jharkhand	10/2023	07/2025 11/2025	513.82 (513.82)	220.42	69



All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
712	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617254)	Jharkhand	04/2024	06/2026 (-)	260.37 (260.37)	44.22	22
713	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617257)	Jharkhand	12/2023	11/2026 (-)	627.31 (627.31)	88.21	37
714	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. (National Mineral Development Corporation Limited [NMDC]) (400121)	Karnataka	06/2024	08/2026 (-)	1043.63 (1043.63)	214.48	25
715	Installation of 4th Slab Caster along with its Auxiliaries and a New Ladle Furnace in SMS-II at Rourkela Steel Plant (Steel Authority of India Limited [SAIL]) (400065)	Odisha	02/2022	05/2025 07/2025	1105.23 (1105.23)	736.47	96
716	Rebuilding of COB 4 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (612781)	West Bengal	12/2023	12/2026 (-)	916.78 (916.78)	118.63	12
717	Installation of New Bar Mill at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617242)	West Bengal	10/2024	06/2027 (-)	2115.44 (2115.44)	206.67	24
718	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617246)	West Bengal	10/2024	06/2026 (-)	758.09 (758.09)	53.31	3
719	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617248)	West Bengal	12/2024	07/2026 (-)	227.96 (227.96)	16.24	29
720	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617251)	West Bengal	12/2024	05/2026 (-)	196.4 (196.4)	0.19	2
Total (19)					16748.25	7759.53	
Department for Promotion of Industry & Internal Trade							
Real Estate							
721	Krishnapatnam Node - Phase 1 - Roads and Services Development (National Industrial Corridor Development Corporation) (701658)	Andhra Pradesh	02/2024	02/2028 (-)	2139.44 (2139.44)	327.99	14
722	Tumakuru Node - Phase 1 - Roads and Services Development (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (701657)	Karnataka	02/2023	09/2026 (-)	1701.81 (1701.81)	95	8
Total (2)					3841.25	422.99	
Tourism, Hospitality & Wellness							
723	Exhibition cum Convention Centre Dwarka [Phase I] (India International Convention & Expo Centre) (400429)	Delhi	12/2017	10/2019 01/2025	5178 (5401)	4470	97.4
Total (1)					5178	4470	
Department of Telecommunications							
Telecommunication							
724	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance (Erstwhile NICF)) (709859)	Delhi	04/2018	02/2020 10/2025	248.2 (248.2)	236.91	98
725	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications [DoT]) (701598)	Meghalaya	09/2020	03/2022 03/2025	971.96 (971.96)	208.25	98
726	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 (Department of Telecommunications [DoT]) (701599)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	09/2021	03/2023 11/2025	1577.57 (1577.57)	596.17	87
727	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha (Department of Telecommunications [DoT]) (701602)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	05/2022	11/2023 11/2025	3685 (3685)	1101.39	79
728	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications [DoT]) (701597)	Multi-States (Arunachal Pradesh, Assam)	10/2021	04/2023 09/2025	1255.49 (1255.49)	284.04	89
729	354 Uncovered Villages Scheme (Department of Telecommunications [DoT]) (701600)	Multi-States (Bihar, Gujarat, Himachal Pradesh, Jammu and Kashmir, Ladakh, Rajasthan, Uttar Pradesh)	04/2020	10/2021 08/2025	336.89 (301.13)	225.71	97
730	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajasthan and Uttar Pradesh (Department of Telecommunications [DoT]) (704495)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	03/2021	03/2022 12/2025	421.65 (228.94)	126.45	96
731	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (709749)	Multi-States (Maharashtra, Telangana)	03/2020	06/2021 12/2025	461.42 (461.42)	166.02	81

All Ongoing Projects

JULY 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
732	Saturation 4G mobile coverage of Uncovered Villages through USOF <i>(Department of Telecommunications [DoT])</i> (400013)	PAN India	07/2022	06/2024 03/2026	26316 (30620)	9291.8	72
733	4G Services by BSNL <i>(Department of Telecommunications [DoT])</i> (701593)	PAN India	11/2020	03/2024 03/2026	28466 (19592)	8332.52	92
734	BharatNet <i>(Department of Telecommunications [DoT])</i> (706775)	PAN India	10/2011	08/2023 03/2027	61109 (188000)	41486.14	80.52
735	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LEBEL SWITCHING [IPMPLS] NETWORK <i>(BSNL)</i> (709855)	PAN India	03/2023	03/2024 03/2025	239.6 (239.6)	179.63	100
736	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT <i>(BSNL)</i> (709856)	PAN India	05/2023	08/2024 08/2025	645.13 (645.13)	522.88	90
737	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. <i>(BSNL)</i> (709857)	PAN India	06/2023	06/2025 03/2026	24544.55 (24544.5)	8333.37	96
738	OPTICAL TRANSPORT NETWORK [OTN] PH-4 IN BSNL <i>(BSNL)</i> (709858)	PAN India	02/2024	08/2025 (-)	810.99 (810.99)	741.9	100
	Total (15)				151089.45	71833.18	
	Department of Water Resources, River Development & GR						
	Waste & Water						
739	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616600)	Bihar	03/2022	02/2025 12/2025	413.29 (413.29)	126.67	0
740	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616611)	Bihar	07/2019	12/2025 (-)	824 (824)	385.32	55
741	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh- Patna under Hybrid annuity based PPP mode-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616612)	Bihar	07/2019	12/2025 (-)	578.89 (578.89)	165.84	53
742	Sewer Network, SPS and STP at Begusarai <i>(National Mission for Clean Ganga)</i> (616615)	Bihar	03/2018	04/2025 12/2025	230.06 (230.06)	261.48	97
743	Sewer Networks, SPS and STP at Hajipur <i>(National Mission for Clean Ganga)</i> (616616)	Bihar	03/2018	06/2025 12/2025	305.19 (305.19)	346.44	95
744	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616594)	Uttar Pradesh	04/2023	04/2025 12/2025	842.25 (842.25)	208.64	69
745	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP <i>(National Mission for Clean Ganga)</i> (616605)	Uttar Pradesh	11/2024	12/2024 05/2027	690.71 (690.71)	0	27
746	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP <i>(National Mission for Clean Ganga)</i> (616604)	West Bengal	12/2021	03/2025 12/2025	154.73 (154.73)	96.17	92
	Total (8)				4039.12	1590.56	
	Water Resources						
747	Sardar Gouthu Latchanna Thotapalli Barrage Project <i>(Water Resources-AP)</i> (400100)	Andhra Pradesh	01/2006	12/2019 03/2025	353.05 (1023.24)	869.11	95
748	Gundlakamma project <i>(Water Resources-AP)</i> (400101)	Andhra Pradesh	04/2005	12/2019 03/2027	397.41 (697.39)	610.89	98
749	Polavaram Irrigation Project <i>(Water Resources-AP)</i> (701415)	Andhra Pradesh	11/2004	04/2022 03/2026	10151.04 (55548.9)	24347.76	83
750	Borolia Irrigation Project <i>(Department of Water Resources, River Development & GR)</i> (701370)	Assam	12/1996	12/2022 03/2025	256.16 (256.16)	0	0
751	Punpun Barrage Project <i>(Water Resources-BR)</i> (400104)	Bihar	04/2007	12/2019 03/2026	571.07 (658.12)	469.66	44
752	Durgawati Reservoir Project <i>(Irrigation and CAD-TG)</i> (701371)	Bihar	04/1997	12/2019 12/2024	691.15 (971.96)	978.51	87
753	Kelo Irrigation Project <i>(Water Resources-CT)</i> (400111)	Chhattisgarh	04/2008	12/2019 06/2025	459.97 (727.04)	616.93	71
754	Kudali Irrigation Project <i>(Department of Water Resources, River Development & GR)</i> (701399)	Chhattisgarh	12/2009	12/2022 (-)	382.29 (382.29)	0	81.8
755	Sardar Sarovar CADWM Project <i>(Narmada and Water Resources, Water Supply and Kalpsar Department-GJ)</i> (400097)	Gujarat	04/2004	12/2019 03/2025	5021.76 (6670.31)	4954.99	90.3
756	Sardar Sarovar Project <i>(Narmada and Water Resources, Water Supply and Kalpsar Department-GJ)</i> (701372)	Gujarat	04/1996	12/2019 03/2025	20718.17 (33412.5)	31767.59	93
757	Subernarekha Multipurpose Project, Jharkhand <i>(Department of Water Resources-JH)</i> (701376)	Jharkhand	01/2012	12/2019 04/2025	3807.77 (9579.58)	5550.74	69

All Ongoing Projects

JULY 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
758	Upper Tunga Irrigation Project (<i>Water Resources-KA</i>) (701377)	Karnataka	04/2014	12/2019 03/2025	770.16 (1606.07)	1511.22	99
759	Omkareshwar CADWM Project (<i>Water resource-mp</i>) (400096)	Madhya Pradesh	04/2015	12/2019 03/2026	648.09 (648.09)	172.56	3
760	Bargi Diversion Project Phase - IV [km. 154 to km 197] (<i>Water Resources-MP</i>) (400115)	Madhya Pradesh	01/2009	12/2019 07/2025	751.03 (893.35)	777.99	74
761	Bargi Diversion Project Phase - III [km. 104 to km 154] (<i>Water Resources-MP</i>) (400116)	Madhya Pradesh	04/2007	12/2019 07/2025	1229.15 (1399.7)	1807.2	79
762	Gosikhurd CADWM Project (<i>Department of water resources-MH - II</i>) (400095)	Maharashtra	04/2017	12/2019 06/2026	743.73 (743.73)	252	50
763	Urmodi Irrigation Project (<i>Department of water resources-MH - II</i>) (400105)	Maharashtra	04/2018	06/2022 06/2025	580.79 (895.81)	713.46	76.22
764	Sulwade-Jamphal-Kanoli Lift Irrigation Scheme (<i>Department of water resources-MH - II</i>) (400107)	Maharashtra	02/2019	06/2023 06/2027	2407.67 (2407.67)	2436.43	80
765	Purna Barrage-2 [Ner Dhamana] Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (400109)	Maharashtra	04/2018	06/2020 06/2025	848.07 (888.43)	690.49	69
766	Jigaon Irrigation Project (<i>Department of water resources-MH - II</i>) (400112)	Maharashtra	04/2018	06/2028 (-)	7222.95 (7222.95)	8501.45	90
767	Waghur Project (<i>Department of water resources-MH - II</i>) (701383)	Maharashtra	04/1996	12/2019 03/2026	1058.99 (1758.51)	1530.36	89
768	Tillari Irrigation Project (<i>Department of water resources-MH - II</i>) (701384)	Maharashtra	01/2006	12/2019 01/2025	368.34 (649.6)	724.36	99
769	Gosikhurd Project (<i>Department of water resources-MH - II</i>) (701386)	Maharashtra	04/2008	12/2019 06/2026	7196.47 (12770.1)	13533.29	72
770	Bembla Irrigation Project (<i>Department of water resources-MH - II</i>) (701388)	Maharashtra	04/2007	12/2019 06/2025	1352.53 (2685.41)	2689.7	98
771	Arjuna Medium Irrigation project (<i>Department of water resources-MH - II</i>) (701390)	Maharashtra	01/2008	12/2019 12/2024	333.87 (611)	803.89	100
772	Aruna Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (701391)	Maharashtra	01/2010	12/2019 01/2025	210.45 (1472.14)	1697.94	97
773	Krishna Koyana Lift Irrigation Project (<i>Department of water resources-MH - II</i>) (701392)	Maharashtra	04/2009	12/2019 12/2023	973.62 (2774.9)	1069.82	90
774	Lower Pedhi Project (<i>Department of water resources-MH - II</i>) (701396)	Maharashtra	04/2008	12/2019 06/2026	255.97 (1480.7)	1324.78	64
775	Nardave Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (701398)	Maharashtra	04/2009	12/2019 03/2025	211.46 (781.85)	623.5	72.59
776	Thoubal Multipurpose Project (<i>Water Resources Department-MN</i>) (701400)	Manipur	04/1997	12/2019 03/2026	1449.44 (1822.24)	1837.91	98
777	North Koel Reservoir Project (<i>Department of Water Resources, River Development & GR</i>) (701412)	Multi-States (Bihar, Jharkhand)	01/2021	03/2021 03/2026	1622.27 (2430.76)	142.1	32
778	Integrated Anandpur Barrage Project (<i>Water Resources-OR</i>) (603945)	Odisha	01/1998	12/2019 06/2025	567.03 (2990.05)	2629.74	62
779	Kanupur Irrigation Project (<i>Irrigation and CAD-TG</i>) (701404)	Odisha	01/2004	12/2019 12/2024	989.43 (2301.28)	2563.56	79
780	Relining of Rajasthan feeder and Sirhind Feeder canal (<i>Department of Water Resources-PB</i>) (701410)	Punjab	04/2018	06/2021 06/2025	1441.26 (2462.16)	2962.99	80
781	Shahpur Kandi Dam Project (<i>Department of Water Resources-PB</i>) (701411)	Punjab	04/2018	06/2022 10/2025	2285.81 (2715.7)	2072.33	80
782	J. ChokhaRao LIS CADWM Project (<i>Irrigation and CAD-TG</i>) (400094)	Telangana	04/2016	12/2019 03/2023	759.94 (13445.4)	0	0
783	Sri Ram Sagar Project Stage - II (<i>Irrigation and CAD-TG</i>) (400102)	Telangana	04/2005	12/2019 12/2024	736.13 (949.87)	940.7	96
784	Indiramma Flood Flow Canal Project (<i>Irrigation and CAD-TG</i>) (400103)	Telangana	01/2006	12/2019 03/2025	1331.3 (5940.09)	4491.08	92
785	J. Chokka Rao Devadula Lift Irrigation Scheme (<i>Irrigation and CAD-TG</i>) (701405)	Telangana	04/2006	12/2019 12/2025	8200.71 (14730)	4558.89	87
786	Rajiv Bhima Lift Irrigation Scheme (<i>Irrigation and CAD-TG</i>) (701406)	Telangana	01/2008	12/2019 03/2026	1402 (2509.66)	1839.76	100
787	Saryu Nahar CADWM Project (<i>Irrigation & Water Resources-UP</i>) (400093)	Uttar Pradesh	04/2017	12/2019 03/2026	1672.7 (1672.7)	0	0
788	Arjun Sahayak Project (<i>Irrigation & Water Resources-UP</i>) (400117)	Uttar Pradesh	04/2009	12/2019 12/2019	741.38 (2465.68)	3218.3	100

All Ongoing Projects							JULY 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
789	Morna [Gureghar] Irrigation Project (Department of Water Resources, River Development & GR) (701395)	Uttar Pradesh	12/2007	06/2023 (-)	219.9 (219.9)	0	0
790	Madhya Ganga canal Phase-II (Irrigation & Water Resources-UP) (701408)	Uttar Pradesh	07/2007	12/2019 12/2024	1060.67 (4417.21)	4415.24	82
791	Jamrani Dam Multipurpose Project (Irrigation-UK) (613787)	Uttarakhand	04/2023	06/2029 (-)	2584.1 (2584.1)	486.52	16
	Total (45)				97037.25	143185.74	



सत्यमेव जयते

**Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.ipm.mospi.gov.in>**
