



INFRASTRUCTURE AND
PROJECT MONITORING DIVISION

MINISTRY OF STATISTICS AND PROGRAMME
IMPLEMENTATION



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation



479th Flash Report on Central Sector Infrastructure Projects



Scan the QR code to access the
PAIMANA Portal.

(Rs. 150 crore
& above)

SEPTEMBER 2025

www.mospi.gov.in [@GoIStats](#) [/GoIStats](#) [GoIStats](#) [Ministry of Statistics & PI](#)



CONTENTS

I. Overview*	2-4
II. North Eastern Region	5-6
III. As per Harmonized Master List (HML) 2022	7-13
IV. Major Infrastructure Central Ministries & Departments	14-19
V. Appendix : <i>List of Tables</i>	20 onwards
Table 1: Ministry-wise Ongoing Projects	
Table 2: State-wise Ongoing Projects	
Table 3: Completed Projects	
Table 4: Newly Added Projects	
Table 5: Ongoing Projects of North Eastern Region	
Table 6: All Ongoing Projects	

**Note: This report is web-generated from the PAIMANA portal (ipm.mospi.gov.in) as of September 2025, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies (excluding Ministry of Road Transport & Highways, may reflect from next month onwards) on the IPM portal (indiainvestmentgrid.gov.in) latest by 14th October 2025.*





Overview





Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above

SEPTEMBER 2025

793 | 14

Ongoing Projects |
Line Ministries & Departments

₹ 25,32,002

Original Cost
(crores)

₹ 30,62,204

Revised Cost
(crores)


₹ 15,85,492

(51.78% of Revised Cost)

Expenditure
(crores)


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

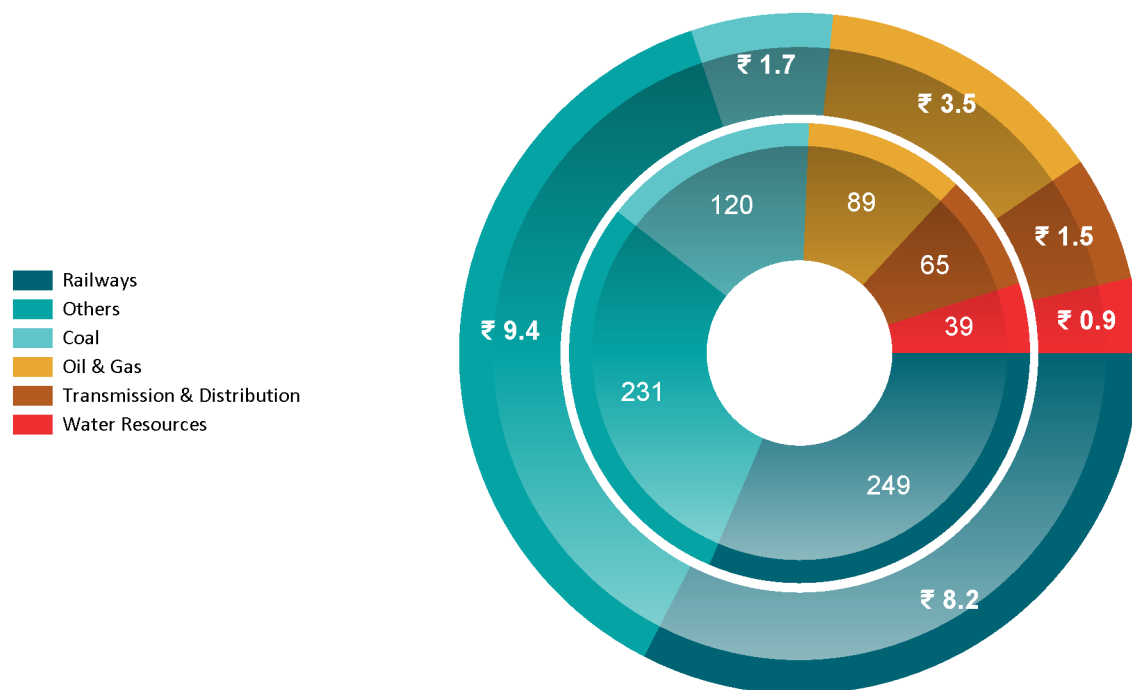


Ministry Comparison : Major Ministries*


[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

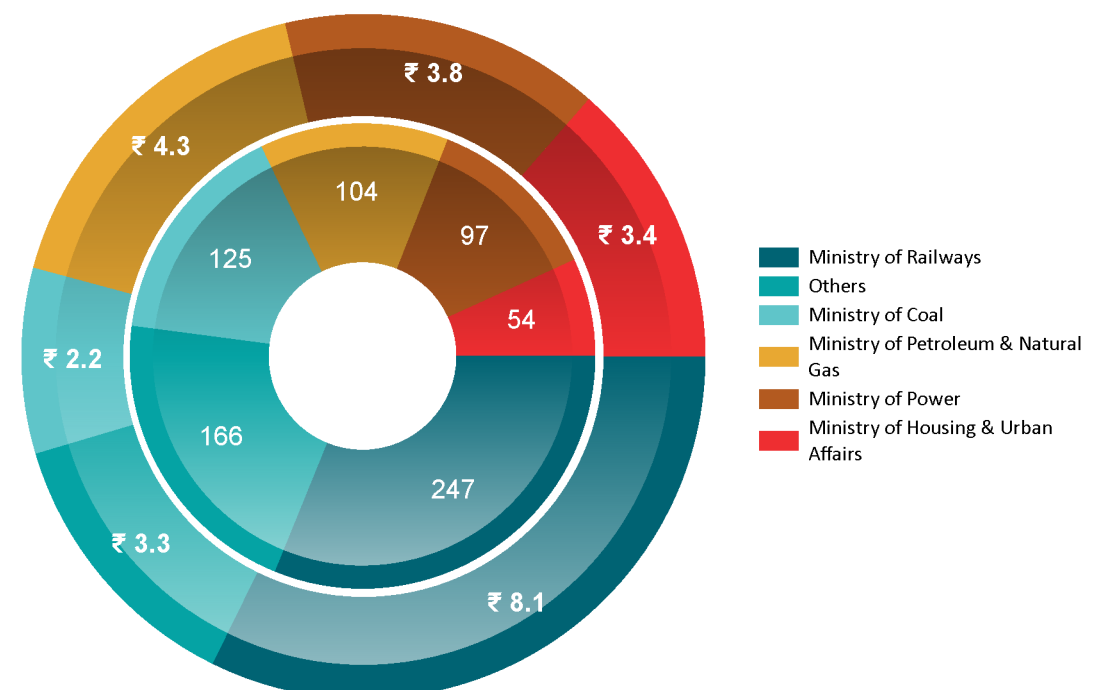

Cost Analytics : Major Sectors*

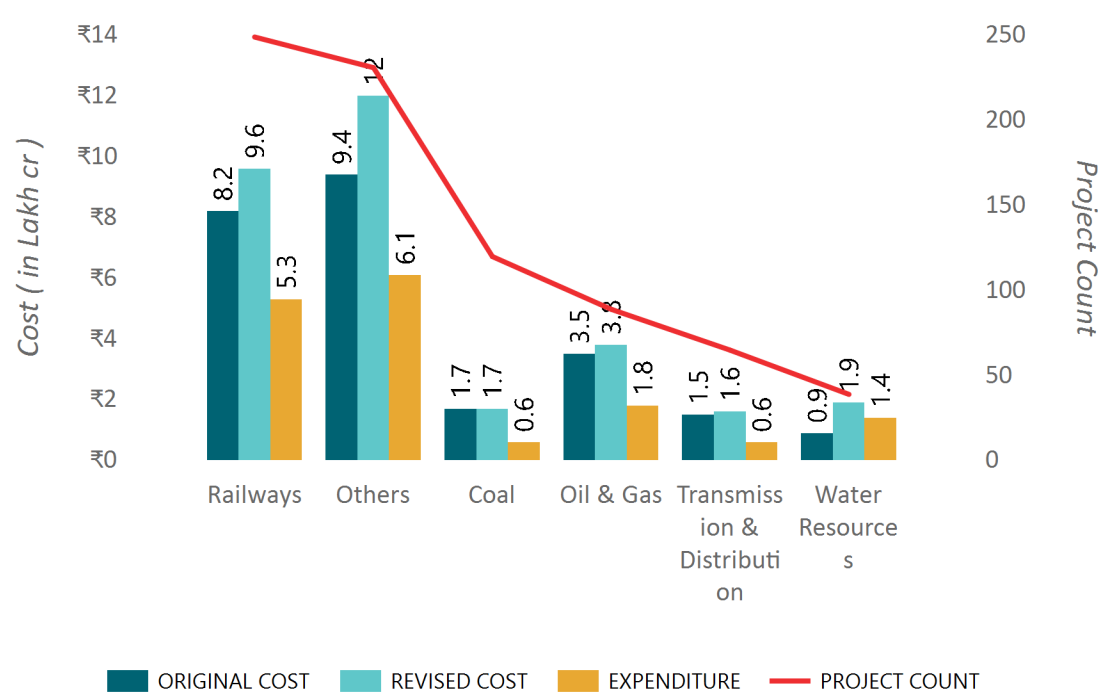


Cost Analytics : Major Ministries*

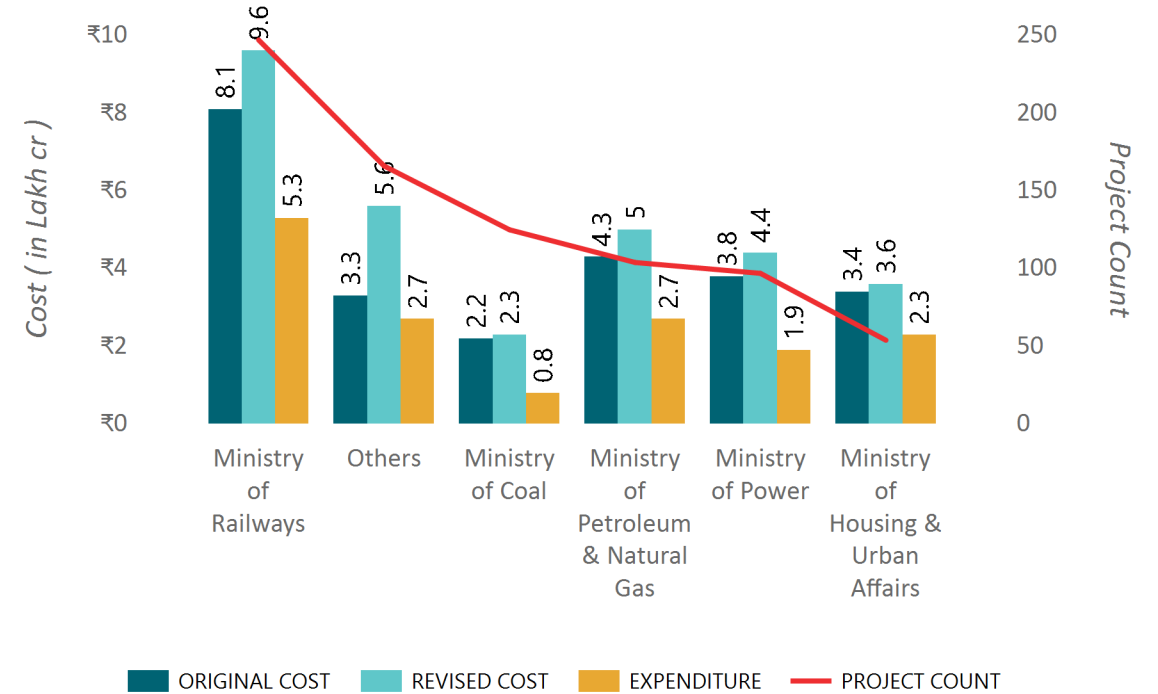


Note: * as per Project Count

Analytics: as per HML

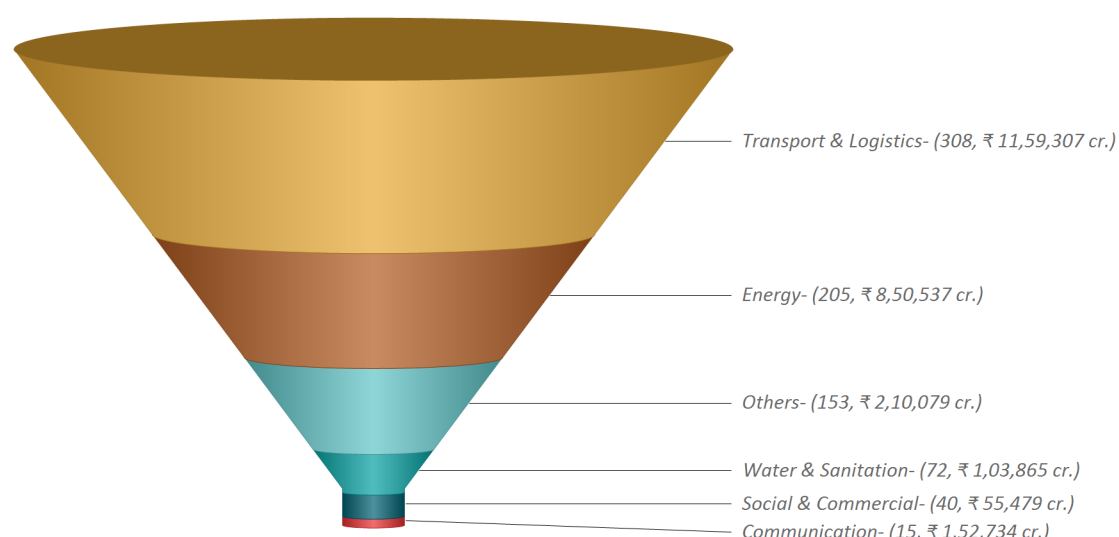


Note: all indicated legends are in format (Project count, Original Cost in crores)

Physical & Financial progress (%) : Project count

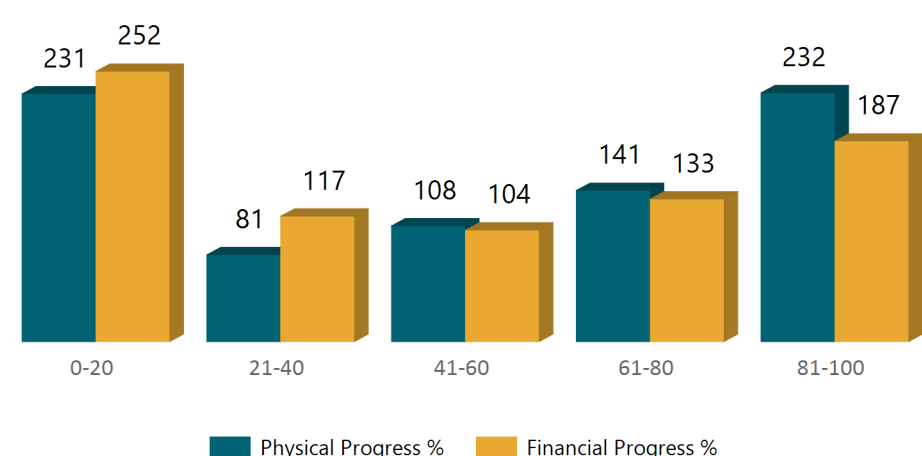




State Comparison : Major States*

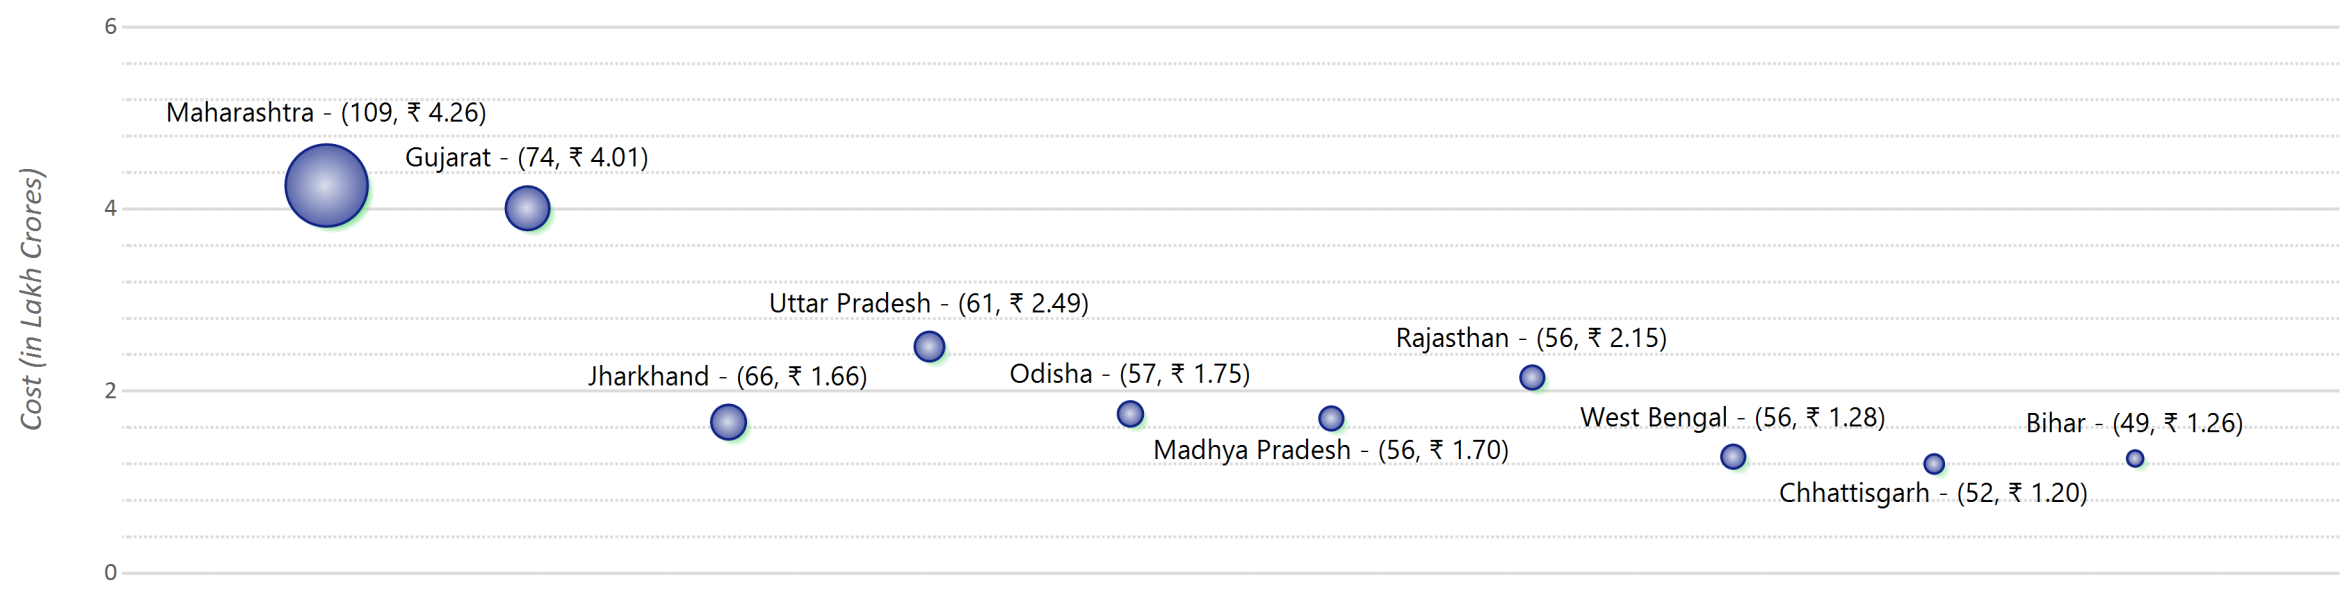


Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count


Ministry-wise Distribution of total 232 projects with reported Physical Progress between 81-100%

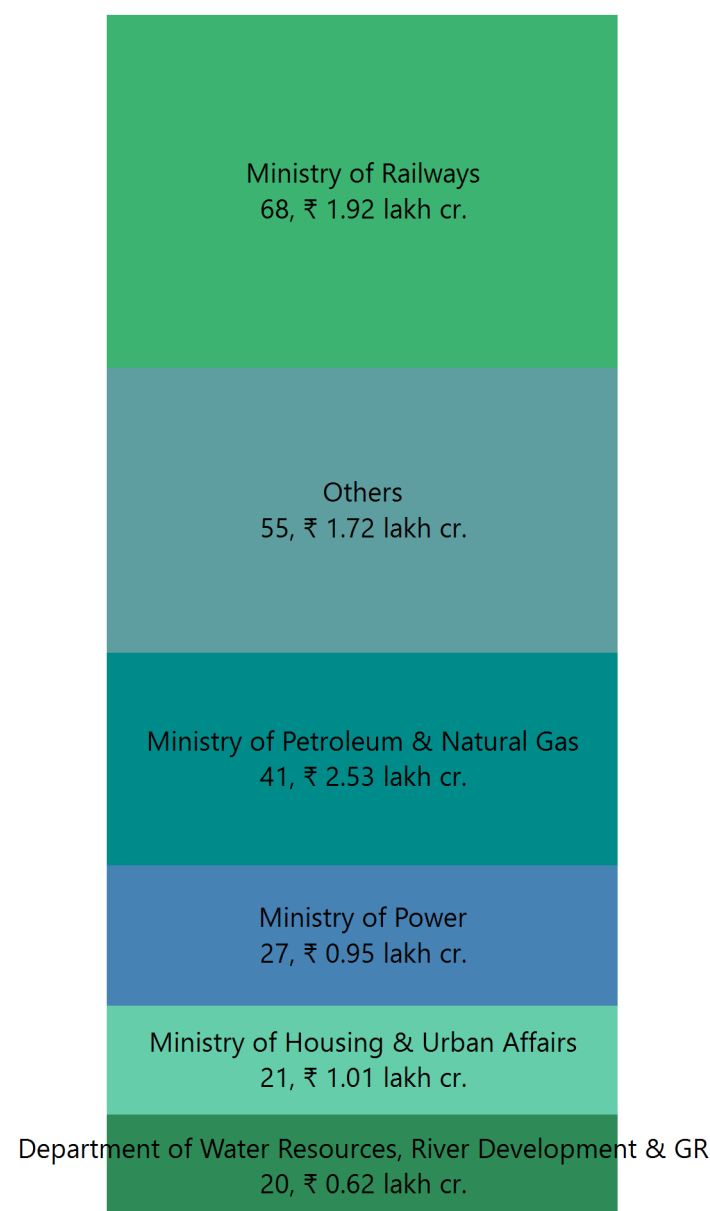

Total Ongoing Projects: Mega & Major

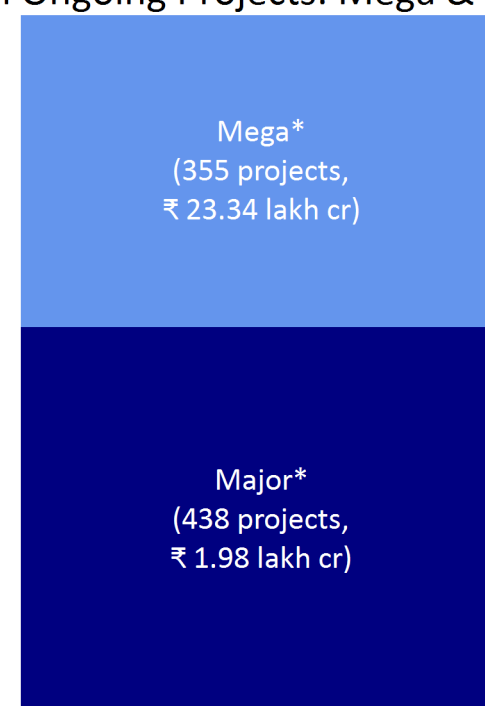


Total North East Region Ongoing Projects: Mega & Major




Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost ≥ 1000 crore
* Major project if having original cost < 1000 crore


Project volume (nos.)



Total Project value (in lakh crore)

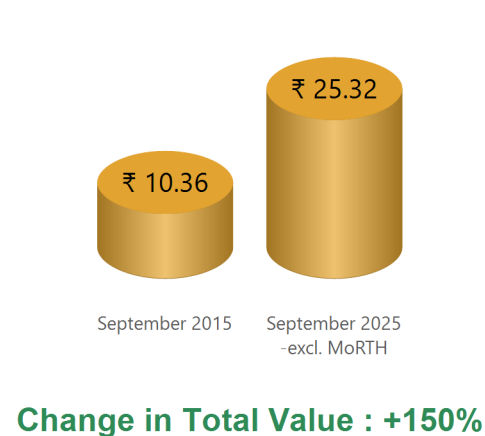

Cumulative Expenditure (in lakh crore)

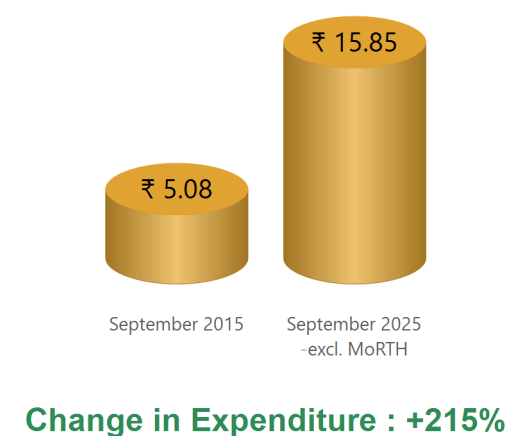



North Eastern Region





Special Focus : North Eastern Region

SEPTEMBER 2025

54 | 9

Ongoing Projects |
Line Ministries & Departments

₹ 1,86,759

Original Cost
(crores)

₹ 2,75,020

Revised Cost
(crores)


₹ 1,88,497

(68.54% of Revised Cost)


Expenditure
(crores)

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

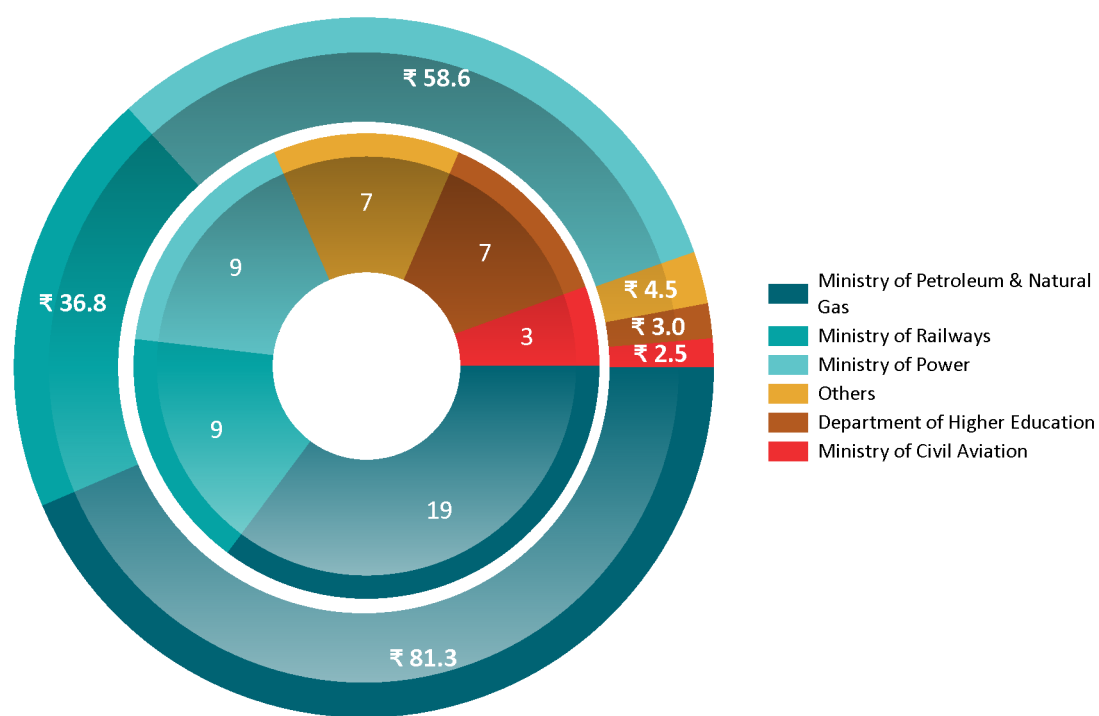


Cost Analytics : Major Ministries*

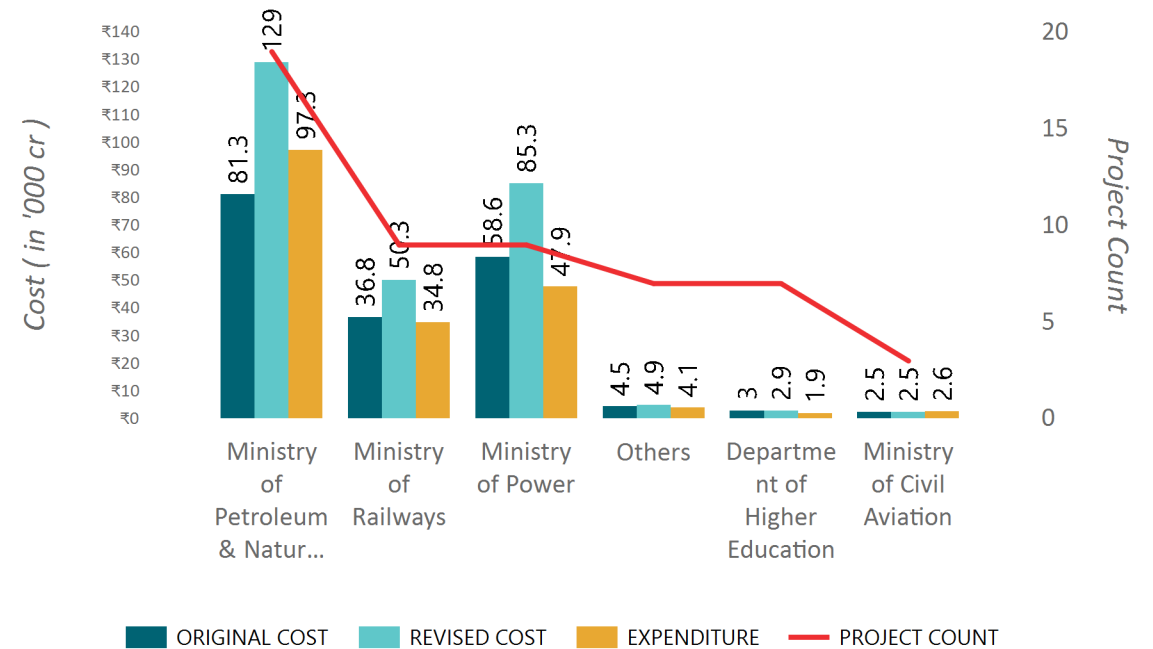


Note: * as per Project Count

Analytics: as per HML

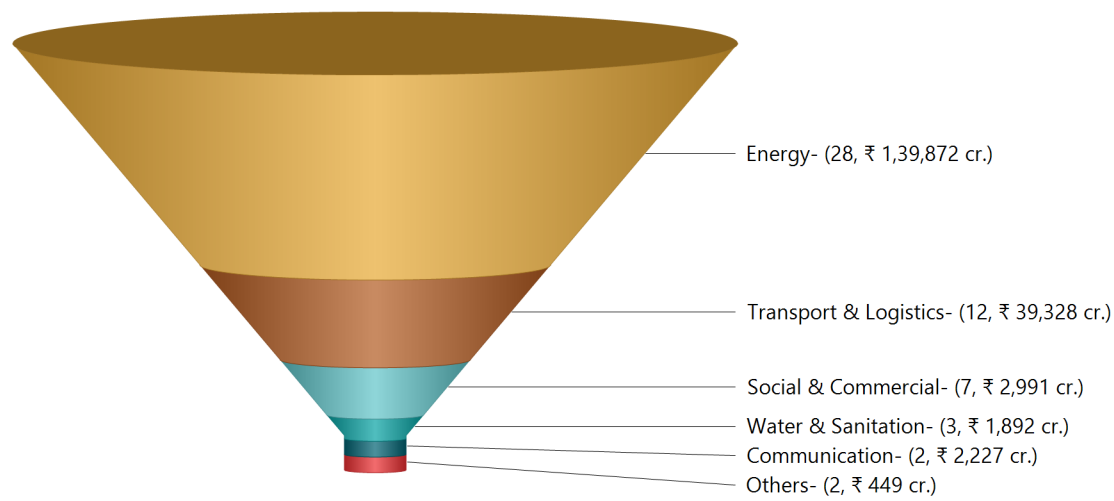


Physical & Financial progress (%) : Project count

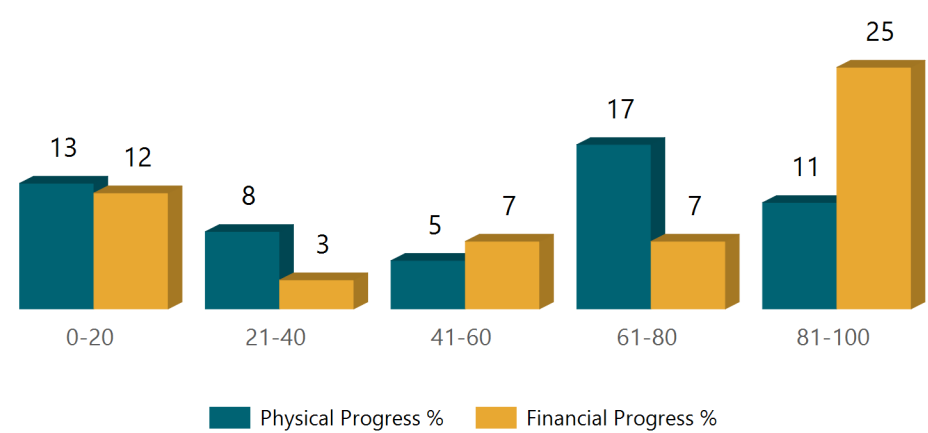

Note: all indicated legends are in format (Project count, Original Cost in crores)

State Comparison : All States

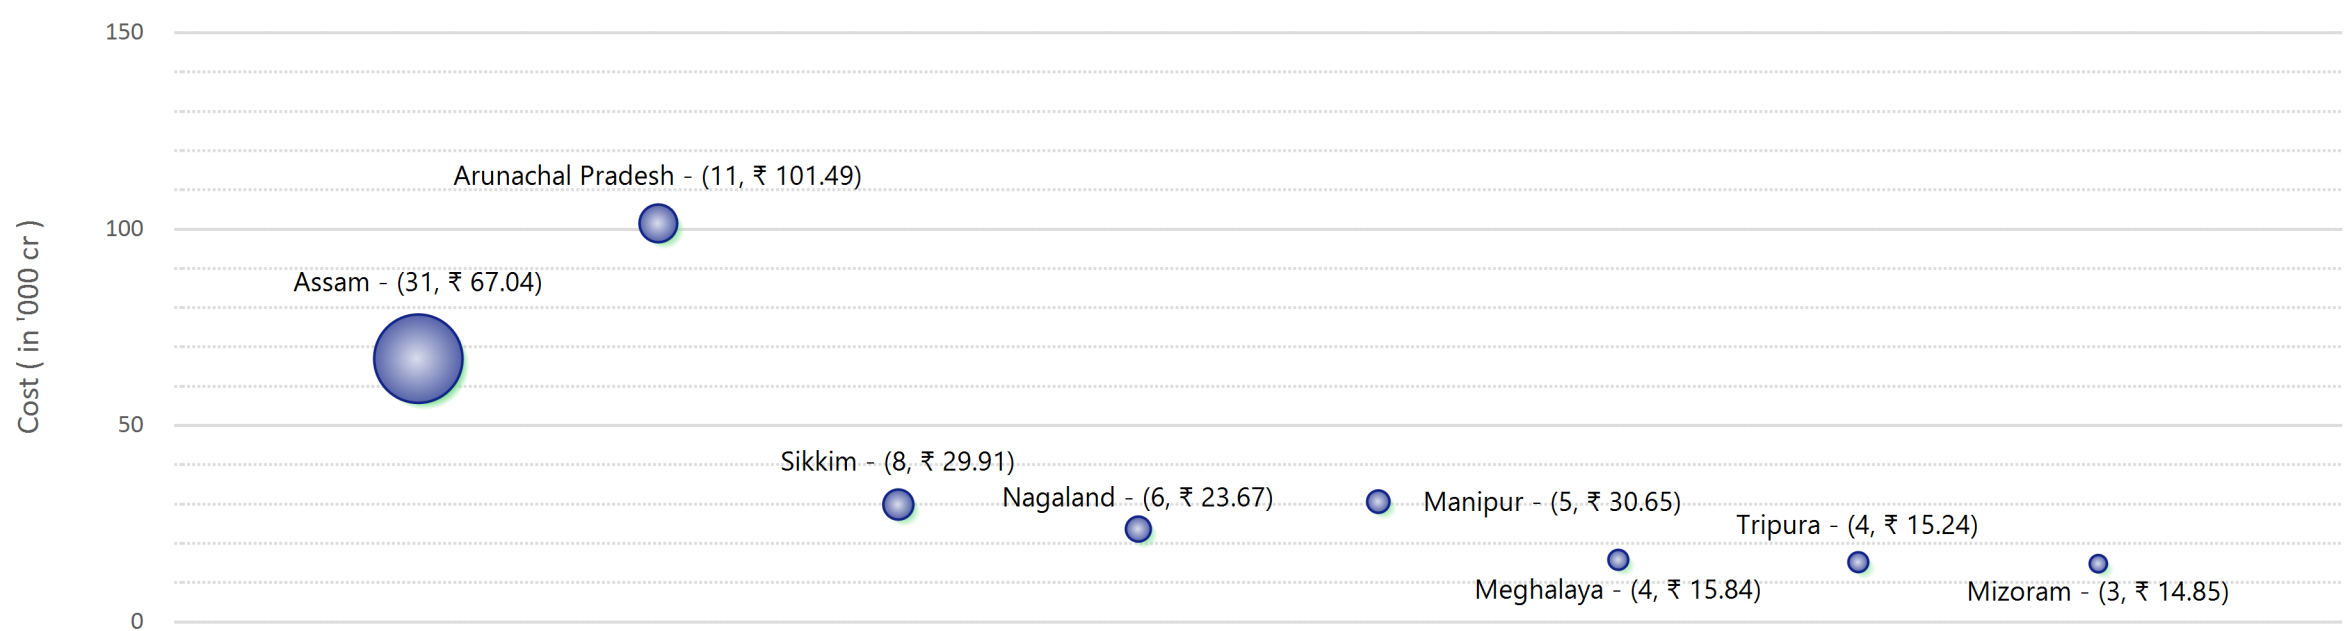

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022



HML Category 1 : Transport & Logistics



SEPTEMBER 2025

308
Ongoing Projects

₹ 11,59,307
Original Cost
(crores)

₹ 13,29,245
Revised Cost
(crores)

₹ 7,65,328
(57.58% of Revised Cost)
Expenditure
(crores)

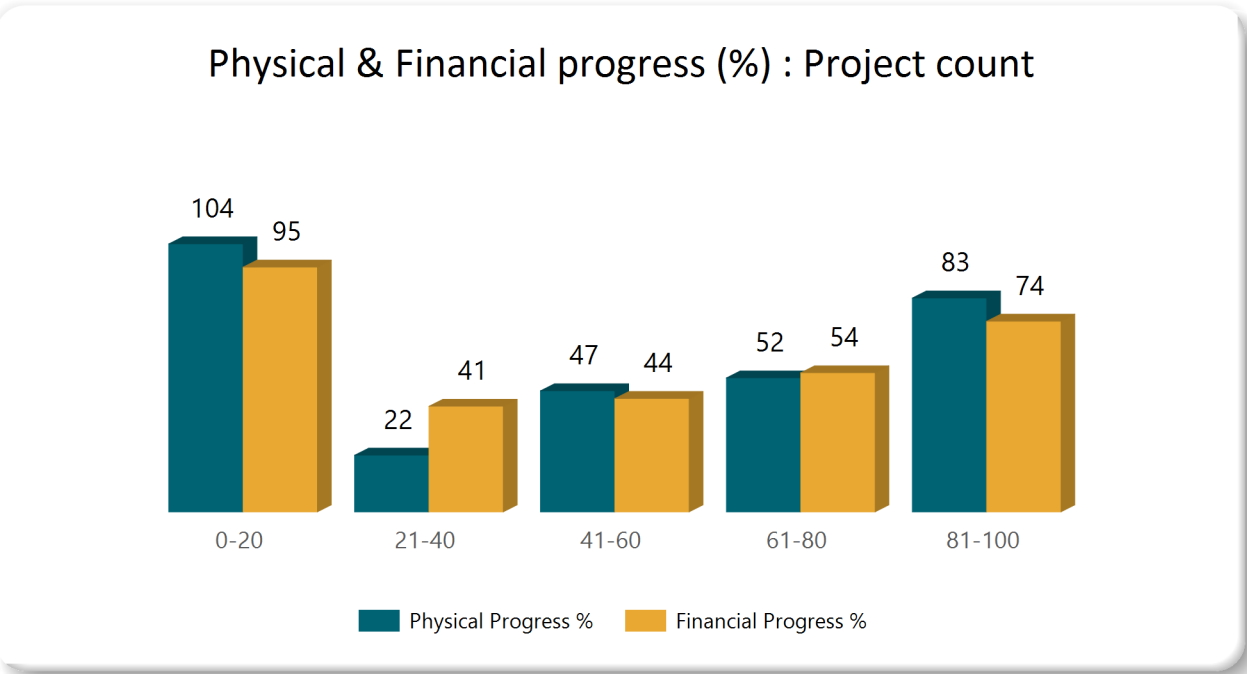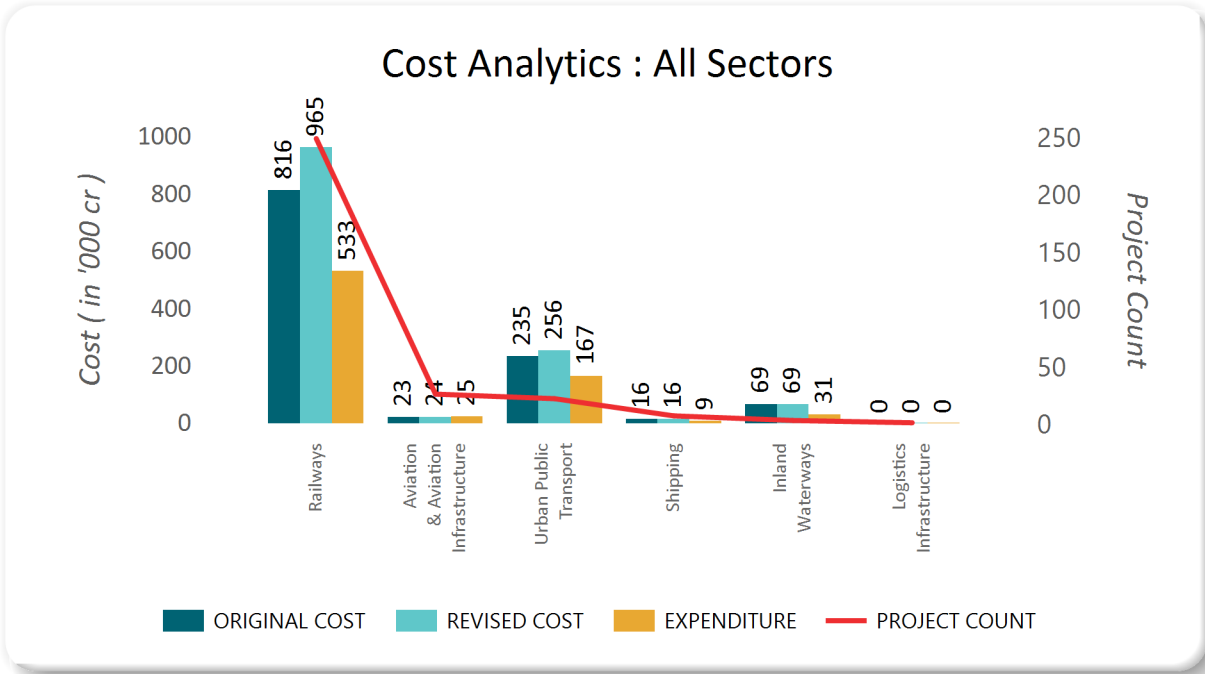

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Railways	249	815,578	964,721	532,944
2	Aviation & Aviation Infrastructure	26	23,050	23,511	24,583
3	Urban Public Transport	22	235,217	255,798	167,263
4	Shipping	7	16,499	16,499	9,272
5	Inland Waterways	3	68,792	68,504	31,128
6	Logistics Infrastructure	1	171	212	138

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	617321	GODHANI-KALUMNA CHORD 13.7 KM	150,000		1,940	11
2	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	81,243	54
3	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		27,456	46
4	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
5	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65



HML Category 2 : Energy

SEPTEMBER 2025

205

Ongoing Projects

₹ 8,50,537

Original Cost
(crores)


₹ 9,84,505

Revised Cost
(crores)


₹ 4,91,974

(49.97% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

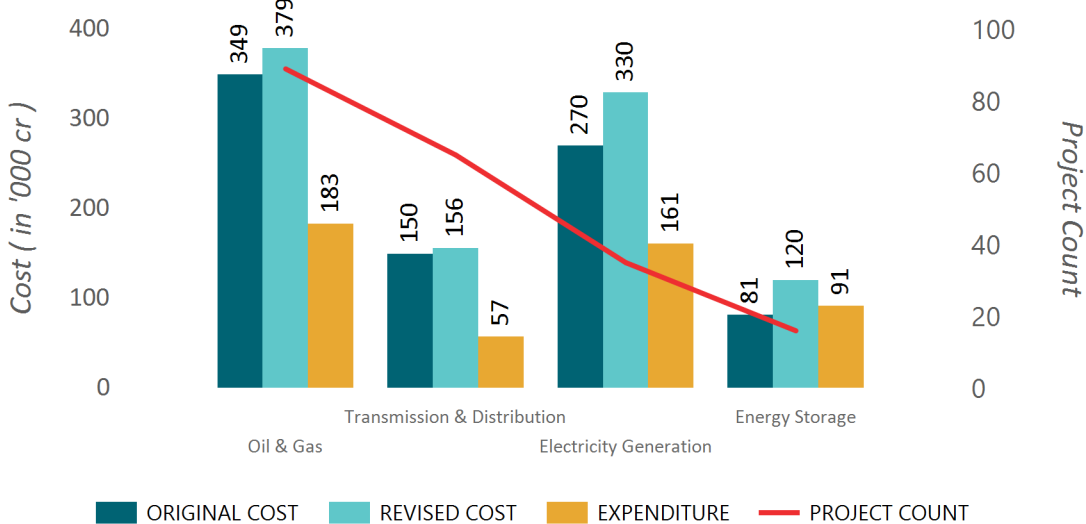

Physical & Financial progress (%) : Project count

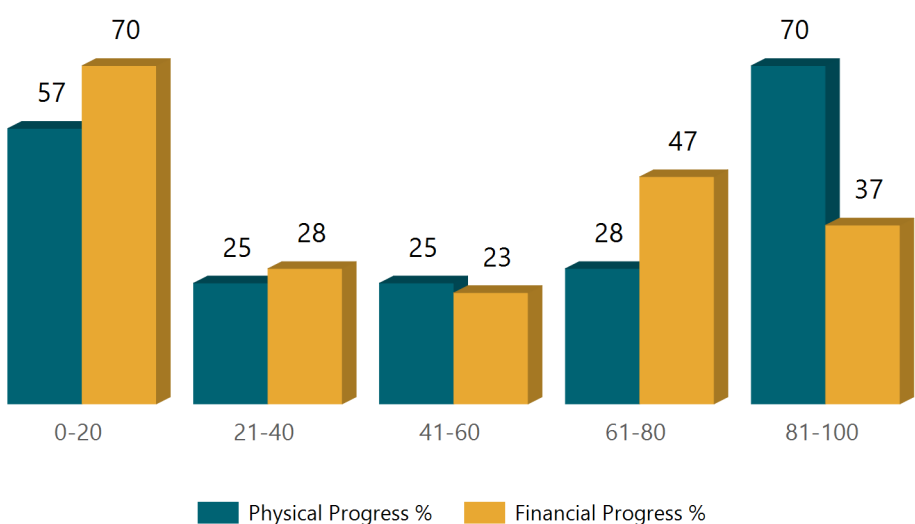

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	89	349,436	378,613	182,909
2	Transmission & Distribution	65	149,516	156,031	57,067
3	Electricity Generation	35	270,284	329,637	160,640
4	Energy Storage	16	81,301	120,224	91,359

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,914	15
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	60,545	88
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA	34,627	36,225	25,029	89
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,239	96
5	602182	DIBANG MULTIPURPOSE PROJECT	31,876		3,639	16



HML Category 3 : Water & Sanitation

SEPTEMBER 2025

72

Ongoing Projects

₹ 1,03,865

Original Cost
(crores)


₹ 2,03,719

Revised Cost
(crores)


₹ 1,72,148

(84.5% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

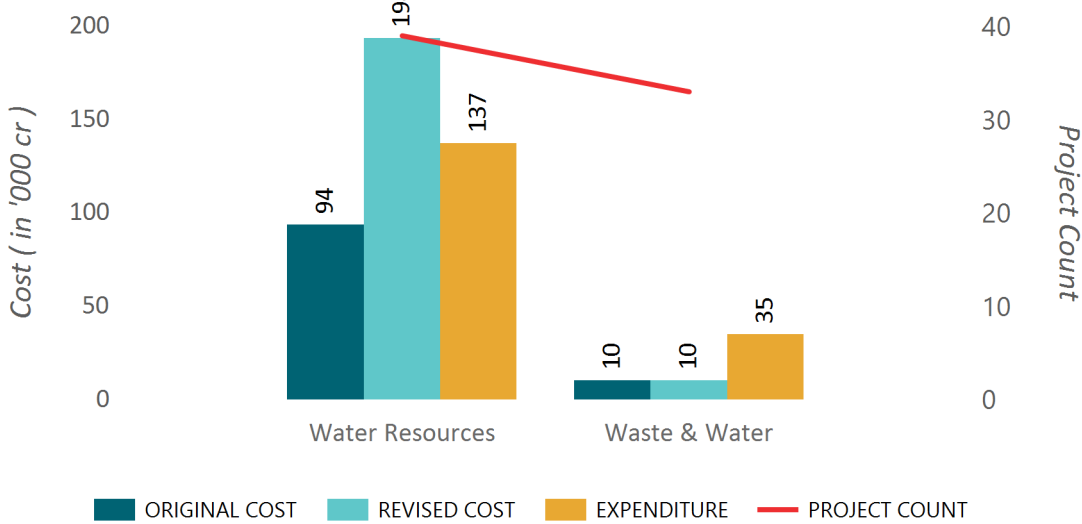

Physical & Financial progress (%) : Project count

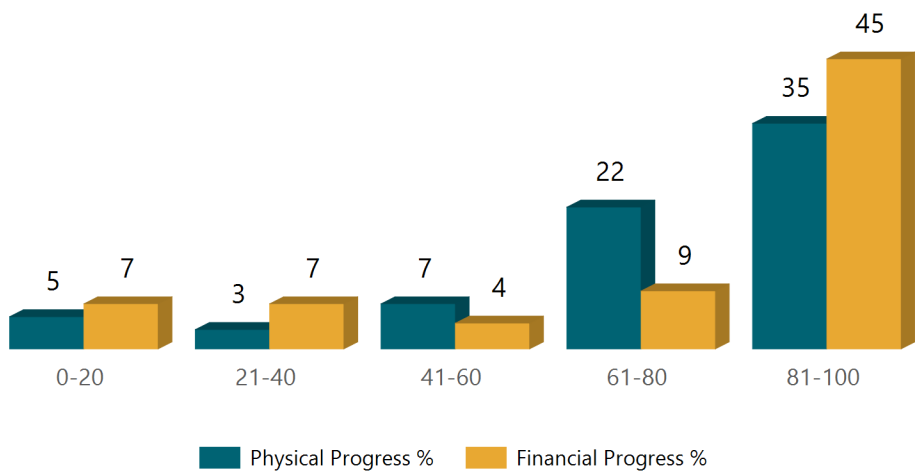

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	39	93,740	193,594	137,306
2	Waste & Water	33	10,125	10,125	34,842

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,861	93
2	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	24,746	84
3	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,559	87
4	400112	JIGAON IRRIGATION PROJECT	7,223		8,723	90
5	701386	GOSIKHURD PROJECT	7,196	12,770	13,691	72

HML Category 4 : Communication



SEPTEMBER 2025

15
Ongoing Projects

₹ 1,52,734
Original Cost
(crores)

₹ 2,74,827
Revised Cost
(crores)

₹ 72,373
(26.33% of Revised Cost)
Expenditure
(crores)

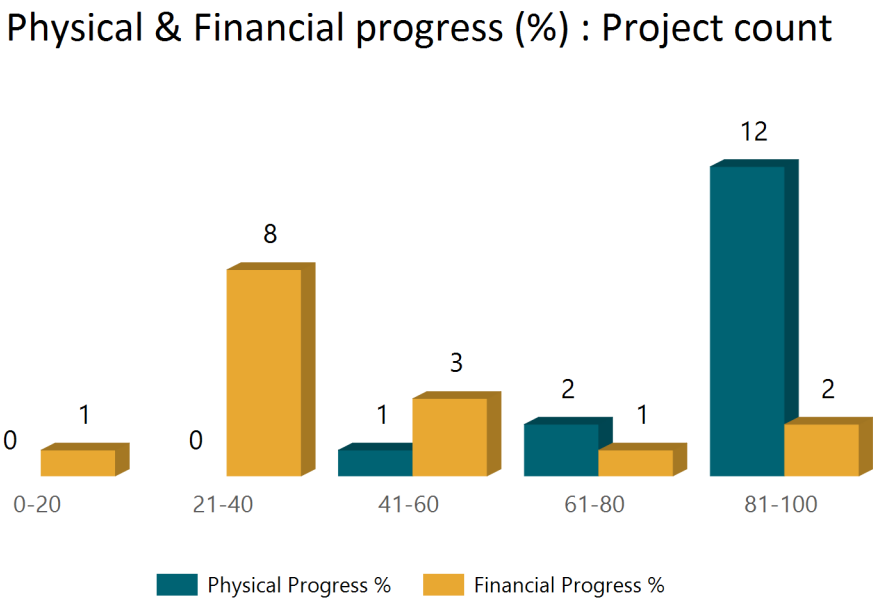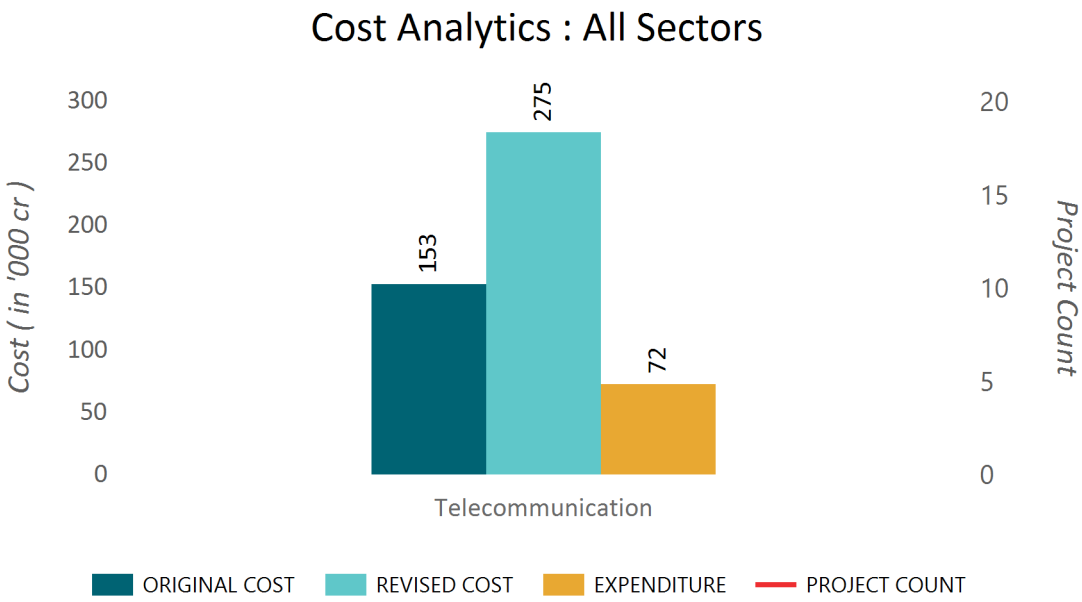

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	15	152,734	274,827	72,373

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	706775	BHARATNET	61,109	188,000	41,486	81
2	701593	4G SERVICES BY BSNL	28,466	19,592	8,419	96
3	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	30,620	9,792	75
4	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		8,420	96
5	701602	PROVISION OF 4G BASED MOBILE SERVICES IN 7,287 UNCOVERED VILLAGES OF 44 ASPIRATIONAL DISTRICT ACROSS 5 STATES OF ANDHRA PRADESH, CHHATTISGARH, JHARKHAND, MAHARASHTRA & ODISHA	3,685		1,135	80

HML Category 5 : Social & Commercial

SEPTEMBER 2025

40

Ongoing Projects

₹ 55,479



Original Cost
(crores)

₹ 56,416

Revised Cost
(crores)

₹ 11,829

(20.97% of Revised Cost)
Expenditure
(crores)

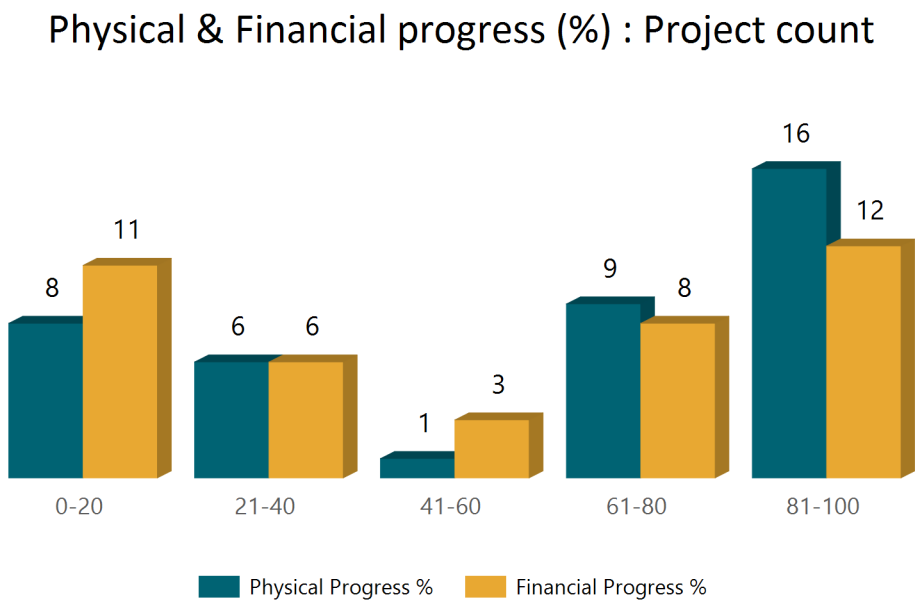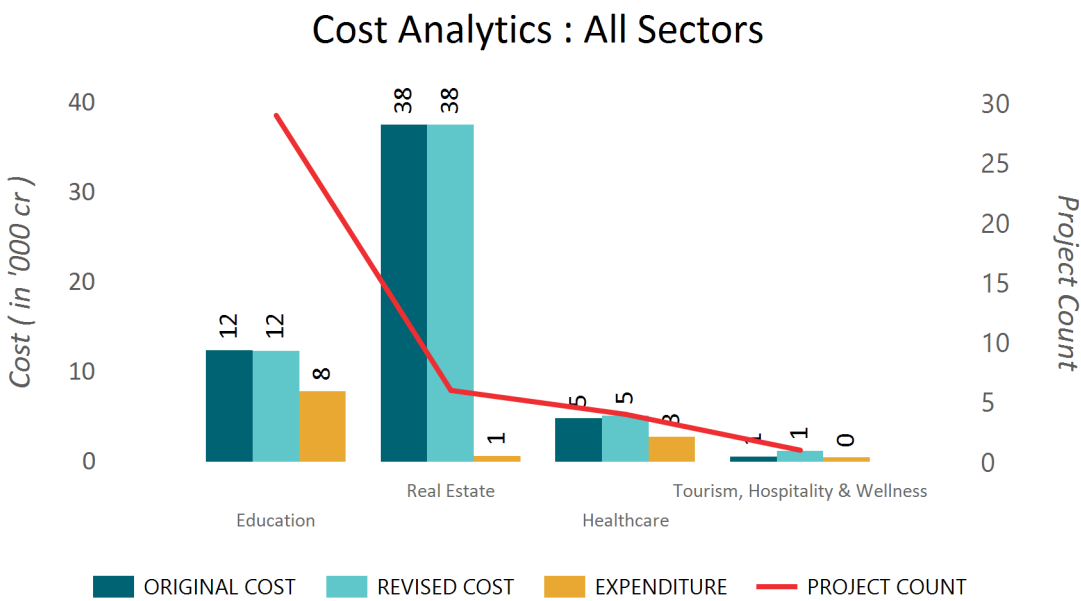

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Education	29	12,467	12,401	7,891
2	Real Estate	6	37,591	37,591	646
3	Healthcare	4	4,848	5,186	2,795
4	Tourism, Hospitality & Wellness	1	573	1,238	497

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850		0	0
2	701658	KRISHNAPATNAM NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	2,139		471	21
3	701167	AIIMS KASHMIR AT AWANTIPORA JAMMU & KASHMIR	1,828	1,828	1,565	67
4	701657	TUMAKURU NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	1,702		117	9
5	701173	AIIMS MAJRA REWARI HARYANA	1,299		349	28



Other Sectors

SEPTEMBER 2025

153

Ongoing Projects

₹ 2,10,079

Original Cost
(crores)


₹ 2,13,492

Revised Cost
(crores)

₹ 71,840

(33.65% of Revised Cost)
Expenditure
(crores)

Physical & Financial progress (%) : Project count

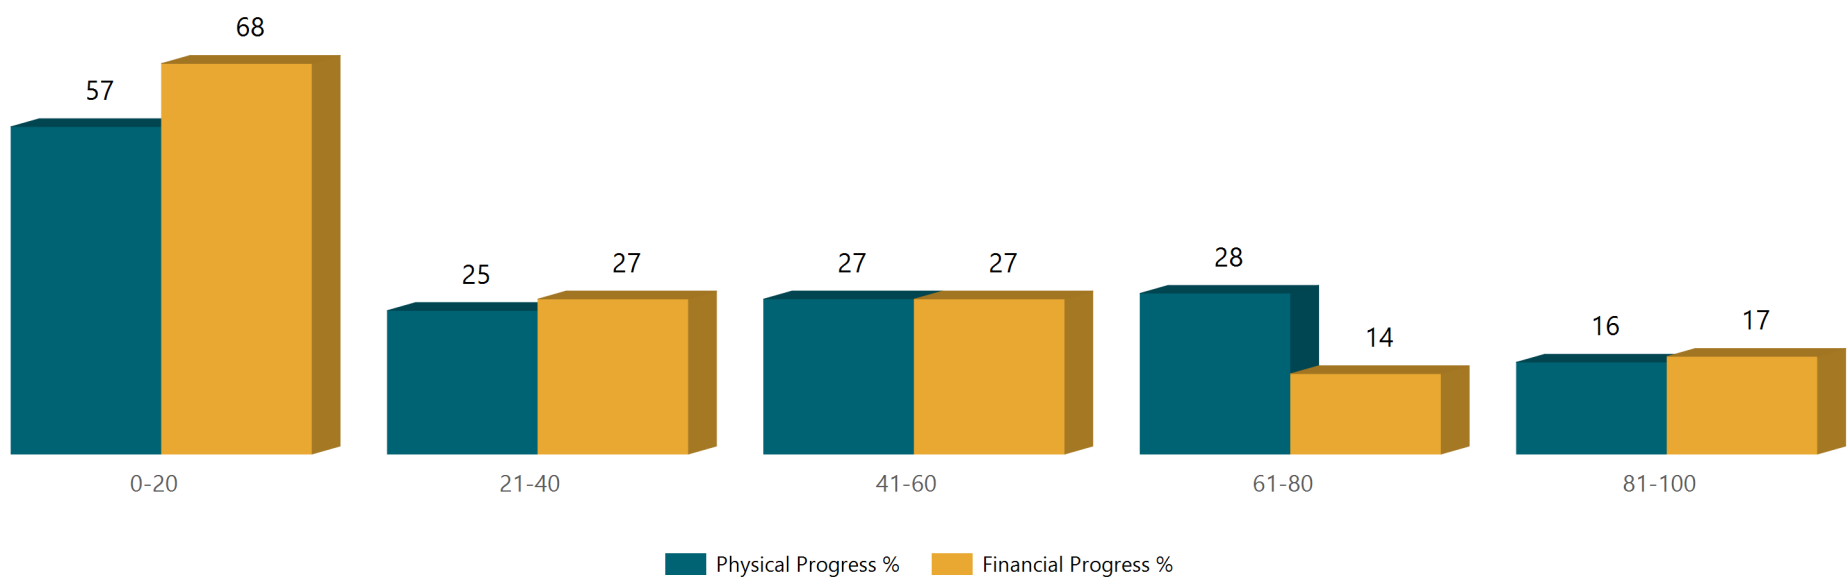

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	120	174,830	172,568	56,469
2	Steel	20	19,267	22,505	8,278
3	Metals & Mining	10	14,436	16,873	6,383
4	Construction	3	1,546	1,546	711

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400424	GEVRA OC [70 MTY]	11,816		6,677	78
2	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,730	17
3	400147	KUSMUNDA OC EXPANSION [15 TO 50 MTY]	7,612		4,698	81
4	612838	DIPKA OC	7,580		3,091	65
5	400150	RPR MAGADH EXP OCP	7,254		1,548	38



Major Infrastructure Central Ministries & Departments



Ministry of Railways

SEPTEMBER 2025

247
Ongoing Projects

₹ 8,12,092
Original Cost
(crores)


₹ 9,60,470
Revised Cost
(crores)

₹ 5,31,131
(55.3% of Revised Cost)
Expenditure
(crores)

120 | ₹ 752,247
Mega Projects
Count | Original Cost (crores)

127 | ₹ 59,845
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

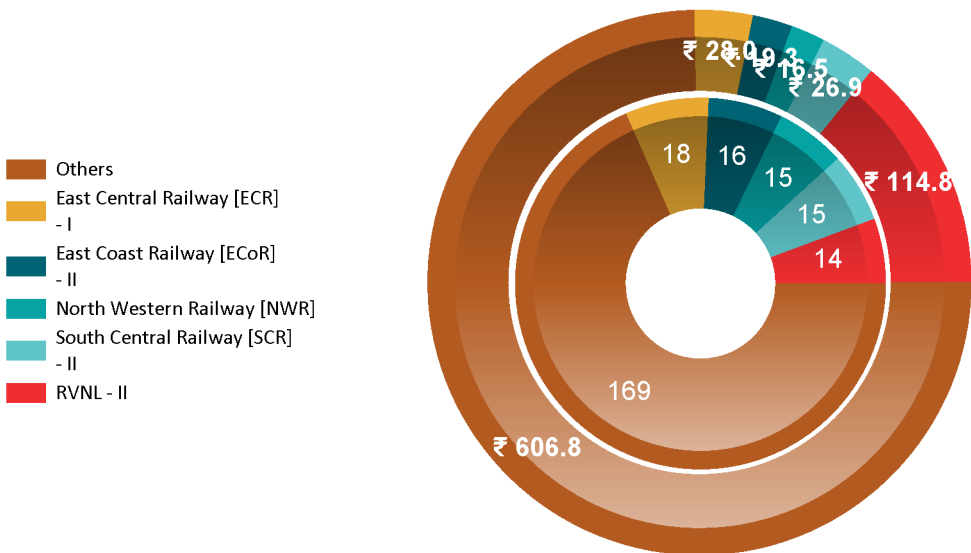


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Physical & Financial progress (%) : Project count

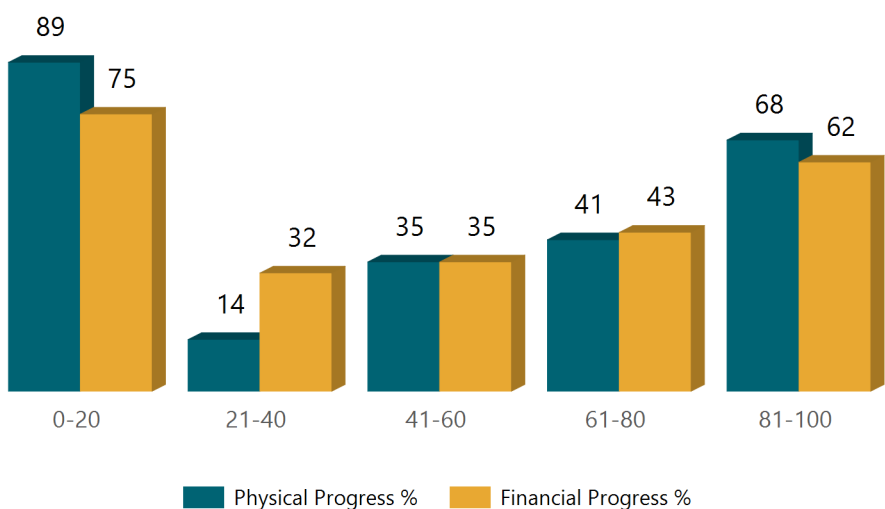

Cost Analytics : Major Sectors*

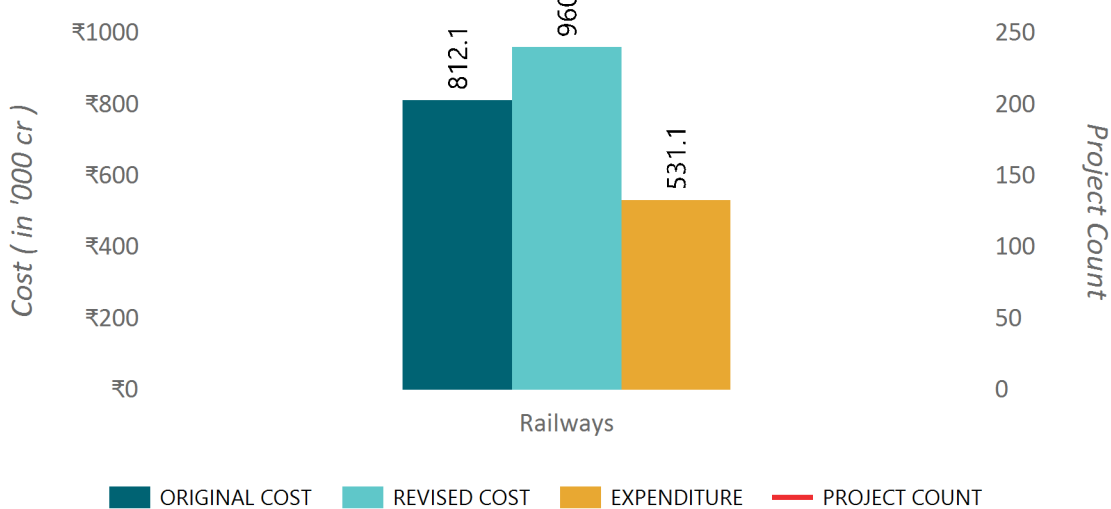

State Comparison : Major States*

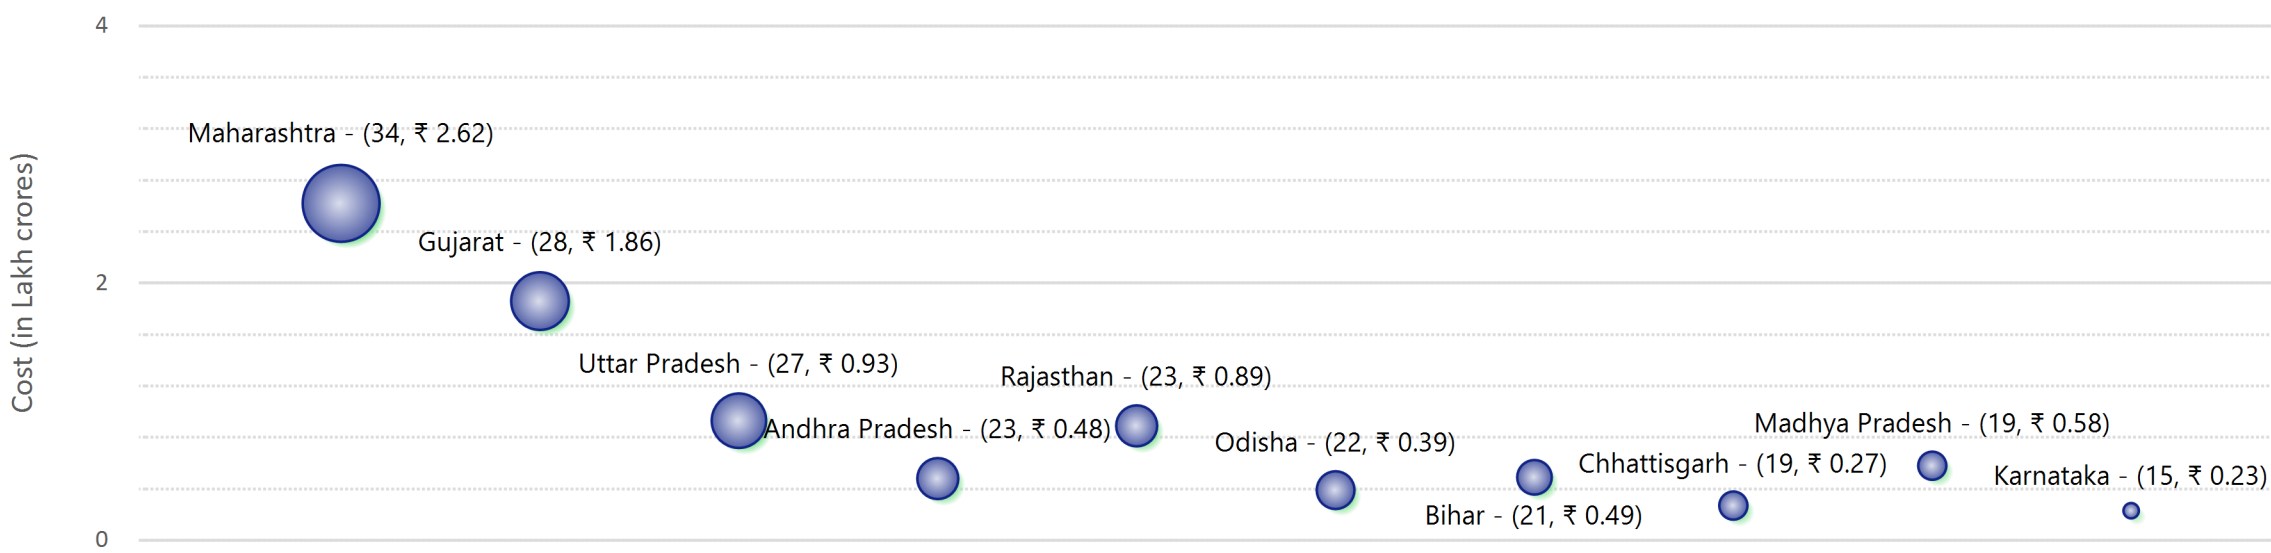

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	617321	GODHANI-KALUMNA CHORD 13.7 KM	150,000	150,000	1,940	11
2	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	81,243	54
3	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
4	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
5	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,361	16

Ministry of Coal

SEPTEMBER 2025

125
Ongoing Projects

₹ 2,23,099
Original Cost
(crores)


₹ 2,25,863
Revised Cost
(crores)

₹ 81,901
(36.26% of Revised Cost)
Expenditure
(crores)


40 | ₹ 181,342
Mega Projects
Count | Original Cost (crores)

85 | ₹ 41,757
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

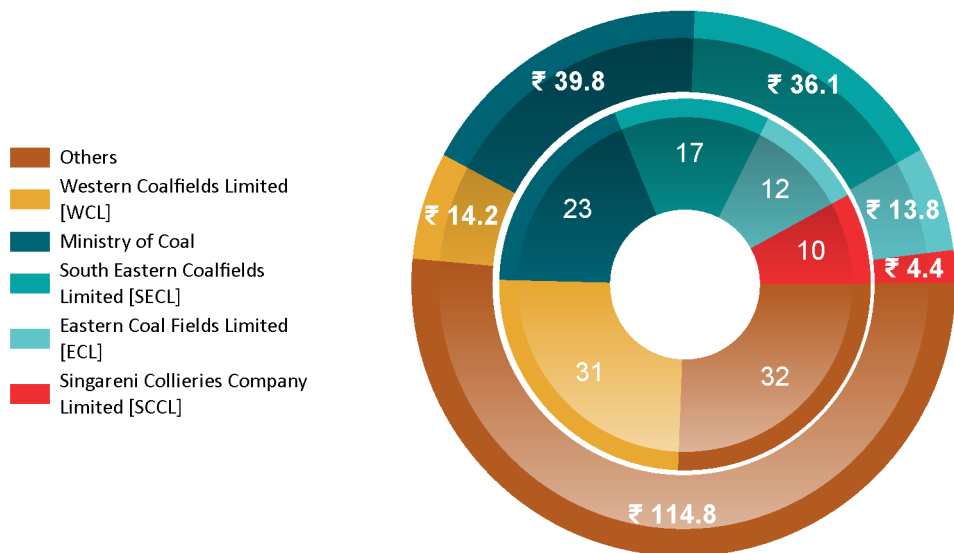


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

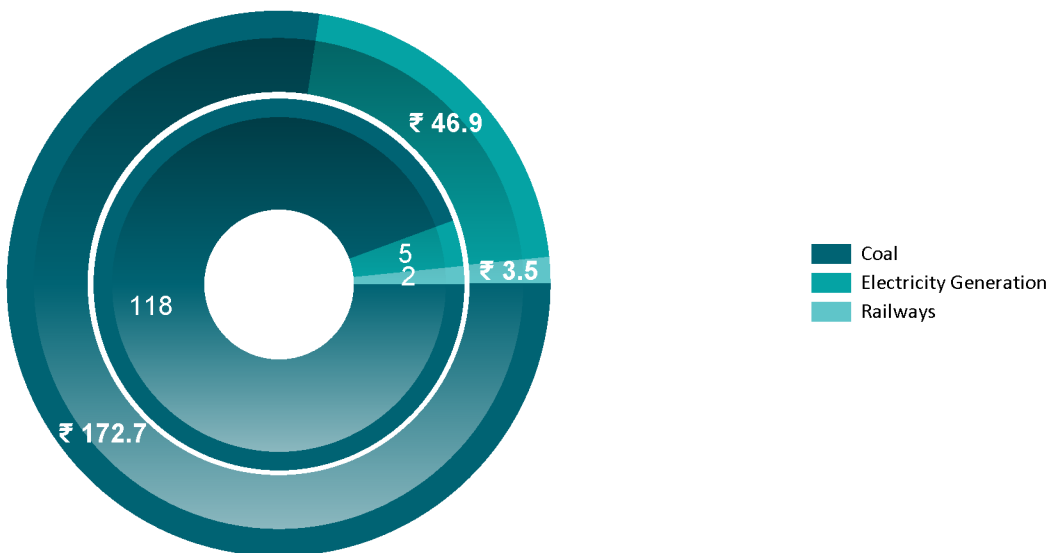


Physical & Financial progress (%) : Project count

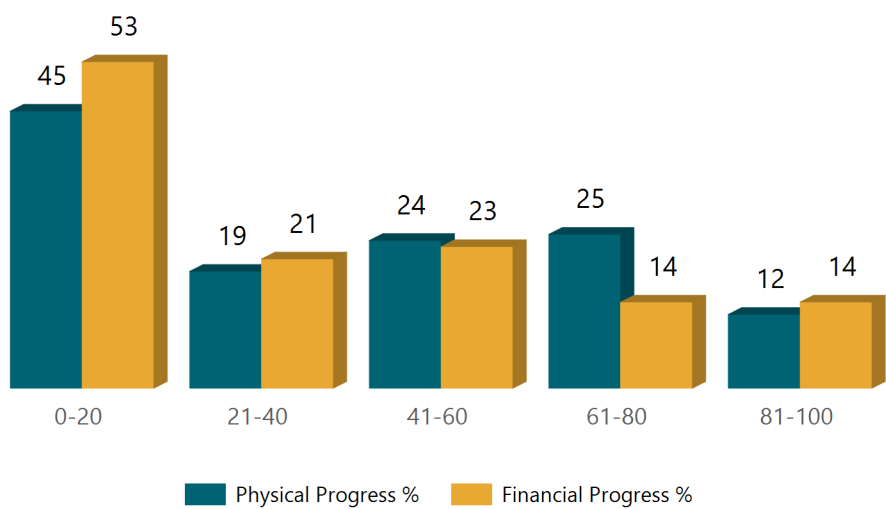

Cost Analytics : Major Sectors*

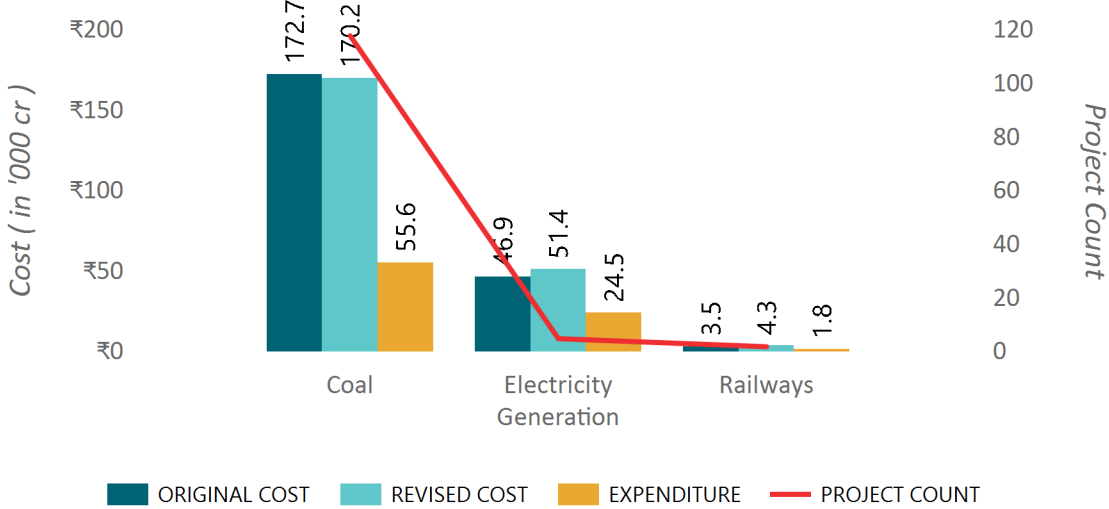

State Comparison : Major States*

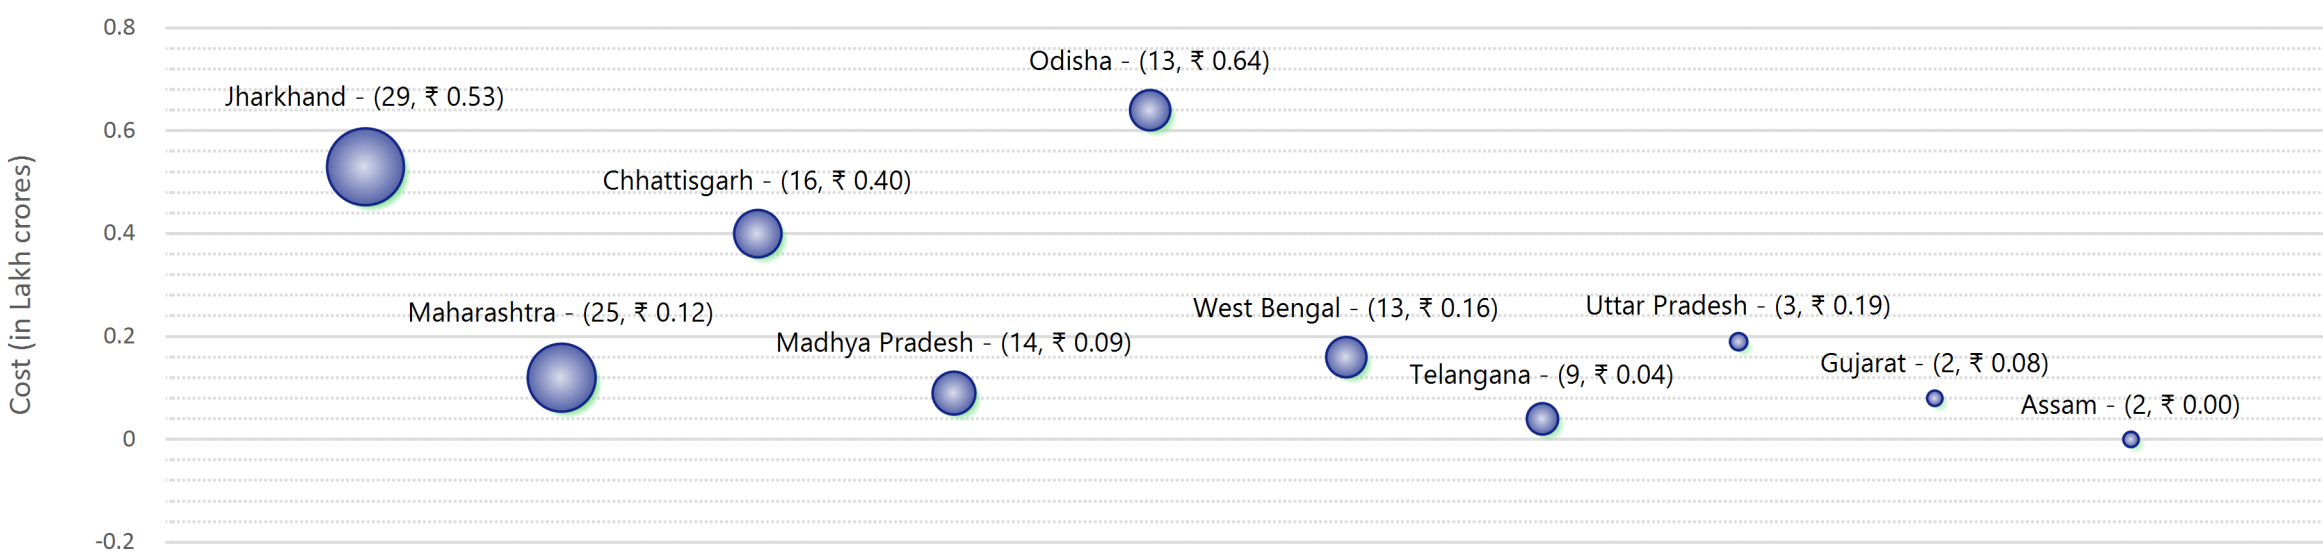

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	2,517	1
2	400259	GHATAMPUR THERMAL POWER PLANT 3 X 660 MW	17,238	21,781	20,510	92
3	400424	GEVRA OC [70 MTY]	11,816	11,816	6,677	78
4	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,730	17
5	400147	KUSMUNDA OC EXPANSION [15 TO 50 MTY]	7,612	7,612	4,698	81



Ministry of Petroleum & Natural Gas

SEPTEMBER 2025

104

Ongoing Projects

₹ 4,30,637

Original Cost
(crores)

₹ 4,98,611

Revised Cost
(crores)

₹ 2,74,101

(54.97% of Revised Cost)

Expenditure
(crores)

48 | ₹ 405,555


Mega Projects
Count | Original Cost (crores)

56 | ₹ 25,082

Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

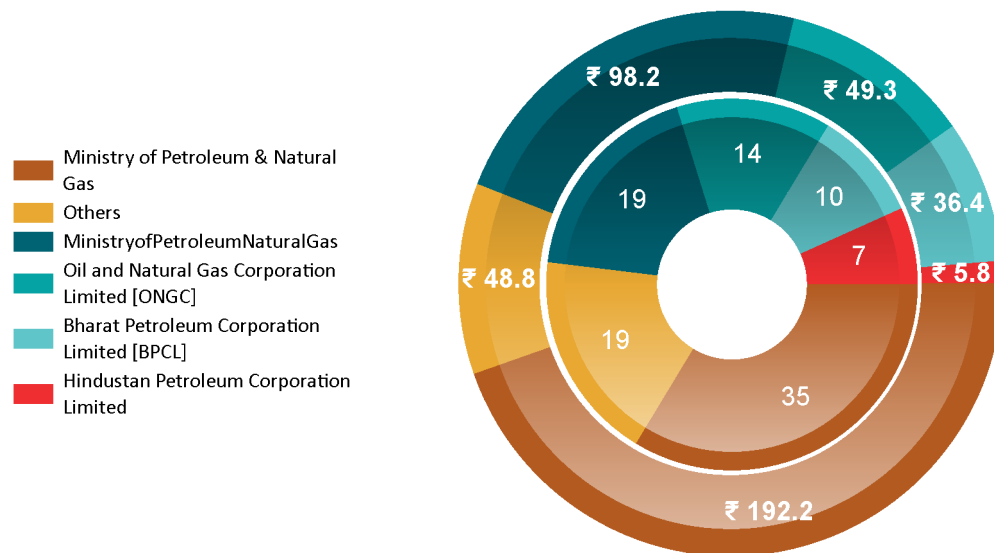


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

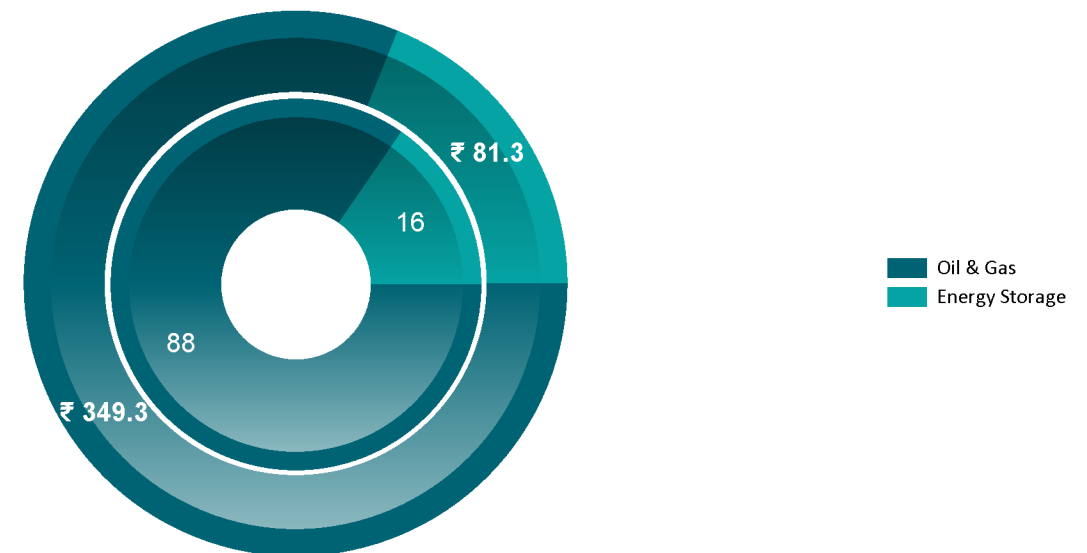


Physical & Financial progress (%) : Project count

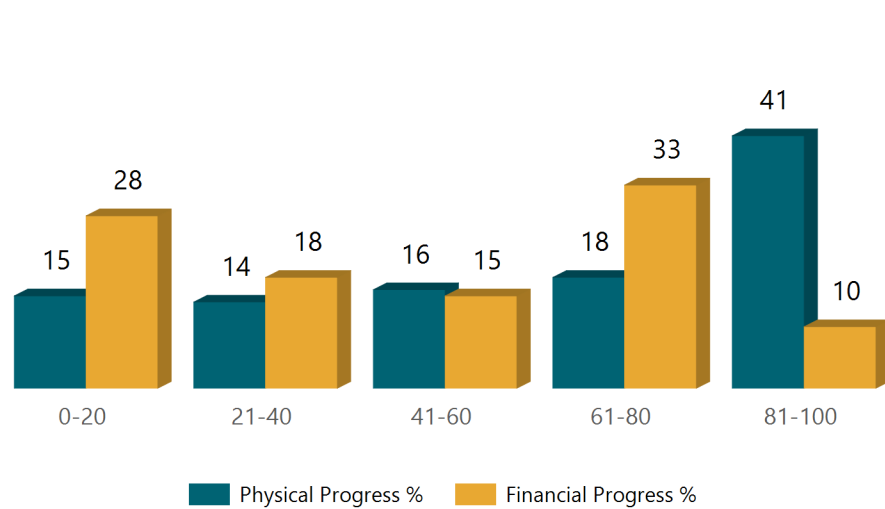

Cost Analytics : Major Sectors*

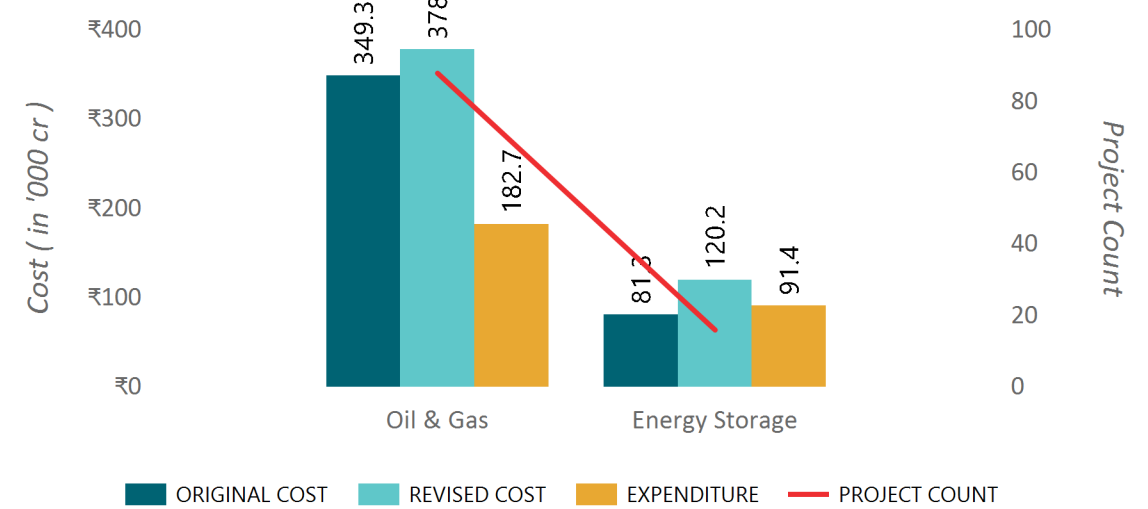

State Comparison : Major States*

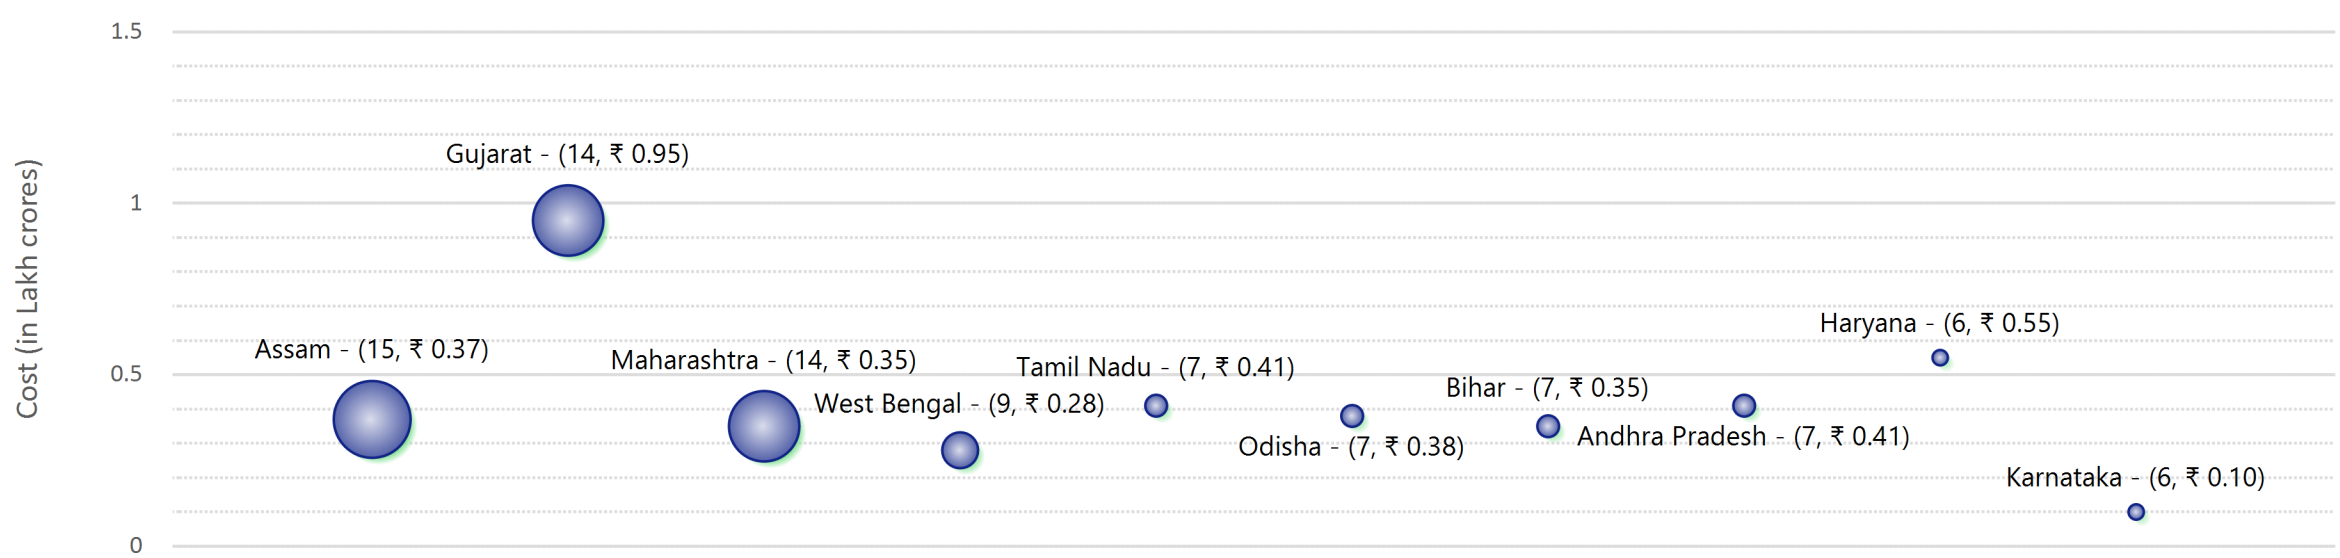

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,914	15
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	60,545	88
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	25,029	89
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,239	96
5	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,342	10



Ministry of Power

SEPTEMBER 2025

97

Ongoing Projects

₹ 3,75,018

Original Cost
(crores)

₹ 4,36,624

Revised Cost
(crores)

₹ 1,94,087

(44.45% of Revised Cost)
Expenditure
(crores)

65 | ₹ 361,496


Mega Projects
Count | Original Cost (crores)

32 | ₹ 13,521

Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

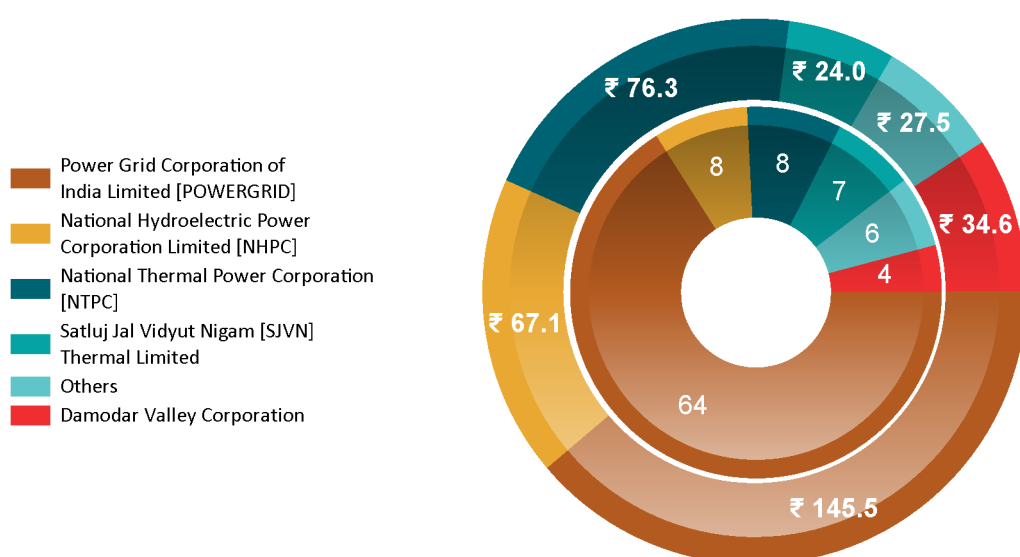


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

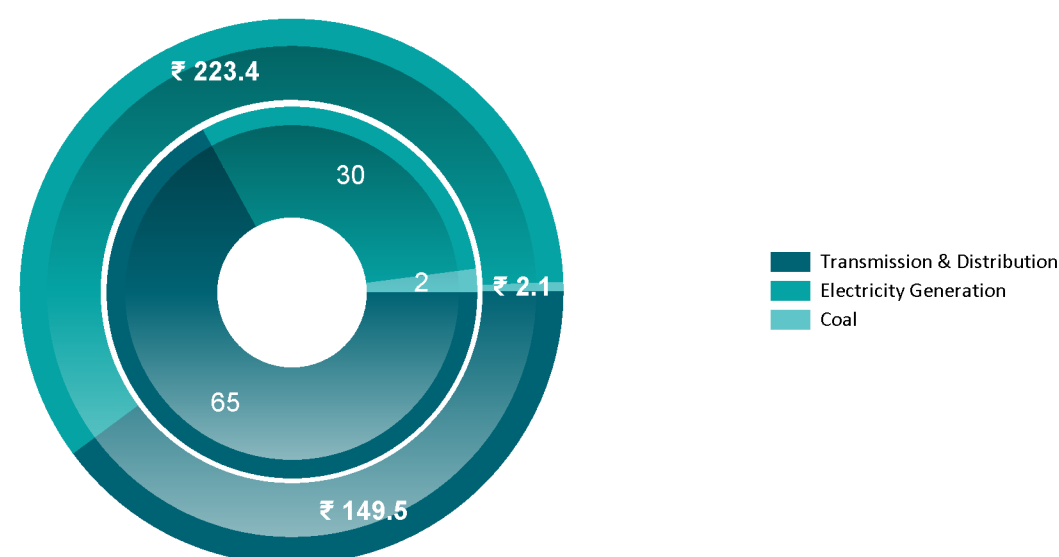


Physical & Financial progress (%) : Project count

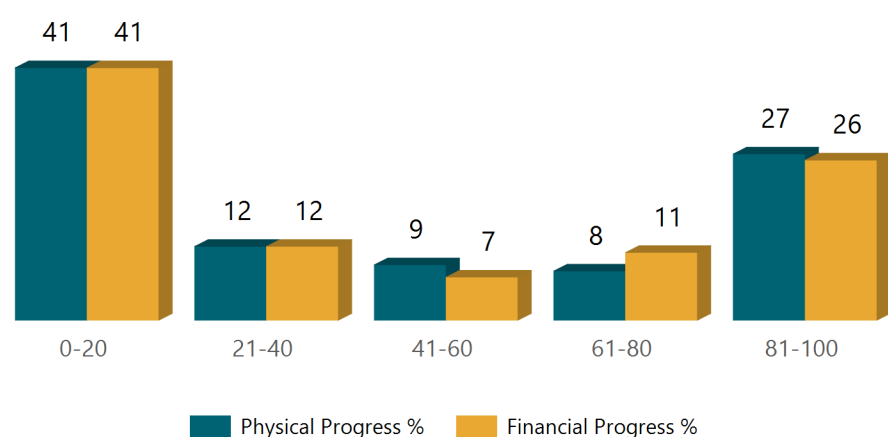

Cost Analytics : Major Sectors*

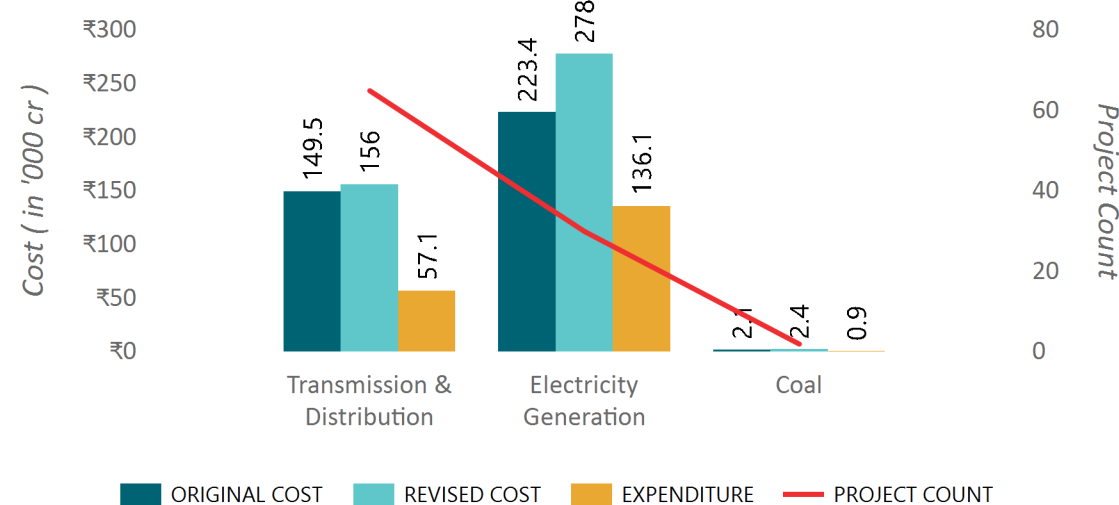

State Comparison : Major States*

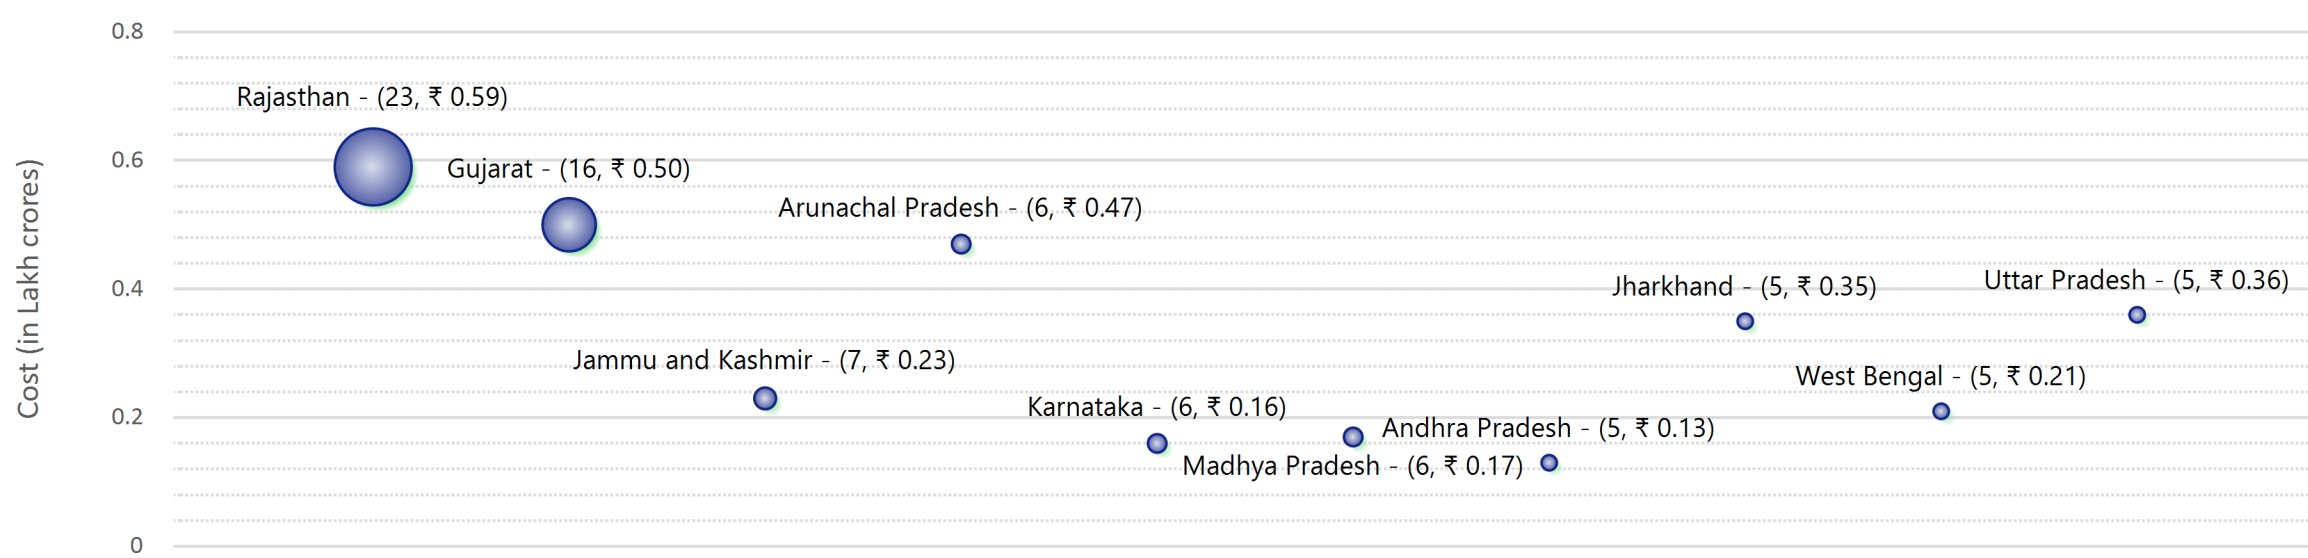

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	3,639	16
2	615347	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV NAME POWERGRID WEST CENTRAL TRANSMISSION LIMITED]	24,819	24,819	1,856	1
3	400062	RAGHUNATHPUR THERMAL POWER STATION PHASE II [2X660 MW] AT RAGHUNATHPUR, PURULIA, WEST BENGAL	17,673	17,673	1,372	2
4	612142	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III [2X800 MW]	17,195	17,195	1,916	10
5	400261	PATRATU THERMAL POWER STATION EXPANSION PROJECT PHASE-I [3X800 MW]	17,112	20,302	17,860	85



Ministry of Housing & Urban Affairs

SEPTEMBER 2025

54

Ongoing Projects

₹ 3,39,589

Original Cost
(crores)

₹ 3,60,170

Revised Cost
(crores)

₹ 2,28,605

(63.47% of Revised Cost)

Expenditure
(crores)

21 | ₹ 329,540


Mega Projects
Count | Original Cost (crores)

33 | ₹ 10,049

Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

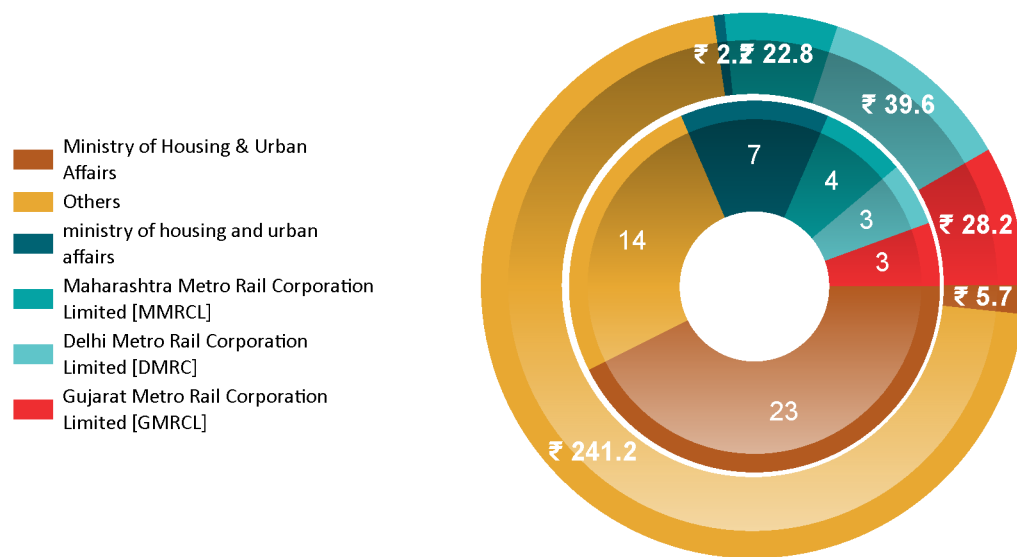


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

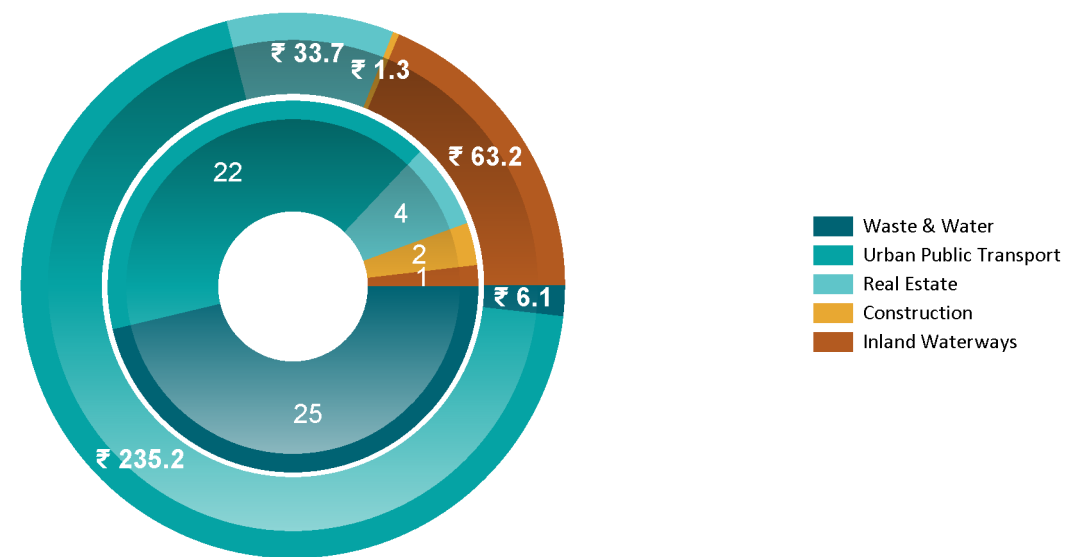


Physical & Financial progress (%) : Project count

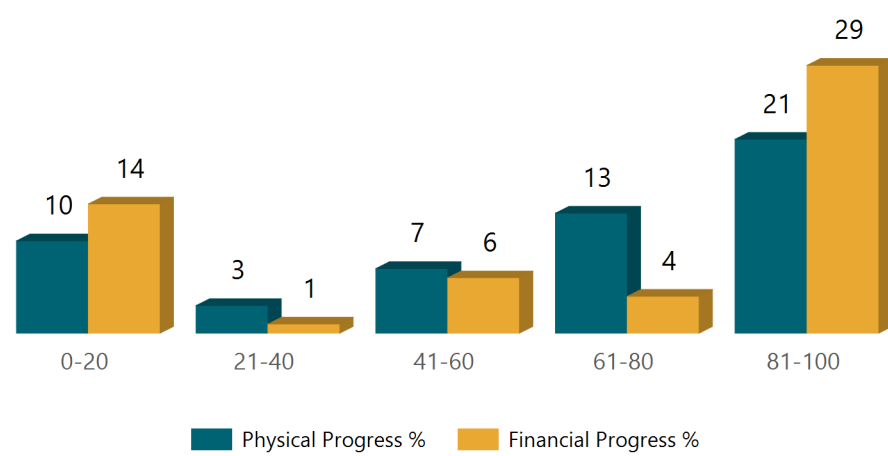

Cost Analytics : Major Sectors*

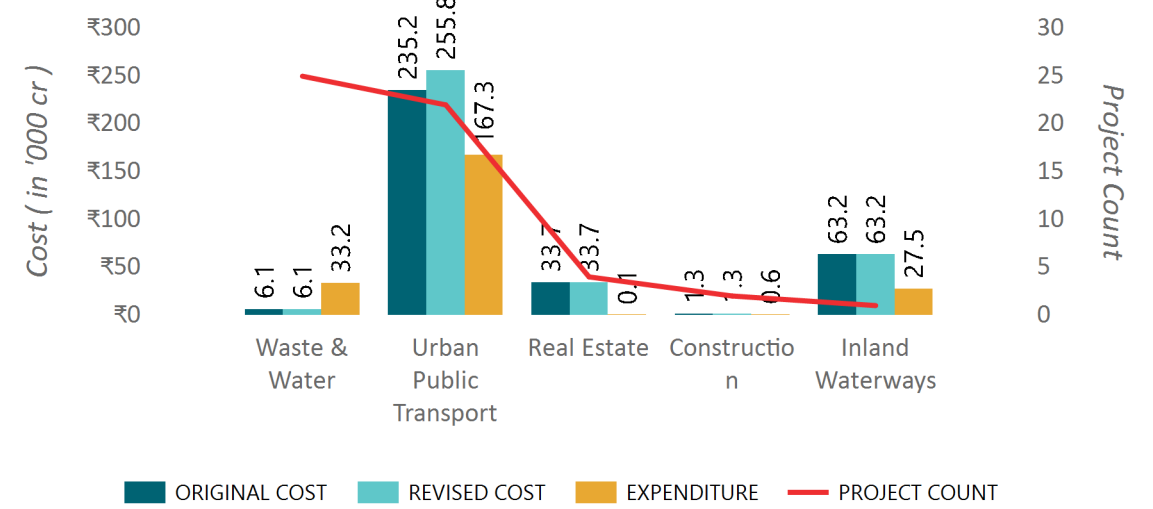

State Comparison : Major States*

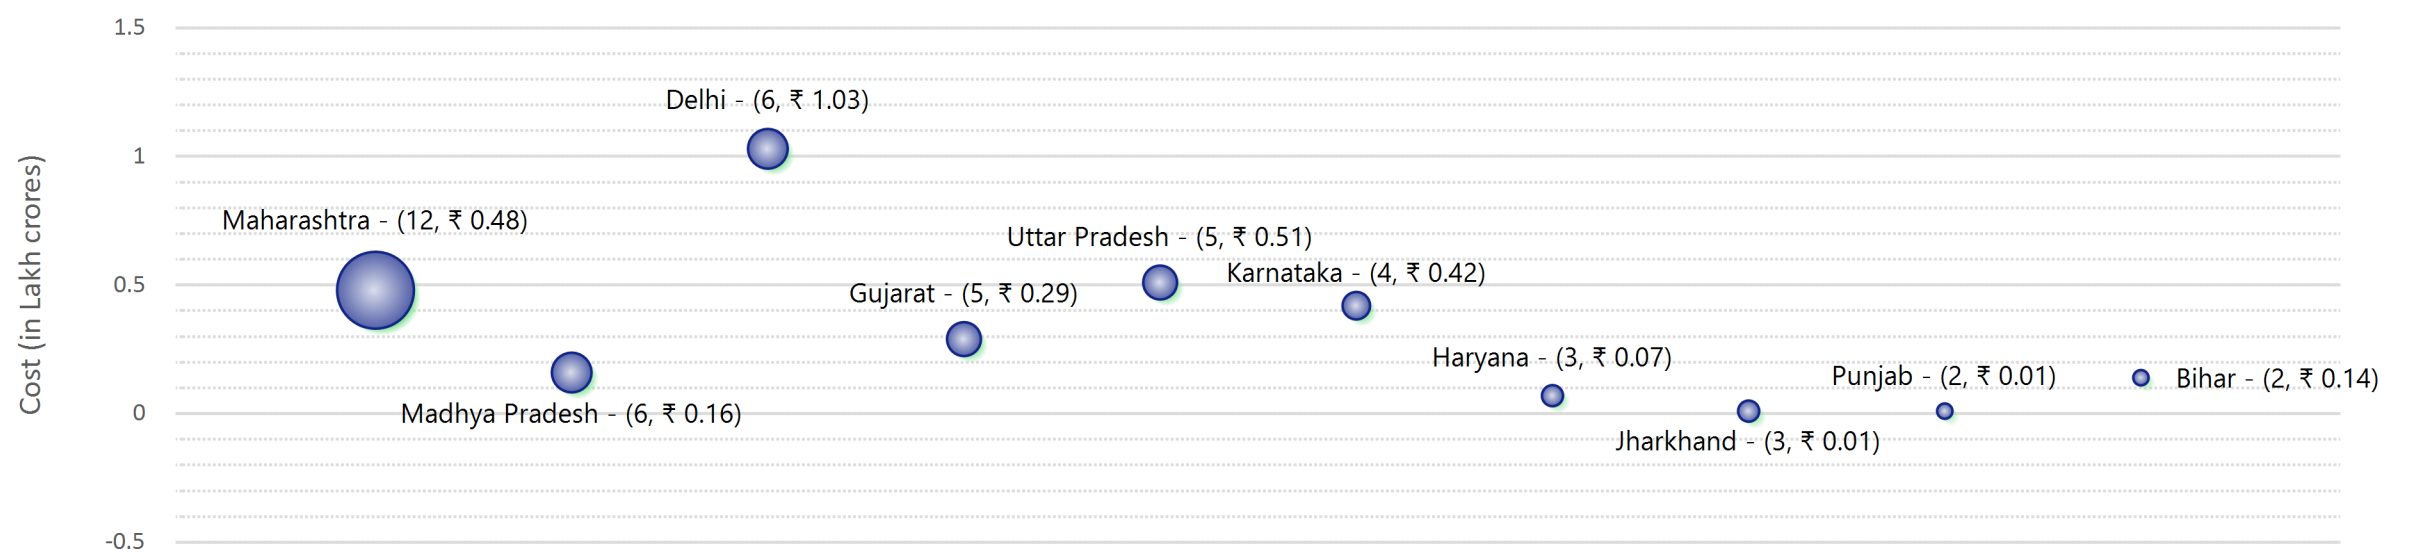

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246	63,246	27,456	46
2	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850	32,850	0	0
3	702633	DELHI-GHAZIABAD-MEERUT REGIONAL RAPID TRANSIT SYSTEM [RRTS] CORRIDOR	30,274	30,274	26,612	95
4	702635	CONSTRUCTION OF BANGALORE METRO RAIL PROJECT PHASE 2.	26,405	30,695	29,568	94
5	702632	DMRTS PHASE - IV [3 PRIORITY CORRIDORS]	24,949	24,949	17,380	70



List of Tables



Table 1: Ministry-wise Ongoing Projects





Ministry-wise Ongoing Projects

SEPTEMBER 2025

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Real Estate	2	3841.25 3841.25	587.67
		Total	2	3,841.25	587.67
2	Department of Higher Education	Education	29	12467.21 12401.2	7891.19
		Total	29	12,467.21	7,891.19
3	Department of Telecommunications	Telecommunication	15	152734.45 274827	72372.8
		Total	15	152,734.45	72,372.80
4	Department of Water Resources, River Development & GR	Waste & Water	8	4039.12 4039.12	1643.05
		Water Resources	39	93740.23 193594	137306
		Total	47	97,779.35	138,949.05
5	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	26	23049.84 23511	24583.3
		Total	26	23,049.84	24,583.30
6	Ministry of Coal	Coal	118	172747.29 170203	55557.5
		Electricity Generation	5	46865.63 51408.8	24531
		Railways	2	3485.86 4250.56	1812.56
		Total	125	223,098.78	81,901.06
7	Ministry of Health & Family Welfare	Healthcare	3	4155 4492.95	2736.65
		Total	3	4,155.00	2,736.65
8	Ministry of Housing & Urban Affairs	Construction	2	1290.53 1290.52	627.64
		Inland Waterways	1	63246 63246	27456.4
		Real Estate	4	33749.85 33749.8	58.58
		Urban Public Transport	22	235216.87 255798	167263
		Waste & Water	25	6085.6 6085.6	33199.3
		Total	54	339,588.85	228,604.92
9	Ministry of Mines	Construction	1	255.37 255.37	83.03
		Metals & Mining	9	12736.35 15116.5	6257.96
		Total	10	12,991.72	6,340.99
10	Ministry of Petroleum & Natural Gas	Energy Storage	16	81301.48 120224	91358.6
		Oil & Gas	88	349335.78 378387	182742
		Total	104	430,637.26	274,100.60
11	Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58
		Inland Waterways	2	5546.18 5258.15	3671.92
		Logistics Infrastructure	1	171 211.61	137.51
		Oil & Gas	1	100 225.85	166.48
		Shipping	7	16499.18 16499.2	9272.35
		Tourism, Hospitality & Wellness	1	573 1238.05	496.63
		Total	13	23,582.36	13,802.89
12	Ministry of Power	Coal	2	2083 2365	911.38
		Electricity Generation	30	223418.07 278228	136109
		Transmission & Distribution	65	149516.43 156031	57066.7
		Total	97	375,017.50	194,087.08
13	Ministry of Railways	Railways	247	812091.77 960470	531131
		Total	247	812,091.77	531,131.00
14	Ministry of Steel	Metals & Mining	1	1700 1756.2	124.9
		Steel	20	19266.64 22504.9	8277.97
		Total	21	20,966.64	8,402.87
Total			793	2,532,001.98	1,585,492.07



Table 2: State-wise Ongoing Projects



Ongoing Projects State-Wise

SEPTEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1		Ministry of Steel	Steel	1	2518.39 2518.39	62.72
	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	6	19714.58 22972.8	11337.22
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	177 197	183.32
		Ministry of Railways	Railways	2	150819 150819	2520.51
	PAN India	Department of Telecommunications	Telecommunication	6	141891.67 264213	69279.89
	Total			16	315120.64	83383.66
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 209.88	0.00
	Total			1	209.88	0.00
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	2139.44 2139.44	470.66
		Department of Higher Education	Education	1	305 305	84.96
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1835.32
		Department of Water Resources, River Development & GR	Water Resources	3	10901.5 57269.5	26234.12
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1224.86 1224.86	648.97
		Ministry of Housing & Urban Affairs	Waste & Water	1	172.22 172.22	710.62
		Ministry of Petroleum & Natural Gas	Energy Storage	2	2898.34 3050	2322.55
			Oil & Gas	5	37997 38057	33508.26
		Ministry of Power	Transmission & Distribution	5	13395.24 13395.2	4708.73
		Ministry of Railways	Railways	23	48181.47 55406.5	32751.48
	Total			47	124362.24	103275.67
4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 592.61	550.22
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Ministry of Petroleum & Natural Gas	Energy Storage	1	43129 79459	60545.24
			Oil & Gas	1	9265 9265	6426.54
		Ministry of Power	Electricity Generation	4	41850.64 61640.8	28863.93
			Transmission & Distribution	2	4963.8 9338.7	7598.35
		Ministry of Railways	Railways	1	435 1250	540.27
	Total			11	101491.54	104808.59
5	Assam	Department of Higher Education	Education	1	153.71 153.71	124.33
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 256.16	44.70
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1712 1712	2397.37
		Ministry of Coal	Coal	2	449.23 449.23	187.07
		Ministry of Housing & Urban Affairs	Waste & Water	1	186.8 186.8	1477.98
		Ministry of Petroleum & Natural Gas	Energy Storage	3	10768.4 11947.4	9999.53
			Oil & Gas	12	26269.15 36624	26216.72
		Ministry of Power	Electricity Generation	1	6285.33 26075.5	25058.77
			Transmission & Distribution	1	5111.33 6700	5295.68
		Ministry of Railways	Railways	7	14593.57 16308.6	10171.81
	Total			31	67041.17	81258.00
6	Bihar	Department of Higher Education	Education	1	499.21 499.21	434.67
		Department of Telecommunications	Telecommunication	4	4220.71 3992.24	1062.37
		Department of Water Resources, River Development & GR	Waste & Water	5	2351.43 2351.43	1303.45
			Water Resources	2	2193.34 3088.88	598.72
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3541.56 3541.56	1310.96
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	13365.77 13365.8	4039.77
			Waste & Water	1	158.78 158.78	509.50

Ongoing Projects State-Wise

SEPTEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9811.29
			Oil & Gas	6	24473.5 26338.2	13311.31
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3488.60
		Ministry of Power	Electricity Generation	1	10439.09 13756.6	12426.32
			Transmission & Distribution	2	751.63 751.63	1.01
		Ministry of Railways	Railways	21	48872.05 52873.6	22447.78
		Total		49	126464.25	70745.75
7	Chhattisgarh	Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1835.32
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 1109.33	616.93
		Ministry of Coal	Coal	15	38654.89 38654.9	17713.97
			Railways	1	1686.22 1686.22	350.21
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	10056.25 10467	6625.93
		Ministry of Power	Electricity Generation	2	25321 25321	3677.06
			Transmission & Distribution	1	385.84 385.84	378.74
		Ministry of Railways	Railways	19	26865.42 28510.7	19398.32
		Ministry of Steel	Metals & Mining	1	1700 1756.2	124.90
			Steel	6	7530.14 10050.1	5400.74
		Total		52	120189.19	56122.12
8	Dadra & Nagar Haveli and Daman & Diu	Ministry of Housing & Urban Affairs	Waste & Water	1	210 210	0.00
		Ministry of Power	Transmission & Distribution	1	4546.26 4546.26	4210.29
		Ministry of Railways	Railways	1	108000 108000	81242.89
		Total		3	112756.26	85453.18
9	Delhi	Department of Higher Education	Education	2	706.49 709.42	304.34
		Department of Telecommunications	Telecommunication	1	248.2 248.2	236.91
		Ministry of Housing & Urban Affairs	Construction	1	646.53 646.52	540.04
			Real Estate	1	32850 32850	0.00
			Urban Public Transport	4	69853.45 69853.4	44023.66
		Ministry of Power	Transmission & Distribution	4	4356.47 4908.47	4014.48
		Ministry of Railways	Railways	15	28623.17 28623.2	5952.85
		Total		28	137284.31	55072.28
10	Goa	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	255.69 255.69	154.30
		Ministry of Railways	Railways	2	5804.49 6182.62	5976.87
		Total		3	6060.18	6131.17
11	Gujarat	Department of Higher Education	Education	1	490.63 490.63	312.06
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Department of Water Resources, River Development & GR	Water Resources	2	25739.93 40082.8	36815.85
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1305 1551	696.39
		Ministry of Coal	Coal	1	7580 7580	3091.00
			Electricity Generation	1	383.84 383.84	303.50
		Ministry of Housing & Urban Affairs	Real Estate	1	539 539	39.63
			Urban Public Transport	3	28177.49 30329	24213.19
			Waste & Water	1	200 200	100.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	62245 98575	75712.08
			Oil & Gas	11	32704.12 32178.7	23320.53
		Ministry of Ports, Shipping and Waterways	Logistics Infrastructure	1	171 211.61	137.51
			Oil & Gas	1	100 225.85	166.48

Ongoing Projects State-Wise						SEPTEMBER 2025
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
11	Gujarat	Ministry of Ports, Shipping and Waterways	Shipping	1	4243.64 4243.64	70.00
			Tourism, Hospitality & Wellness	1	573 1238.05	496.63
		Ministry of Power	Electricity Generation	1	339.35 339.35	317.59
			Transmission & Distribution	15	49807.7 49807.2	13321.24
		Ministry of Railways	Railways	28	186416.66 262937	218029.49
		Total			74	401353.25
12	Haryana	Ministry of Health & Family Welfare	Healthcare	1	1299 1299	349.41
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	6230.99 6230.99	0.78
			Waste & Water	2	491.2 491.2	3026.70
		Ministry of Petroleum & Natural Gas	Energy Storage	1	9028 9028	7186.98
			Oil & Gas	5	45925.07 49596.1	34405.10
		Ministry of Power	Transmission & Distribution	4	13362 13914	2827.44
		Ministry of Railways	Railways	4	53464 126368	125612.30
		Total			18	129800.26
13	Himachal Pradesh	Department of Higher Education	Education	3	811.15 921.89	591.50
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Power	Electricity Generation	4	7728.04 12252.1	4196.71
		Ministry of Railways	Railways	3	17005 17005.1	9479.02
		Total			11	25881.08
14	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 500.91	484.52
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 861.37	192.59
		Ministry of Health & Family Welfare	Healthcare	1	1828 1828	1565.25
		Ministry of Petroleum & Natural Gas	Energy Storage	1	676.89 715.89	535.94
			Oil & Gas	2	1059.9 1059.9	209.72
		Ministry of Power	Electricity Generation	4	22207.77 27945.1	12678.64
			Transmission & Distribution	3	825.43 825.43	552.11
		Total			14	28221.18
15	Jharkhand	Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1835.32
		Department of Water Resources, River Development & GR	Water Resources	2	5430.04 12010.3	5713.01
		Ministry of Coal	Coal	28	51354.95 51119.3	10470.97
			Railways	1	1799.64 2564.34	1462.35
		Ministry of Housing & Urban Affairs	Waste & Water	3	654.14 654.14	2935.64
		Ministry of Mines	Metals & Mining	2	3370.02 3370.02	19.80
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9811.29
			Oil & Gas	3	2010.07 2010.07	613.95
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3488.60
		Ministry of Power	Coal	2	2083 2365	911.38
			Electricity Generation	2	31470 34660	19115.79
			Transmission & Distribution	1	1842.25 1842.25	1643.00
		Ministry of Railways	Railways	11	40310.82 40704.8	15043.66
		Ministry of Steel	Steel	6	2854.58 3572.87	1330.79
		Total			66	165923.86
16	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1701.81 1701.81	117.01
		Department of Higher Education	Education	1	420.41 420.41	364.44
		Department of Water Resources, River Development & GR	Water Resources	1	770.16 1606.07	1515.32



Ongoing Projects State-Wise

SEPTEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore	
16	Karnataka	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1143.4 1143.4	535.64	
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	41193.24 45483.2	38385.84	
			Waste & Water	2	337.69 337.69	1461.50	
		Ministry of Petroleum & Natural Gas	Energy Storage	1	678 1732	767.09	
			Oil & Gas	5	9662 12693.6	8795.03	
		Ministry of Power	Transmission & Distribution	6	15682.01 15682	3165.63	
		Ministry of Railways	Railways	15	23023.29 29441.9	17503.36	
		Ministry of Steel	Steel	1	1043.63 1043.63	262.34	
		Total			38	95655.64	72873.20
17	Kerala	Department of Higher Education	Education	1	1006.45 1217.4	632.59	
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	484.57 484.57	85.16	
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1957.05 1957.05	363.54	
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	7996.87 10990.9	4939.69	
		Ministry of Ports, Shipping and Waterways	Shipping	1	1799 1799	1558.39	
		Ministry of Railways	Railways	3	2846 5183.19	2807.21	
		Total			10	16089.94	10386.58
18	Ladakh	Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82	
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480 640	456.22	
		Ministry of Power	Transmission & Distribution	1	288.71 288.71	242.52	
		Total			3	1105.6	926.56
19	Madhya Pradesh	Department of Higher Education	Education	1	496.28 496.28	38.62	
		Department of Telecommunications	Telecommunication	3	3883.82 3691.11	834.55	
		Department of Water Resources, River Development & GR	Water Resources	3	2628.27 2941.14	2825.25	
		Ministry of Coal	Coal	14	8634.02 8634.02	3430.25	
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	14442.2 14442.2	7713.93	
			Waste & Water	4	1243.05 1243.05	8721.84	
		Ministry of Mines	Metals & Mining	1	1856.36 1856.36	935.32	
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10088 10088	7979.86	
			Oil & Gas	2	51211.25 51622	8523.00	
		Ministry of Power	Transmission & Distribution	6	17446 17446	3446.38	
		Ministry of Railways	Railways	19	58468.02 72465.1	43219.83	
		Total			56	170397.27	87668.83
		20	Maharashtra	Department of Higher Education	Education	2	250.33 446.26
Department of Telecommunications	Telecommunication			4	7608.59 7608.59	2001.34	
Department of Water Resources, River Development & GR	Water Resources			11	22660.36 32345.7	33603.52	
Ministry of Civil Aviation	Aviation & Aviation Infrastructure			1	500.48 500.48	332.26	
Ministry of Coal	Coal			25	12455.88 12455.9	3092.43	
Ministry of Housing & Urban Affairs	Urban Public Transport			7	46771.57 60911.6	33377.40	
	Waste & Water			5	1088.72 1088.72	7594.40	
Ministry of Petroleum & Natural Gas	Energy Storage			1	281.35 389.67	234.60	
	Oil & Gas			13	34264.24 37660.4	21065.98	
Ministry of Ports, Shipping and Waterways	Healthcare			1	693 693	58.00	
	Shipping			2	6900 6900	6064.89	
Ministry of Power	Transmission & Distribution			3	29589.67 29589.7	6092.55	
Ministry of Railways	Railways			34	262485.75 354459	263737.65	
Total				109	425549.94	377423.41	



Ongoing Projects State-Wise

SEPTEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
21	Manipur	Department of Water Resources, River Development & GR	Water Resources	1	1449.44 1822.24	1837.91
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499 499	154.43
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6426.54
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5295.68
		Ministry of Railways	Railways	1	14323 21885.9	15598.11
	Total			5	30647.77	29312.67
22	Meghalaya	Department of Higher Education	Education	1	494.52 494.52	413.57
		Department of Telecommunications	Telecommunication	1	971.96 971.96	208.25
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6426.54
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5295.68
	Total			4	15842.81	12344.04
23	Mizoram	Department of Higher Education	Education	1	474.23 474.23	167.55
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6426.54
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5295.68
	Total			3	14850.56	11889.77
24	Nagaland	Department of Higher Education	Education	1	275.63 275.63	261.24
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	9492.62 9492.62	6435.88
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5295.68
		Ministry of Railways	Railways	2	8786.7 8786.7	5532.06
	Total			6	23666.28	17524.86
25	Odisha	Department of Higher Education	Education	1	1229.32 773.76	837.04
		Department of Telecommunications	Telecommunication	3	7147.17 7147.17	1835.32
		Department of Water Resources, River Development & GR	Water Resources	2	1556.46 5291.33	5342.49
		Ministry of Coal	Coal	12	36526.28 34218	13055.11
			Electricity Generation	1	27212.96 27213	2517.13
		Ministry of Mines	Metals & Mining	5	7343.97 9724.14	5167.84
		Ministry of Petroleum & Natural Gas	Energy Storage	2	12886.34 14217	12084.27
			Oil & Gas	5	25285.44 23768.5	15972.39
		Ministry of Ports, Shipping and Waterways	Shipping	1	3004.63 3004.63	1149.79
		Ministry of Power	Electricity Generation	1	11843.75 12543	4574.68
			Transmission & Distribution	1	342.69 342.69	0.70
		Ministry of Railways	Railways	21	38899.99 43632	32329.67
			Railways	1	267.61 267.61	0.00
	Ministry of Steel	Steel	1	1105.23 1105.23	769.08	
Total			57	174651.84	95635.51	
26	Puducherry	Department of Higher Education	Education	1	618.34 544.34	509.55
		Ministry of Railways	Railways	1	713 981	598.38
	Total			2	1331.34	1107.93
27	Punjab	Department of Higher Education	Education	2	559.3 559.3	300.39
		Department of Water Resources, River Development & GR	Water Resources	2	3727.07 5177.86	5072.69
		Ministry of Housing & Urban Affairs	Waste & Water	2	545.53 545.53	1842.39
		Ministry of Petroleum & Natural Gas	Oil & Gas	6	13060.36 13090.4	8400.69
		Ministry of Power	Transmission & Distribution	1	5969 5969	344.41
		Ministry of Railways	Railways	3	15702.64 15703	9091.19
	Total			16	39563.9	25051.76
28	Rajasthan	Department of Telecommunications	Telecommunication	2	758.54 530.07	362.33

Ongoing Projects State-Wise

SEPTEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
28	Rajasthan	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1367 1367	680.64
		Ministry of Coal	Electricity Generation	1	1813 1813	1038.13
		Ministry of Petroleum & Natural Gas	Energy Storage	3	52618.05 88948.1	67860.06
			Oil & Gas	2	10599 10599	6653.10
		Ministry of Power	Electricity Generation	1	5491.89 5491.89	5009.15
			Transmission & Distribution	22	53646.51 54198.2	18830.67
		Ministry of Railways	Railways	23	88639.51 164210	139887.44
		Total		56	214933.5	240321.52
29	Sikkim	Department of Higher Education	Education	2	999.82 924.82	359.78
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 323.26	34.30
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6426.54
		Ministry of Power	Electricity Generation	2	6686.33 7576.15	6102.42
			Transmission & Distribution	1	4754.42 9129.32	7598.33
		Ministry of Railways	Railways	1	7877 12133	9039.91
		Total		8	29905.83	29561.28
30	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1207 1207	164.13
		Ministry of Coal	Electricity Generation	1	218.03 218.03	161.73
		Ministry of Housing & Urban Affairs	Inland Waterways	1	63246 63246	27456.44
		Ministry of Mines	Metals & Mining	1	166 166	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	2334 3448.71	1721.14
			Oil & Gas	4	38385 46153	6084.92
		Ministry of Power	Transmission & Distribution	1	548 548	23.72
		Ministry of Railways	Railways	7	8370.7 11489.7	5801.30
		Total		19	114474.73	41548.38
31	Telangana	Department of Higher Education	Education	1	262 262	178.17
		Department of Telecommunications	Telecommunication	3	3923.59 3923.59	866.06
		Department of Water Resources, River Development & GR	Water Resources	4	11670.14 24129.6	11830.43
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	332.26
		Ministry of Coal	Coal	9	3890.03 3890.03	2473.74
		Ministry of Health & Family Welfare	Healthcare	1	1028 1365.95	821.99
		Ministry of Housing & Urban Affairs	Construction	1	644 644	87.60
		Ministry of Power	Transmission & Distribution	2	5694.56 5694.56	4573.22
		Ministry of Railways	Railways	9	16396.23 20160.2	9819.59
		Total		31	44009.03	30983.06
32	Tripura	Ministry of Petroleum & Natural Gas	Energy Storage	1	656 656	483.90
			Oil & Gas	2	9474.33 9396.51	6495.44
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5295.68
		Total		4	15241.66	12275.02
33	Uttar Pradesh	Department of Higher Education	Education	1	246 246	194.14
		Department of Telecommunications	Telecommunication	4	4220.71 3992.24	1062.37
		Department of Water Resources, River Development & GR	Waste & Water	2	1532.96 1532.96	243.43
			Water Resources	3	2953.27 6309.81	4437.48
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	5	7268.31 7323.51	17006.35
		Ministry of Coal	Coal	2	1328.09 1328.09	1042.00
			Electricity Generation	1	17237.8 21780.9	20510.47
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	49730.1 49730.1	41757.77

Ongoing Projects State-Wise

SEPTEMBER 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
33	Uttar Pradesh	Ministry of Housing & Urban Affairs	Waste & Water	2	797.47 797.47	4818.74
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11068.45 11068.5	8200.83
			Oil & Gas	3	17824.68 18213.1	1620.78
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3488.60
		Ministry of Power	Electricity Generation	2	28284.42 30471.2	14804.23
			Transmission & Distribution	3	8114.81 8114.81	1975.10
		Ministry of Railways	Railways	27	92871.92 167498	148127.42
		Total		61	248848.17	269289.71
34	Uttarakhand	Department of Higher Education	Education	1	650.85 650.85	195.52
		Department of Water Resources, River Development & GR	Water Resources	1	2584.1 2584.1	968.52
		Ministry of Housing & Urban Affairs	Real Estate	1	150.97 150.97	18.95
		Ministry of Power	Electricity Generation	3	11663.95 26070	20568.54
		Ministry of Railways	Railways	1	38953 38953	24645.15
		Total		7	54002.87	46396.68
35	West Bengal	Department of Higher Education	Education	1	500 442	383.60
		Department of Telecommunications	Telecommunication	2	3462.17 3462.17	700.04
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 154.73	96.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1877.3 1877.3	398.12
		Ministry of Coal	Coal	13	15863.74 15863.7	2832.85
		Ministry of Mines	Construction	1	255.37 255.37	83.03
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9811.29
			Oil & Gas	8	18159.65 19007.2	11428.96
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3488.60
			Shipping	2	551.91 551.91	429.28
		Ministry of Power	Electricity Generation	3	20091.84 20160.8	3773.75
			Transmission & Distribution	2	751.63 751.63	1.01
		Ministry of Railways	Railways	14	46167.32 56739.3	33671.35
		Ministry of Steel	Steel	5	4214.67 4214.67	452.30
		Total		56	127647.51	67550.35




Table 3: Completed Projects



Completed Projects During Month

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
	Department of Higher Education					
	Education					
1	IoE Projects [Civil Works], IIT Kharagpur <i>(Indian Institute of Technology, Kharagpur)</i> 609041	West Bengal	01/2018 (01/2019)	08/2025 (03/2023) (12/2026)	287.2 (-)	310
	Total (1)				287.2	310
	Department of Water Resources, River Development & GR					
	Water Resources					
2	Durgawati Reservoir Project <i>(Irrigation and CAD-TG)</i> 701371	Bihar	04/1996 (04/1997)	09/2025 (12/2019) (03/2026)	691.15 (971.96)	978.51
3	Arjun Sahayak Project <i>(Irrigation & Water Resources-UP)</i> 400117	Uttar Pradesh	04/2009 (04/2009)	10/2025 (12/2019) (12/2019)	741.38 (2465.68)	3037.68
	Total (2)				1432.53	4016.19
	Ministry of Petroleum & Natural Gas					
	Oil & Gas					
4	Assam Bio Refinery, ABRPL <i>(Ministry of Petroleum & Natural Gas)</i> 604792	Assam	02/2018 (02/2018)	09/2025 (09/2021) (09/2025)	1750 (4930)	4770
5	City Gas Distribution Project at Khagaria, Saharsa and Madhepura <i>(Ministry of Petroleum & Natural Gas)</i> 617303	Bihar	03/2019 (03/2019)	09/2025 (03/2030) (09/2025)	163 (163)	96.95
	Total (2)				1913	4866.95
	Ministry of Ports, Shipping and Waterways					
	Shipping					
6	Operationalization of Coastal Berth & Shallow Water Berth through PPP <i>(Jawaharlal Nehru Port Authority [JNPA])</i> 708655	Maharashtra	(07/2021)	NA (01/2026) (-)	366.8 (-)	376.86
	Total (1)				366.8	376.86
	Ministry of Railways					
	Railways					
7	Gorakhpur-Valmikinagar Doubling project <i>(NER)</i> 617224	Multi-States (Bihar, Uttar Pradesh)	08/2023 (03/2024)	NA (12/2027) (-)	1120 (-)	220.18
	Total (1)				1120	220.18

Note: Cumulative Expenditure is as per last reporting by Central Line Ministries/ Departments on the IPM portal, this may not be the actual completion cost.



Table 4: Newly Added Projects

Newly Added Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
	Department of Telecommunications				
	Telecommunication				
1	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase 1 Upgradation (Department of Telecommunications [DoT]) (617413)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	04/2022 (05/2024)	05/2025 (11/2025)	1884.6 (-)
	Total (1)				1884.6
	Department of Water Resources, River Development & GR				
	Water Resources				
2	Bodwad Parisar Sinchan Yojna (Department of Water Resources-MH) (617422)	Maharashtra	05/2002 (01/2017)	07/2027 (-)	1923.81 (-)
	Total (1)				1923.81
	Ministry of Coal				
	Coal				
3	Revised Jharia Master Plan for Dealing with Fire, Subsidence & Rehabilitation of affected families in Jharia Coalfield- Reg. (Bharat Coking Coal Limited (BCCL)) (617416)	Jharkhand	06/2025 (07/2025)	12/2028 (-)	5940.47 (-)
	Total (1)				5940.47
	Ministry of Housing & Urban Affairs				
	Construction				
4	Construction of One Tower of Office Complex and another Tower of Residential quarters consisting of 10Nos. Type-V, 10Nos. Type-VI & 1No.Type-VII Quarters i/c internal water supply, sanitary installation and all development and bulk services, Horticulture works on EPC Mode-I basis i/c comprehensive operation and maintenance of Civil, E&M services for 7 years after completion of original construction work for Ranga Reddy, Secunderabad, Medchal, Audit-I, Audit-II Commissionerates of Central Tax at Khajaguda, Serilingampally, Hyderabad. (Central Public Works Department - CPWD) (617412)	Telangana	03/2024 (11/2024)	09/2027 (-)	644 (-)
	Total (1)				644
	Urban Public Transport				
5	Thane Integral Ring Metro Rail Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617327)	Maharashtra	09/2024 (09/2024)	09/2029 (-)	12200.1 (-)
	Total (1)				12200.1
	Ministry of Ports, Shipping and Waterways				
	Inland Waterways				
6	Fairway Development in West Bengal Farakka - Kahelgaon (Inland Waterways Authority of India [IWA]) (611142)	Offshore	(08/2018)	07/2023 (04/2024)	177 (197)
	Total (1)				177
	Logistics Infrastructure				
7	Replacement and revamping of pipeline projects in oil jetty area, Kandla (Deendayal Port Trust [DPT]) (701570)	Gujarat	(09/2021)	09/2023 (03/2025)	171 (211.61)
	Total (1)				171
	Oil & Gas				
8	Construction of oil jetty No.8 at old kandla through internal resources (Deendayal Port Trust [DPT]) (701568)	Gujarat	(02/2021)	02/2023 (07/2024)	100 (225.85)
	Total (1)				100
	Shipping				
9	Construction of new dry dock at exisitng Cochin Shipyard Limited premises at Perumanoor, Kochi 682 015 (Cochin Shipyard) (701564)	Kerala	04/2018 (05/2018)	12/2022 (03/2025)	1799 (-)
10	Rewas Port Project (Reliance Industries Ltd) (400382)	Maharashtra	(01/2020)	03/2023 (-)	6000 (-)
	Total (2)				7799
	Ministry of Power				
	Transmission & Distribution				
11	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (-)
12	Augmentation of Transformation Capacity at Bhuj-II PS [GIS] (Power Grid Corporation of India Limited [POWERGRID]) (617391)	Gujarat	02/2025 (02/2025)	11/2026 (03/2027)	488.29 (-)
13	Jamnagar Transmission Limited (Adani Transmission Limited) (617405)	Gujarat	(10/2024)	10/2026 (-)	4000 (-)
14	Implementation of Transmission Systems in the State of Jharkhand consisting of 400/220/132/33 kV transmission lines and substations under Jharkhand Consultancy Project (Power Grid Corporation of India Limited [POWERGRID]) (617326)	Jharkhand	02/2012 (02/2012)	03/2026 (-)	1842.25 (-)
	Total (4)				6539.92

Newly Added Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
	Ministry of Railways				
	Railways				
15	Jhajha-Batai New Line Project (East Central Railway [ECR] - I) (617373)	Bihar	03/2023 (03/2023)	03/2027 (-)	588.18 (-)
16	JHAJHA - BATIA (East Central Railway [ECR] - I) (900874)	Bihar	03/2023 (03/2023)	03/2028 (01/2030)	588.18 (-)
17	Dallirajhara - Rowghat New Rail Line Project, Phase-I (Rail Vikas Nigam Limited) (617374)	Chhattisgarh	(11/2009)	03/2025 (-)	1516.45 (-)
18	Development of New Bijwasan Railway Terminal (Northern Railways) (617379)	Delhi	02/2008 (03/2013)	03/2020 (-)	446.21 (-)
19	Doubling between Pradhankunta-Patherih-Bhojudih of East Central Railway (East Central Railway [ECR] - I) (617372)	Jharkhand	11/2022 (11/2022)	12/2025 (-)	349.22 (-)
20	Babupeth - Sasti New Rail Line [13.114 KMs] (Central Railway [CR] - II) (617361)	Maharashtra	10/2024 (10/2024)	03/2028 (-)	362.81 (362.81)
21	Double Chord line Between Nilaje-Kopar (Central Railway [CR] - II) (617364)	Maharashtra	01/2025 (01/2025)	07/2028 (-)	338.33 (205)
22	Sardega -Bhalumuda New Double line [37.24 Km] (SECR) (617390)	Multi-States (Chhattisgarh, Odisha)	09/2024 (09/2024)	03/2028 (-)	1281.81 (-)
23	RATLAM- DUNGARPUR VIA BANSWARA NEW LINE PROJECT (North Western Railway [NWR]) (617406)	Multi-States (Madhya Pradesh, Rajasthan)	10/2015 (05/2023)	03/2028 (-)	2417.24 (-)
24	Jeypore - Malkangiri New BG Line Project (Indian Railways) (617290)	Odisha	(02/2018)	12/2030 (-)	2343.64 (-)
25	New B.G Railway Line between Jeypore & Navarangpur [38 Km] with Electrification (Indian Railway and Govt of Odisha) (617320)	Odisha	07/2017 (09/2022)	09/2025 (-)	747.91 (-)
26	Godhani-Kalumna Chord 13.7 km (Ministry of Railways) (617321)	Offshore	07/2018 (07/2018)	07/2028 (-)	150000 (-)
27	NATHDWARA- NATHDWARA TOWN NL (North Western Railway [NWR]) (617408)	Rajasthan	03/2019 (04/2024)	03/2027 (-)	166.33 (-)
28	SADULPUR - CHURU DOUBLING PROJECT (North Western Railway [NWR]) (617403)	Rajasthan	01/2024 (01/2024)	06/2026 (-)	468.64 (-)
29	POKHRAN - RAMDEVRA New Line (North Western Railway [NWR]) (617404)	Rajasthan	04/2025 (04/2025)	03/2028 (-)	189.21 (-)
30	Railway Manufacturing Unit (South Central Railway [SCR] - II) (617409)	Telangana	07/2016 (02/2023)	12/2026 (-)	521.36 (-)
31	Surface triangle line bet. Bhadura stn and new crossing stn Karma (East Central Railway [ECR] - I) (617333)	Uttar Pradesh	10/2022 (05/2024)	02/2027 (-)	199.96 (-)
32	Doubling between Jaunpur Jn - Zaffarabad 6.28 km (M/S SRC company Infra Private Limited) (617370)	Uttar Pradesh	03/2023 (02/2025)	01/2027 (-)	180.66 (-)
33	SER Upgradation of maintenance infrastructure at Shalimar into Vande Bharat Chair Car maintenance cum workshop depot. (South Eastern Railway - JH) (617345)	West Bengal	(12/2024)	10/2026 (-)	226.87 (-)
	Total (19)				162933.01
	Ministry of Steel				
	Steel				
34	Stamp Charge Battery No.12 Battery Proper at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617338)		01/2025 (02/2025)	07/2028 (-)	2518.39 (-)
	Total (1)				2518.39




Table 5: Ongoing Projects

North Eastern Region



Ongoing Projects of North-East Region

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (11/2025)	1712 (1712)	2397.37	91
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	154.43	41
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	34.3	13
	Total (3)				2534.26	2586.1	
	Ministry of Coal						
	Coal						
4	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	81.47	0
5	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.6	3
	Total (2)				449.23	187.07	
	Department of Higher Education						
	Education						
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (-)	592.61 (592.61)	550.22	75
7	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (10/2025)	153.71 (153.71)	124.33	97
8	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (07/2025)	494.52 (494.52)	413.57	86
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (12/2029)	474.23 (474.23)	167.55	4
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	261.24	97
11	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	121.56	12
12	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (09/2025)	314.06 (314.06)	238.22	83
	Total (7)				2990.52	1876.69	
	Ministry of Power						
	Electricity Generation						
13	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3639.39	16
14	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	49.69	3
15	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	116.08	2
16	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	25058.77	96
17	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	4656.92	69
18	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (12/2025)	938.29 (1828.11)	1445.5	93
	Total (6)				48536.97	34966.35	
	Transmission & Distribution						
19	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	0.02	0
20	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	7598.33	82
21	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (12/2025)	5111.33 (6700)	5295.68	96
	Total (3)				10075.13	12894.03	



Ongoing Projects of North-East Region

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Petroleum & Natural Gas						
	Energy Storage						
22	Rajasthan Refinery Project (Ministry of Petroleum & Natural Gas) (701263)	Arunachal Pradesh	10/2017 (10/2017)	10/2022 (03/2026)	43129 (79459)	60545.24	88
23	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Assam	NA (01/2019)	07/2024 (10/2025)	10228 (11407)	9811.29	87
24	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	58.27	48
25	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	129.97	55
26	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	NA (06/2022)	09/2025 (06/2026)	656 (656)	483.9	88
	Total (5)				54553.4	71028.67	
	Oil & Gas						
27	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	NA (07/2020)	07/2024 (12/2025)	12366 (22494)	17007.22	78
28	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	NA (01/2018)	02/2020 (12/2025)	682.9 (726.93)	489.6	94
29	Guwahati Refinery Expansion [1.0 to 1.2 MMTA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	NA (05/2021)	10/2023 (05/2026)	412.3 (577)	435.92	86
30	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	NA (12/2020)	03/2024 (12/2025)	430.76 (430.76)	327.47	86
31	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTA to 5.5 MMTA (Ministry of Petroleum & Natural Gas) (701350)	Assam	NA (06/2021)	12/2024 (10/2025)	860 (860)	615.47	98
32	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Ministry of Petroleum & Natural Gas) (709776)	Assam	NA (04/2022)	09/2026 (09/2026)	277 (323.09)	186.17	68
33	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTA (Ministry of Petroleum & Natural Gas) (709779)	Assam	NA (06/2022)	03/2026 (07/2027)	768 (740)	115.21	42
34	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2026)	344.99 (344.99)	211.1	48
35	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	09/2023 (09/2023)	05/2026 (05/2026)	198.7 (198.7)	39.45	36
36	DCU Revamp Project (NRL) (709864)	Assam	NA (08/2021)	07/2024 (10/2025)	370 (370)	265.35	61
37	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	NA (04/2023)	12/2024 (10/2025)	293.5 (293.5)	97.22	95
38	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura)	NA (04/2020)	03/2024 (03/2026)	9265 (9265)	6426.54	85
39	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum & Natural Gas) (709786)	Nagaland	NA (08/2023)	11/2027 (11/2027)	227.62 (227.62)	9.34	23
40	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022 (03/2022)	05/2024 (12/2025)	209.33 (131.51)	68.9	63
	Total (14)				26706.1	26294.96	
	Ministry of Railways						
	Railways						
41	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3707.75	93
42	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
43	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
44	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
45	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15598.11	69
46	Murkongselek-Pasighat (Northeast Frontier Railway [NFR] - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (03/2023)	03/2025 (05/2026)	435 (1250)	540.27	60

Ongoing Projects of North-East Region

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
47	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5518.32	81
48	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
49	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Sikkim	10/2009 (05/2010)	05/2015 (12/2027)	7877 (12133)	9039.91	84
	Total (9)				36793.57	34809.83	
	Department of Telecommunications						
	Telecommunication						
50	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (09/2025)	971.96 (971.96)	208.25	99
51	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (09/2025)	1255.49 (1255.49)	284.04	91
	Total (2)				2227.45	492.29	
	Ministry of Housing & Urban Affairs						
	Waste & Water						
52	Dibrugarh Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702682)	Assam	NA (01/2020)	03/2023 (12/2025)	186.8 (186.8)	1477.98	98
	Total (1)				186.8	1477.98	
	Department of Water Resources, River Development & GR						
	Water Resources						
53	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55
54	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
	Total (2)				1705.6	1882.61	




Table 6: All Ongoing Projects



All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport (Airport Authority of India [AAI]) (612786)	Andhra Pradesh	03/2023 (01/2024)	01/2026 (03/2026)	265.91 (265.91)	59.43	35
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. (Airport Authority of India [AAI]) (701107)	Andhra Pradesh	06/2020 (09/2020)	09/2022 (12/2025)	611.8 (611.8)	494.08	81
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. (Airport Authority of India [AAI]) (701121)	Andhra Pradesh	12/2022 (08/2023)	08/2025 (12/2025)	347.15 (347.15)	95.46	54
4	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (11/2025)	1712 (1712)	2397.37	91
5	Development of New Civil Enclave at Bihta (Airport Authority of India [AAI]) (612183)	Bihar	08/2024 (03/2025)	09/2027 (-)	1413 (1413)	0	1
6	Development of New Civil Enclave and associated works at Darbhanga Airport (Airport Authority of India [AAI]) (612194)	Bihar	07/2024 (07/2024)	01/2026 (-)	911.66 (911.66)	191.27	32
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna (Airport Authority of India [AAI]) (701101)	Bihar	12/2018 (10/2018)	07/2023 (11/2025)	1216.9 (1216.9)	1119.69	94
8	Goa Airport Terminal Building Extension Project (Airport Authority of India [AAI]) (701105)	Goa	11/2017 (12/2019)	12/2021 (09/2025)	255.69 (255.69)	154.3	92
9	Development of Dholera International Greenfield Airport , Gujarat (Airport Authority of India [AAI]) (701126)	Gujarat	06/2022 (07/2022)	06/2026 (06/2026)	1305 (1551)	696.39	66
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. (Airport Authority of India [AAI]) (611047)	Jammu and Kashmir	07/2022 (07/2023)	06/2026 (06/2026)	861.37 (861.37)	192.59	36
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport (Airport Authority of India [AAI]) (612787)	Karnataka	06/2023 (01/2024)	01/2026 (03/2026)	320.47 (320.47)	71.37	41
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. (Airport Authority of India [AAI]) (612788)	Karnataka	06/2023 (02/2024)	01/2026 (01/2026)	322.45 (322.45)	132.01	55
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 (Airport Authority of India [AAI]) (612789)	Kerala	06/2023 (02/2024)	09/2025 (03/2026)	484.57 (484.57)	85.16	22
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh (Airport Authority of India [AAI]) (400010)	Ladakh	07/2018 (09/2018)	09/2021 (10/2025)	480 (640)	456.22	71
15	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	154.43	41
16	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, Jewar [earlier MOPA, without ASMGCS], HIAL & BIAL (Airport Authority of India [AAI]) (611570)	Multi-States (Karnataka, Maharashtra, Telangana, Uttar Pradesh)	NA (10/2022)	09/2025 (08/2026)	500.48 (500.48)	332.26	75
17	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. (Airport Authority of India [AAI]) (701127)	Rajasthan	05/2022 (04/2023)	11/2024 (10/2025)	480 (480)	301.83	89
18	Construction of New Integrated Passenger Terminal Building at Udaipur Airport (Airport Authority of India [AAI]) (701128)	Rajasthan	06/2023 (11/2022)	03/2026 (10/2026)	887 (887)	378.81	50
19	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	02/2026 (-)	323.26 (323.26)	34.3	13
20	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAI]) (611602)	Tamil Nadu	05/2018 (06/2023)	07/2025 (06/2026)	1207 (1207)	164.13	24
21	Construction of New Terminal Building, Second Link Taxi Track, Apron Expansion, and associated works at Prayagraj Airport- On Design & Build Basis. (Airport Authority of India [AAI]) (612063)	Uttar Pradesh	NA (08/2023)	11/2024 (08/2025)	219.18 (274.38)	215.2	100
22	Lucknow Airport-Terminal 3- Phase 1 & Other Associated Works (Adani Airport Holdings Limited) (701091)	Uttar Pradesh	06/2018 (09/2018)	03/2026 (-)	3100 (3100)	16024.42	100
23	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAI]) (701113)	Uttar Pradesh	07/2024 (07/2024)	07/2027 (07/2027)	2869.65 (2869.65)	346.36	17
24	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAI]) (701122)	Uttar Pradesh	06/2024 (07/2024)	07/2026 (-)	579 (579)	88.11	17
25	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAI]) (611495)	West Bengal	08/2024 (10/2023)	01/2027 (01/2027)	1549 (1549)	292.71	13

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
26	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCB Airport Kolkata. <i>(Airport Authority of India [AAI])</i> (612791)	West Bengal	04/2023 (12/2023)	02/2025 (08/2026)	328.3 (328.3)	105.41	47
	Total (26)				23049.84	24583.31	
	Ministry of Coal						
	Coal						
27	TIKAK EXTENSION OCP <i>(MIS MoCoal Integration Logins)</i> (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	81.47	0
28	TIRAP OCP <i>(MIS MoCoal Integration Logins)</i> (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.6	3
29	PORDA CHINTAPANI OCP [10 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400144)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	2310.12 (2310.12)	85.77	10
30	CHHAL OC SEAM III [6 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400145)	Chhattisgarh	12/2013 (12/2013)	03/2022 (10/2025)	610.63 (610.63)	579.82	85
31	KUSMUNDA OC EXPANSION [15 TO 50 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400147)	Chhattisgarh	08/2013 (08/2013)	03/2023 (03/2030)	7612.33 (7612.33)	4697.95	81
32	BAROUD OC EXPANSION [3.0-10.0M] <i>(South Eastern Coalfields Limited [SECL])</i> (400149)	Chhattisgarh	08/2020 (08/2020)	03/2029 (-)	2309.8 (2309.8)	935.64	50
33	DIPKA EXPANSION OCP [40 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400354)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	5241.4 (5241.4)	2830.43	37
34	GEVRA OC [70 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400424)	Chhattisgarh	03/2016 (03/2016)	03/2023 (03/2026)	11816.4 (11816.4)	6677.26	78
35	JAMPALI OC RCE [2.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613795)	Chhattisgarh	05/2020 (05/2020)	03/2025 (06/2025)	278.64 (278.64)	210.07	82
36	AMERA OC RCE [1.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613798)	Chhattisgarh	02/2015 (02/2015)	03/2026 (-)	335.97 (335.97)	88.24	42
37	AMGAON OC RCE [1.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613799)	Chhattisgarh	07/2015 (07/2015)	03/2026 (-)	316.11 (316.11)	188.6	78
38	JAGANNATHPUR OC RCE PROJECT <i>(South Eastern Coalfields Limited [SECL])</i> (613800)	Chhattisgarh	07/2016 (07/2016)	03/2025 (03/2026)	459.49 (459.49)	274.35	96
39	MAHAMAYA OCP [1.50 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613801)	Chhattisgarh	05/2018 (05/2018)	03/2026 (-)	410.26 (410.26)	181.59	54
40	KATKONA RO UG MINE <i>(South Eastern Coalfields Limited [SECL])</i> (615191)	Chhattisgarh	01/2023 (01/2023)	03/2029 (-)	329.21 (329.21)	60.81	2
41	PELMA OC MDO <i>(South Eastern Coalfields Limited [SECL])</i> (616234)	Chhattisgarh	10/2022 (10/2022)	03/2033 (-)	1725.04 (1725.04)	15.66	40
42	KUSMUNDA OC EXPANSION PROJECT <i>(SECL - CIL)</i> (617287)	Chhattisgarh	11/2024 (11/2024)	03/2030 (-)	4516.88 (4516.88)	774.91	21
43	MANIKPUR OC EXPANSION PROJECT <i>(South Eastern Coalfields Limited [SECL])</i> (617288)	Chhattisgarh	01/2025 (01/2025)	03/2029 (-)	382.61 (382.61)	112.87	21
44	DIPKA OC <i>(SECL - CIL)</i> (612838)	Gujarat	NA (01/2017)	03/2025 (-)	7580 (7580)	3091	65
45	HURA C OCP <i>(ECL - CIL)</i> (400018)	Jharkhand	08/2022 (08/2022)	03/2029 (-)	859.41 (859.41)	451.61	62
46	KONAR EXPANSION OCP <i>(Ministry of Coal)</i> (400073)	Jharkhand	01/2022 (01/2022)	03/2032 (-)	799.34 (799.34)	429.42	45
47	KARO EXPANSION OCP <i>(Ministry of Coal)</i> (400074)	Jharkhand	01/2022 (01/2022)	03/2029 (-)	908.47 (908.47)	269.18	22
48	SANGHMITRA OC <i>(Ministry of Coal)</i> (400136)	Jharkhand	03/2024 (03/2027)	03/2032 (-)	2660 (2660)	0	0
49	CHANDRAGUPT OCP <i>(Ministry of Coal)</i> (400138)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	973.5 (973.5)	440.56	24
50	KOTRE BASANTPUR PACHMO OCP <i>(Ministry of Coal)</i> (400139)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	861.06 (625.4)	455.95	42
51	Pachwara South Coal Block <i>(NLC India Limited [NLCIL])</i> (400142)	Jharkhand	03/2016 (11/2019)	09/2028 (-)	2242.9 (2242.9)	1186.18	74
52	RPR MAGADH EXP OCP <i>(Ministry of Coal)</i> (400150)	Jharkhand	08/2020 (08/2020)	03/2028 (-)	7254.37 (7254.37)	1548.41	38
53	NORTH URIMARI EXPANSION OCP <i>(Ministry of Coal)</i> (400151)	Jharkhand	07/2021 (07/2021)	03/2029 (-)	778.8 (778.8)	696.05	67
54	EPR ROHINI - KARKETTA OCP <i>(Central Coalfields Limited [CCL])</i> (400153)	Jharkhand	01/2021 (01/2021)	03/2028 (-)	1020.42 (1020.42)	83.95	20

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
55	EPR PUNDI OCP (Ministry of Coal) (400154)	Jharkhand	11/2020 (11/2020)	03/2027 (-)	713.35 (713.35)	236.58	10
56	EPR ASHOK OC (Ministry of Coal) (400155)	Jharkhand	05/2021 (05/2021)	03/2031 (-)	2898.28 (2898.28)	179.7	24
57	EPR AMRAPALI OCP (Ministry of Coal) (400156)	Jharkhand	02/2020 (02/2020)	03/2028 (-)	5136.15 (5136.15)	1159.17	42
58	RAJRAPPA RCE OCP (Ministry of Coal) (400160)	Jharkhand	12/2009 (12/2009)	03/2016 (03/2027)	510.85 (510.85)	488.67	76
59	CHITRA EAST OC (Eastern Coal Fields Limited [ECL]) (400172)	Jharkhand	08/2018 (08/2018)	03/2026 (-)	513.99 (513.99)	229.01	51
60	JHARKHAND-LAIYO OCP (Ministry of Coal) (400352)	Jharkhand	08/2020 (08/2020)	03/2031 (-)	764.57 (764.57)	145.81	29
61	MOONIDIH XV SEAM UG (Ministry of Coal) (400425)	Jharkhand	08/2011 (08/2011)	03/2019 (05/2026)	1230.27 (1230.27)	629.58	81
62	2.5 MTPA PATHERDIH NLW WASHERY (Ministry of Coal) (611017)	Jharkhand	10/2015 (04/2016)	04/2018 (03/2026)	334.27 (334.27)	142.64	48
63	AMALAGAMATED NTST KUJAMA OCP 8.5MTY (Ministry of Coal) (611864)	Jharkhand	01/2023 (01/2023)	03/2030 (-)	4011.85 (4011.85)	404.49	28
64	MURAIIDH UG PROJECT (Ministry of Coal) (613808)	Jharkhand	02/2011 (02/2011)	04/2014 (12/2026)	339.87 (339.87)	191	70
65	TAPIN SOUTH EXPN (Ministry of Coal) (615349)	Jharkhand	11/2020 (11/2020)	03/2028 (-)	230.41 (230.41)	22.02	20
66	SIRKA OC (Ministry of Coal) (615822)	Jharkhand	05/2020 (05/2020)	03/2028 (-)	222.82 (222.82)	140.58	53
67	TETARIAKHAR OC (Ministry of Coal) (615843)	Jharkhand	11/2019 (11/2019)	03/2025 (03/2027)	243.52 (243.52)	44.64	29
68	CHUPERBHITA SIMLONG OCP MDO 6 MTY (Eastern Coal Fields Limited [ECL]) (616225)	Jharkhand	12/2023 (12/2023)	03/2037 (-)	979.08 (979.08)	0	0
69	JARANGDIH EXPN. OCP 1.5 MTY (CCL - CIL) (616236)	Jharkhand	02/2020 (02/2020)	03/2029 (-)	414.37 (414.37)	85.6	32
70	BLOCK E OCP (Ministry of Coal) (616253)	Jharkhand	03/2024 (03/2024)	03/2029 (-)	5850.83 (5850.83)	20.32	3
71	Revised Jharia Master Plan for Dealing with Fire, Subsidence & Rehabilitation of affected families in Jharia Coalfield- Reg. (Bharat Coking Coal Limited [BCCL]) (617416)	Jharkhand	06/2025 (07/2025)	12/2028 (-)	5940.47 (5940.47)	0	6
72	AMADAND OCP[4.0MTY] (Ministry of Coal) (400148)	Madhya Pradesh	03/2016 (03/2016)	03/2021 (03/2027)	869.44 (869.44)	275.35	75
73	RAMPUR BATURA OCP [4.0MTY] (South Eastern Coalfields Limited [SECL]) (400152)	Madhya Pradesh	07/2019 (07/2019)	03/2026 (-)	1248.93 (1248.93)	495.4	44
74	BLOCK B EXPANSION [3.5 TO 8.0 (Northern Coalfields Limited [NCL]) (400162)	Madhya Pradesh	07/2019 (07/2019)	03/2023 (03/2027)	998.71 (998.71)	468.13	47
75	NIGAH I EXPANSION [15 TO 25 MTP (Northern Coalfields Limited [NCL]) (400321)	Madhya Pradesh	11/2020 (11/2020)	03/2025 (03/2028)	1729.68 (1729.68)	827.47	47
76	KANCHAN OC EXP (South Eastern Coalfields Limited [SECL]) (613802)	Madhya Pradesh	12/2014 (12/2014)	03/2026 (-)	371.04 (371.04)	144.61	58
77	JHIRIA WEST OCP [1.5 MTY] (South Eastern Coalfields Limited [SECL]) (613803)	Madhya Pradesh	01/2024 (01/2024)	03/2029 (-)	366.94 (366.94)	34.06	41
78	RPR TAWA-III UG 0.84 MTY (Western Coalfields Limited [WCL]) (613804)	Madhya Pradesh	12/2021 (12/2021)	03/2027 (-)	314.09 (314.09)	5.87	17
79	AMALGAMATED DHANKASA & JAMUNIA (Western Coalfields Limited [WCL]) (615185)	Madhya Pradesh	09/2022 (09/2022)	03/2027 (-)	399.2 (399.2)	92.44	66
80	RPR OF VISHNUPURI UG TO OC (Western Coalfields Limited [WCL]) (615187)	Madhya Pradesh	11/2022 (11/2022)	03/2029 (-)	220.62 (220.62)	0	11
81	URDHAN EXPANSION OC COST PLUS (Western Coalfields Limited [WCL]) (615194)	Madhya Pradesh	07/2022 (01/2023)	03/2031 (-)	206.88 (206.88)	27.19	0
82	SHARDA UG MINE (Western Coalfields Limited [WCL]) (615195)	Madhya Pradesh	07/2022 (09/2023)	03/2028 (-)	166.25 (166.25)	4.35	9
83	GANDHIGRAM UG MINE (Western Coalfields Limited [WCL]) (615206)	Madhya Pradesh	08/2019 (08/2019)	03/2026 (-)	414.15 (414.15)	13.38	57
84	BHATADI EXPANSION OC (Western Coalfields Limited [WCL]) (400033)	Maharashtra	02/2020 (05/2022)	03/2028 (-)	580.61 (580.61)	69.77	28
85	AMALGAMATED YEKONA I & YEKONA (Western Coalfields Limited [WCL]) (400177)	Maharashtra	08/2015 (08/2015)	03/2025 (03/2026)	727.28 (727.28)	538.4	80



All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
86	DINESH[MAKARDHOKRA-III] OC (<i>Western Coalfields Limited [WCL]</i>) (400178)	Maharashtra	02/2020 (02/2020)	03/2027 (-)	822.88 (822.88)	621.73	35
87	DHUPTALA OC [SASTI UG TO OC] (<i>Western Coalfields Limited [WCL]</i>) (400353)	Maharashtra	10/2021 (10/2021)	03/2028 (-)	711.01 (711.01)	80.61	17
88	SAONER UG MINE -1 EXPANSION 1. (<i>Western Coalfields Limited [WCL]</i>) (615184)	Maharashtra	01/2022 (01/2022)	03/2028 (-)	228.64 (228.64)	142.4	68
89	SASTI EXPANSION OPENCAST (<i>Western Coalfields Limited [WCL]</i>) (615186)	Maharashtra	08/2020 (08/2020)	03/2026 (-)	319.04 (319.04)	90.31	20
90	NEW MAJRI UG TO OC 3 MTY COST (<i>Western Coalfields Limited [WCL]</i>) (615188)	Maharashtra	05/2019 (09/2022)	03/2027 (-)	402.27 (402.27)	55.44	24
91	MAKARDHOKRA EXPN OC 4.9 MTY (<i>Western Coalfields Limited [WCL]</i>) (615189)	Maharashtra	06/2022 (06/2022)	03/2026 (-)	361.87 (361.87)	70.22	11
92	SINGHORI DEEP OC MIN 2.0 MTY (<i>Western Coalfields Limited [WCL]</i>) (615190)	Maharashtra	05/2022 (05/2022)	03/2029 (-)	335.75 (335.75)	26.98	6
93	GOKUL EXTENSION OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615192)	Maharashtra	04/2021 (04/2021)	03/2026 (-)	309.58 (309.58)	42.75	8
94	KOLGAON EXPANSION DEEP OC MINE 0.80 MTY (<i>Western Coalfields Limited [WCL]</i>) (615199)	Maharashtra	01/2023 (09/2023)	03/2027 (-)	198.71 (198.71)	0.71	2
95	BALLARPUR NORTH WEST OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615330)	Maharashtra	12/2022 (12/2022)	03/2029 (-)	360.81 (360.81)	0.02	4
96	GADEGAON OC 3 MTY (<i>Western Coalfields Limited [WCL]</i>) (615331)	Maharashtra	10/2023 (10/2023)	03/2030 (-)	497.41 (497.41)	0.08	0
97	GHONSA EXPANSION DEEP OC MINE (<i>Western Coalfields Limited [WCL]</i>) (615914)	Maharashtra	03/2021 (03/2021)	03/2029 (-)	184.71 (184.71)	11.48	5
98	AMLG GAURI PAUNI EXPANSION OC (<i>Western Coalfields Limited [WCL]</i>) (615916)	Maharashtra	04/2024 (04/2024)	03/2030 (-)	1225.21 (1225.21)	78.68	1
99	GAURIDEEP/GAURI CENTRAL OCP 7. (<i>Western Coalfields Limited [WCL]</i>) (615917)	Maharashtra	08/2023 (06/2024)	03/2030 (-)	973.07 (973.07)	0.24	0
100	RPR OF BHANEGAON OC (<i>Western Coalfields Limited [WCL]</i>) (615918)	Maharashtra	02/2017 (09/2022)	03/2028 (-)	405.2 (405.2)	12.36	7
101	N. EXTN. MUNGOLI NIRGUDA D OCP (<i>Western Coalfields Limited [WCL]</i>) (615919)	Maharashtra	06/2024 (06/2024)	03/2029 (-)	1024.91 (1024.91)	169.91	0
102	NILJAI EXPANSION DEEP OCP (<i>Western Coalfields Limited [WCL]</i>) (615982)	Maharashtra	08/2016 (11/2018)	03/2024 (03/2026)	319.75 (319.75)	367.6	79
103	UKNI DEEP OC MINE -COST PLUS (<i>Western Coalfields Limited [WCL]</i>) (616044)	Maharashtra	11/2018 (01/2019)	03/2021 (03/2026)	237.06 (237.06)	165.57	87
104	AMALGAMATED INDER-KAMPTEE DEEP OC (<i>Western Coalfields Limited [WCL]</i>) (616050)	Maharashtra	09/2018 (09/2018)	03/2024 (03/2026)	235.9 (235.9)	237.12	98
105	ADASA UG TO OC MINE (<i>Western Coalfields Limited [WCL]</i>) (616223)	Maharashtra	11/2018 (11/2018)	03/2024 (03/2026)	316 (316)	308.84	86
106	AMAL GONDEGAON GHATROHANA EXPN (<i>Western Coalfields Limited [WCL]</i>) (616229)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	668.54 (668.54)	1.21	0
107	WAGHODA UG MINE [1.02 MTY] (<i>Western Coalfields Limited [WCL]</i>) (617233)	Maharashtra	01/2024 (01/2025)	03/2030 (-)	379.3 (379.3)	0	0
108	KOLARPIMPRI EXPANSION OC [2.5 MTY] (<i>Western Coalfields Limited [WCL]</i>) (617278)	Maharashtra	06/2024 (02/2025)	03/2030 (-)	630.37 (630.37)	0	0
109	Master Plan for Jharia and Raniganj Coalfields (<i>Bharat Coking Coal Limited [BCLL]</i>) (400313)	Multi-States (Jharkhand, West Bengal)	08/2009 (08/2009)	08/2019 (12/2028)	2661.73 (2661.73)	789.85	43
110	BINA KAKRI AMALGAMATION EXPANS (<i>Northern Coalfields Limited [NCL]</i>) (400369)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020 (08/2020)	03/2024 (03/2027)	836.42 (836.42)	805.98	89
111	KHADIA EXPANSION [10 TO 16 MTP (<i>Northern Coalfields Limited [NCL]</i>) (615183)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021 (06/2021)	03/2025 (03/2027)	491.67 (491.67)	236.02	46
112	SUBHADRA OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400165)	Odisha	05/2021 (05/2021)	04/2032 (-)	1693.81 (1693.81)	1323.54	42
113	SIARMAL OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400166)	Odisha	02/2021 (02/2021)	03/2029 (-)	5194.95 (5194.95)	3456.71	55
114	BALARAM EXPANSION OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400183)	Odisha	06/2020 (08/2020)	03/2029 (-)	3504.21 (3504.21)	774.52	53
115	GOPALJI KANIHA OCP [10 TO 30 M (<i>MCL - CIL</i>) (400185)	Odisha	04/2022 (04/2022)	03/2030 (-)	8416.19 (6107.87)	1730.11	17
116	INTEGRATED LAKHANPUR-BELPAHAR- (<i>Mahanadi Coalfields Limited [MCL]</i>) (400187)	Odisha	05/2018 (05/2018)	03/2027 (-)	2434.75 (2434.75)	1814.65	69

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
117	BHARATPUR RE-ORGANIZATION OCP (<i>Mahanadi Coalfields Limited [MCL]</i>) (400392)	Odisha	11/2018 (11/2018)	03/2029 (-)	2838.86 (2838.86)	1672.82	47
118	BASUNDHARA WEST EXTENSION OPEN (<i>MCL - CIL</i>) (615193)	Odisha	05/2014 (05/2014)	03/2019 (03/2029)	479.15 (479.15)	273.75	64
119	Naini Coal Mine (<i>Singareni Collieries Company Limited [SCCL]</i>) (615857)	Odisha	03/2020 (03/2020)	03/2026 (-)	494.3 (494.3)	491.33	80
120	INTEGRATED KULDA GARJANBAHAL O (<i>Mahanadi Coalfields Limited [MCL]</i>) (616226)	Odisha	04/2023 (04/2023)	03/2033 (-)	3563.5 (3563.5)	568.54	3
121	BHUBANESWARI EXPN OCP 50 MTY (<i>MCL - CIL</i>) (616231)	Odisha	03/2024 (03/2024)	03/2033 (-)	5366.27 (5366.27)	466.03	14
122	HINGULA II OC EXPN PH III 15 M (<i>MCL - CIL</i>) (616232)	Odisha	11/2022 (11/2022)	03/2029 (-)	1561.85 (1561.85)	271.74	24
123	BALABHADRA OCP (<i>MCL - CIL</i>) (616233)	Odisha	04/2023 (04/2023)	03/2030 (-)	978.44 (978.44)	211.37	11
124	Jawahar Khani Open Cast Mine (<i>Singareni Collieries Company Limited [SCCL]</i>) (615818)	Telangana	12/2021 (12/2021)	03/2025 (03/2027)	297.88 (297.88)	46.82	20
125	Kalyanikhani Opencast Project (<i>Singareni Collieries Company Limited [SCCL]</i>) (615858)	Telangana	03/2016 (05/2017)	03/2026 (-)	384.32 (384.32)	281.83	75
126	Kakathiya Khani Opencast - III Project Phase - I (<i>Singareni Collieries Company Limited [SCCL]</i>) (615859)	Telangana	03/2017 (05/2017)	03/2026 (-)	413.84 (413.84)	397.55	79
127	Godavarikhani Coal Mine - 5 (<i>Singareni Collieries Company Limited [SCCL]</i>) (615860)	Telangana	07/2019 (05/2019)	03/2025 (03/2026)	607.04 (607.04)	191.08	71
128	Indaram Opencast Project (<i>Singareni Collieries Company Limited [SCCL]</i>) (615861)	Telangana	08/2017 (12/2022)	03/2025 (03/2026)	424.81 (424.81)	402.64	80
129	Goleti Opencast Mine (<i>Singareni Collieries Company Limited [SCCL]</i>) (615862)	Telangana	07/2021 (08/2021)	03/2026 (-)	345.6 (345.6)	75.87	21
130	Venkatesh Khani Coal Mine (<i>Singareni Collieries Company Limited [SCCL]</i>) (615863)	Telangana	10/2020 (06/2020)	03/2026 (-)	484.5 (484.5)	466.62	96
131	Ramagundam OC-II Extension Project (<i>Singareni Collieries Company Limited [SCCL]</i>) (615864)	Telangana	11/2015 (06/2015)	03/2026 (-)	489.62 (489.62)	405.54	77
132	Kakatiyakhani OC - 2 Project (<i>Singareni Collieries Company Limited [SCCL]</i>) (615865)	Telangana	08/2017 (09/2017)	03/2025 (03/2026)	442.42 (442.42)	205.79	63
133	MOHANPUR EXPANSION OC -PHASE II (<i>Eastern Coal Fields Limited [ECL]</i>) (400173)	West Bengal	11/2020 (11/2020)	03/2026 (-)	888.99 (888.99)	108.25	30
134	BONJEMEHARI EXPANSION OCP (<i>Eastern Coal Fields Limited [ECL]</i>) (400180)	West Bengal	08/2021 (08/2021)	03/2026 (03/2026)	570.11 (570.11)	81.9	16
135	NAKRAKONDA KUMARDIH- B OCP (<i>Eastern Coal Fields Limited [ECL]</i>) (400181)	West Bengal	08/2018 (08/2018)	03/2029 (-)	502.68 (502.67)	67.68	26
136	SIDULI [OC & UG] (<i>ECL - CIL</i>) (400182)	West Bengal	05/2018 (05/2018)	03/2027 (-)	535.18 (535.17)	5.27	14
137	TILABONI UG (<i>Eastern Coal Fields Limited [ECL]</i>) (400186)	West Bengal	01/2023 (03/2023)	03/2029 (03/2029)	749.08 (749.08)	52.18	10
138	JHANJRA EXPANSION UG (<i>Eastern Coal Fields Limited [ECL]</i>) (400312)	West Bengal	04/2020 (04/2020)	03/2029 (-)	1210.12 (1210.12)	534.84	44
139	SONEPUR BAZARI EXPANSION OCP [12 MTY] (<i>Eastern Coal Fields Limited [ECL]</i>) (400315)	West Bengal	07/2021 (07/2021)	03/2029 (-)	5365.88 (5365.88)	570.02	17
140	2.0 MTPA BHOJUDIH NLW WASHERY (<i>Ministry of Coal</i>) (611016)	West Bengal	12/2015 (03/2019)	09/2020 (11/2025)	384.57 (384.57)	354.75	97
141	ITAPARA OCP (<i>Eastern Coal Fields Limited [ECL]</i>) (612816)	West Bengal	12/2023 (12/2023)	03/2030 (-)	929.1 (929.1)	68.14	7
142	SHYAMSUNDARPUR UG INCLUDING SA (<i>Eastern Coal Fields Limited [ECL]</i>) (613793)	West Bengal	04/2020 (04/2020)	03/2026 (-)	483.65 (483.65)	59.03	12
143	PARASEA-BELBAID UG PROJECT (<i>Eastern Coal Fields Limited [ECL]</i>) (613794)	West Bengal	01/2023 (01/2023)	03/2028 (-)	389.1 (389.1)	131.42	17
144	PARASCOLE JAMBAD OCP (<i>Eastern Coal Fields Limited [ECL]</i>) (616230)	West Bengal	11/2024 (11/2024)	03/2037 (-)	1193.55 (1193.55)	9.52	0
Total (118)					172747.29	55557.54	
Electricity Generation							
145	50 MW Wind Power Project (<i>NLC India Limited [NLCIL]</i>) (617299)	Gujarat	07/2022 (01/2024)	06/2025 (01/2026)	383.84 (383.84)	303.5	41
146	NLC Talabira Thermal Power Project (<i>NLC India Limited [NLCIL]</i>) (400231)	Odisha	01/2017 (01/2024)	03/2030 (-)	27212.96 (27213)	2517.13	1

All Ongoing Projects

SEPTEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
147	300 MW SPP part of 510 MW CPSU scheme <i>(NLC India Limited [NLCIL])</i> (612819)	Rajasthan	07/2022 (03/2023)	09/2024 (12/2025)	1813 (1813)	1038.13	79
148	50 MW Solar PP Minedout Area <i>(NLC India Limited [NLCIL])</i> (615327)	Tamil Nadu	08/2023 (02/2024)	03/2025 (12/2025)	218.03 (218.03)	161.73	64
149	Ghatampur Thermal Power Plant 3 X 660 MW <i>(NLC India Limited [NLCIL])</i> (400259)	Uttar Pradesh	07/2015 (02/2016)	11/2020 (12/2025)	17237.8 (21780.9)	20510.47	92
	Total (5)				46865.63	24530.96	
	Railways						
150	Dharamjaigarh-Korba <i>(Railway)</i> (400203)	Chhattisgarh	05/2018 (03/2017)	12/2026 (08/2026)	1686.22 (1686.22)	350.21	41
151	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] <i>(Ministry of Coal)</i> (400416)	Jharkhand	02/2018 (05/2022)	06/2025 (06/2026)	1799.64 (2564.34)	1462.35	61
	Total (2)				3485.86	1812.56	
	Ministry of Power						
	Coal						
152	Tubed Coal Mine <i>(Damodar Valley Corporation)</i> (400192)	Jharkhand	07/2016 (10/2016)	05/2026 (05/2026)	1581 (1581)	597.5	35
153	Badam Coal Mining project of NTPC <i>(National Thermal Power Corporation [NTPC])</i> (603293)	Jharkhand	02/2019 (09/2019)	12/2056 (04/2027)	502 (784)	313.88	59
	Total (2)				2083	911.38	
	Electricity Generation						
154	Dibang Multipurpose Project <i>(National Hydroelectric Power Corporation Limited [NHPC])</i> (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	3639.39	16
155	240MW Heo HE Project <i>(North Eastern Electric Power Corporation Limited)</i> (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	49.69	3
156	186 MW Tato-I H E Project <i>(North Eastern Electric Power Corporation Limited)</i> (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	116.08	2
157	Buxar Thermal Power Project [1320 MW] <i>(Satluj Jal Vidyut Nigam [SJVN] Thermal Limited)</i> (602579)	Bihar	03/2019 (06/2019)	01/2024 (12/2025)	10439.09 (13756.6)	12426.32	92
158	Lara Super Thermal Power Project Stage-II [2 x 800 MW] <i>(National Thermal Power Corporation [NTPC])</i> (611930)	Chhattisgarh	08/2023 (08/2023)	06/2028 (-)	15530 (15530)	2812	15
159	Sipat Super Thermal Power Project, Stage-III [1x800 MW] <i>(National Thermal Power Corporation [NTPC])</i> (617188)	Chhattisgarh	09/2024 (09/2024)	09/2029 (-)	9791 (9791)	865.06	8
160	Bagodara Solar Power Project <i>(Satluj Jal Vidyut Nigam [SJVN] Thermal Limited)</i> (709747)	Gujarat	03/2021 (05/2021)	12/2025 (12/2025)	339.35 (339.35)	317.59	51
161	Dhaulasidh Hydro Electric Project [66 MW] <i>(Satluj Jal Vidyut Nigam [SJVN] Thermal Limited)</i> (602582)	Himachal Pradesh	10/2020 (05/2021)	11/2025 (03/2027)	687.97 (1511.87)	949.59	68
162	Luhri Stage-I Hydro Electric Project [210 MW] <i>(Satluj Jal Vidyut Nigam [SJVN] Thermal Limited)</i> (602593)	Himachal Pradesh	11/2020 (11/2020)	01/2026 (10/2029)	1810.56 (3584.53)	1781.54	51
163	382 MW Sunni Dam HEP <i>(Satluj Jal Vidyut Nigam [SJVN] Thermal Limited)</i> (602633)	Himachal Pradesh	NA (04/2018)	03/2027 (-)	2615 (2615)	495.57	0.5
164	Sunni Dam Hydro Electric Project [382 MW] <i>(Satluj Jal Vidyut Nigam [SJVN] Thermal Limited)</i> (611586)	Himachal Pradesh	01/2023 (01/2023)	04/2028 (12/2029)	2614.51 (4540.71)	970.01	30
165	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW <i>(National Hydroelectric Power Corporation Limited [NHPC])</i> (602525)	Jammu and Kashmir	10/2014 (02/2018)	04/2020 (12/2026)	8112.12 (12728)	7457.57	73
166	Kiru HE Project <i>(National Hydroelectric Power Corporation Limited [NHPC])</i> (602532)	Jammu and Kashmir	03/2019 (02/2020)	09/2023 (12/2026)	4287.59 (5409)	3035.03	70
167	Rattle HE Project - 850 MW, Rattle Hydroelectric Power Corporation Limited. <i>(National Hydroelectric Power Corporation Limited [NHPC])</i> (602535)	Jammu and Kashmir	02/2021 (01/2022)	02/2026 (08/2029)	5281.94 (5281.94)	1029.67	24
168	Kwar HE Project <i>(National Hydroelectric Power Corporation Limited [NHPC])</i> (605155)	Jammu and Kashmir	05/2022 (11/2022)	11/2026 (03/2028)	4526.12 (4526.12)	1156.37	24
169	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] <i>(National Thermal Power Corporation [NTPC])</i> (400261)	Jharkhand	07/2017 (11/2017)	03/2023 (11/2026)	17112 (20302)	17860	85
170	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand <i>(Damodar Valley Corporation)</i> (611509)	Jharkhand	04/2023 (11/2024)	03/2029 (-)	14358 (14358)	1255.79	3
171	Subansiri Lower HE Project [2000 MW] <i>(National Hydroelectric Power Corporation Limited [NHPC])</i> (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	25058.77	96
172	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion <i>(National Thermal Power Corporation [NTPC])</i> (602961)	Odisha	08/2022 (09/2022)	05/2027 (03/2028)	11843.75 (12543)	4574.68	34
173	BIKANER SOLAR POWER PROJECT <i>(Satluj Jal Vidyut Nigam [SJVN] Thermal Limited)</i> (709748)	Rajasthan	10/2021 (05/2022)	04/2024 (12/2025)	5491.89 (5491.89)	5009.15	86

All Ongoing Projects							SEPTEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
174	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	4656.92	69
175	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] -A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (12/2025)	938.29 (1828.11)	1445.5	93
176	Khurja super Thermal Power Plant [2X660 MW] (THDC India Limited) (602194)	Uttar Pradesh	03/2019 (08/2019)	02/2024 (09/2025)	11089.42 (13276.2)	12888.23	100
177	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] (National Thermal Power Corporation [NTPC]) (612142)	Uttar Pradesh	03/2024 (03/2024)	02/2030 (-)	17195 (17195)	1916	10
178	Tapovan-Vishnugad HEP [4x130 MW] (National Thermal Power Corporation [NTPC]) (602185)	Uttarakhand	11/2006 (11/2006)	03/2013 (04/2029)	2978 (10907.3)	7260.25	77
179	Tehri Pumped Storage Plant Project [4x250 MW] (THDC India Limited) (602193)	Uttarakhand	07/2006 (06/2011)	06/2022 (11/2025)	4825.6 (8339)	8121.61	98
180	Vishnugad Pipalkoti Hydro Electric Project [444 MW] (THDC India Limited) (602195)	Uttarakhand	08/2008 (01/2014)	12/2022 (03/2027)	3860.35 (6823.72)	5186.68	72
181	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal (Damodar Valley Corporation) (400062)	West Bengal	01/2023 (02/2025)	06/2029 (-)	17673 (17673)	1372.17	2
182	Rammam-III HEPP [3x40 MW] (National Thermal Power Corporation [NTPC]) (602184)	West Bengal	10/2014 (09/2014)	09/2019 (03/2029)	1381.84 (1381.84)	1303.42	47
183	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 (Damodar Valley Corporation) (602538)	West Bengal	06/2019 (02/2021)	01/2024 (12/2025)	1037 (1106)	1098.16	92
	Total (30)				223418.07	136108.81	
	Transmission & Distribution						
184	Transmission Scheme for Solar Energy Zone in Ananthpuram 2500MW and Kurnool 1000MW (Power Grid Corporation of India Limited [POWERGRID]) (611967)	Andhra Pradesh	09/2023 (09/2023)	09/2025 (03/2026)	1248.69 (1248.69)	924.03	84
185	Augmentation of 1x1500 MVA 3rd 765/400 kV transformation capacity at Kurnool New Substation (Power Grid Corporation of India Limited [POWERGRID]) (612856)	Andhra Pradesh	05/2023 (12/2023)	09/2025 (01/2026)	163.61 (163.61)	71.98	56
186	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617183)	Andhra Pradesh	03/2025 (03/2025)	12/2027 (-)	2886 (2886)	129.86	0
187	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	0.02	0
188	Western Region Expansion Scheme-XXV (Power Grid Corporation of India Limited [POWERGRID]) (611737)	Chhattisgarh	02/2023 (02/2023)	11/2023 (12/2025)	385.84 (385.84)	378.74	97
189	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan 8.1 GW under Phase II- Part- G1 (Power Grid Corporation of India Limited [POWERGRID]) (608301)	Delhi	02/2022 (02/2022)	09/2023 (11/2025)	359.47 (359.47)	336.11	94
190	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part B (Power Grid Corporation of India Limited [POWERGRID]) (611656)	Gujarat	03/2023 (03/2023)	03/2025 (10/2025)	1167.55 (1167)	1105.5	94
191	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part C (Power Grid Corporation of India Limited [POWERGRID]) (611657)	Gujarat	03/2023 (03/2023)	03/2025 (11/2025)	2820.99 (2820.99)	2639.03	90
192	Establishment of Khavda Pooling Station-2 KPS2 in Khavda RE Park KPS2 TRANSMISSION SYSTEM LIMITED (Power Grid Corporation of India Limited [POWERGRID]) (611660)	Gujarat	03/2023 (03/2023)	12/2024 (10/2025)	966.79 (966.79)	911.97	96
193	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (612139)	Gujarat	12/2023 (12/2023)	12/2025 (12/2026)	3751.82 (3751.82)	1688.32	25
194	Transmission System for Evacuation of Power from potential Renewable Energy zone in Khavda Area of Gujarat under Phase IV [7 GW] Part E3 (Power Grid Corporation of India Limited [POWERGRID]) (612151)	Gujarat	07/2023 (07/2023)	07/2025 (12/2025)	334 (334)	93.52	33
195	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (612855)	Gujarat	05/2024 (05/2024)	05/2026 (06/2026)	679 (679)	101.85	24
196	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615342)	Gujarat	10/2024 (10/2024)	07/2026 (-)	329 (329)	10.17	2
197	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] (Power Grid Corporation of India Limited [POWERGRID]) (615343)	Gujarat	11/2024 (11/2024)	11/2026 (-)	501 (501)	6.11	1
198	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345)	Gujarat	10/2024 (10/2024)	10/2026 (03/2027)	4766 (4766)	667.24	8

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
199	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069)	Gujarat	02/2025 (02/2025)	02/2027 (-)	466 (466)	23.3	1
200	Augmentation of Banaskantha [Raghanesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182)	Gujarat	03/2025 (03/2025)	03/2027 (-)	172 (172)	7.37	3
201	Augmentation of Transformation Capacity at Bhuj-II PS [GIS] (Power Grid Corporation of India Limited [POWERGRID]) (617391)	Gujarat	02/2025 (02/2025)	11/2026 (03/2027)	488.29 (488.29)	0.11	0
202	Jamnagar Transmission Limited (Adani Transmission Limited) (617405)	Gujarat	NA (10/2024)	10/2026 (-)	4000 (4000)	0	0
203	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272)	Haryana	06/2024 (06/2024)	12/2026 (-)	370 (370)	5.55	1
204	Transmission system for evacuation of Power from Pakaldul HEP in Chenab Valley HEPs - LTA System (Power Grid Corporation of India Limited [POWERGRID]) (608302)	Jammu and Kashmir	02/2022 (02/2022)	04/2025 (09/2025)	318.12 (318.12)	308.58	99
205	Transmission Scheme for evacuation of Power from Ratle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179)	Jammu and Kashmir	07/2024 (07/2024)	07/2026 (03/2027)	218.6 (218.6)	1.01	0
206	Implementation of Transmission Systems in the State of Jharkhand consisting of 400/220/132/33 kV transmission lines and substations under Jharkhand Consultancy Project (Power Grid Corporation of India Limited [POWERGRID]) (617326)	Jharkhand	02/2012 (02/2012)	03/2026 (-)	1842.25 (1842.25)	1643	95
207	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140)	Karnataka	12/2023 (12/2023)	12/2025 (03/2026)	2889.39 (2889.39)	1462.89	50
208	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672)	Karnataka	01/2025 (01/2025)	06/2027 (-)	1354 (1354)	18.14	0
209	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068)	Karnataka	02/2025 (02/2025)	06/2027 (-)	288 (288)	6.89	0
210	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184)	Karnataka	03/2025 (03/2025)	09/2027 (-)	3453 (3453)	47.99	0
211	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344)	Madhya Pradesh	10/2024 (10/2024)	10/2026 (03/2027)	3674 (3674)	551.1	14
212	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346)	Madhya Pradesh	08/2024 (08/2024)	08/2026 (12/2026)	2708 (2708)	920.72	37
213	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279)	Madhya Pradesh	06/2025 (06/2025)	12/2027 (-)	558 (558)	27.9	0
214	Transmission System for Evacuation of power from Potential RE Zone in Khavda Area of Gujarat under phase IV 7GW-Part E4 (Power Grid Corporation of India Limited [POWERGRID]) (611966)	Maharashtra	11/2023 (11/2023)	07/2025 (12/2025)	224.41 (224.41)	25.8	12
215	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185)	Multi-States (Andhra Pradesh, Karnataka)	03/2025 (03/2025)	03/2027 (-)	5550 (5550)	319.68	0
216	Transmission System for Kurnool Wind Energy Zone/ Solar Energy Zone Part-A and Part-B (Power Grid Corporation of India Limited [POWERGRID]) (900808)	Multi-States (Andhra Pradesh, Telangana)	11/2022 (03/2023)	11/2024 (12/2025)	3546.94 (3546.94)	3263.18	96
217	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	7598.33	82
218	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (12/2025)	5111.33 (6700)	5295.68	96
219	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271)	Multi-States (Bihar, Odisha, West Bengal)	09/2024 (09/2024)	03/2026 (06/2026)	342.69 (342.69)	0.7	0
220	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270)	Multi-States (Bihar, West Bengal)	11/2024 (11/2024)	05/2026 (03/2027)	408.94 (408.94)	0.31	0

All Ongoing Projects

SEPTEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
221	Transmission Network Expansion in Gujarat to increase its ATC from ISTS Part B (Power Grid Corporation of India Limited [POWERGRID]) (400005)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	01/2022 (07/2022)	06/2023 (12/2025)	4546.26 (4546.26)	4210.29	93
222	Transmission System Strengthening Scheme for evacuation of power from SEZ in Rajasthan 8.1 GW under Phase II Part G (Power Grid Corporation of India Limited [POWERGRID]) (608922)	Multi-States (Delhi, Haryana, Rajasthan)	05/2022 (05/2022)	11/2023 (11/2025)	1666 (2218)	2129.28	95
223	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735)	Multi-States (Delhi, Rajasthan)	12/2022 (12/2022)	03/2025 (04/2026)	331 (331)	129.09	30
224	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132)	Multi-States (Delhi, Rajasthan)	02/2024 (02/2024)	08/2025 (05/2026)	2000 (2000)	1420	65
225	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347)	Multi-States (Gujarat, Maharashtra)	11/2024 (11/2024)	05/2029 (-)	24819 (24819)	1856.46	1
226	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5969 (5969)	344.41	8
227	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Sivani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340)	Multi-States (Haryana, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5357 (5357)	348.2	11
228	Transmission System for Strengthening of Srinagar-Leh Tr. System (Power Grid Corporation of India Limited [POWERGRID]) (606781)	Multi-States (Jammu and Kashmir, Ladakh)	03/2022 (03/2022)	12/2024 (10/2025)	288.71 (288.71)	242.52	91
229	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138)	Multi-States (Karnataka, Telangana)	02/2024 (02/2024)	02/2026 (06/2026)	2147.62 (2147.62)	1310.04	64
230	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (-)	2227 (2227)	779.45	21
231	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (03/2027)	3251 (3251)	910.28	20
232	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [Rajasthan V Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025 (03/2025)	03/2027 (-)	5028 (5028)	256.93	1
233	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023 (12/2023)	12/2025 (06/2026)	2056 (2056)	1583.12	60
234	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024 (12/2024)	12/2026 (03/2027)	5846 (5846)	391.68	6
235	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan[8.1 GW] under phase-II- Part E (Power Grid Corporation of India Limited [POWERGRID]) (611659)	Rajasthan	03/2023 (03/2023)	09/2024 (10/2025)	1433.28 (1433)	1390.01	97
236	Transmission System for Evacuation of Power from REZ in Rajasthan 20GW under Phase III- Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (611947)	Rajasthan	11/2023 (11/2023)	06/2025 (12/2025)	428.3 (428.3)	205.58	54
237	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part H (Power Grid Corporation of India Limited [POWERGRID]) (611948)	Rajasthan	10/2023 (10/2023)	04/2025 (12/2025)	2211.29 (2211.29)	1879.59	84
238	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949)	Rajasthan	10/2023 (10/2023)	04/2025 (03/2026)	1796.02 (1796.02)	1347.01	85
239	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part B1 (Power Grid Corporation of India Limited [POWERGRID]) (611950)	Rajasthan	09/2023 (09/2023)	04/2025 (12/2025)	2190.54 (2190.54)	1905.77	89
240	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part E1 (Power Grid Corporation of India Limited [POWERGRID]) (611951)	Rajasthan	12/2021 (08/2023)	02/2025 (09/2025)	688.74 (688.74)	633.42	97
241	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134)	Rajasthan	12/2023 (12/2023)	12/2025 (06/2026)	2998.34 (2998.34)	1978.9	54
242	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332)	Rajasthan	08/2024 (08/2024)	08/2026 (12/2026)	3279 (3279)	819.75	23

All Ongoing Projects							SEPTEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
243	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (615335)	Rajasthan	08/2024 (08/2024)	08/2026 (12/2026)	1382 (1382)	113.46	7
244	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (615337)	Rajasthan	08/2024 (08/2024)	02/2026 (03/2026)	369 (369)	92.26	19
245	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (615338)	Rajasthan	11/2024 (11/2024)	11/2026 (06/2027)	2735 (2735)	156.44	10
246	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (617181)	Rajasthan	03/2025 (03/2025)	12/2026 (03/2027)	404 (404)	16.04	0
247	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Tarnsmission Limited] <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (616671)	Tamil Nadu	01/2025 (01/2025)	12/2026 (12/2026)	548 (548)	23.72	7
248	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex <i>(Power Grid Corporation of India Limited [POWERGRID])</i> (617269)	Uttar Pradesh	12/2024 (12/2024)	06/2026 (08/2026)	212.81 (212.81)	0.3	0
Total (65)					149516.43	57066.68	
Ministry of Housing & Urban Affairs							
Construction							
249	C/o 184 MS Flats for Hon'ble MPs at BKS Marg, New Delhi <i>(Central Public Works Department [CPWD])</i> (617282)	Delhi	01/2022 (05/2022)	05/2025 (09/2025)	646.53 (646.52)	540.04	100
250	Construction of One Tower of Office Complex and another Tower of Residential quarters consisting of 10Nos. Type-V, 10Nos. Type-VI & 1No.Type-VII Quarters i/c internal water supply, sanitary installation and all development and bulk services, Horticulture works on EPC Mode-I basis i/c comprehensive operation and maintenance of Civil, E&M services for 7 years after completion of original construction work for Ranga Reddy, Secunderabad, Medchal, Auditl, Audit-II Commissionerates of Central Tax at Khajaguda, Serilingampally, Hyderabad. <i>(Central Public Works Department - CPWD)</i> (617412)	Telangana	03/2024 (11/2024)	09/2027 (-)	644 (644)	87.6	6
Total (2)					1290.53	627.64	
Inland Waterways							
251	Chennai Metro Rail Phase-II Development Project <i>(Chennai Metro Rail Limited [CMRL])</i> (702668)	Tamil Nadu	10/2024 (11/2020)	08/2029 (-)	63246 (63246)	27456.44	46
Total (1)					63246	27456.44	
Real Estate							
252	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System <i>(ministry of housing and urban affairs)</i> (707229)	Andaman & Nicobar	07/2021 (11/2021)	05/2023 (-)	209.88 (209.88)	0	70
253	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi <i>(National Buildings Construction Corporation [NBCC])</i> (400188)	Delhi	07/2016 (05/2018)	12/2025 (12/2025)	32850 (32850)	0	0
254	Rehabilitation in Junavadaj Area Smart City Project <i>(ministry of housing and urban affairs)</i> (701719)	Gujarat	NA (06/2016)	07/2022 (-)	539 (539)	39.63	50
255	Green Building Development Project <i>(ministry of housing and urban affairs)</i> (701766)	Uttarakhand	NA (08/2019)	11/2023 (-)	150.97 (150.97)	18.95	31
Total (4)					33749.85	58.58	
Urban Public Transport							
256	Patna Metro Rail Project <i>(Patna Metro Rail Corporation Ltd. [PMRCL])</i> (702627)	Bihar	02/2019 (02/2019)	02/2024 (06/2027)	13365.77 (13365.8)	4039.77	46
257	Delhi Metro Rail Phase-IV [2 Corridors] <i>(Delhi Metro Rail Corporation Limited [DMRC])</i> (617207)	Delhi	03/2024 (03/2024)	03/2029 (-)	8399.81 (8399.81)	30.27	0
258	DMRTS Phase - IV [3 Priority Corridors] <i>(Delhi Metro Rail Corporation Limited [DMRC])</i> (702632)	Delhi	NA (07/2019)	03/2025 (03/2026)	24948.65 (24948.7)	17380.16	70
259	Surat Metro Rail Project <i>(Gujarat Metro Rail Corporation Limited [GMRCL])</i> (702630)	Gujarat	03/2019 (04/2019)	03/2024 (06/2026)	12020.32 (12020.3)	7791.18	71
260	Ahmedabad Metro Rail Project, Phase-II <i>(Gujarat Metro Rail Corporation Limited [GMRCL])</i> (702631)	Gujarat	03/2019 (03/2019)	03/2024 (12/2025)	5384.17 (5384.17)	4220.88	89
261	Ahmedabad Metro Rail Project [Phase-I] <i>(Gujarat Metro Rail Corporation Limited [GMRCL])</i> (702639)	Gujarat	11/2014 (02/2015)	03/2018 (10/2025)	10773 (12924.5)	12201.13	99
262	Construction of Bangalore Metro Rail Project Phase 2. <i>(Bengaluru Metro Rail)</i> (702635)	Karnataka	02/2014 (02/2016)	03/2021 (09/2026)	26405.14 (30695.1)	29567.97	94
263	Construction Bangalore Metro Rail Project Phase-2A & 2B <i>(Bengaluru Metro Rail)</i> (702665)	Karnataka	06/2021 (01/2019)	06/2026 (06/2026)	14788.1 (14788.1)	8817.87	56
264	Kochi Metro Rail Phase 2 Development Project <i>(CSPCC Projects)</i> (702664)	Kerala	11/2022 (11/2022)	11/2026 (11/2026)	1957.05 (1957.05)	363.54	14

All Ongoing Projects							SEPTEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
265	Bhopal Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702625)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (06/2028)	6941.4 (6941.4)	3598.51	45
266	Indore Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702626)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (12/2028)	7500.8 (7500.8)	4115.42	56
267	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617225)	Maharashtra	10/2023 (10/2023)	01/2027 (-)	910.18 (910.18)	127.55	23
268	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617226)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	2954.53 (2954.53)	20.89	3
269	Thane Integral Ring Metro Rail Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617327)	Maharashtra	09/2024 (09/2024)	09/2029 (-)	12200.1 (12200.1)	7.11	3
270	New Suburba Station Development Project (ministry of housing and urban affairs) (701745)	Maharashtra	NA (03/2019)	07/2022 (-)	262.76 (262.76)	17.62	6
271	Kalyan Station Precinct Imporvement Project (ministry of housing and urban affairs) (701991)	Maharashtra	NA (07/2020)	07/2023 (-)	600 (600)	272.42	70
272	Mumbai Metro Line 3 (Mumbai Metro Rail Corporation Limited [MMRC]) (702637)	Maharashtra	07/2013 (06/2016)	03/2023 (08/2025)	23136 (37276)	31783.93	96
273	Nagpur Metro Rail Phase II Development Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (702658)	Maharashtra	12/2022 (12/2022)	12/2027 (-)	6708 (6708)	1147.88	27
274	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] (Delhi Metro Rail Corporation Limited [DMRC]) (617206)	Multi-States (Delhi, Haryana)	01/2025 (01/2025)	01/2029 (-)	6230.99 (6230.99)	0.78	0
275	Delhi-Ghaziabad-Meerut Regional Rapid Transit System [RRTS] corridor (National Capital Region Transport Corporation [NCRTC]) (702633)	Multi-States (Delhi, Uttar Pradesh)	03/2019 (03/2019)	06/2025 (10/2025)	30274 (30274)	26612.45	95
276	Kanpur Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702628)	Uttar Pradesh	05/2019 (11/2019)	05/2024 (03/2027)	11076.48 (11076.5)	9085.11	74
277	Agra Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702629)	Uttar Pradesh	05/2019 (12/2020)	05/2024 (06/2027)	8379.62 (8379.62)	6060.21	63
	Total (22)				235216.87	167262.65	
Waste & Water							
278	ESR - 8 nos., distribution system - 216 Km, new house service connections - 38760 nos. upgrading of feeder mains, pumping station etc. - Phase II (Ministry of Housing & Urban Affairs) (702674)	Andhra Pradesh	NA (07/2018)	03/2023 (12/2025)	172.22 (172.22)	710.62	82
279	Dibrugarh Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702682)	Assam	NA (01/2020)	03/2023 (12/2025)	186.8 (186.8)	1477.98	98
280	Muzaffarpur Storm Water Drainage Phase-I Project (Ministry of Housing & Urban Affairs) (702699)	Bihar	NA (02/2019)	10/2023 (12/2025)	158.78 (158.78)	509.5	83
281	Storm water drainag Development Project (ministry of housing and urban affairs) (702355)	Dadra & Nagar Haveli and Daman & Diu	NA (12/2021)	03/2024 (-)	210 (210)	0	20
282	Upgradation of Sewerage system in Gandhinagar City (ministry of housing and urban affairs) (707267)	Gujarat	NA (03/2021)	06/2023 (-)	200 (200)	100	10
283	Sewerage Management Scheme Part-3 Implementation (Ministry of Housing & Urban Affairs) (702734)	Haryana	NA (11/2017)	09/2023 (03/2026)	278.01 (278.01)	1776.64	88
284	Sewerage Management Scheme Part-3 Implementation (Ministry of Housing & Urban Affairs) (702735)	Haryana	NA (10/2018)	03/2023 (12/2025)	213.19 (213.19)	1250.06	91
285	Dhanbad Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702741)	Jharkhand	NA (12/2018)	03/2023 (03/2026)	216.55 (216.55)	825.64	72
286	SAAP-3 Water Supply Infrastructure SAAP-3 Project (Ministry of Housing & Urban Affairs) (702742)	Jharkhand	NA (12/2018)	10/2023 (03/2026)	159.31 (159.31)	700	65
287	Augmentation and Strenghthning of Urban Water Supply Phase 1 - SAAP 3 (Ministry of Housing & Urban Affairs) (702746)	Jharkhand	NA (12/2018)	03/2023 (03/2026)	278.28 (278.28)	1410	78
288	Belgavi Improvement in Sewerage System Project (Ministry of Housing & Urban Affairs) (702760)	Karnataka	NA (10/2016)	07/2023 (12/2025)	162.73 (162.73)	642.21	80
289	24/7 water supply under AMRUT for Davanagere (Ministry of Housing & Urban Affairs) (702764)	Karnataka	NA (01/2018)	03/2023 (12/2025)	174.96 (174.96)	819.29	65
290	Indore Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702793)	Madhya Pradesh	NA (11/2017)	03/2023 (12/2025)	287.17 (287.17)	2018.5	99
291	Jabalpur Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702798)	Madhya Pradesh	NA (12/2017)	03/2023 (12/2025)	362.31 (362.31)	2597.57	93
292	Satna Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702808)	Madhya Pradesh	NA (12/2016)	03/2024 (12/2025)	191.56 (191.56)	1305.45	86
293	Singrauli Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702810)	Madhya Pradesh	NA (11/2017)	03/2023 (12/2025)	402.01 (402.01)	2800.32	90
294	Kalyan-Dombivali Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702833)	Maharashtra	NA (09/2019)	10/2023 (12/2025)	194.2 (194.2)	919.08	70

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
295	Mira-Bhayandar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702840)	Maharashtra	NA (08/2018)	03/2023 (12/2025)	204.55 (204.55)	1568.49	99
296	Nagpur Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702842)	Maharashtra	NA (08/2018)	03/2023 (12/2025)	273.78 (273.78)	2138.69	99
297	Pune Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702851)	Maharashtra	NA (07/2017)	03/2023 (10/2025)	235.95 (235.95)	1686.76	92
298	Solapur Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702854)	Maharashtra	NA (04/2018)	03/2023 (12/2025)	180.24 (180.24)	1281.38	91
299	Jalandhar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (703021)	Punjab	NA (08/2020)	08/2023 (03/2026)	258.53 (258.53)	1229.71	58
300	Patiala Water Supply Infrastructure Part-2 Project (Ministry of Housing & Urban Affairs) (703057)	Punjab	NA (08/2020)	10/2023 (12/2025)	287 (287)	612.68	74
301	Jaunpur Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702948)	Uttar Pradesh	NA (08/2019)	06/2023 (12/2025)	235.73 (235.73)	1695.47	87
302	Jhansi Water Supply Infrastructure Phase-II Project (Ministry of Housing & Urban Affairs) (702949)	Uttar Pradesh	NA (06/2019)	07/2023 (09/2025)	561.74 (561.74)	3123.27	91
Total (25)					6085.6	33199.31	
Ministry of Mines							
Construction							
303	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata (Central Public Works Department (CPWD)) (617280)	West Bengal	04/2019 (02/2020)	08/2026 (-)	255.37 (255.37)	83.03	40
Total (1)					255.37	83.03	
Metals & Mining							
304	Rakha Underground Mining Project (Hindustan Copper Limited [HCL]) (611798)	Jharkhand	12/2022 (03/2024)	03/2033 (-)	2705 (2705)	0	0
305	Surda Underground Copper Mining Project (Hindustan Copper Limited [HCL]) (611800)	Jharkhand	02/2022 (03/2024)	03/2028 (-)	665.02 (665.02)	19.8	1
306	Expansion of Malanjkhand Copper Project (Hindustan Copper Limited [HCL]) (400426)	Madhya Pradesh	09/2011 (04/2015)	04/2020 (04/2026)	1856.36 (1856.36)	935.32	80
307	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonne Per Annum (National Aluminium Company Limited [NALCO]) (400141)	Odisha	04/2017 (04/2017)	12/2022 (09/2025)	4103 (5677.4)	4111.16	77
308	Pottangi Bauxite Mines Project (National Aluminium Company Limited [NALCO]) (400299)	Odisha	05/2018 (05/2018)	03/2025 (05/2026)	1381 (1960.77)	650.04	51
309	UTKAL D AND E COAL BLOCK (National Aluminium Company Limited [NALCO]) (709829)	Odisha	NA (02/2016)	03/2025 (-)	1021.97 (1021.97)	0	0
310	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (Ministry of Mines) (709830)	Odisha	NA (04/2017)	11/2026 (-)	355 (581)	0	0
311	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (National Aluminium Company Limited [NALCO]) (709831)	Odisha	11/2017 (11/2019)	05/2025 (06/2026)	483 (483)	406.64	90
312	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (National Aluminium Company Limited [NALCO]) (709832)	Tamil Nadu	09/2017 (12/2017)	03/2025 (03/2026)	166 (166)	135	65
Total (9)					12736.35	6257.96	
Department of Higher Education							
Education							
313	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008)	Andhra Pradesh	09/2019 (12/2023)	06/2027 (-)	305 (305)	84.96	25
314	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (-)	592.61 (592.61)	550.22	75
315	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (10/2025)	153.71 (153.71)	124.33	97
316	Additional Campus of NITPatna (NIT Patna) (606013)	Bihar	07/2022 (08/2022)	07/2024 (01/2026)	499.21 (499.21)	434.67	98
317	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis (National Institute of Technology Delhi) (612851)	Delhi	09/2009 (11/2022)	09/2025 (-)	333.49 (336.42)	283.21	93
318	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886)	Delhi	09/2024 (03/2025)	10/2026 (-)	373 (373)	21.13	15

All Ongoing Projects							SEPTEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
319	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Central University of Gujarat) (612916)	Gujarat	12/2020 (02/2021)	03/2025 (03/2026)	490.63 (490.63)	312.06	80
320	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099)	Himachal Pradesh	09/2018 (08/2020)	10/2023 (02/2026)	392.51 (454.78)	323.81	93
321	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128)	Himachal Pradesh	03/2023 (03/2024)	03/2026 (03/2026)	166.66 (166.66)	84.25	70
322	Construction of Permanent Campus of Central University of Himachal Pradesh at Dehra, District - Kangra, [H.P.] on Engineering. Procurement and Construction [EPC Mode 1] Basis. (Central University, Himachal Pradesh) (612894)	Himachal Pradesh	03/2021 (08/2022)	11/2024 (11/2025)	251.98 (300.45)	183.44	79
323	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098)	Jammu and Kashmir	03/2019 (10/2020)	06/2023 (09/2025)	424.93 (500.91)	484.52	96
324	Additional Infrastructure at IISc Bangalore-RCC Monolithic for Men Hostel S14, Women Hostel S11 , Postdoctoral Hostel S12 2 Block , International Hostel S 12 , D&E Block S 12 2 Block FR. (IISc Bangalore) (610940)	Karnataka	08/2021 (08/2021)	03/2024 (09/2025)	420.41 (420.41)	364.44	99
325	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431)	Kerala	07/2017 (03/2020)	06/2022 (11/2026)	1006.45 (1217.4)	632.59	72
326	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] (Indian Institute of Technology, Indore) (611957)	Madhya Pradesh	12/2023 (04/2024)	02/2027 (-)	496.28 (496.28)	38.62	36
327	Hostel 4 -Earlier Known as Hostel 20 (Indian Institute of Technology, Bombay) (612135)	Maharashtra	09/2022 (12/2023)	09/2025 (-)	182.33 (182.33)	144.21	97
328	Academic Block 1 & 2 (Indian Institute of Technology, Bombay) (612203)	Maharashtra	09/2022 (05/2023)	07/2026 (03/2027)	68 (263.93)	24.18	19
329	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (07/2025)	494.52 (494.52)	413.57	86
330	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (12/2029)	474.23 (474.23)	167.55	4
331	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	261.24	97
332	IISER BERHAMPUR (Indian Institutes of Science Education and Research, Behrampur) (610315)	Odisha	10/2018 (09/2019)	03/2021 (12/2025)	1229.32 (773.76)	837.04	97
333	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] (National Institute of Technology, Puducherry) (612877)	Puducherry	09/2009 (07/2013)	12/2024 (08/2025)	618.34 (544.34)	509.55	94
334	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I (Indian intitue of Management, Amritsar) (605292)	Punjab	10/2019 (07/2020)	06/2023 (12/2025)	348.31 (348.31)	290.39	91
335	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment (Central University of Punjab) (617221)	Punjab	08/2024 (04/2025)	10/2027 (-)	210.99 (210.99)	10	6
336	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (09/2025)	314.06 (314.06)	238.22	83
337	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	121.56	12
338	Construction of Precast housing and hostels at IIT Hyderabad (Indian Institute of Technology, Hyderabad) (609996)	Telangana	09/2022 (11/2022)	10/2024 (01/2026)	262 (262)	178.17	76
339	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] (Banaras Hindu University) (606479)	Uttar Pradesh	06/2020 (06/2020)	09/2022 (03/2026)	246 (246)	194.14	95
340	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal (National Institute of Technology Uttarakhand) (611963)	Uttarakhand	06/2020 (04/2024)	09/2027 (-)	650.85 (650.85)	195.52	30
341	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur (Indian Institute of Technology, Kharagpur) (609019)	West Bengal	06/2018 (04/2019)	03/2023 (03/2026)	500 (442)	383.6	88
Total (29)					12467.21	7891.19	
Ministry of Petroleum & Natural Gas							
Energy Storage							
342	Construction of Aviation Fuel farm Facilities at Bhogapuram Airport (Ministry of Petroleum & Natural Gas) (616235)	Andhra Pradesh	08/2024 (08/2024)	03/2026 (03/2026)	240 (240)	49.57	70
343	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	58.27	48

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
344	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	129.97	55
345	Setting up a common user Petroleum Terminal at Jammu, J&K for resitement of existing PSU OMC's Depots from Jammu City (Bharat Petroleum Corporation Limited [BPCL]) (400235)	Jammu and Kashmir	04/2023 (04/2023)	03/2025 (01/2026)	676.89 (715.89)	535.94	82
346	Andheri Residential Towers, Mumbai (Ministry of Petroleum & Natural Gas) (604833)	Maharashtra	NA (06/2017)	05/2025 (06/2026)	281.35 (389.67)	234.6	50
347	Srikakulam Angul Gas Pipeline Project (Ministry of Petroleum & Natural Gas) (701343)	Multi-States (Andhra Pradesh, Odisha)	09/2019 (09/2019)	07/2022 (12/2025)	2658.34 (2810)	2272.98	95
348	Rajasthan Refinery Project (Ministry of Petroleum & Natural Gas) (701263)	Multi-States (Arunachal Pradesh, Gujarat, Rajasthan)	10/2017 (10/2017)	10/2022 (03/2026)	43129 (79459)	60545.24	88
349	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Multi-States (Assam, Bihar, Jharkhand, Odisha, West Bengal)	NA (01/2019)	07/2024 (10/2025)	10228 (11407)	9811.29	87
350	New Mundra Panipat Crude Oil Pipeline (Ministry of Petroleum & Natural Gas) (400078)	Multi-States (Gujarat, Haryana, Rajasthan)	NA (12/2021)	12/2024 (12/2025)	9028 (9028)	7186.98	85
351	Kandla Gorakhpur LPG Pipeline (Ministry of Petroleum & Natural Gas) (400012)	Multi-States (Gujarat, Madhya Pradesh, Uttar Pradesh)	NA (12/2018)	12/2021 (12/2025)	10088 (10088)	7979.86	93
352	Multi Product Pipeline from Irugur to Devangonthi (Department of Water Resources, River Development & GR) (400301)	Multi-States (Karnataka, Tamil Nadu)	11/2012 (11/2012)	02/2017 (09/2026)	678 (1732)	767.09	71
353	Petrochemical evacuation marketing terminal at Barmer, Rajasthan (Hindustan Petroleum Corporation Limited [HPCL]) (709759)	Rajasthan	12/2023 (12/2023)	12/2026 (12/2026)	461.05 (461.05)	127.84	60
354	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] (Ministry of Petroleum & Natural Gas) (400043)	Tamil Nadu	NA (01/2022)	05/2026 (05/2026)	829 (829)	320.63	66
355	Grass root POL Terminal at Vallur, Chennai (Indian Oil Corporation Limited [IOCL]) (400077)	Tamil Nadu	NA (01/2022)	12/2024 (03/2026)	827 (887.71)	633.42	88
356	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	NA (06/2022)	09/2025 (06/2026)	656 (656)	483.9	88
357	Grass-root Terminal at Mirzapur, Uttar Pradesh (Ministry of Petroleum & Natural Gas) (604852)	Uttar Pradesh	NA (09/2022)	11/2026 (11/2026)	980.45 (980.45)	220.97	53
Total (16)					81301.48	91358.55	
Oil & Gas							
358	KG-DWN-98/2 Cluster - II Development Project - NELP Block (Oil and Natural Gas Corporation Limited [ONGC]) (400120)	Andhra Pradesh	03/2016 (03/2016)	06/2020 (06/2026)	34012 (34012)	33238.5	96
359	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery (Hindustan Petroleum Corporation Limited) (709752)	Andhra Pradesh	09/2021 (09/2021)	06/2024 (03/2026)	160 (220)	89.34	72
360	HP Trijet Unit in Visakh Refinery (Hindustan Petroleum Corporation Limited) (709761)	Andhra Pradesh	07/2024 (07/2024)	07/2027 (07/2027)	193 (193)	0.43	23
361	City Gas Distribution Project at Kurnool, Guntur & Prakasam Districts (Ministry of Petroleum & Natural Gas) (709766)	Andhra Pradesh	03/2022 (03/2022)	03/2030 (03/2030)	1420 (1420)	163.46	6
362	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	NA (07/2020)	07/2024 (12/2025)	12366 (22494)	17007.22	78
363	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	NA (01/2018)	02/2020 (12/2025)	682.9 (726.93)	489.6	94
364	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	NA (05/2021)	10/2023 (05/2026)	412.3 (577)	435.92	86
365	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	NA (12/2020)	03/2024 (12/2025)	430.76 (430.76)	327.47	86
366	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Ministry of Petroleum & Natural Gas) (709776)	Assam	NA (04/2022)	09/2026 (09/2026)	277 (323.09)	186.17	68
367	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Ministry of Petroleum & Natural Gas) (709779)	Assam	NA (06/2022)	03/2026 (07/2027)	768 (740)	115.21	42
368	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2026)	344.99 (344.99)	211.1	48
369	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	09/2023 (09/2023)	05/2026 (05/2026)	198.7 (198.7)	39.45	36
370	DCU Revamp Project (NRL) (709864)	Assam	NA (08/2021)	07/2024 (10/2025)	370 (370)	265.35	61

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
371	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	NA (04/2023)	12/2024 (10/2025)	293.5 (293.5)	97.22	95
372	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar (MinistryofPetroleumNaturalGas) (617304)	Bihar	NA (10/2023)	03/2027 (03/2027)	340.15 (340.15)	94.41	28
373	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA (Ministry of Petroleum & Natural Gas) (701324)	Bihar	NA (01/2020)	04/2023 (08/2026)	14810 (16724)	11997.29	88
374	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery (MinistryofPetroleumNaturalGas) (709777)	Bihar	NA (01/2022)	04/2025 (10/2026)	389.35 (340)	56.85	42
375	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts (Bharat Petroleum Corporation Limited [BPCL]) (709792)	Bihar	12/2022 (12/2022)	03/2030 (03/2030)	3638 (3638)	414.14	29
376	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts (Bharat Petroleum Corporation Limited [BPCL]) (709793)	Bihar	12/2022 (12/2022)	06/2030 (06/2030)	3919 (3919)	412.83	19
377	Redevelopment of Sobhasan Complex (Oil and Natural Gas Corporation Limited [ONGC]) (400087)	Gujarat	08/2021 (08/2021)	02/2026 (02/2026)	885.63 (1286.67)	830.89	79
378	Redevelopment of Santhal Field [Onshore-Mehsana Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (400167)	Gujarat	02/2017 (02/2017)	03/2026 (03/2026)	1162.56 (1162.56)	1157	94
379	Redevelopment of Linch Field (Oil and Natural Gas Corporation Limited [ONGC]) (400169)	Gujarat	04/2021 (04/2021)	03/2025 (10/2025)	631.03 (860.04)	539.03	83
380	Petrochemical and Lube Integration Project at Gujarat Refinery (Ministry of Petroleum & Natural Gas) (701329)	Gujarat	NA (09/2020)	08/2024 (06/2026)	18936 (17825)	12645.17	84
381	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery (MinistryofPetroleumNaturalGas) (709778)	Gujarat	NA (01/2022)	08/2025 (09/2026)	328.29 (287)	160.45	62
382	Commercial Polymer Flooding Project in Bechraji field (Oil and Natural Gas Corporation Limited [ONGC]) (709838)	Gujarat	01/2022 (01/2022)	11/2024 (11/2025)	621.4 (621.4)	137.72	21
383	Restoration of Gas Terminal, Phase-I [Part-A], Hazira (Oil and Natural Gas Corporation Limited [ONGC]) (709840)	Gujarat	05/2022 (05/2022)	02/2025 (12/2025)	249.43 (249.43)	209.89	94
384	Old Pipe Line Replacement [OPRP] Group-A (Oil and Natural Gas Corporation Limited [ONGC]) (709841)	Gujarat	07/2021 (07/2021)	07/2025 (03/2026)	173.03 (169.84)	147.77	88
385	Kalol Redevelopment Project, Ahmedabad Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709842)	Gujarat	08/2022 (08/2022)	03/2027 (03/2027)	1487.41 (1487.41)	927.55	62
386	Revamping of SV Stations, Gas Terminal & Kribhco Terminal (Oil and Natural Gas Corporation Limited [ONGC]) (709845)	Gujarat	11/2022 (11/2022)	08/2026 (08/2026)	837.34 (837.34)	257.06	54
387	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad (Ministry of Petroleum & Natural Gas) (604853)	Haryana	NA (06/2019)	12/2022 (10/2026)	2281.94 (3200)	1810.8	64
388	Poly Butadiene Rubber plant at Panipat (Indian Oil Corporation Limited [IOCL]) (611917)	Haryana	NA (03/2022)	03/2025 (06/2026)	1459 (2531.44)	1119.16	72
389	Capacity Expansion of Panipat Refinery from 15 to 25 MMTPA (Ministry of Petroleum & Natural Gas) (701289)	Haryana	NA (02/2021)	09/2024 (06/2026)	34627 (36225)	25028.79	89
390	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. (MinistryofPetroleumNaturalGas) (709783)	Haryana	NA (12/2020)	06/2023 (06/2026)	165.13 (247.69)	138.35	74
391	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts (MinistryofPetroleumNaturalGas) (709773)	Jammu and Kashmir	03/2022 (03/2022)	03/2032 (03/2032)	538 (538)	3.72	0
392	Development of Jharia CBM Block [Phase-1] (Oil and Natural Gas Corporation Limited [ONGC]) (610984)	Jharkhand	11/2019 (11/2019)	01/2024 (11/2025)	431 (431)	217.93	59
393	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] (MinistryofPetroleumNaturalGas) (709785)	Jharkhand	NA (02/2023)	02/2026 (02/2026)	202.07 (202.07)	60.23	47
394	Power System Upgradation Project (Mangalore Refinery and Petrochemicals Limited) (612790)	Karnataka	NA (10/2023)	11/2025 (05/2026)	385 (385)	151.3	67
395	Demo Bio-ATF Project (Ministry of Petroleum & Natural Gas) (616879)	Karnataka	NA (03/2024)	01/2027 (01/2027)	364 (364)	29.47	15
396	Revamping/ Augmentation of facilities at existing port terminal at Mangalore (Ministry of Petroleum & Natural Gas) (709774)	Karnataka	NA (01/2022)	12/2025 (12/2025)	463 (500.62)	277.72	82
397	Replacement and Extension of Jetty Pipelines [REJP] at KR (Bharat Petroleum Corporation Limited [BPCL]) (709790)	Kerala	NA (03/2023)	03/2026 (03/2026)	621.87 (621.87)	198.6	87
398	Setting up Polypropylene Unit at Kochi Refinery (MinistryofPetroleumNaturalGas) (709799)	Kerala	NA (12/2023)	10/2027 (10/2027)	4460 (4460)	287.8	15
399	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery (MinistryofPetroleumNaturalGas) (709798)	Madhya Pradesh	05/2023 (05/2023)	05/2028 (05/2028)	43367 (43367)	1913.6	15



All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
400	Debottlenecking and Augmentation of Cryogenic facilities at Uran LPG Import Terminal (Department of Water Resources, River Development & GR) (400158)	Maharashtra	04/2021 (04/2021)	02/2024 (12/2025)	1164.69 (1629.86)	947.22	88
401	500 KTA PDHPP Project, Usar (Ministry of Petroleum & Natural Gas) (400168)	Maharashtra	04/2021 (04/2021)	04/2025 (12/2025)	8797 (11256)	6990.28	86
402	Construction of lube oil blending plant at Rasayani (Ministry of Petroleum & Natural Gas) (610985)	Maharashtra	05/2022 (05/2022)	12/2023 (12/2025)	423.39 (526.26)	305.71	81
403	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery (Ministry of Petroleum and Natural Gas) (616933)	Maharashtra	12/2024 (12/2024)	03/2028 (03/2028)	4679 (4679)	200.79	5
404	HP TDAE Unit in Mumbai Refinery (Hindustan Petroleum Corporation Limited) (709760)	Maharashtra	06/2024 (06/2024)	04/2026 (04/2026)	240 (240)	43.29	45
405	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts (Ministry of Petroleum Natural Gas) (709771)	Maharashtra	03/2022 (03/2022)	09/2031 (09/2031)	865 (865)	69.15	2
406	Construction of Additional Tankages and Allied Facilities at JNPT Terminal (Ministry of Petroleum Natural Gas) (709780)	Maharashtra	NA (04/2022)	08/2026 (08/2026)	341.43 (436.14)	284.39	51
407	ATF Pipeline from Jawaharlal Nehru Port Trust to Navi Mumbai International Airport (Indian Oil Corporation Limited [IOCL]) (709782)	Maharashtra	NA (08/2022)	08/2025 (03/2026)	165 (165)	94.21	75
408	Installation of Independent De-Aromatized Solvents [DAS] production facilities at MR (Bharat Petroleum Corporation Limited [BPCL]) (709789)	Maharashtra	03/2023 (03/2023)	07/2025 (12/2025)	405 (343)	214.5	89
409	POL & LOBS Installations with Receipt Pipelines at Rasayani (Bharat Petroleum Corporation Limited [BPCL]) (709797)	Maharashtra	05/2023 (05/2023)	05/2026 (05/2026)	2585 (2585)	678.79	63
410	Part Replacement Pipeline Project [PRPP] (Oil and Natural Gas Corporation Limited [ONGC]) (709846)	Maharashtra	11/2022 (11/2022)	05/2024 (11/2025)	1219.48 (1145.1)	745	90
411	Visakh Raipur Pipeline Project (Ministry of Petroleum and Natural Gas) (616254)	Multi-States (Andhra Pradesh, Chhattisgarh, Odisha)	09/2024 (09/2024)	09/2027 (09/2027)	2212 (2212)	16.53	10
412	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura, West Bengal)	NA (04/2020)	03/2024 (03/2026)	9265 (9265)	6426.54	85
413	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Multi-States (Assam, West Bengal)	NA (06/2021)	12/2024 (10/2025)	860 (860)	615.47	98
414	CGD Project in Banka, Dumka, Godda, Jamtara, Pakur, Sahibganj GA ID 11A.02 (Hindustan Petroleum Corporation Limited) (709757)	Multi-States (Bihar, Jharkhand)	06/2022 (06/2022)	06/2030 (06/2030)	1377 (1377)	335.79	27
415	Mumbai Nagpur Jharsuguda Pipeline Project (Ministry of Petroleum & Natural Gas) (701354)	Multi-States (Chhattisgarh, Madhya Pradesh, Maharashtra, Odisha)	06/2020 (06/2020)	05/2023 (12/2025)	7844.25 (8255)	6609.4	96
416	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (Ministry of Petroleum & Natural Gas) (701330)	Multi-States (Gujarat, Haryana, Punjab, Rajasthan)	NA (07/2011)	06/2024 (12/2025)	7392 (7392)	6308	90
417	Gurdaspur Jammu Pipeline (Gas Authority of India Limited [GAIL]) (612853)	Multi-States (Jammu and Kashmir, Punjab)	07/2023 (07/2023)	07/2026 (07/2026)	521.9 (521.9)	206	37
418	Kochi - Kootanad - Bangalore - Mangalore Pipeline Phase-II (Ministry of Petroleum & Natural Gas) (701228)	Multi-States (Karnataka, Kerala, Tamil Nadu)	06/2009 (06/2009)	12/2012 (12/2025)	2915 (5909)	4453.29	95
419	City Gas Distribution Maharashtra Natural Gas Limited (Ministry of Petroleum & Natural Gas) (701338)	Multi-States (Karnataka, Maharashtra)	01/2006 (01/2006)	06/2031 (06/2031)	5535 (5535)	3883.25	0
420	Dhamra Haldia Pipeline Project (Ministry of Petroleum & Natural Gas) (701344)	Multi-States (Odisha, West Bengal)	03/2020 (03/2020)	11/2022 (12/2025)	1030.65 (1125)	865.2	88
421	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (Bharat Petroleum Corporation Limited [BPCL]) (709794)	Multi-States (Punjab, Rajasthan)	12/2022 (12/2022)	06/2030 (06/2030)	3207 (3207)	345.1	24
422	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum Natural Gas) (709786)	Nagaland	NA (08/2023)	11/2027 (11/2027)	227.62 (227.62)	9.34	23
423	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (Ministry of Petroleum & Natural Gas) (604859)	Odisha	NA (07/2020)	01/2024 (08/2026)	13805 (11783)	8373.41	91
424	CUF POL Depot at Sadashibpur [Meramundali], Odisha (Ministry of Petroleum Natural Gas) (709800)	Odisha	NA (04/2021)	03/2026 (03/2026)	393.54 (393.54)	107.85	45
425	Life Extension of 48 well platforms of Mumbai High & Heera Fields (Oil and Natural Gas Corporation Limited [ONGC]) (400119)	Offshore	12/2015 (12/2015)	04/2018 (12/2025)	3190.69 (3375.9)	3113.26	89

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
426	PRP-VIII [Group-A] <i>(Ministry of Petroleum & Natural Gas)</i> (616950)	Offshore	09/2024 (09/2024)	02/2026 (02/2026)	1486.4 (1486.4)	272.3	21
427	Daman Upside Development Project <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709839)	Offshore	06/2022 (06/2022)	10/2025 (02/2026)	4144.41 (6406.9)	4401.66	87
428	MHN TCPP PGC BGC Project [MTPBP] <i>(Ministry of Petroleum & Natural Gas)</i> (709848)	Offshore	06/2022 (06/2022)	05/2026 (05/2026)	2329.45 (2354.23)	1148.9	56
429	PRP-VIII Group B [NH & BS Asset] <i>(Ministry of Petroleum & Natural Gas)</i> (709849)	Offshore	06/2024 (06/2024)	02/2026 (02/2026)	2379.84 (3165.53)	1806.82	63
430	Integrated Development of 4 Contract Areas under DSF-II <i>(Ministry of Petroleum & Natural Gas)</i> (709851)	Offshore	05/2023 (05/2023)	04/2027 (04/2027)	6183.79 (6183.79)	594.28	21
431	2G Ethanol Biorefinery at Bathinda <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (400171)	Punjab	05/2020 (05/2020)	02/2023 (03/2026)	1421.46 (1421.46)	1185.85	95
432	Bathinda Sangrur Pipeline <i>(Ministry of Petroleum and Natural Gas)</i> (612998)	Punjab	11/2021 (11/2021)	05/2024 (10/2025)	367 (397)	347	94
433	City Gas Distribution Project at Pathankot District <i>(Ministry of Petroleum Natural Gas)</i> (709770)	Punjab	03/2022 (03/2022)	09/2033 (09/2033)	151 (151)	8.74	2
434	CBR 9 MMTPA Project <i>(Chennai Petroleum Corporation Limited [CPCL])</i> (604795)	Tamil Nadu	NA (09/2021)	06/2025 (10/2028)	31580 (36354)	1342.27	10
435	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore <i>(Chennai Petroleum Corporation Limited [CPCL])</i> (709750)	Tamil Nadu	NA (01/2024)	09/2025 (12/2025)	205 (205)	51.31	48
436	City Gas Distribution Projects at the Nilgiris and Erode districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709796)	Tamil Nadu	12/2022 (12/2022)	03/2030 (03/2030)	3685 (3685)	238.05	18
437	Creation of Gas Dehydration Facilities, Tripura Asset <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (709837)	Tripura	03/2022 (03/2022)	05/2024 (12/2025)	209.33 (131.51)	68.9	63
438	PP Project, Pata <i>(Gas Authority of India Limited [GAIL])</i> (400161)	Uttar Pradesh	03/2019 (03/2019)	01/2024 (10/2025)	910.56 (1299.02)	1029	98
439	Revamping / Augmentation of Facilities at Mathura Bitumen Plant <i>(Ministry of Petroleum Natural Gas)</i> (709781)	Uttar Pradesh	NA (04/2022)	06/2027 (12/2026)	260.12 (260.12)	1.11	28
440	City Gas Distribution Projects at Lakhimpur Kheri, Sitapur, Bahraich, Shravasti, Balrampur, Siddharth Nagar & Maharajganj districts <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709795)	Uttar Pradesh	12/2022 (12/2022)	06/2030 (06/2030)	16654 (16654)	590.67	11
441	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] <i>(Ministry of Petroleum & Natural Gas)</i> (617302)	West Bengal	03/2017 (03/2017)	12/2020 (12/2025)	1740 (2493.15)	2261	90
442	Haldia Panagarh Pipeline Project <i>(Hindustan Petroleum Corporation Limited)</i> (709753)	West Bengal	11/2022 (11/2022)	11/2025 (11/2025)	1010 (1010)	669.15	82
443	CGD Project in Malda, Birbhum, Murshidabad, Dakshin Dinajpur GA ID 11A.03 <i>(Hindustan Petroleum Corporation Limited)</i> (709758)	West Bengal	06/2022 (06/2022)	06/2030 (06/2030)	2628 (2628)	340.69	28
444	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts <i>(Ministry of Petroleum Natural Gas)</i> (709772)	West Bengal	03/2022 (03/2022)	06/2031 (06/2031)	609 (609)	56.58	2
445	City Gas Distribution Projects at Alipurduar and Cooch Behar <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709791)	West Bengal	12/2022 (12/2022)	03/2030 (03/2030)	1017 (1017)	194.33	39
Total (88)					349335.78	182742.33	
Ministry of Health & Family Welfare							
Healthcare							
446	AIIMS Majra Rewari Haryana <i>(PMSSY/Institute of National Importance (INI))</i> (701173)	Haryana	12/2023 (02/2019)	02/2023 (12/2026)	1299 (1299)	349.41	28
447	AIIMS Kashmir at Awantipora Jammu & Kashmir <i>(PMSSY/Institute of National Importance (INI))</i> (701167)	Jammu and Kashmir	01/2019 (11/2020)	01/2025 (12/2025)	1828 (1828)	1565.25	67
448	AIIMS Bibinagar <i>(PMSSY/Institute of National Importance (INI))</i> (701171)	Telangana	12/2018 (07/2022)	09/2022 (12/2025)	1028 (1365.95)	821.99	85
Total (3)					4155	2736.65	
Ministry of Ports, Shipping and Waterways							
Healthcare							
449	Establishment of 600 bed super specialty hospital with optional development of Medical college and further expansion on PPP basis. <i>(Mumbai Port Trust [MPT])</i> (708662)	Maharashtra	08/2019 (01/2022)	06/2026 (12/2027)	693 (693)	58	0
Total (1)					693	58	
Inland Waterways							
450	Jal Marg Vikas Project <i>(Inland Waterways Authority of India [IWAI])</i> (701565)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	01/2018 (02/2018)	12/2023 (12/2025)	5369.18 (5061.15)	3488.6	71
451	Fairway Development in West Bengal Farakka - Kahelgaon <i>(Inland Waterways Authority of India [IWAI])</i> (611142)	Offshore	NA (08/2018)	07/2023 (04/2024)	177 (197)	183.32	100

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (2)				5546.18	3671.92	
	Logistics Infrastructure						
452	Replacement and revamping of pipeline projects in oil jetty area, Kandla (Deendayal Port Trust [DPT]) (701570)	Gujarat	NA (09/2021)	09/2023 (03/2025)	171 (211.61)	137.51	71
	Total (1)				171	137.51	
	Oil & Gas						
453	Construction of oil jetty No.8 at old kandla through internal resources (Deendayal Port Trust [DPT]) (701568)	Gujarat	NA (02/2021)	02/2023 (07/2024)	100 (225.85)	166.48	90
	Total (1)				100	166.48	
	Shipping						
454	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust [DPT]) (609424)	Gujarat	10/2022 (12/2023)	12/2026 (-)	4243.64 (4243.64)	70	10
455	Construction of new dry dock at existitng Cochin Shipyard Limited premises at Perumanoor, Kochi 682 015 (Cochin Shipyard) (701564)	Kerala	04/2018 (05/2018)	12/2022 (03/2025)	1799 (1799)	1558.39	96
456	Rewas Port Project (Reliance Industries Ltd) (400382)	Maharashtra	NA (01/2020)	03/2023 (-)	6000 (6000)	5999.89	0
457	Setting up of a Floating Storage and Regasification Unit [FSRU] - Mumbai (Mumbai Port Trust [MPT]) (701586)	Maharashtra	NA (04/2021)	11/2026 (11/2026)	900 (900)	65	0
458	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574)	Odisha	05/2022 (01/2023)	12/2027 (10/2028)	3004.63 (3004.63)	1149.79	40
459	Berth No. 2 [previously Berth 3] of HDC Mechanization Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701576)	West Bengal	NA (03/2023)	09/2025 (01/2026)	298.26 (298.26)	420	91
460	Shalukkhali Liquid Cargo Handling Facility Development Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701577)	West Bengal	NA (08/2022)	08/2025 (-)	253.65 (253.65)	9.28	0
	Total (7)				16499.18	9272.35	
	Tourism, Hospitality & Wellness						
461	National Maritime Heritage Complex [NMHC] Phase-I (Indian Port Rail & Ropeway Corporation Ltd. [IPRCL]) (707215)	Gujarat	02/2019 (01/2022)	03/2024 (09/2025)	573 (1238.05)	496.63	66
	Total (1)				573	496.63	
	Ministry of Steel						
	Metals & Mining						
462	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul (National Mineral Development Corporation Limited [NMDC]) (615202)	Chhattisgarh	08/2021 (07/2022)	12/2028 (03/2028)	1700 (1756.2)	124.9	4
	Total (1)				1700	124.9	
	Steel						
463	Stamp Charge Battery No.12 Battery Proper at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617338)		01/2025 (02/2025)	07/2028 (-)	2518.39 (2518.39)	62.72	4
464	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617243)	Chhattisgarh	07/2024 (08/2024)	07/2026 (-)	198.62 (198.62)	11.98	12
465	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617255)	Chhattisgarh	10/2023 (12/2023)	06/2026 (-)	471.83 (471.83)	136.99	44
466	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617256)	Chhattisgarh	11/2023 (01/2024)	10/2025 (-)	884.1 (884.1)	493.34	79
467	NMDC Slurry Pipeline Project Phase-1 (National Mineral Development Corporation Limited [NMDC]) (706811)	Chhattisgarh	11/2015 (09/2020)	06/2023 (12/2025)	2907 (5427)	3107.45	87
468	SCREENING PLANT-III AT KIRANDUL (National Mineral Development Corporation Limited [NMDC]) (709826)	Chhattisgarh	NA (10/2021)	01/2026 (-)	2718.84 (2718.84)	1362.18	73
469	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (National Mineral Development Corporation Limited [NMDC]) (709827)	Chhattisgarh	NA (10/2022)	12/2025 (-)	349.75 (349.75)	288.8	91
470	New Sinter Plant at BSL, SAIL (Steel Authority of India Limited [SAIL]) (400174)	Jharkhand	03/2015 (10/2015)	10/2017 (06/2027)	1034.01 (1752.3)	885.08	53
471	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617249)	Jharkhand	01/2025 (02/2025)	01/2027 (-)	211.94 (211.94)	15.04	10
472	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617250)	Jharkhand	01/2025 (02/2025)	10/2026 (-)	207.13 (207.13)	15.76	8
473	Revamping of old sub-systems of Blast Furnace 3 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617253)	Jharkhand	08/2023 (03/2023)	07/2025 (11/2025)	513.82 (513.82)	237.34	73
474	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617254)	Jharkhand	03/2024 (04/2024)	06/2026 (-)	260.37 (260.37)	51.12	22

All Ongoing Projects							SEPTEMBER 2025
SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
475	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617257)	Jharkhand	11/2023 (12/2023)	11/2026 (-)	627.31 (627.31)	126.45	42
476	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. (National Mineral Development Corporation Limited [NMDC]) (400121)	Karnataka	11/2014 (06/2024)	08/2026 (-)	1043.63 (1043.63)	262.34	32
477	Installation of 4th Slab Caster along with its Auxiliaries and a New Ladle Furnace in SMS-II at Rourkela Steel Plant (Steel Authority of India Limited [SAIL]) (400065)	Odisha	01/2022 (02/2022)	05/2025 (09/2025)	1105.23 (1105.23)	769.08	99
478	Rebuilding of COB 4 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (612781)	West Bengal	09/2023 (09/2023)	12/2026 (-)	916.78 (916.78)	137.01	18
479	Installation of New Bar Mill at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617242)	West Bengal	07/2024 (08/2024)	06/2027 (-)	2115.44 (2115.44)	228.35	29
480	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617246)	West Bengal	09/2024 (08/2024)	06/2026 (-)	758.09 (758.09)	67.14	6
481	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617248)	West Bengal	11/2024 (12/2024)	07/2026 (-)	227.96 (227.96)	19.61	31
482	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617251)	West Bengal	07/2024 (12/2024)	05/2026 (-)	196.4 (196.4)	0.19	3
	Total (20)				19266.64	8277.97	
	Ministry of Railways						
	Railways						
483	Nadikudi - Srikalahasti New Line (South Central Railway [SCR] - II) (400298)	Andhra Pradesh	03/2012 (12/2016)	05/2027 (03/2028)	2312 (5200)	2179	54
484	GOOTY-PENDEKALLU DOUBLING 29.225 Km (South Central Railway [SCR] - II) (611752)	Andhra Pradesh	03/2023 (06/2023)	03/2027 (03/2027)	351.83 (351.83)	18	25
485	GUNTAKAL WEST-MALLAPPA GATE RAIL OVER RAIL - ROR TRACK (South Central Railway [SCR] - II) (611754)	Andhra Pradesh	07/2023 (07/2023)	07/2026 (-)	293.3 (293.3)	0	0
486	Kurnool - Setting up facilities for coach midlife rehabilitation workshop (WPO/Patna) (611927)	Andhra Pradesh	01/2014 (10/2017)	12/2023 (-)	560.72 (560.72)	276.66	65
487	Flyover between Pendurthi and Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB 73 of 2023 24 NR (East Coast Railway [ECor] - II) (612827)	Andhra Pradesh	04/2023 (05/2024)	04/2027 (-)	183.65 (183.65)	5.11	11
488	3rd & 4th line between Vadlapudi -Gate Jn. cabin and Tie line between Gate Junction to Gangavaram port (East Coast Railway [ECor] - II) (616697)	Andhra Pradesh	04/2023 (03/2024)	06/2026 (-)	154.28 (154.28)	15.92	18
489	Kurnool Coach Midlife Rehabilitation Project (WPO/Patna) (705253)	Andhra Pradesh	05/2016 (07/2014)	12/2020 (-)	563 (563)	120	0
490	Kotapalli - Narasapur New Line (South Central Railway [SCR] - II) (705436)	Andhra Pradesh	03/2009 (09/2013)	03/2028 (03/2028)	2501 (2501)	1303.41	29
491	Guntur-Guntakal Doubling Project (South Central Railway [SCR] - II) (705633)	Andhra Pradesh	03/2017 (11/2017)	12/2025 (12/2026)	3733 (4295)	4357.74	93
492	Vijaywada-Gudur 3rd Line (RVNL - II) (705648)	Andhra Pradesh	08/2016 (04/2018)	11/2024 (12/2025)	6654 (6654)	5922	90
493	Penukonda - Dharmavaram Doubling Project [41.5 Km] (South Western Railway [SWR] - II) (705789)	Andhra Pradesh	06/2018 (12/2018)	03/2026 (03/2026)	307.66 (307.66)	292.98	61
494	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3707.75	93
495	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
496	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
497	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
498	Sakri -Hasanpur [via Harnagar - Kusheshwar Asthan] New Railway line (East Central Railway [ECR] - I) (400254)	Bihar	12/2023 (08/1997)	12/2024 (03/2027)	735.2 (735.2)	587.39	82
499	Jhajha-Batai New Line Project (East Central Railway [ECR] - I) (617373)	Bihar	03/2023 (03/2023)	03/2027 (-)	588.18 (588.18)	2.74	0
500	Khagaria-Kusheshwar Asthan [42Km] new line project (East Central Railway [ECR] - I) (705364)	Bihar	04/2019 (12/1998)	12/2024 (03/2027)	614 (1384)	485.71	55
501	Hajipur-Sagauli New line (East Central Railway [ECR] - I) (705366)	Bihar	10/2007 (10/2004)	03/2020 (12/2026)	2067 (2087)	1997.26	74
502	Araria Supaul New BG Line (East Central Railway [ECR] - I) (705368)	Bihar	06/2018 (03/2009)	03/2024 (01/2027)	1605 (2514)	1528.41	35



All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
503	Fatuha-Islampur incl. MM for extn.of NL from Neora to Daniawan , Daniawan to Biharsharif, Biharsharif to Barbigha , Barbigha to Shekhpura (East Central Railway [ECR] - I) (705373)	Bihar	08/2002 (03/2002)	03/2023 (08/2025)	1473 (2882)	2522.41	94
504	Jogbani-Biratnagar New Rail Line project (Indian Railway Construction International Limited [IRCON]) (705450)	Bihar	06/2010 (01/2011)	03/2022 (12/2026)	402 (486)	367.54	86
505	Samastipur-Darbhanga Doubling Railway Project (East Central Railway [ECR] - I) (705526)	Bihar	11/2015 (12/2015)	03/2025 (10/2025)	519 (519)	354.98	84
506	Sagauli-Valmiknagar (East Central Railway [ECR] - I) (705527)	Bihar	03/2018 (03/2017)	12/2025 (12/2025)	1216 (2222)	2062.27	91
507	Muzaffarpur-Sugauli (East Central Railway [ECR] - I) (705528)	Bihar	03/2018 (03/2017)	06/2024 (02/2026)	1586 (1586)	1465.64	99
508	Rampur Dumra-Tal-Rajendrapul Additional Bridge and Railway Line Doubling (Indian Railway Construction International Limited [IRCON]) (706759)	Bihar	03/2016 (05/2017)	12/2024 (12/2025)	2373.64 (1700.24)	1414.12	96
509	Barauni-Bachwara [16 km] - 3rd & 4th line incl. Barauni yard remodelling [32 km] (East Central Railway [ECR] - I) (706860)	Bihar	10/2022 (08/2025)	08/2025 (10/2026)	645 (645)	7.61	55
510	JHAJHA - BATIA (East Central Railway [ECR] - I) (900874)	Bihar	03/2023 (03/2023)	03/2028 (01/2030)	588.18 (588.18)	0.49	0
511	Kharsia-Dharamjaygarh with Spur line [East Corridor-Phase 1] (Indian Railway Construction International Limited [IRCON]) (400220)	Chhattisgarh	03/2016 (01/2014)	09/2018 (03/2026)	3055 (3438)	2587.28	94
512	Doubling of Kirandul-Jagdalpur Line [150 km] (East Coast Railway [ECoR] - II) (400291)	Chhattisgarh	02/2013 (03/2013)	03/2020 (12/2025)	1589 (1798)	1542.79	92
513	Gauge Conversion of Kendri-Dhamtari including Abhanpur - Rajim Branch line 67.20 Kms - 2nd Material Modification to Raipur Titlagarh doubling. (SECR) (602792)	Chhattisgarh	07/2011 (05/2021)	02/2025 (11/2025)	1171 (1171)	848	82
514	4th line between Nipania Bhatapara 14.4 Km (South East Central Railway [SECR] - II) (612815)	Chhattisgarh	12/2022 (05/2024)	03/2027 (-)	170.49 (170.49)	0	2
515	Dharamjaigarh-Korba 63 km (CERL) (613003)	Chhattisgarh	08/2023 (07/2022)	08/2026 (-)	1686.26 (1686.26)	288.83	18.5
516	Dallirajhara - Rowghat New Rail Line Project, Phase-I (Rail Vikas Nigam Limited) (617374)	Chhattisgarh	NA (11/2009)	03/2025 (-)	1516.45 (1516.45)	873.79	92
517	Dallirajhra- Rowghat New Railway Line - Phase I [95 km] (RVNL - II) (705433)	Chhattisgarh	07/2009 (12/2009)	09/2025 (12/2025)	1628 (1628)	1440.85	82
518	Gevra Road-Pendra Road New Railway Line [135 km] (Indian Railway Construction International Limited [IRCON]) (705444)	Chhattisgarh	04/2014 (04/2014)	03/2022 (12/2025)	4970 (4970)	4449.99	73
519	Boridand - Ambikapur Doubling Line Project (South East Central Railway [SECR] - II) (706854)	Chhattisgarh	06/2022 (04/2022)	06/2030 (06/2030)	1376 (1576.23)	218	18
520	NIPANIA-BHATAPRA [14.4 KM] 4TH LINE [PB-72/NR/2022-23] (SECR) (709814)	Chhattisgarh	12/2022 (05/2024)	12/2026 (12/2026)	170 (184)	0	2
521	4TH LINE - BHATAPARA-HATHBAND [8.8 KM] [PB-72/NR/2022-23] (SECR) (709815)	Chhattisgarh	09/2022 (05/2024)	01/2027 (12/2027)	177.03 (177.03)	0	2
522	4TH LINE - BHILAI-BHILAI NAGAR [8.8 KM] [PB-72/NR/2022-23] (SECR) (709816)	Chhattisgarh	09/2022 (05/2024)	02/2027 (02/2027)	177.34 (177.34)	1.64	4
523	4TH LINE - DADHAPARA-BELHA [9.2 KM] [PB-72/NR/2022-23] (SECR) (709817)	Chhattisgarh	09/2022 (05/2024)	11/2026 (11/2026)	169.06 (169.06)	15.58	60
524	4TH LINE RAJNANDGAON-DONGARHGARH [31.2 KM] [PB-72/NR/2022-23] (SECR) (709818)	Chhattisgarh	09/2022 (05/2024)	01/2027 (01/2027)	328.34 (328.34)	53.88	25
525	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (709819)	Chhattisgarh	09/2022 (05/2025)	12/2026 (12/2026)	167.64 (167.64)	0.04	3
526	Redevelopment of New Delhi Railway Station and construction of associated infrastructure (Rail Land Development Authority) (613785)	Delhi	01/2023 (06/2024)	12/2028 (-)	4744 (4744)	119.71	1
527	Development of New Bijwasan Railway Terminal (Northern Railways) (617379)	Delhi	02/2008 (03/2013)	03/2020 (-)	446.21 (446.21)	511.94	80
528	North Region Video Surveillance Project (RCIL) (705298)	Delhi	06/2020 (04/2023)	03/2024 (-)	274.39 (274.39)	0	0
529	Anand Vihar-Tilak Bridge 3rd & 4th line (CAO/C/NR) (705583)	Delhi	03/2013 (03/2013)	03/2023 (12/2027)	667 (667)	285.44	62
530	Provision of Work-site Tampers [WST] Railway Project (EDTK[MC]/RB) (705694)	Delhi	01/2016 (01/2016)	12/2023 (01/2026)	187.72 (187.72)	141.91	100
531	WST Machine Procurement Project (EDTK[MC]/RB) (705708)	Delhi	06/2018 (06/2018)	03/2024 (12/2027)	176 (176)	0	0
532	PCT Machine Procurement Project (EDTK[MC]/RB) (705710)	Delhi	04/2019 (04/2019)	04/2024 (06/2027)	336 (336)	74.32	85



All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
533	RBMV Machine Procurement Project (EDTK[MC]/RB) (705712)	Delhi	10/2019 (10/2019)	06/2024 (12/2027)	480 (480)	0.33	7
534	SRGM Machine Procurement Project (EDTK[MC]/RB) (705717)	Delhi	10/2019 (10/2019)	12/2023 (03/2026)	440 (440)	390.03	90
535	WST Machine Procurement Project (EDTK[MC]/RB) (705720)	Delhi	12/2019 (12/2019)	04/2024 (12/2026)	384 (384)	0	0
536	DTS Machine Procurement Project (EDTK[MC]/RB) (705721)	Delhi	12/2019 (12/2019)	12/2024 (12/2026)	447.6 (447.6)	0	0
537	BRM Machine Procurement Project (EDTK[MC]/RB) (705722)	Delhi	09/2019 (09/2019)	06/2024 (12/2027)	210 (210)	0.02	0
538	Track Machine Procurement Project (EDTK[MC]/RB) (705726)	Delhi	04/2020 (04/2020)	03/2025 (01/2028)	6339 (6339)	4166.47	41
539	Kosamba Umarpada 70 Km (PCE/WR) (611918)	Gujarat	07/2023 (07/2022)	03/2027 (-)	468 (468)	20	8
540	Adraj Moti Vijapur 40 Kms (Western Railway [WR] - II) (611937)	Gujarat	05/2022 (05/2022)	05/2026 (05/2026)	417.53 (417.53)	223	86
541	Vijapur Ambliyan 42 km (PCE/WR) (611938)	Gujarat	05/2022 (05/2022)	05/2026 (05/2026)	415.38 (415.38)	364	96
542	Himatnagar Khedbrahma 55 km (Railway) (611939)	Gujarat	06/2022 (04/2017)	06/2001 (06/2026)	482.42 (482.42)	461	96
543	New broad gauge line between Naliya Jakhau Port 25 Kms (PCE/WR) (611943)	Gujarat	02/2023 (02/2023)	01/2028 (01/2028)	410.26 (410.26)	6	4
544	Quadrupling between Gandhidham Adipur with Y connection at Adipur for providing direct entry towards Mundra Port and Bhuj and high level platform at Gopalpur 11Kms (PCE/WR) (611944)	Gujarat	02/2023 (02/2023)	03/2026 (03/2026)	152.44 (152.44)	20	68
545	Petlad Bhadran 23 Kms (PCE/WR) (611945)	Gujarat	05/2022 (05/2022)	05/2030 (05/2030)	307.11 (307.11)	82	17
546	Samlaya Timba Road 54 km (PCE/WR) (611970)	Gujarat	02/2023 (02/2023)	03/2030 (03/2030)	670.17 (670.17)	102	12
547	Samni Jambusar 24 km (PCE/WR) (611971)	Gujarat	05/2022 (05/2022)	03/2030 (03/2030)	350 (349.93)	87	31
548	Western Railway Samakhiali Gandhidham Quadrupiling 53 Kms (PCE/WR) (611974)	Gujarat	08/2023 (08/2023)	12/2026 (-)	1430 (1430)	0	0
549	Dahod Creation of Infrastructure facilities for 9000 HP Electric locomotives Manufacturing at (PCE/WR) (611977)	Gujarat	05/2022 (02/2023)	02/2025 (-)	487 (487)	108.69	0
550	Dahod Rolling Stock Workshop Provision of Infrastructure for CBS at (PCE/WR) (611978)	Gujarat	11/2022 (03/2023)	03/2025 (-)	158 (158)	47.31	0
551	Sabarmati Setting up of Maintenance Facilities for Train Sets Phase ii (PCE/WR) (611979)	Gujarat	01/2023 (04/2023)	06/2025 (-)	250 (250)	0	0
552	4th LINE BETWEEN BAREJADI NANDEJ-SANAND-AHMEDABAD BYPASS (Western Railway) (612072)	Gujarat	02/2023 (02/2023)	03/2027 (03/2027)	961.67 (961.67)	333.21	17
553	Redevelopment of Ahmedabad railway station and associated infrastructure on engineering, procurement and construction mode (Rail Land Development Authority) (613786)	Gujarat	01/2023 (11/2023)	03/2028 (-)	2379 (2379)	682.86	18
554	Miyagam-Karjan-Dabhoi-Samlaya [GC] (Western Railway [WR] - II) (705458)	Gujarat	01/2017 (01/2017)	03/2021 (12/2026)	483.88 (1039.13)	621.37	41
555	Modasa-Shamlaji Road Railway Line Project (SECR) (706757)	Gujarat	09/2012 (04/2008)	03/2025 (03/2027)	262 (262)	203	58
556	Rajkot - Kanalus Doubling Project [111.2 Kms] (Western Railway [WR] - II) (706763)	Gujarat	10/2021 (12/2021)	10/2026 (10/2026)	1080.58 (1080.58)	787.69	76
557	NADIAD-PETLAD [37.26 KM] (Railway) (709812)	Gujarat	05/2022 (-)	06/2030 (06/2030)	461.91 (461.91)	75	7
558	NEW BG LINE INTERSECTION [5 NOS] BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD [16.51 KM] [PB#29/NR/202 (SECR) (709813)	Gujarat	10/2022 (-)	10/2027 (10/2027)	437.21 (437.21)	43	15
559	Bhiwani - Dobh Bahali Doubling Project [42.30 Km] (North Western Railway [NWR]) (611884)	Haryana	02/2023 (02/2023)	02/2028 (02/2028)	471 (471)	208.84	65
560	Doubling between Pradhankunta-Patherih-Bhojudih of East Central Railway (East Central Railway [ECR] - I) (617372)	Jharkhand	11/2022 (11/2022)	12/2025 (-)	349.22 (349.22)	86.48	70
561	Gomoh - Flyover for DN trains (East Central Railway [ECR] - I) (705765)	Jharkhand	01/2018 (01/2018)	03/2026 (03/2026)	686 (686)	546.05	59
562	Lodhma - Piska - Link Line bypassing Hatia/Ranchi with Y connection (South Eastern Railway [SER] - I) (705785)	Jharkhand	08/2021 (03/2019)	06/2026 (05/2027)	473 (473)	287.38	5

All Ongoing Projects

SEPTEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
563	Pradhan Kuntha Jn Line Doubling Project (East Central Railway [ECR] - I) (706837)	Jharkhand	11/2022 (11/2022)	11/2027 (11/2027)	349.22 (349.22)	100.96	62
564	Yeshvanthpur - Channasandra Doubling Project [21.70 Km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703585)	Karnataka	04/2019 (10/2019)	03/2024 (03/2026)	314.1 (683.57)	152.31	53
565	New Railway Line between Ginigera and Raichur [165.57 km] (South Western Railway [SWR] - II) (705434)	Karnataka	03/2008 (05/2009)	03/2019 (03/2027)	2565 (3034.98)	2096.35	66
566	Gadag-Wadi New Railway Line [257 km] (South Western Railway [SWR] - II) (705490)	Karnataka	04/2013 (08/2017)	03/2027 (12/2027)	2842 (6700)	1383.77	30
567	Kadur - Chickamagalur - Sakleshpur [93km] (South Western Railway [SWR] - II) (705492)	Karnataka	01/2014 (11/2016)	06/2025 (12/2025)	825 (825)	799.76	83
568	Bagalkot-Kudachi New Railway Line [142 km] (South Western Railway [SWR] - II) (705495)	Karnataka	10/2013 (11/2012)	03/2027 (01/2027)	1378 (1649)	700.24	35
569	Tumkur-Chitradurga-Davangere New Rail Line Project [191 km] (South Western Railway [SWR] - II) (705496)	Karnataka	10/2013 (01/2017)	03/2019 (12/2027)	1876 (1876)	530.62	13
570	Bangalore-Whitefield-Bangalore City-Krishnarajapuram [23.08 km] - Quadrupling (South Western Railway [SWR] - II) (705663)	Karnataka	02/2018 (06/2022)	02/2026 (02/2026)	493 (493)	252.45	82
571	SHIMOGA - SHIKARIPURA - RANEBENNUR [96 Km] (South Western Railway [SWR] - II) (705761)	Karnataka	09/2019 (02/2023)	12/2027 (06/2028)	1454 (1454)	69.95	11
572	Kumbalam-Turavur doubling project [15.59 Km] (Southern Railway [SR] - II) (705638)	Kerala	04/2023 (04/2023)	03/2027 (03/2027)	813 (802.8)	66.69	17
573	Ernakulam-Kumbalam doubling project [7.71 Km] (SR-ERS) (705639)	Kerala	04/2023 (04/2023)	03/2028 (02/2027)	601 (595.39)	289.52	18
574	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho (North Central Railway) (705480)	Madhya Pradesh	01/2007 (03/1998)	03/2027 (12/2027)	8914 (8914)	5013.49	72
575	Katni - Bina Third Railway Line [279 km] (West Central Railway WCR I) (705651)	Madhya Pradesh	06/2016 (01/2017)	03/2022 (12/2025)	2478.23 (4127.23)	3301.89	90
576	Satna-Rewa Railway Line Doubling Project (West Central Railway [WCR] - II) (705659)	Madhya Pradesh	11/2015 (08/2017)	03/2026 (03/2026)	500 (584)	561.38	80
577	Doubling of Katni - Singrauli Railway Line [261 km] (Indian Railway Construction International Limited [IRCON]) (705660)	Madhya Pradesh	03/2016 (03/2017)	12/2025 (12/2025)	2445 (4377)	3218.87	100
578	Katni Grade Separator/Bye Pass (Indian Railway Construction International Limited [IRCON]) (705661)	Madhya Pradesh	03/2016 (09/2017)	09/2024 (03/2026)	1248 (1248)	1615.7	94
579	Indore - Budni New Railway Line [198 kms] (RVNL - II) (705763)	Madhya Pradesh	08/2019 (10/2020)	09/2030 (09/2030)	7474 (7474)	1698.94	23
580	Nimach-Ratlam Doubling [133 Km] (Western Railway [WR] - II) (705933)	Madhya Pradesh	10/2021 (10/2021)	10/2027 (10/2027)	1095.88 (1095.88)	1067.49	89
581	DHULE [BORVIHIR] - NARDANA NEW LINE [50.60 KMS] (Central Railway [CR] - II) (400019)	Maharashtra	01/2019 (04/2023)	12/2026 (09/2027)	492.76 (1170.83)	256.28	16
582	Wardha-Nanded Via Yavatmal New BG Line (Central Railway [CR] - II) (400271)	Maharashtra	12/2017 (04/2008)	03/2028 (03/2028)	3445 (3445)	3002.93	50
583	AURANGABAD-ANKAI - DOUBLING PROJECT 98.25 Km (South Central Railway [SCR] - II) (611751)	Maharashtra	05/2023 (05/2023)	03/2027 (-)	960.64 (960.64)	0	0.01
584	Redevelopment of Chhatrapati Shivaji Maharaj Terminus [CSMT] and construction of associated infrastructure (Rail Land Development Authority) (613015)	Maharashtra	04/2023 (07/2023)	03/2027 (-)	1813 (1813)	584.61	14
585	Doubling between Parbhani Parli Vajjanath stations 64.71 Km (South Central Railway [SCR] - II) (617215)	Maharashtra	12/2023 (12/2023)	03/2028 (-)	769.93 (769.93)	0	0
586	Babupeth - Sasti New Rail Line [13.114 KMs] (Central Railway [CR] - II) (617361)	Maharashtra	10/2024 (10/2024)	03/2028 (-)	362.81 (362.81)	0	0
587	Double Chord line Between Nilaje-Kopar (Central Railway [CR] - II) (617364)	Maharashtra	01/2025 (01/2025)	07/2028 (-)	338.33 (205)	3.42	0
588	Western Region Video Surveillance Project (RCIL) (705300)	Maharashtra	06/2020 (04/2023)	12/2023 (-)	227.59 (227.59)	0	0
589	Ahmednagar - Beed - Parli - Vajjnath New Broad Gauge Line Railway Project [261.3 km] (Central Railway [CR] - II) (705356)	Maharashtra	01/1999 (10/2002)	03/2026 (03/2026)	2538.67 (4957.27)	5015.05	98
590	Baramati Lonand New Line Project (Central Railway [CR] - II) (705357)	Maharashtra	03/2016 (03/1999)	03/2027 (03/2027)	138.48 (1843.9)	748.88	51
591	Wadsa-Gadchiroli (South East Central Railway) (705479)	Maharashtra	05/2017 (03/2012)	03/2027 (03/2027)	1886 (1886)	727.28	52
592	3rd Line Kalyan - Kasara [67.35 Kilometres] (Central Railway [CR] - II) (705498)	Maharashtra	09/2015 (09/2015)	12/2026 (12/2026)	792.89 (1395.79)	912.1	51

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
593	3rd Line Wardha - Sewagram - Nagpur (Central Railway [CR] - II) (705500)	Maharashtra	09/2015 (05/2016)	12/2025 (12/2025)	540.02 (944.24)	764.69	81
594	3rd Line Wardha - Ballarshah [132 Kilometres] (Central Railway (CR) - II) (705502)	Maharashtra	03/2016 (12/2016)	12/2025 (02/2026)	1384.72 (2033.59)	1655.88	68
595	Pune - Miraj-Londa [467 Kilometres] (Central Railway (CR) - II) (705503)	Maharashtra	06/2016 (06/2016)	02/2025 (08/2025)	4027.53 (4872.52)	4833.04	85
596	Doubling of Daund Manmad Line [247.6 km] (Central Railway (CR) - II) (705504)	Maharashtra	10/2017 (03/2017)	12/2025 (03/2026)	2081.27 (3267.06)	2829.9	88
597	4th Line Wardha - Nagpur [78.7 Kilometres] (Central Railway [CR] - II) (705505)	Maharashtra	04/2017 (05/2018)	12/2025 (02/2026)	637.95 (1341.28)	988.87	81
598	3rd Line Manmad - Jalgaon [160 Kilometres] (Central Railway [CR] - II) (705506)	Maharashtra	05/2017 (04/2018)	12/2024 (08/2025)	1035.16 (1558.75)	1726.94	95
599	Solapur-tuljapur-Osmanabad (Central Railway (CR) - II) (705735)	Maharashtra	08/2018 (12/2023)	03/2027 (03/2028)	904.92 (3295.74)	1134.58	12
600	Nagpur- Nagbhir Railway Line Gauge Conversion Project (MRIDC) (705799)	Maharashtra	10/2019 (04/2020)	12/2025 (12/2025)	1400 (1400)	1472	80
601	Mumbai Urban Transport Project [MUTP] - PHASE II (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706779)	Maharashtra	05/2008 (04/2008)	03/2014 (12/2027)	8087 (8087)	7364	87
602	Mumbai Urban Transport Project [MUTP] Phase-IIIA (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706780)	Maharashtra	04/2019 (04/2019)	12/2027 (12/2027)	33690 (33690)	2361.45	16
603	Mumbai Urban Transport Project Phase-III (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706781)	Maharashtra	11/2016 (12/2016)	03/2022 (12/2026)	10947 (10947)	5303.76	65
604	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (709808)	Maharashtra	08/2022 (01/2022)	08/2027 (03/2028)	955.39 (2093.82)	130.42	11
605	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	15598.11	69
606	Marikuppam - Kuppam New Line Project [23.70 Km] (South Western Railway [SWR] - II) (705491)	Multi-States (Andhra Pradesh, Karnataka)	04/2012 (10/2018)	06/2026 (06/2026)	297 (297)	131.13	15
607	Rayadurg-Tumkur via Kalyandurg New Line [207 km] (South Western Railway [SWR] - II) (705494)	Multi-States (Andhra Pradesh, Karnataka)	03/2008 (07/2010)	09/2015 (02/2028)	2496 (2496)	1730.22	68
608	Renigunta, Wadi & Gooty Bypass Railway Project (South Central Railway [SCR] - I) (705610)	Multi-States (Andhra Pradesh, Karnataka)	04/2016 (04/2016)	12/2025 (12/2025)	302 (543)	381	50
609	Doubling between Mudkhed Medchal & Mahbubnagar Dhone section 417.88 Km (South Central Railway [SCR] - II) (617212)	Multi-States (Andhra Pradesh, Maharashtra, Telangana)	08/2023 (08/2023)	03/2029 (-)	4686.09 (4686.09)	0	0
610	Vizianagaram - Titlagarh 3rd line [272 Km including By - pass line of 7.68 KM] (RVNL - II) (400253)	Multi-States (Andhra Pradesh, Odisha)	06/2016 (11/2016)	12/2026 (12/2026)	4803 (6670)	5722.01	89
611	Doubling of Kottavalasa-Koraput Rail Line [189 KM] (East Coast Railway [ECOR] - II) (705512)	Multi-States (Andhra Pradesh, Odisha)	12/2015 (01/2016)	03/2022 (03/2028)	2500 (2500)	1999.9	70
612	Vizianagaram-Sambhalpur 3rd Line Project (RVNL) (705520)	Multi-States (Andhra Pradesh, Odisha)	06/2016 (12/2016)	03/2025 (-)	4803.16 (4803.16)	2979.23	0
613	Tindivanam-Nagari New Line Project [184.5 km] (Southern Railway [SR] - II) (400275)	Multi-States (Andhra Pradesh, Tamil Nadu)	07/2008 (10/2008)	09/2016 (03/2028)	3631 (3631)	1113.53	18
614	Doubling between Motumari Vishnupuram - 88.81 Km and Rail over Rail - RoR at Motumari - 10.877 Km (South Central Railway [SCR] - II) (616857)	Multi-States (Andhra Pradesh, Telangana)	02/2024 (03/2025)	03/2029 (-)	1595.55 (1595.55)	9.59	1
615	Doubling of Guntur Bibinagar 239 Km (South Central Railway [SCR] - II) (617211)	Multi-States (Andhra Pradesh, Telangana)	08/2023 (08/2023)	03/2029 (-)	2853.23 (2853.23)	46.87	1
616	Kazipet-Vijayawada 3rd line with electrification [220 km] (South Central Railway [SCR] - II) (705612)	Multi-States (Andhra Pradesh, Telangana)	03/2013 (08/2014)	02/2025 (12/2025)	1953 (3363)	3246.08	92
617	Vijayawada - Kazipet Bypass line (South Central Railway [SCR] - II) (705632)	Multi-States (Andhra Pradesh, Telangana)	04/2016 (04/2016)	01/2025 (12/2025)	647 (904)	901.1	92
618	Murkongselek-Pasighat (Northeast Frontier Railway [NFR] - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (03/2023)	03/2025 (05/2026)	435 (1250)	540.27	60
619	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	13.74	0
620	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2025)	6663 (6663)	5518.32	81
621	New Delhi- Howrah Speed Booster[160Kmph] Project (PCE/NCR) (705794)	Multi-States (Bihar, Delhi, Jharkhand, Uttar Pradesh, West Bengal)	09/2019 (09/2019)	03/2024 (-)	6684.81 (6684.81)	127.03	0
622	Third Railway Line between Patratu-Sonnagar [281 kms] (RVNL - II) (400234)	Multi-States (Bihar, Jharkhand)	11/2016 (08/2018)	03/2026 (07/2026)	8975 (8975)	4950	88

All Ongoing Projects

SEPTEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
623	Multi tracking of Son Nagar-Andal 374.53 rkm & 814.38 tkm (East Central Railway [ECR] - I) (616699)	Multi-States (Bihar, Jharkhand)	08/2023 (08/2023)	03/2028 (-)	12333.57 (12333.6)	508.44	12
624	Koderma-Tilaiya New Line (East Central Railway [ECR] - I) (705375)	Multi-States (Bihar, Jharkhand)	11/2004 (03/2002)	02/2025 (02/2026)	1626 (2020)	2000.4	95
625	Pirpainti - Jasidih [100.52 Km] New BG line (Eastern Railway [ER] - I) (705385)	Multi-States (Bihar, Jharkhand)	03/2014 (03/2022)	03/2028 (03/2028)	2555 (2555)	773.15	48
626	NER Provision of Automatic Block Signalling on Gorakhpur Cantt[Excl] Chhapra Gramin & Burhwal Jn [Excl] Sitapur Jn section of high density routes (North Eastern Railway [NER]) (611669)	Multi-States (Bihar, Uttar Pradesh)	NA (06/2023)	03/2027 (-)	380.47 (380.47)	24.53	0
627	Chhapra-Ballia Patch Doubling (North Eastern Railway [NER]) (705562)	Multi-States (Bihar, Uttar Pradesh)	03/2013 (12/2015)	02/2025 (03/2026)	963 (1046)	911.66	95
628	Katihar - Kumedpur Doubling Line Project (GM/C/ NFR) (706844)	Multi-States (Bihar, West Bengal)	08/2022 (0)	08/2027 (08/2027)	942 (942)	356	45
629	Rajnandgaon - Nagpur [Kalumna] Third Railway Line [228.30 km] (South East Central Railway [SECR] - II) (705617)	Multi-States (Chhattisgarh, Maharashtra)	09/2016 (12/2016)	12/2024 (06/2026)	3545 (3545)	3466.53	96
630	Sardega -Bhalumuda New Double line [37.24 Km] (SECR) (617390)	Multi-States (Chhattisgarh, Odisha)	09/2024 (09/2024)	03/2028 (-)	1281.81 (1281.81)	128	0
631	Jagdalspur-Koraput (East Coast Railway [ECor] - II) (705511)	Multi-States (Chhattisgarh, Odisha)	12/2015 (03/2016)	03/2024 (12/2026)	1547 (1547)	1323.05	90
632	Jharsuguda-Bilaspur Fourth Railway Line [206 km] (SECR) (705616)	Multi-States (Chhattisgarh, Odisha)	09/2016 (09/2016)	10/2024 (12/2025)	2140 (2979)	2160.07	92
633	Mumbai-Ahmedabad High Speed Rail Project- 508 km (National High Speed Rail Corporation [NHSRC]) (705728)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	03/2015 (09/2017)	08/2027 (12/2029)	108000 (108000)	81242.89	54
634	New Delhi- Mumbai Speed Booster[160Kmph] Project (PCE/WR) (705793)	Multi-States (Delhi, Gujarat, Madhya Pradesh, Maharashtra, Rajasthan)	09/2019 (09/2019)	03/2024 (-)	6806.44 (6806.44)	135.65	0
635	Hospet - Tinaighat - Vasco Rail Doubling Project (RVNL - II) (705650)	Multi-States (Goa, Karnataka)	03/2010 (07/2012)	03/2027 (12/2027)	5060 (5060)	5007.82	86
636	Hospet-Hubli-Vasco da Gama Line Electrification Project (RVNL) (706950)	Multi-States (Goa, Karnataka)	07/2015 (05/2018)	03/2023 (03/2024)	744.49 (1122.62)	969.05	95
637	Western Dedicated Freight Corridor (DFCCIL) (705237)	Multi-States (Gujarat, Haryana, Maharashtra, Rajasthan, Uttar Pradesh)	02/2008 (01/2012)	03/2022 (12/2025)	51101 (124005)	124623	96
638	New line Dahod-Indore via Sardarpur, Jabuwa and Dhar (Western Railway [WR] - II) (705453)	Multi-States (Gujarat, Madhya Pradesh)	06/2012 (06/2012)	02/2027 (02/2027)	456.07 (3516.77)	3531	48
639	Chhota Udaipur - Dhar New Line Project [157 km] (Western Railway [WR] - II) (705454)	Multi-States (Gujarat, Madhya Pradesh)	11/2008 (01/2014)	12/2025 (12/2025)	1794 (1794)	1812.56	80
640	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (Western Railway) (611452)	Multi-States (Gujarat, Maharashtra)	09/2019 (03/2023)	12/2025 (06/2025)	311 (311)	208	92
641	Taranga Hill-Abu Road via Ambaji (North Western Railway [NWR]) (400022)	Multi-States (Gujarat, Rajasthan)	07/2022 (07/2022)	07/2030 (07/2030)	2798 (2798)	1931.66	16
642	LUNI- SAMDARI- BHILDI DOUBLING (North Western Railway [NWR]) (616842)	Multi-States (Gujarat, Rajasthan)	02/2024 (02/2024)	07/2027 (-)	3085.59 (3085.59)	277.6	12
643	Chandigarh-Baddi New Rail Line- 36 km (Northen Railway [NR]) (705424)	Multi-States (Haryana, Himachal Pradesh)	02/2018 (02/2018)	12/2026 (12/2026)	1540 (1540.13)	522.31	31
644	Rewari - Kathuwas Doubling Project [27.72 Km] (North Western Railway [NWR]) (611861)	Multi-States (Haryana, Rajasthan)	02/2023 (12/2022)	06/2027 (06/2027)	352 (352)	258.15	65
645	Nangal Dam-Talwara New Broad Gauge Line [84 KM] and Taking Over Siding Mukerian-Talwara [29 KM] (Northen Railway [NR]) (705410)	Multi-States (Himachal Pradesh, Punjab)	03/1983 (05/1985)	12/2025 (01/2027)	2018 (2018)	2053.9	45
646	Bhanupalli-Bilaspur-Beri New Railway Line Project (RVNL - II) (705428)	Multi-States (Himachal Pradesh, Punjab)	03/2009 (04/2015)	12/2026 (12/2027)	13447 (13447)	6902.81	60
647	Doubling of Hatia [Ranchi]-Bondamunda Rail Line - 159 km (South Eastern Railway - JH) (705628)	Multi-States (Jharkhand, Odisha)	03/2016 (02/2017)	06/2025 (06/2026)	3029 (3029)	2487.31	86
648	KHARAGPUR-ADITYAPUR THIRD RAIL LINE- 132 KM (RVNL - II) (705668)	Multi-States (Jharkhand, West Bengal)	09/2016 (01/2018)	03/2025 (12/2025)	3250 (3250)	3176.46	97
649	Hotgi-Kudgi-Gadag Doubling Project (South Western Railway [SWR] - II) (705662)	Multi-States (Karnataka, Maharashtra)	04/2014 (01/2016)	12/2024 (03/2026)	1878 (2459)	2668.28	92
650	Baiyyappanahalli - Hosur Doubling Project [48 km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703586)	Multi-States (Karnataka, Tamil Nadu)	04/2019 (02/2019)	03/2024 (01/2026)	498.7 (748.7)	630.41	86



All Ongoing Projects

SEPTEMBER 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
651	Trivandrum- Kanyakumari (Southern Railway (SR) - I) (705635)	Multi-States (Kerala, Tamil Nadu)	08/2017 (03/2016)	03/2024 (12/2027)	1432 (3785)	2451	46
652	Ratlam-Mhow-Khandwa-Akola Gauge Conversion (Western Railway [WR] - II) (705457)	Multi-States (Madhya Pradesh, Maharashtra)	04/2008 (03/2010)	03/2027 (09/2028)	1656.25 (6499.86)	4433.45	80
653	Itarsi - Nagpur Third Railway Line [280 km] (Central Railway (CR) - II) (705507)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016 (09/2016)	03/2027 (03/2027)	2449.91 (2506.68)	1850.73	51
654	RATLAM- DUNGARPUR VIA BANSWARA NEW LINE PROJECT (North Western Railway [NWR]) (617406)	Multi-States (Madhya Pradesh, Rajasthan)	10/2015 (05/2023)	03/2028 (-)	2417.24 (2417.24)	5.66	7
655	Gwalior - Seopurkala with extension to Kota [Gauge Conversion] (North Central Railway) (705419)	Multi-States (Madhya Pradesh, Rajasthan)	03/2011 (07/2018)	03/2025 (02/2026)	2913 (2913)	2097.51	78
656	Ramganjmandi-Bhopal New Line Project [262 km] (West Central Railway [WCR] - II) (705481)	Multi-States (Madhya Pradesh, Rajasthan)	03/2001 (10/2004)	12/2025 (12/2027)	3032 (5073)	3669.29	70
657	Nimach-Badi Sadri New Rail Line Project (Western Railway [WR] - II) (705764)	Multi-States (Madhya Pradesh, Rajasthan)	04/2017 (09/2021)	03/2026 (06/2026)	495 (825)	107.83	55
658	Mathura-Jhansi Third Railway Line [274 Km] (RVNL - II) (705667)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	12/2015 (03/2018)	12/2024 (12/2026)	5961 (5961)	4928.62	94
659	Jhansi - Bina Third Railway Line [153 Km] (CAO/C/NCR) (705598)	Multi-States (Madhya Pradesh, Uttar Pradesh)	09/2016 (03/2018)	03/2022 (03/2026)	2002 (2002)	1806.86	93
660	Jhansi-Khairar-Manikpur & Khirar-Bhimsen (North Central Railway) (705608)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2018 (04/2019)	03/2026 (03/2026)	4330 (4330)	2362.91	60
661	Third Line [new] between Kazipet - Balharshah with electrification [201.04 Km] (South Central Railway [SCR] - II) (705613)	Multi-States (Maharashtra, Telangana)	09/2016 (10/2016)	01/2025 (11/2025)	2595 (3071)	3293.04	94
662	Narayangarh-Bhadrak 3rd line (South Eastern Railway [SER] - I) (705629)	Multi-States (Odisha, West Bengal)	03/2019 (03/2017)	12/2025 (06/2026)	2400 (2400)	2278.8	65
663	Nagapattinam-Tiruturaipundi and Karaikal-Peralam New Line (Southern Railway [SR] - II) (400223)	Multi-States (Puducherry, Tamil Nadu)	07/2008 (01/2019)	03/2026 (03/2027)	713 (981)	598.38	80
664	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Multi-States (Sikkim, West Bengal)	10/2009 (05/2010)	05/2015 (12/2027)	7877 (12133)	9039.91	84
665	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass Line Project (Eastern Railway [ER] - I) (602797)	Multi-States (Uttar Pradesh, West Bengal)	08/2017 (12/2017)	03/2027 (03/2027)	461.64 (461.64)	192.67	8
666	Proposed 6 nos Road Over Bridge [ROB] at different locations under MCL Talcher Under Deposit Scheme. (East Coast Railway [ECoR] - II) (400045)	Odisha	08/2022 (07/2022)	03/2025 (01/2025)	168.32 (168.32)	69.85	82
667	Brundamal-Jharsuguda- flyover connection for joining downline (East Coast Railway [ECoR] - II) (400232)	Odisha	01/2014 (01/2014)	12/2026 (12/2026)	297 (297)	193.22	30
668	3rd & 4th line between Sarla - Sason [8 km] [PB 73/2023-24/NR] (East Coast Railway [ECoR] - II) (612834)	Odisha	04/2023 (04/2023)	12/2025 (-)	252 (252)	79.55	45
669	Paradeep - Badabandha 3rd & 4th Line / 18.51kms (East Coast Railway [ECoR] - II) (616695)	Odisha	08/2023 (04/2025)	11/2028 (-)	300.15 (300.15)	0.01	0
670	Jeypore - Malkangiri New BG Line Project (Indian Railways) (617290)	Odisha	NA (02/2018)	12/2030 (-)	2343.64 (2343.64)	437.48	2
671	New B.G Railway Line between Jeypore & Navarangpur [38 Km] with Electrification (Indian Railway and Govt of Odisha) (617320)	Odisha	07/2017 (09/2022)	09/2025 (-)	747.91 (747.91)	5.71	0
672	Khurda-Bolangir New Broad Gauge Rail Link [301km] (East Coast Railway [ECoR] - II) (705358)	Odisha	03/1994 (03/2001)	12/2026 (12/2026)	3792 (5089)	5027.62	89
673	Talcher-Bimlagarh New Railway Line (East Coast Railway [ECoR] - II) (705359)	Odisha	03/2004 (12/2004)	03/2025 (03/2027)	1928 (1928)	1952.83	48
674	Bhadrak-Nergundi Third Line (East Coast Railway [ECoR] - II) (705510)	Odisha	10/2015 (04/2015)	11/2024 (01/2026)	1284 (1284)	1298	80
675	Koraput - Singapur Railway Doubling (East Coast Railway [ECoR] - II) (705513)	Odisha	12/2015 (12/2015)	12/2027 (03/2028)	2362 (2362)	1798.71	68
676	Jarapada- Budhapank with flyover at Talcher road 3rd and 4th Line (East Coast Railway [ECoR] - II) (705514)	Odisha	11/2015 (12/2015)	11/2018 (03/2026)	1000 (810.02)	406.76	37
677	3rd & 4th Railway Line Project from Salegaon to Budhapank via Rajathgarh. (East Coast Railway [ECoR] - II) (705515)	Odisha	07/2013 (12/2015)	03/2026 (03/2026)	1173 (2092)	1971	80
678	Jeypore-Navarangpur New Rail Line Project (East Coast Railway [ECoR] - II) (705741)	Odisha	07/2017 (04/2023)	07/2028 (12/2029)	748 (748)	10.56	1
679	Khurda Road - Balangir Electrification of Railway Track Project (Ministry of Railways) (706898)	Odisha	09/2018 (09/2019)	03/2021 (-)	267.61 (267.61)	0	0
680	Godhani-Kalumna Chord 13.7 km (Ministry of Railways) (617321)	Offshore	07/2018 (07/2018)	07/2028 (-)	150000 (150000)	1940	11

All Ongoing Projects							SEPTEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
681	Jaynagar-Bijalpura, incl. extn. Bet, Bijalpura-Bardibas [Nepal] (East Central Railway [ECR] - I) (705362)	Offshore	08/2015 (03/2011)	03/2022 (03/2026)	819 (819)	580.51	75
682	Ludhiana- Killa Raipur Railway Doubling Project (Railway) (705783)	Punjab	03/2019 (12/2022)	03/2025 (03/2026)	237.64 (238)	134.48	50
683	Dedicated Test Track for RDSO Phase II (North Western Railway [NWR]) (611614)	Rajasthan	11/2021 (11/2021)	11/2026 (11/2026)	819.48 (967.06)	471	86
684	Devgarh Madariya - Nathdwara Gauge Conversion [82.54 Km] part of Marwar - Mavli Gauge Conversion [152 Km] (North Western Railway [NWR]) (611849)	Rajasthan	01/2023 (01/2023)	06/2028 (06/2028)	968.92 (968.92)	137.16	51
685	Maintenance cum workshop depot for Vande Bharat Sleeper Trains as per conditions under WTA 527 (WPO/Patna) (611929)	Rajasthan	09/2022 (06/2023)	12/2024 (-)	166.86 (166.86)	0	0
686	PUSHKAR- MERTA CITY NEW LINE (North Western Railway [NWR]) (616841)	Rajasthan	02/2024 (02/2024)	12/2026 (-)	799.64 (799.64)	14.64	4
687	AJMER- CHANDERIYA DOUBLING (North Western Railway [NWR]) (616843)	Rajasthan	02/2024 (02/2024)	06/2027 (-)	1634.79 (1634.79)	84.29	6
688	SADULPUR - CHURU DOUBLING PROJECT (North Western Railway [NWR]) (617403)	Rajasthan	01/2024 (01/2024)	06/2026 (-)	468.64 (468.64)	99.51	50
689	POKHRAN - RAMDEVRA New Line (North Western Railway [NWR]) (617404)	Rajasthan	04/2025 (04/2025)	03/2028 (-)	189.21 (189.21)	0	0
690	NATHDWARA- NATHDWARA TOWN NL (North Western Railway [NWR]) (617408)	Rajasthan	03/2019 (04/2024)	03/2027 (-)	166.33 (166.33)	71.48	1
691	Dholpur - Sirmuttra Gauge Conversion (North Central Railway) (705482)	Rajasthan	03/2022 (04/2020)	02/2019 (02/2027)	747 (747)	355.13	43
692	Gudha-Thatha Mithri Construction of Railway Track Project (North Western Railway [NWR]) (705752)	Rajasthan	04/2019 (04/2019)	11/2026 (11/2026)	819.48 (967.06)	377.59	99
693	Sawai Madhopur-Jaipur Railway Line Project (North Western Railway [NWR]) (705912)	Rajasthan	02/2024 (04/2023)	03/2027 (-)	1203.89 (1203.89)	73.03	7
694	Agra Fort-Bandikui Doubling Line Project (CAO/C/NCR) (705919)	Rajasthan	06/2022 (02/2021)	06/2027 (06/2027)	1390 (1390)	123	25
695	Sawaimadhopur Bye Pass Line Project (North Western Railway [NWR]) (706866)	Rajasthan	12/2022 (01/2023)	03/2026 (05/2027)	304 (304)	45.64	45
696	Ph II extension of MRTS from Velachery to St Thomas Mount (Southern Railways [SR] - construction) (400280)	Tamil Nadu	11/2007 (11/2008)	07/2024 (08/2025)	734 (982)	475.73	99
697	Redevelopment of Chennai Egmore Station (Railway) (613002)	Tamil Nadu	05/2022 (10/2022)	03/2026 (-)	842 (842)	340	0
698	Coach Production Factory Upgradation Project (CPM/ICF) (705244)	Tamil Nadu	12/2017 (07/2018)	12/2021 (-)	520 (520)	192.25	0
699	Railway Manufacturing Unit (South Central Railway [SCR] - II) (617409)	Telangana	07/2016 (02/2023)	12/2026 (-)	521.36 (521.36)	420	58
700	Kazipet Wagon Overhauling Project (RVNL) (705252)	Telangana	09/2017 (07/2017)	12/2023 (-)	385 (385)	0	0
701	Manoharabad-Kothapalli New Rail Line [151 km] (South Central Railway [SCR] - II) (705437)	Telangana	07/2016 (01/2017)	03/2027 (12/2027)	1160 (2781)	1902.91	71
702	Bahraich-Shravasti-Balrampur-Siddharthnagar -Santkabinagar (North Eastern Railway [NER]) (400204)	Uttar Pradesh	10/2018 (03/2017)	10/2030 (10/2030)	4939.78 (4939.78)	1239.61	8
703	Sahjanwa-Dohrighat (North Eastern Railway [NER]) (400205)	Uttar Pradesh	08/2019 (03/2017)	03/2029 (03/2029)	1319.75 (1319.75)	473.69	3
704	Anandnagar - Ghugli via Maharajganj New line 52.7 km (Construction NER) (617252)	Uttar Pradesh	10/2023 (11/2023)	03/2028 (-)	958.27 (958.27)	445.85	23
705	Chunar-Chopan doubling project (North Central Railway) (617284)	Uttar Pradesh	08/2023 (01/2025)	03/2028 (-)	1423.96 (1423.96)	49.57	2
706	Surface triangle line bet. Bhadura stn and new crossing stn Karma (East Central Railway [ECR] - I) (617333)	Uttar Pradesh	10/2022 (05/2024)	02/2027 (-)	199.96 (199.96)	0	0
707	Doubling between Jaunpur Jn - Zaffarabad 6.28 km (M/S SRC company Infra Private Limited) (617370)	Uttar Pradesh	03/2023 (02/2025)	01/2027 (-)	180.66 (180.66)	4	10
708	Domingarh-Gorakhpur-Gorakhpur Cantt.-Kusumhi - 3rd Railway Line Project (North Eastern Railway [NER]) (705566)	Uttar Pradesh	11/2016 (06/2018)	02/2025 (09/2025)	351 (521.47)	499.64	98
709	Burhwal Gonda 3rd line (North Eastern Railway [NER]) (705567)	Uttar Pradesh	11/2017 (07/2019)	03/2025 (11/2025)	1016 (1118)	1373.8	73
710	Janghai-Pratapgarh- Amethi (CAO/C/III/IR) (705588)	Uttar Pradesh	11/2017 (03/2017)	03/2025 (03/2026)	722 (1194)	1567	70

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
711	Lalitpur-Birari with flyover at Lalitpur- 16 Km (North Central Railway) (705766)	Uttar Pradesh	03/2017 (11/2017)	12/2024 (01/2026)	304.44 (356)	224.8	75
712	Allahabad-Bamhrauli Flyover Construction & 4th Railway Line Project (North Central Railway) (705771)	Uttar Pradesh	04/2019 (10/2020)	03/2026 (03/2026)	494 (494)	333	70
713	Mughalsarai-Allahabad, 3rd line (North Central Railway) (705772)	Uttar Pradesh	12/2015 (03/2016)	12/2026 (03/2027)	2649 (2649.44)	1561.89	62
714	Aligarh -Daud Khan Flyover Construction & 3rd Railway Line Project (CAO/C/INCR) (705774)	Uttar Pradesh	04/2019 (09/2020)	01/2025 (03/2027)	758 (779.49)	319.14	55
715	Bhandai - Flyover for Etawah bound down train- 10 Km (North Central Railway (NCR) - II) (705777)	Uttar Pradesh	07/2020 (04/2021)	02/2026 (02/2027)	250.18 (250.18)	113.94	3
716	Phephna-Indara, Mau-Shahganj doubling excluding Indara-Mau (South Eastern Railway [SER] - I) (705779)	Uttar Pradesh	05/2017 (10/2019)	12/2024 (03/2026)	1178 (1777)	1489.5	85
717	Bhatni-Aurnihar with electrification excluding Indara-Mau (RVNL - II) (705780)	Uttar Pradesh	03/2018 (03/2017)	12/2024 (10/2025)	2529 (2529.46)	2051.69	94
718	Barabanki-Malhaur 3rd & 4th Railway Line Project (CAO/C/INR) (705782)	Uttar Pradesh	01/2019 (04/2017)	03/2025 (03/2026)	407 (407)	317	75
719	Janghai-Phaphamau Doubling Rail Line Project (RVNL) (705784)	Uttar Pradesh	11/2018 (03/2020)	03/2025 (03/2025)	357 (978.77)	579	95
720	Bahraich - Nanpara - Nepalganj Road Gauge Conversion (North Eastern Railway [NER]) (705863)	Uttar Pradesh	07/2020 (04/2021)	07/2025 (09/2025)	950 (550)	507.02	100
721	Rishikesh-Karnaprayag New Rail Line- 125 km (RVNL - II) (705429)	Uttarakhand	11/2016 (08/2018)	12/2025 (03/2027)	38953 (38953)	24645.15	65
722	Kalinarayanpur-Krishnanagar Doubling Alongwith Krishnanagar - Chapra New Line And Naihati-Ranaghat 3rd Line. (Eastern Railway [ER] - I) (400247)	West Bengal	07/2015 (11/2005)	02/2027 (02/2027)	1000 (1000)	1034.35	67
723	Tarakeshwar-Bishnupur New Line [82.47 km] (Eastern Railway [ER] - I) (400273)	West Bengal	03/2001 (02/2008)	03/2019 (02/2026)	1189 (1542)	1320.81	91
724	Dum Dum Airport-New Garia via Rajarhat-Construction of Metro Railway (RVNL - II) (400277)	West Bengal	03/2010 (10/2011)	12/2025 (03/2026)	8964 (8964)	8097.47	80
725	Construction of Balurghat-Hilli new BG Line (Northeast Frontier Railway [NFR]) (612096)	West Bengal	12/2010 (12/2010)	03/2027 (03/2025)	1209 (1209)	405.31	9
726	SER Upgradation of maintenance infrastructure at Shalimar into Vande Bharat Chair Car maintenance cum workshop depot. (South Eastern Railway - JH) (617345)	West Bengal	NA (12/2024)	10/2026 (-)	226.87 (226.87)	0.21	5
727	Joka-BBD Bag new metro project (RVNL - II) (705730)	West Bengal	03/2010 (04/2010)	12/2026 (12/2028)	4835 (10362)	4485.2	59
728	Noapara-Barasat via Bimanbandar - Construction of Metro railway [18 km] (Metro Railway, Kolkata) (706776)	West Bengal	11/2010 (03/2010)	08/2026 (03/2029)	4830 (4830)	2764.13	32
729	Baranagar-Barrackpore and Dakshineshwar- Construction of Metro Railway (RVNL - II) (706777)	West Bengal	03/2010 (03/2010)	12/2026 (12/2025)	2298 (2734)	393	17
	Total (247)				812091.77	531130.95	
	Department for Promotion of Industry & Internal Trade						
	Real Estate						
730	Krishnapatnam Node - Phase 1 - Roads and Services Development (National Industrial Corridor Development Corporation) (701658)	Andhra Pradesh	12/2020 (02/2024)	02/2028 (-)	2139.44 (2139.44)	470.66	21
731	Tumakuru Node - Phase 1 - Roads and Services Development (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (701657)	Karnataka	12/2020 (02/2023)	09/2026 (-)	1701.81 (1701.81)	117.01	9
	Total (2)				3841.25	587.67	
	Department of Telecommunications						
	Telecommunication						
732	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance (Erstwhile NICF)) (709859)	Delhi	10/2014 (04/2018)	02/2020 (10/2025)	248.2 (248.2)	236.91	98
733	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (09/2025)	971.96 (971.96)	208.25	99
734	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase 1 Upgradation (Department of Telecommunications [DoT]) (617413)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	04/2022 (05/2024)	05/2025 (11/2025)	1884.6 (1884.6)	100	55

All Ongoing Projects							SEPTEMBER 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
735	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 (Department of Telecommunications [DoT]) (701599)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	NA (09/2021)	03/2023 (11/2025)	1577.57 (1577.57)	600.04	87
736	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha (Department of Telecommunications [DoT]) (701602)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	11/2021 (05/2022)	11/2023 (11/2025)	3685 (3685)	1135.28	80
737	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (09/2025)	1255.49 (1255.49)	284.04	91
738	354 Uncovered Villages Scheme (Department of Telecommunications [DoT]) (701600)	Multi-States (Bihar, Gujarat, Himachal Pradesh, Jammu and Kashmir, Ladakh, Rajasthan, Uttar Pradesh)	12/2019 (04/2020)	10/2021 (08/2025)	336.89 (301.13)	227.82	97
739	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajasthan and Uttar Pradesh (Department of Telecommunications [DoT]) (704495)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	NA (03/2021)	03/2022 (12/2025)	421.65 (228.94)	134.51	96
740	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (709749)	Multi-States (Maharashtra, Telangana)	03/2020 (03/2020)	06/2021 (12/2025)	461.42 (461.42)	166.02	81
741	Saturation 4G mobile coverage of Uncovered Villages through USOF (Department of Telecommunications [DoT]) (400013)	PAN India	07/2022 (07/2022)	06/2024 (03/2026)	26316 (30620)	9791.8	75
742	4G Services by BSNL (Department of Telecommunications [DoT]) (701593)	PAN India	11/2020 (11/2020)	03/2024 (03/2026)	28466 (19592)	8419.04	96
743	BharatNet (Department of Telecommunications [DoT]) (706775)	PAN India	07/2017 (10/2011)	08/2023 (03/2027)	61109 (188000)	41486.14	81
744	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (709856)	PAN India	05/2023 (05/2023)	08/2024 (10/2025)	645.13 (645.13)	376.72	92
745	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. (BSNL) (709857)	PAN India	05/2023 (06/2023)	06/2025 (03/2026)	24544.55 (24544.5)	8419.89	96
746	OPTICAL TRANSPORT NETWORK [OTN] PH-4 IN BSNL (BSNL) (709858)	PAN India	02/2024 (02/2024)	08/2025 (10/2025)	810.99 (810.99)	786.3	100
Total (15)					152734.45	72372.76	
Department of Water Resources, River Development & GR							
Waste & Water							
747	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616600)	Bihar	10/2017 (03/2022)	02/2025 (12/2025)	413.29 (413.29)	126.67	97
748	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616611)	Bihar	08/2017 (07/2019)	12/2025 (-)	824 (824)	396.71	56
749	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616612)	Bihar	08/2017 (07/2019)	12/2025 (-)	578.89 (578.89)	171.79	54
750	Sewer Network, SPS and STP at Begusarai (National Mission for Clean Ganga) (616615)	Bihar	03/2010 (03/2018)	04/2025 (12/2025)	230.06 (230.06)	261.82	97
751	Sewer Networks, SPS and STP at Hajipur (National Mission for Clean Ganga) (616616)	Bihar	03/2010 (03/2018)	06/2025 (12/2025)	305.19 (305.19)	346.46	95
752	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme (National Mission for Clean Ganga) (616594)	Uttar Pradesh	05/2020 (04/2023)	04/2025 (12/2025)	842.25 (842.25)	208.64	73
753	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP (National Mission for Clean Ganga) (616605)	Uttar Pradesh	05/2020 (11/2024)	12/2024 (05/2027)	690.71 (690.71)	34.79	27
754	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP (National Mission for Clean Ganga) (616604)	West Bengal	05/2018 (12/2021)	03/2025 (12/2025)	154.73 (154.73)	96.17	92
Total (8)					4039.12	1643.05	



All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Water Resources						
755	Sardar Gouthu Latchanna Thotapalli Barrage Project (<i>Water Resources-AP</i>) (400100)	Andhra Pradesh	04/2005 (01/2006)	12/2019 (06/2026)	353.05 (1023.24)	869.11	95
756	Gundlakamma project (<i>Water Resources-AP</i>) (400101)	Andhra Pradesh	04/2005 (04/2005)	12/2019 (03/2027)	397.41 (697.39)	619.09	98
757	Polavaram Irrigation Project (<i>Water Resources-AP</i>) (701415)	Andhra Pradesh	01/2009 (11/2009)	04/2022 (03/2026)	10151.04 (55548.9)	24745.92	84
758	Borolia Irrigation Project (<i>Department of Water Resources, River Development & GR</i>) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55
759	Punpun Barrage Project (<i>Water Resources-BR</i>) (400104)	Bihar	04/2007 (04/2007)	12/2019 (03/2026)	571.07 (658.12)	447.68	44
760	Kelo Irrigation Project (<i>Water Resources-CT</i>) (400111)	Chhattisgarh	04/2008 (04/2008)	12/2019 (06/2026)	459.97 (727.04)	616.93	72
761	Kudali Irrigation Project (<i>Department of Water Resources, River Development & GR</i>) (701399)	Chhattisgarh	04/2009 (12/2009)	12/2025 (-)	382.29 (382.29)	0	86
762	Sardar Sarovar CADWM Project (<i>Narmada and Water Resources, Water Supply and Kalpsar Department-GJ</i>) (400097)	Gujarat	04/2017 (04/2017)	12/2019 (03/2026)	5021.76 (6670.31)	4954.99	90
763	Sardar Sarovar Project (<i>Narmada and Water Resources, Water Supply and Kalpsar Department-GJ</i>) (701372)	Gujarat	04/1996 (04/1996)	12/2019 (03/2026)	20718.17 (33412.5)	31860.86	93
764	Subernarekha Multipurpose Project, Jharkhand (<i>Department of Water Resources-JH</i>) (701376)	Jharkhand	04/2011 (01/2012)	12/2019 (03/2026)	3807.77 (9579.58)	5561.97	69
765	Upper Tunga Irrigation Project (<i>Water Resources-KA</i>) (701377)	Karnataka	04/2014 (04/2014)	12/2019 (03/2026)	770.16 (1606.07)	1515.32	99
766	Omkareshwar CADWM Project (<i>Water resource-mp</i>) (400096)	Madhya Pradesh	04/2017 (04/2017)	12/2019 (03/2026)	648.09 (648.09)	172.56	3
767	Bargi Diversion Project Phase - IV [km. 154 to km 197] (<i>Water Resources-MP</i>) (400115)	Madhya Pradesh	04/2008 (01/2009)	12/2019 (03/2026)	751.03 (893.35)	746.19	75
768	Bargi Diversion Project Phase - III [km. 104 to km 154] (<i>Water Resources-MP</i>) (400116)	Madhya Pradesh	04/2007 (04/2007)	12/2019 (03/2026)	1229.15 (1399.7)	1906.5	80
769	Gosikhurd CADWM Project (<i>Department of water resources-MH - II</i>) (400095)	Maharashtra	04/2017 (04/2017)	12/2019 (06/2026)	743.73 (743.73)	252.43	50
770	Urmodi Irrigation Project (<i>Department of water resources-MH - II</i>) (400105)	Maharashtra	04/2017 (04/2018)	06/2022 (12/2026)	580.79 (895.81)	713.46	76
771	Sulwade-Jamphal-Kanoli Lift Irrigation Scheme (<i>Department of water resources-MH - II</i>) (400107)	Maharashtra	04/2017 (02/2019)	06/2023 (06/2027)	2407.67 (2407.67)	2559.71	80
772	Purna Barrage-2 [Ner Dhamana] Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (400109)	Maharashtra	04/2017 (04/2018)	06/2020 (06/2026)	848.07 (888.43)	690.49	69
773	Jigaon Irrigation Project (<i>Department of water resources-MH - II</i>) (400112)	Maharashtra	04/2017 (04/2018)	06/2028 (-)	7222.95 (7222.95)	8722.81	90
774	Bodwad Parisar Sinchan Yojna (<i>Department of Water Resources-MH</i>) (617422)	Maharashtra	05/2002 (01/2017)	07/2027 (-)	1923.81 (1923.81)	1770.13	49
775	Waghur Project (<i>Department of water resources-MH - II</i>) (701383)	Maharashtra	04/1996 (04/1996)	12/2019 (03/2026)	1058.99 (1758.51)	1557.14	89
776	Gosikhurd Project (<i>Department of water resources-MH - II</i>) (701386)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2028)	7196.47 (12770.1)	13691.13	72
777	Aruna Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (701391)	Maharashtra	04/2009 (01/2010)	12/2019 (12/2025)	210.45 (1472.14)	1697.94	97
778	Lower Pedhi Project (<i>Department of water resources-MH - II</i>) (701396)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2026)	255.97 (1480.7)	1324.78	65
779	Nardave Medium Irrigation Project (<i>Department of water resources-MH - II</i>) (701398)	Maharashtra	04/2009 (04/2009)	12/2019 (06/2026)	211.46 (781.85)	623.5	72
780	Thoubal Multipurpose Project (<i>Water Resources Department-MN</i>) (701400)	Manipur	04/1997 (04/1997)	12/2019 (03/2026)	1449.44 (1822.24)	1837.91	98
781	North Koel Reservoir Project (<i>Department of Water Resources, River Development & GR</i>) (701412)	Multi-States (Bihar, Jharkhand)	08/2017 (01/2021)	03/2021 (03/2026)	1622.27 (2430.76)	151.04	32
782	Integrated Anandpur Barrage Project (<i>Water Resources-OR</i>) (603945)	Odisha	04/1997 (01/1998)	12/2019 (06/2026)	567.03 (2990.05)	2629.74	62
783	Kanupur Irrigation Project (<i>Irrigation and CAD-TG</i>) (701404)	Odisha	04/2003 (01/2004)	12/2019 (06/2026)	989.43 (2301.28)	2712.75	79
784	Relining of Rajasthan feeder and Sirhind Feeder canal (<i>Department of Water Resources-PB</i>) (701410)	Punjab	02/2016 (04/2018)	06/2021 (06/2026)	1441.26 (2462.16)	3000.36	80

All Ongoing Projects

SEPTEMBER 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
785	Shahpur Kandi Dam Project (Department of Water Resources-PB) (701411)	Punjab	02/2010 (04/2018)	06/2022 (10/2025)	2285.81 (2715.7)	2072.33	80
786	Sri Ram Sagar Project Stage - II (Irrigation and CAD-TG) (400102)	Telangana	04/2005 (04/2005)	12/2019 (03/2026)	736.13 (949.87)	940.7	96
787	Indiramma Flood Flow Canal Project (Irrigation and CAD-TG) (400103)	Telangana	04/2005 (01/2006)	12/2019 (12/2026)	1331.3 (5940.09)	4491.08	92
788	J. Chokka Rao Devadula Lift Irrigation Scheme (Irrigation and CAD-TG) (701405)	Telangana	04/2006 (04/2006)	12/2019 (12/2025)	8200.71 (14730)	4558.89	87
789	Rajiv Bhima Lift Irrigation Scheme (Irrigation and CAD-TG) (701406)	Telangana	04/2007 (01/2008)	12/2019 (03/2026)	1402 (2509.66)	1839.76	100
790	Saryu Nahar CADWM Project (Irrigation & Water Resources-UP) (400093)	Uttar Pradesh	04/2017 (04/2017)	12/2019 (03/2026)	1672.7 (1672.7)	22.24	1
791	Morna [Gureghar] Irrigation Project (Department of Water Resources, River Development & GR) (701395)	Uttar Pradesh	04/2007 (12/2007)	12/2025 (-)	219.9 (219.9)	0	31
792	Madhya Ganga canal Phase-II (Irrigation & Water Resources-UP) (701408)	Uttar Pradesh	04/2008 (04/2008)	12/2019 (12/2025)	1060.67 (4417.21)	4415.24	82
793	Jamrani Dam Multipurpose Project (Irrigation-UK) (613787)	Uttarakhand	10/2023 (11/2023)	06/2029 (-)	2584.1 (2584.1)	968.52	16
Total (39)					93740.23	137305.9	



सत्यमेव जयते

**Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.ipm.mospi.gov.in>**
